

DESIGN USER GUIDE



Information in this document is subject to change without notice. Companies, names and data used in examples are fictitious.

Copyright ©2026 by InEight. All rights reserved. No part of this document may be reproduced or transmitted in any form or by any means, electronic or mechanical, for any purpose, without the express permission of InEight.

Microsoft Windows, Internet Explorer and Microsoft Excel are registered trademarks of Microsoft Corporation.

Although InEight Design has undergone extensive testing, InEight makes no warranty or representation, either express or implied, with respect to this software or documentation, its quality, performance, merchantability, or fitness for purpose. As a result, this software and documentation are licensed “as is”, and you, the licensee are assuming the entire risk as to its quality and performance. In no event will InEight be liable for direct, indirect, special, incidental or consequential damages arising out of the use or inability to use the software or documentation.

Release 26.7
Last Updated: 14 September 2026

CONTENTS

InEight Design	10
CHAPTER 1 – INEIGHT DESIGN OVERVIEW	11
1.1 Open Design	12
1.1.1 Summary	12
1.1.2 Steps	12
CHAPTER 2 – ADMINISTRATION	15
2.1 Administration overview	15
2.1 Organizational settings for Engineering	17
2.1.1 Considerations	17
2.2 Project values	17
2.2.1 Considerations	18
2.3 Disciplines	19
2.3.1 Steps	19
2.3.2 Considerations	20
2.4 Resource types	20
2.4.1 Steps	20
2.4.2 Considerations	21
2.5 Milestones	21
2.5.1 Steps	22
2.5.2 Considerations	22
2.6 Design elements	22
2.6.1 Steps	23
2.6.2 Considerations	24
2.7 Teams	24
2.7.1 Steps	25
2.7.2 Considerations	25
2.8 Resources	25
2.8.1 Steps	26
2.8.2 Considerations	27
2.9 Account code set	27
2.9.1 Steps	29
2.9.2 Considerations	32
2.10 Cause codes	32

2.10.1 Steps	32
2.10.2 Considerations	33
2.11 Project settings for Engineering	33
2.12 Project values	34
2.12.1 Summary	34
2.12.2 Considerations	36
2.12.3 Related links	36
2.13 Account code set	36
2.13.1 Considerations	37
2.14 Resource types	37
2.14.1 Steps	38
2.14.2 Considerations	39
2.15 Milestones	39
2.15.1 Considerations	40
2.15.2 Related links	40
2.16 Teams	40
2.16.1 Manage teams	41
2.16.2 Resource assignment	41
2.16.3 Considerations	43
2.17 Resources	44
2.17.1 Considerations	44
2.18 Control settings	45
2.18.1 Allow claims to exceed Forecast TO quantity in Control	45
2.18.2 Select a unit rate that will be used to calculate planned man-hours ..	46
2.18.3 Considerations	46
2.19 Dates	46
2.19.0.1 Enable scope item dates	47
2.19.1 Consideration	48
2.20 Documents	48
2.20.1 Document integration	49
2.20.1.1 Document types	50
2.20.1.2 Selected Document Types	50
Associate documents	50
2.20.2 Considerations	50
2.21 Organizational settings for Quantity Forecasting	50
2.21.1 Considerations	51
2.22 Project values	51
2.22.1 Considerations	53

2.23 Account code and discipline sets	53
2.23.1 Considerations	53
2.24 Discipline set	54
2.24.1 Steps	54
2.24.2 Considerations	55
2.25 Account code set	56
2.25.1 Steps	56
2.25.2 Considerations	59
2.26 Design tracking stages	59
2.26.1 Steps	60
2.26.2 Considerations	60
2.27 Design elements	60
2.27.1 Steps	61
2.27.2 Considerations	62
2.28 Notes	62
2.28.1 Tags	62
2.28.2 Steps	63
2.28.3 Considerations	63
2.29 Cause codes	63
2.29.1 Steps	64
2.29.2 Considerations	65
2.30 Project settings for Quantity forecasting	65
2.31 General	65
2.31.1 Considerations	69
2.32 Design element setup	69
2.32.1 Steps	70
2.32.2 Considerations	71
2.33 Design tracking stages	71
2.33.1 Steps	71
2.33.2 Considerations	72
2.34 Attributes and project values	72
2.34.1 Attributes	74
2.34.2 Project values	74
2.34.3 Considerations	74
2.35 Component integration	74
2.35.1 Plan Component Integration	74
2.35.2 Considerations	75
2.36 Linked engineering projects	75
2.36.0.1 Integration with Plan	78

2.36.1 Steps	78
Link projects	78
CHAPTER 3 – ENGINEERING MODULE OVERVIEW	79
3.0.1 Summary	79
3.1 Scope items	79
3.2 Scope items overview	79
3.2.1 Project views	80
3.2.2 Column filter menus	82
3.2.3 Lock columns	82
3.2.4 Scope Item page audit columns	82
3.3 Scope items	83
3.3.1 Summary section	84
3.3.2 Notes section	85
3.4 Add scope items	86
3.4.1 Add a scope item	86
Adding a scope item	86
3.4.2 Import new scope items	88
3.4 Step by Step 1 – Import scope items	88
3.5 Edit scope items	89
3.5.1 Edit a scope item	89
Editing a scope item	89
3.5.2 Edit scope items in bulk	90
3.6 Update scope item quantities	92
3.6.1 Update scope item quantities with no claiming	92
3.6.2 Update scope item quantities with claiming	93
3.6 Step by Step 1 – Updating scope item quantity	95
3.6.3 Update scope item quantities by import	97
3.6 Step by Step 2 – Updating scope item quantity by import	97
3.6.4 Scope item quantity history	98
3.7 Scope item resources	99
3.7.1 Considerations	100
3.8 Scope item claiming	101
3.8.1 Summary	101
3.8.2 Considerations	101
3.8.3 Claim on a scope item	101
3.8 Step by Step 1 – Claim a step on a scope item	102
3.8.4 Import claiming in bulk	103
3.8 Step by Step 2 – Importing claiming	103

3.8.5 Undo claiming	104
3.8 Step by Step 3 – Undo claim for a step	105
3.8 Step by Step 4 – Undo claim for a scope item	105
3.9 Project values in scope items	106
3.9.1 Project value status	107
Update a project value	108
3.10 Compliance issues	108
3.11 Audit log	110
3.12 Vendor access to scope items	112
3.13 Actions	113
3.14 Actions overview	113
3.15 Documents	115
3.16 Documents overview	115
3.16.1 Column filters	116
3.16.2 Lock and unlock columns	116
3.16.3 Considerations	117
3.17 Claiming	117
3.18 Claiming overview	117
3.18.1 Claiming tab columns	119
3.18.2 Lock columns	120
3.18.3 Column filter menus	120
3.19 Manage claiming	120
3.19.1 Claim items	121
3.19.1.1 Sync to document	123
3.19.2 Undo claiming	123
3.19.3 Navigate to claiming schemes	126
3.20 Manage scope items in Claiming	127
3.20.1 Edit scope items	127
3.20.2 View scope item claim details and document associations	128
3.21 Mapping	128
3.22 Mapping overview	128
3.23 Map documents and scope items	130
3.23.1 Manually map items	131
Map documents to scope items	131
Map scope items to documents	132
3.23.2 Auto map	132
3.23.3 Import from a template	132
3.23.4 Scope item dialog box	134
3.24 Associated items	135

3.24.1 Scope items grid	135
3.24.2 Documents grid	136
3.24.3 Unlink associated items	137
Unlink associated items	138
3.24.4 Mapped documents removed from InEight Document	138
3.25 Summary	139
3.26 Claiming schemes	139
3.27 Claiming schemes overview	139
3.27.1 Columns	140
3.28 Manage claiming schemes	141
3.28.1 Add a claiming scheme manually	142
3.28.2 Considerations	142
3.28 Step by Step 1 – Adding a claiming scheme manually	142
3.28.3 Copy a claiming scheme	144
3.28 Step by Step 2 – Copying an existing claiming scheme	144
3.28.4 Import claiming schemes	145
3.28 Step by Step 3 – Import claiming schemes using the Excel template	145
3.29 Document integration - Claiming schemes	146
3.30 Work packages	147
3.31 Work packages	147
3.32 Work packages Overview page	149
3.33 Project values	151
3.33 Step by Step 1 – Add a project value manually	152
3.34 Lock and unlock project scope	153
3.35 Role assignment	153
3.35.1 Considerations	154
3.35 Step by Step 1 – Assign a role, planned team, and user to a resource type	155
3.36 Change integration – Associate scope items to issues	156
3.36.1 Associate a Change issue	156
3.36.2 View number of assigned issues	156
CHAPTER 4 – QUANTITY FORECASTING MODULE OVERVIEW	159
4.0.1 Summary	159
4.1 Quantity items	159
4.1.1 Considerations	160
4.2 Add a quantity item	161
4.2.1 Summary	161
4.2.2 Considerations	161

4.2.3 Steps	161
4.3 Project values	162
4.3.1 Project value status	163
Update a project value	164
4.4 Components section	165
4.4.1 Component ID link	166
4.5 Observations section	167
4.5.1 Observation ID link	168
4.6 Quantity driver	169
4.6.1 Summary	169
4.6.2 Considerations	170
4.7 Data export	170
4.7.1 Summary	170
4.7.2 Considerations	170
4.7.3 Steps	171
4.8 Actions	171
4.8.1 Considerations	172
4.9 Get Control unit rates	172
4.9.1 MHrs Delta columns	173
4.9.2 Get FC Remaining MHrs/Unit - Manual Rate column	174
4.9.3 Considerations	174
4.10 Get Plan components	174
4.10.1 Considerations	176
4.11 Lock and unlock scope	176
4.11.1 Considerations	177
4.12 Observations	177
4.13 Add Observations	179
Add an observation	179
4.13.1 Considerations	179
4.14 Associate to quantity items	179
4.14.1 Considerations	179
Associate quantity items to an observation from the Quantity Items page	180
Associate quantity items to an existing observation	180
4.15 Associate to design elements	180
4.15.1 Considerations	181
Associate design elements to an existing observation	181
4.16 Video Index	183

INEIGHT DESIGN

InEight Design puts you in control of design scope, design deliverables and design quantities. And when combined with InEight Document Control & Turnover, it also helps you manage review and approval workflows associated with design documentation.

InEight Design can use earned value management (EVM) to bring more detail and credibility to the design and engineering phase. Earned value management allows you to track progress on a design project more accurately, avoiding last-minute surprises and overly optimistic reports.

BUILD

Stay in control of engineering project scope, deliverables, and design quantity forecasts.

CONNECT

Manage engineering project budgets, earned values and document workflows.

INNOVATE

Get full visibility across design and construction with a comprehensive project controls solution for design-build projects — before the build starts.

See Design topics below:

CHAPTER 1 – INEIGHT DESIGN OVERVIEW

InEight Design is a design management application that lets designers, engineers, and contractors manage deliverables and quantities during the design process. Design gives you visibility into a project before the design is complete so that you can mitigate risk. Design is especially useful for projects that use alternative delivery methods such as engineering, procurement, and construction (EPC) and design-build. Design brings designers, engineers, and contractors together into one application to stay on top of risks and project delivery impacts and provide transparency.

Design consists of two modules: Engineering and Quantity forecasting. Your organization might use one module more than the other depending on your industry and business processes.

The Engineering module lets you plan, allocate resources, and track the progress of design scope and deliverables.

Quantity forecasting lets EPC contractors consume design changes in quantity form, relate design changes and quantities to the budget, forecast, resource needs, and schedule, among other needs.

Design also integrates with the following InEight applications:

- Control – Budget data is used to accurately forecast.
- Report – Compares latest design quantity to the Control budget.
- Explore – Dashboards are available for both modules.
- Plan – Component data can be sent to Quantity forecasting.

1.1 OPEN DESIGN


1.1.1 Summary

You can open Design from the main menu at the project level.


1.1.2 Steps

To open Design using the main menu at the project level:

1. Use the URL provided, and then open the InEight software in your web browser.
2. Open the **Main menu**, and then click **All projects & organizations**.

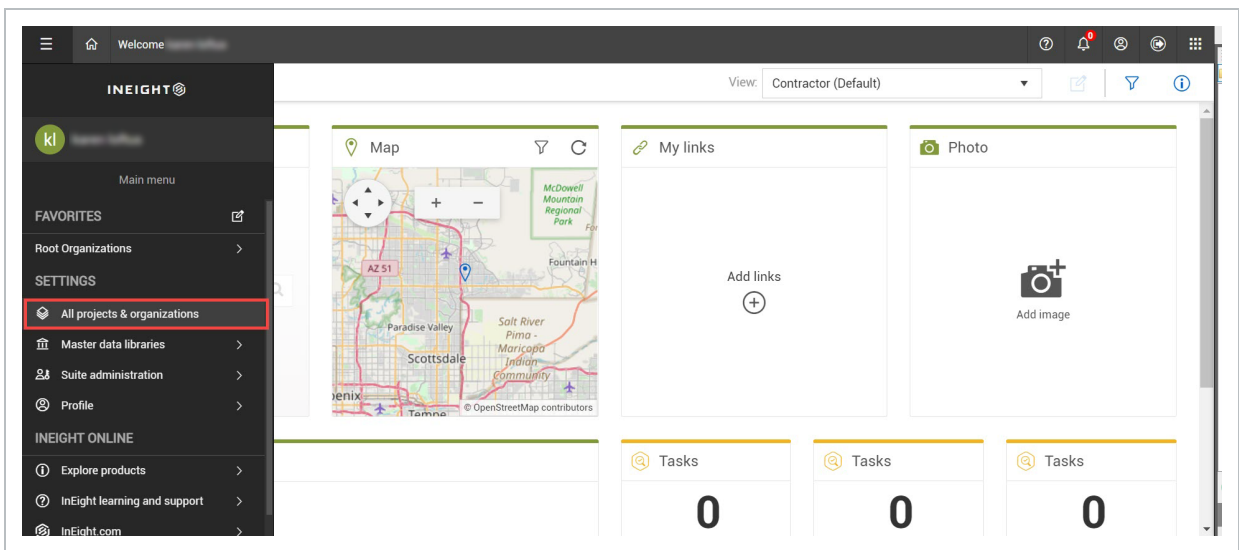


3. From the Projects tab of the All projects & organizations page, select a project by clicking the project name hyperlink. The Project home landing page opens.

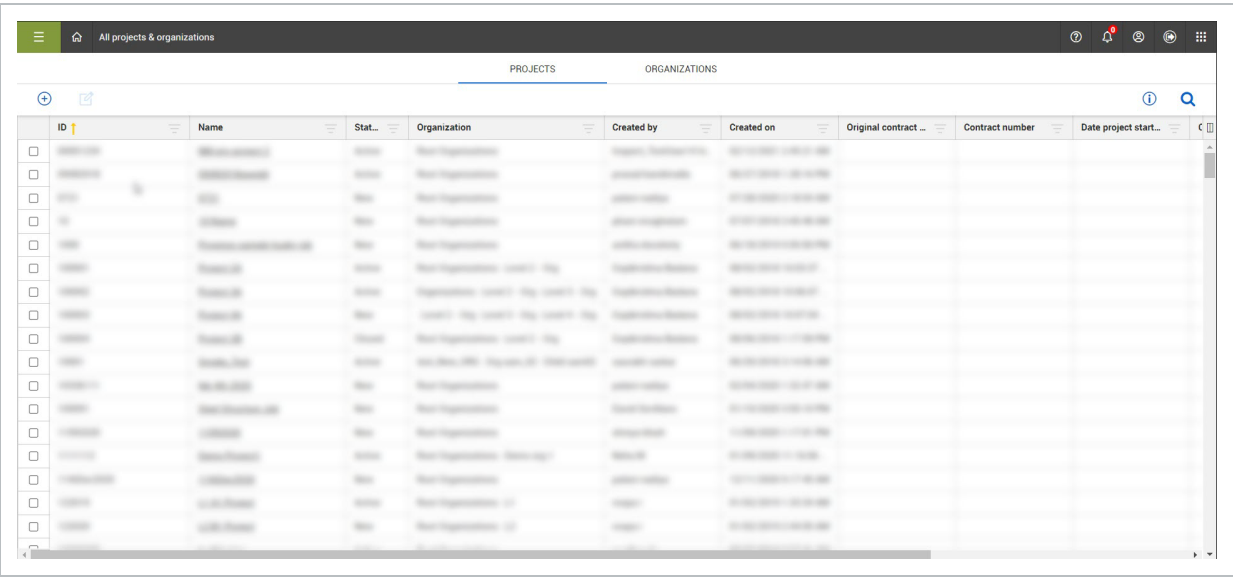


ID	Name	Stat...	Organization	Created by	Created on	Original contract ...	Contract number	Date project start...
1050	Steel Structure Training Job 1050	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1051	Steel Structure Training Job 1051	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1052	Steel Structure Training Job 1052	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1053	Steel Structure Training Job 1053	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1054	Steel Structure Training Job 1054	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1055	Steel Structure Training Job 1055	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1056	Steel Structure Training Job 1056	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1057	Steel Structure Training Job 1057	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1058	Steel Structure Training Job 1058	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1059	Steel Structure Training Job 1059	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1060	Steel Structure Training Job 1060	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1061	Steel Structure Training Job 1061	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1062	Steel Structure Training Job 1062	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1063	Steel Structure Training Job 1063	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1064	Steel Structure Training Job 1064	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1065	Steel Structure Training Job 1065	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1066	Steel Structure Training Job 1066	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1067	Steel Structure Training Job 1067	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1068	Steel Structure Training Job 1068	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1069	Steel Structure Training Job 1069	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1070	Steel Structure Training Job 1070	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1071	Steel Structure Training Job 1071	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1072	Steel Structure Training Job 1072	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1073	Steel Structure Training Job 1073	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1074	Steel Structure Training Job 1074	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1075	Steel Structure Training Job 1075	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1076	Steel Structure Training Job 1076	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1077	Steel Structure Training Job 1077	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1078	Steel Structure Training Job 1078	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1079	Steel Structure Training Job 1079	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1080	Steel Structure Training Job 1080	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1081	Steel Structure Training Job 1081	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1082	Steel Structure Training Job 1082	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1083	Steel Structure Training Job 1083	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1084	Steel Structure Training Job 1084	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1085	Steel Structure Training Job 1085	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1086	Steel Structure Training Job 1086	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1087	Steel Structure Training Job 1087	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1088	Steel Structure Training Job 1088	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1089	Steel Structure Training Job 1089	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1090	Steel Structure Training Job 1090	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1091	Steel Structure Training Job 1091	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1092	Steel Structure Training Job 1092	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1093	Steel Structure Training Job 1093	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1094	Steel Structure Training Job 1094	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1095	Steel Structure Training Job 1095	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1096	Steel Structure Training Job 1096	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1097	Steel Structure Training Job 1097	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1098	Steel Structure Training Job 1098	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1099	Steel Structure Training Job 1099	New	New Organization	John Doe	10/10/2020 10:10:10 AM			
1100	Steel Structure Training Job 1100	New	New Organization	John Doe	10/10/2020 10:10:10 AM			

If your project is not shown on the initial screen, you can search by clicking the **Search** icon in the upper right. This search function searches all terms in all columns.

- 4. From the Project home landing page, click the **Main menu** icon, and then click the **project name** to open the second-level menu.



- 5. From the second-level drop-down menu, select **Design**, and then select the **Engineering** or **Quantity forecasting** module.



CHAPTER 2 – ADMINISTRATION

2.1 ADMINISTRATION OVERVIEW

As an administrator, you can manage settings for the Engineering and Quantity forecasting modules at the organization and project levels.

- **Organizational settings** - Settings configured are inherited by projects within the organization. You can configure organizational settings in Main menu > <organization> > Settings > **Design**.
- **Project settings** - Settings configured at the project level are applied throughout the project. You can configure Engineering settings for your project in Settings > **Design**.

This page intentionally left blank.

2.1 ORGANIZATIONAL SETTINGS FOR ENGINEERING

As an administrator, you can configure settings for the Engineering module at the organization level. Settings at the organization level are inherited by associated child organizations and projects.

The organization Engineering settings gives you access to the following configurations:

- [Project values](#)
- [Disciplines](#)
- [Resource types](#)
- [Milestones](#)
- [Design elements](#)
- [Teams](#)
- [Resources](#)
- [Account code set](#)
- [Cause codes](#)

You can manage engineering settings for your organization in Settings > Design > **Engineering**.

For general information about InEight cloud platform settings, see [Organization Settings](#).

2.1.1 Considerations


You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

2.2 PROJECT VALUES

You can select which project values can be associated to engineering scope items and if they are required in a project. The values are managed in InEight cloud platform. For more information, see [Project values](#).


You can configure project values at the organization level in Settings > Design > Engineering > **Project values**. Project values configured at the organization level are available in all projects.

To configure project values, go to Engineering > **Project values**.

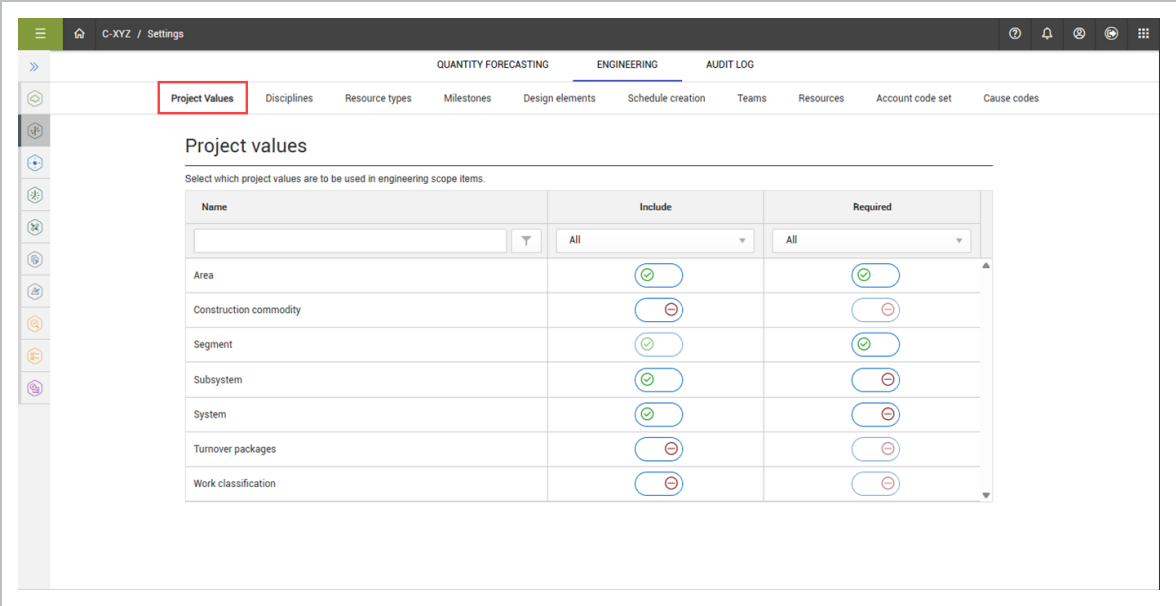

When you include project values, those values are available for selection in Settings at the project level. You can select or deselect the values that are not required for the project.

When you require a project value, the value is required at the project level. The project-level toggles for these values are automatically disabled.

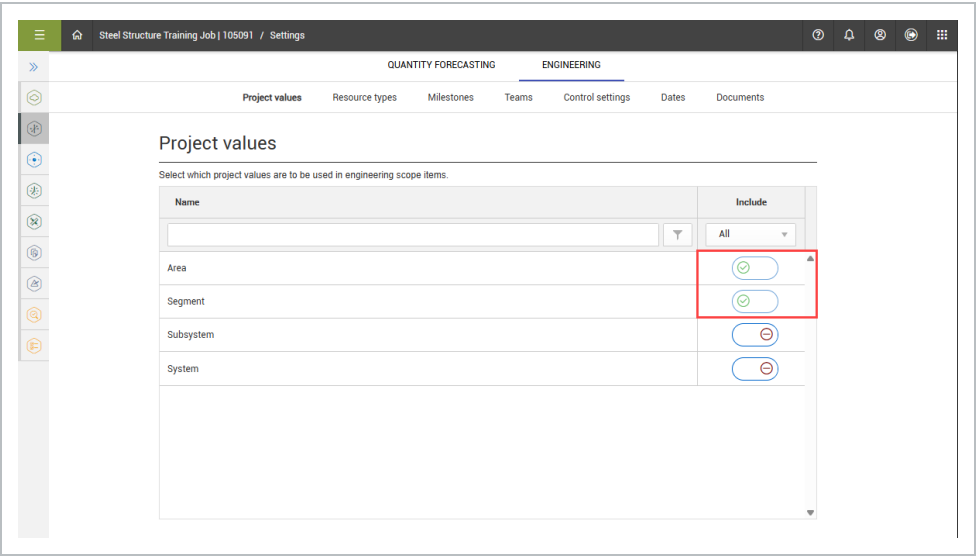


2.2.1 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

2.3 DISCIPLINES

You can define disciplines to associate with resource types and claiming schemes in the Engineering module. Examples of disciplines are architectural, civil, or drainage.

You can manage the disciplines for your organization in Settings > Design > Engineering > **Disciplines**.

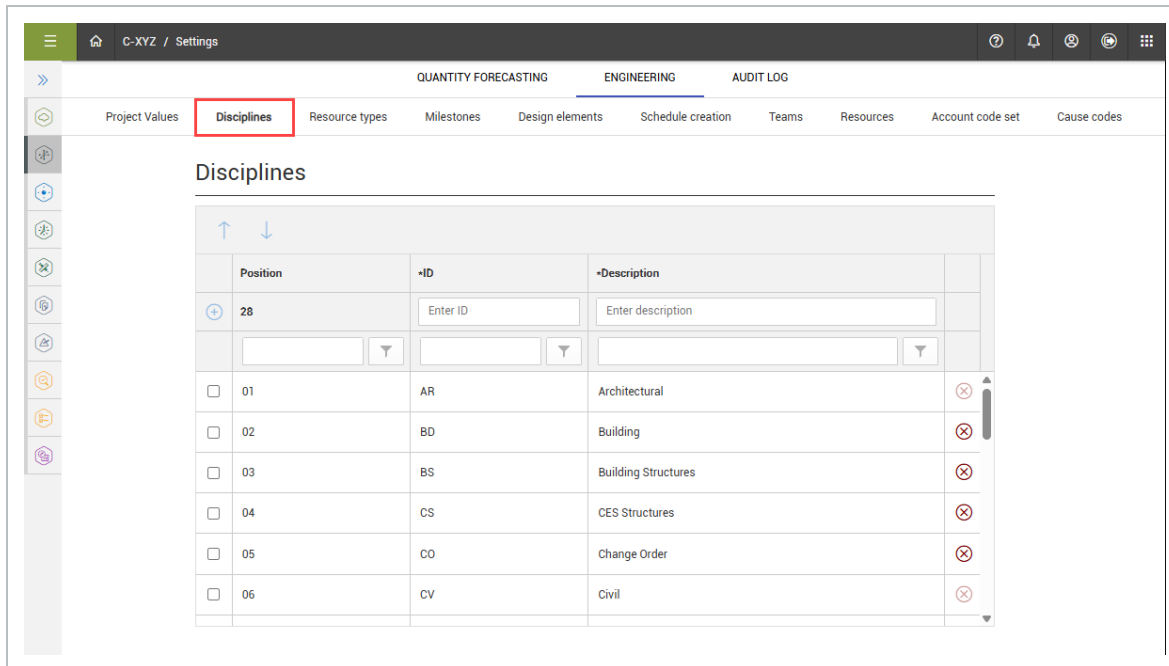

2.3.1 Steps

You can do any of the following actions:

- **Add** – Enter an ID and Description, and then click the **Add discipline** icon.
- **Edit** - Click in the fields, and then enter text.
- **Remove** - Click the **Remove discipline** icon to the right. You cannot remove a discipline assigned to a resource type or a claiming scheme.
- **Sort** - Select a discipline, and then click the up and down arrows to the right of the table to adjust the position of the discipline.

When disciplines are created, they become available to add in resource types and claiming schemes for projects in the organization. For more information, see [Resource types](#) in project settings and [Claiming schemes overview](#).

2.3.2 Considerations

- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Engineering.
- Disciplines must be added to create resource types.

2.4 RESOURCE TYPES

Resource types are associated with disciplines and must be added to add claiming schemes to projects. For more information, see [Claiming schemes overview](#). Each claiming scheme step must have an assigned resource type. Examples of resource types for an Electrical discipline might include Electrical Designer and Electrical Engineer. All resource types are automatically inherited to all projects in the organization.

You can manage resource types in your organization in Settings > Design > Engineering > **Resource types**.

Resource types

Position	ID	Description	Discipline
19	Enter ID	Enter description	<select><option>Select discipline</option></select>
Filter	Filter	Filter	<select><option>All</option></select>
☐ 01	EL	Electrical Lead	Electrical
☐ 02	EE	Electrical Engineer	Electrical
☐ 03	ED	Electrical Designer	Electrical
☐ 04	PM	Project Management	Indirect
☐ 05	ML	Mechanical Lead	Mechanical
☐ 06	ME	Mechanical Engineer	Mechanical

2.4.1 Steps

You can do any of the following actions:

- **Add** - Enter a resource ID, Description, select a discipline from the **Select discipline** drop-down list, and then click the **Add resource** icon.
- **Remove** - Click the **Remove resource type** icon to the right. You cannot remove a resource type that has been assigned to a project.
- **Edit** - Click in the fields, and then enter text.
- **Sort** - Select a resource type, and then click the up and down arrows to the right of the table to adjust the position of a resource type.

When resource types are created, they become available to add to claiming schemes for projects in the organization.

2.4.2 Considerations


- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Engineering.
- Disciplines must be added to create resource types.

2.5 MILESTONES

Milestones are attributes for claiming schemes. In projects, you can define completion milestones to be assigned to claiming scheme steps. Examples of completion milestones are Issue for Review or Issue for Construction. At the project level, all milestones from the parent organization are automatically inherited and you can assign or remove milestones as needed.

A system-generated milestone named Scope Complete is automatically assigned to every project to ensure that all scope item's scope can be planned with dates.

You can manage Milestones for your organization in Settings > Design > Engineering > **Milestones**.

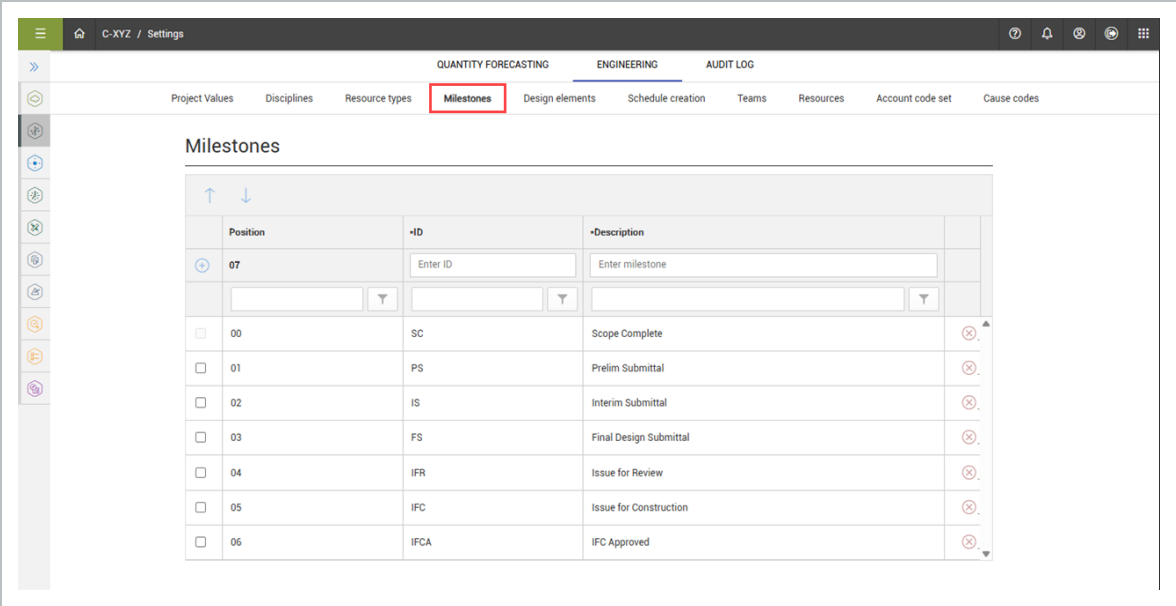

2.5.1 Steps

You can do any of the following actions:

- **Add** - Enter an ID and Description, and then click the **Add milestone** icon.
- **Remove** - Click the **Remove milestone** icon to the right. You cannot remove a milestone that has been assigned to a project.
- **Edit** - Click in the fields, and then enter text.
- **Sort** - Select a milestone, and then click the up and down arrows to the right of the table to adjust the position of the milestone.

2.5.2 Considerations


- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Engineering.

2.6 DESIGN ELEMENTS

Design elements are subdisciplines that you can associate to scope items. Design elements group labor types above account codes for rolling up data. Design elements configured at the organization level are

available to all projects in the organization.

You can manage Design elements for your organization in Settings > Design > Engineering > **Design elements**.

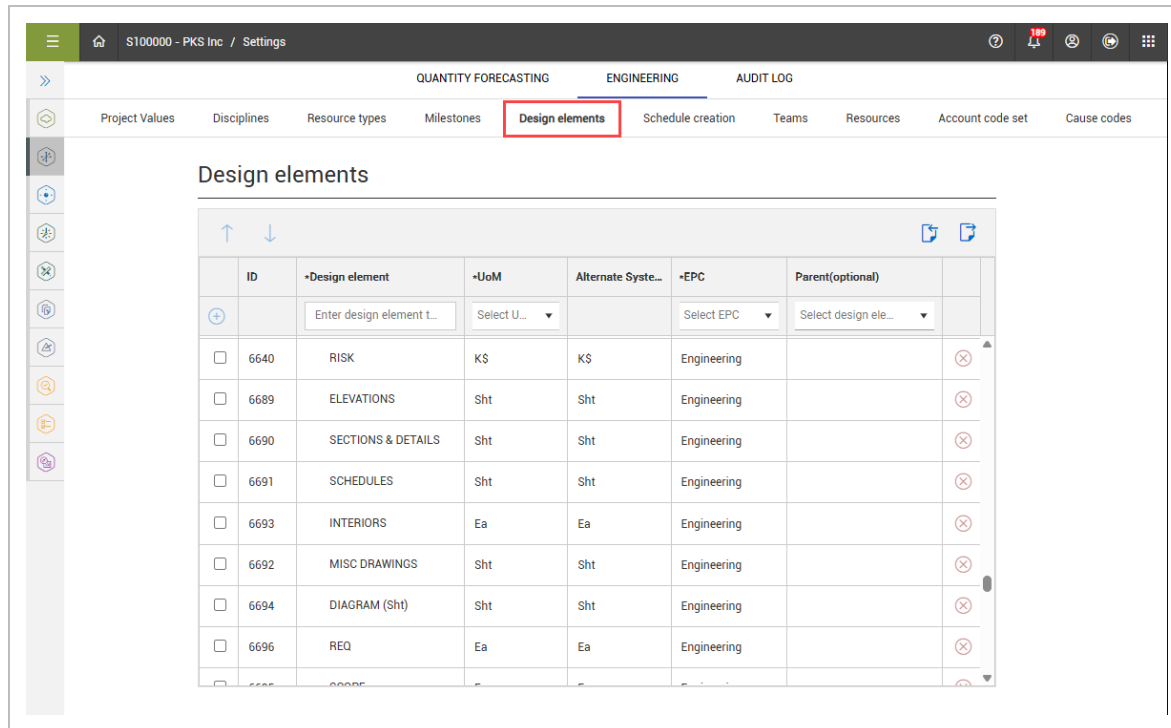

2.6.1 Steps

You can do any of the following actions:

- **Add** - Enter a unique name, select a UoM, select an associated EPC option (engineering, procurement, or construction), optionally select a parent Design element to group elements together, and then click the **Add design element** icon. The Alternate System UoM will be automatically populated based UoM selected. You can also use the import process to import Design elements using the Export and Import icons.
- **Edit** - Click in the fields, and then enter text. You cannot edit a design element's UoM when it is assigned to a scope item.
- **Delete** - Click the **Delete design element** icon to the right. You cannot delete a design element, or a terminal design element assigned to a scope item. You cannot delete a parent design element when it has other design elements associated with it.

- **Sort** - Select the Design element, and then click the up and down arrows to the right of the table to adjust the position of a Design element.

When Design elements are created, they become available to assign to account codes in the organization settings. For more information, see [Account code set](#).


Design elements can be associated to scope items at the resource level for your project. For more information, see [Scope item resources](#).

2.6.2 Considerations

- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Engineering.
- The Alternate system UoM field is automatically populated according to the units of measure in the InEight Platform master data library.

2.7 TEAMS

Teams are used to group resources to assign to claiming steps for scope items. Teams are associated with either organizations or vendors. You can manage Teams for your organization in Settings > Design > Engineering > **Teams**.

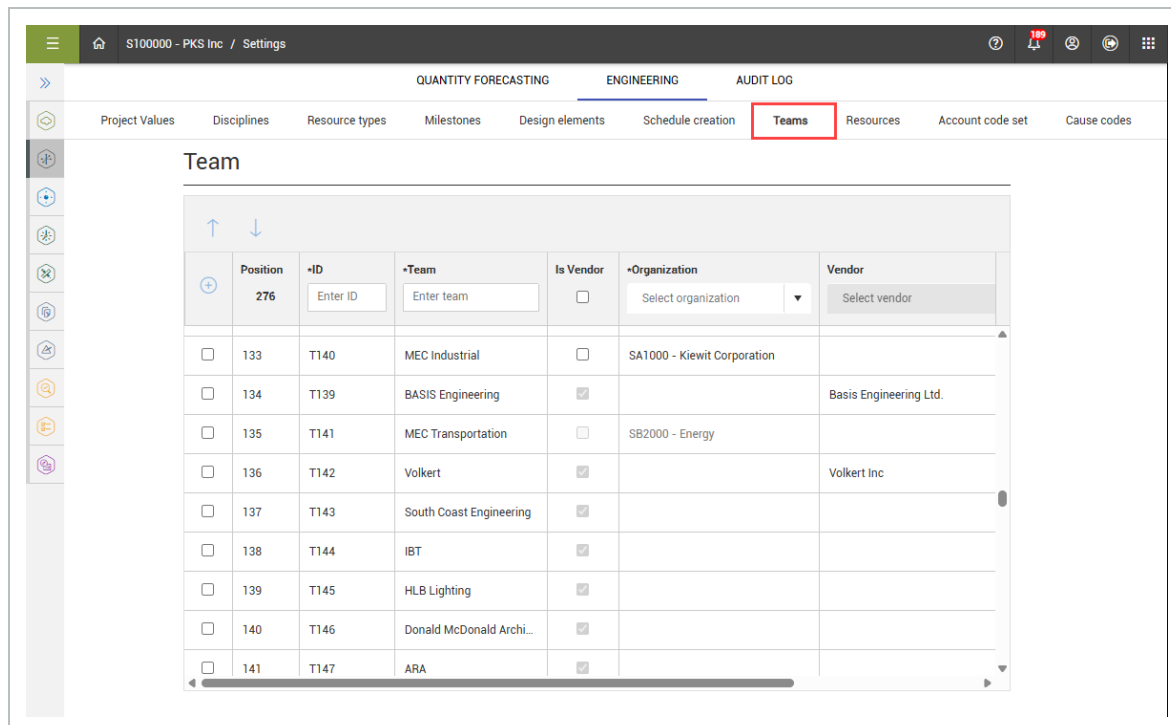

The screenshot displays the 'Teams' management interface. The top navigation bar includes 'QUANTITY FORECASTING', 'ENGINEERING' (selected), and 'AUDIT LOG'. Under 'ENGINEERING', the 'Teams' tab is active and highlighted with a red box. The main content area is titled 'Team' and contains a table with the following data:

Position	ID	Team	Is Vendor	Organization	Vendor	
276	Enter ID	Enter team	☐	Select organization	Select vendor	
☐	133	T140	MEC Industrial	☐	SA1000 - Kiewit Corporation	
☐	134	T139	BASIS Engineering	☒		Basis Engineering Ltd.
☐	135	T141	MEC Transportation	☐	SB2000 - Energy	
☐	136	T142	Volkert	☒		Volkert Inc
☐	137	T143	South Coast Engineering	☒		
☐	138	T144	IBT	☒		
☐	139	T145	HLB Lighting	☒		
☐	140	T146	Donald McDonald Archi...	☒		
☐	141	T147	ARA	☒		

Is Vendor option

When the *Is Vendor* checkbox is not selected, the team can be associated to an organization in InEight Suite. When the *Is Vendor* checkbox is selected, the team can be associated to one-to-many vendors from InEight Platform.

2.7.1 Steps

You can do the following actions:

- **Add** - Enter an ID, Team name, and either select the **Is Vendor** check box and a vendor, or an organization, and then click the **Add team** icon.
- **Remove** - Click the **Remove team** icon to the right. You cannot remove a team assigned to a project.
- **Edit** - Click in the fields, and then enter text or select an option.
- **Sort** - Select a team, and then click the up and down arrows to the right of the table to adjust the position of the team.

In the organization Resource settings, you can assign resource users to a team and add a team when assigning resource users. For more information, see [Resources](#) in organization settings.

At the project level, all teams from the parent organization are automatically inherited. For more information, see [Teams](#) in project settings.

2.7.2 Considerations

- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Engineering.

2.8 RESOURCES

Resource users are used to assign to claiming steps on scope items. Resource users are associated with resource types and can be grouped into teams.

You can create resource users in Settings > Design > Engineering > **Resources**.

User	Resource type	Discipline	Team	
All	All	All		
☐ Vijaya	KT	KTT	WS1, TEAM, KTOrg, org	02/10/2024
☐ Alondra	Document Control	Indirects	aaaa, DUT, WS1, Long tex...	12/20/2024
☐ Ravali	Building Stations	Building	SS1, org	01/17/2024
☐ Aaquibulla	Building Vertical Structur...	Building	SS1	12/20/2024
☐ Aaron	Architectural Landscapin...	AE	SS1	12/01/2024
☐ vinodkumar	Civil/Structural Engineer	Civil/Structural	Long text Long text Long ...	11/01/2024
☐ Ashish	Architectural Landscapin...	AE	TEAM, org	11/11/2024
☐ Babji	Architectural Landscapin...	AE		12/23/2024
☐ David	Building Stations	Building		12/23/2024

2.8.1 Steps

You can do the following actions:

- **Assign resource user** – Add an individual resource user.
 1. Click the **Add resource** icon, and then select **Assign resource user** from the list. The Add resource slide-out panel opens.
 2. Select a user, start date, and resource type.
 3. Optionally, select a team or teams from the **Enter team** drop-down list, select the start date, and then click the **Add team** icon.
 4. Click **Save**.

To remove a team, click the **Remove team** icon to the right.

- **Assign resource users by type** – Add multiple resource users assigned to one resource type.
 1. Click the **Add resource** icon, and then select **Assign resource user by type** from the list. The Assign resource users by type slide-out panel opens.
 2. Click the **Select resource type** drop-down list, and then select a resource type.

3. Click the **Enter resource user** drop-down list, select a resource user from the list, and then select the start date.
4. Click the **Add resource user** icon to add the resource user to the list.
5. Click **Add** to assign resource users by type.

To remove a resource user, click the **Remove resource user** icon to the right.

- **Assign resource users to team** – Add multiple resource users assigned to one team.
 1. Click the **Add resource** icon, and then select **Assign resource users to team** from the list. The Assign resource users to team slide-out panel opens.
 2. Click the **Select team** drop-down list, and then select a team.
 3. Click the **Enter resource user** drop-down list, select a resource user from the list, and then select the start date.
 4. Click the **Add resource user** icon to add the resource user to the list.
 5. Click **Add** to assign resource users to team.

To remove a resource user, click the **Remove resource user** icon to the right.

- **Delete** – Click the **Delete resource** icon to the right. You cannot delete resources assigned to a project. To remove a resource or team, click the **Remove resource user** or **Remove team** icon to the right.
- **Edit** – Select a resource, and then click the **Edit resource** icon.

In settings at the project level, you can set the **Limit user assignments to only those Teams associated with the project** toggle to *On* to allow only those users who are associated to Teams assigned on the project to be able to assign on the project. For more information, see [Resources](#) in project settings.

2.8.2 Considerations

- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Engineering.
- A user can only be assigned as a resource in one organization at a time.
- You can only assign resource users to teams associated with the organization.

2.9 ACCOUNT CODE SET

You can use account code sets to group together account codes and tag them for use with scope items. This lets you narrow down the account codes in the master data library to only those necessary for use

in Design for specific projects. You can only add account codes that exist in Main menu > Master data libraries > **Account codes**.

You can enable and create account code sets for your organization in Settings > Design > Engineering > **Account code set**. To enable account code sets, set the **Account code set enabled** toggle to *On*.

QUANTITY FORECASTINGENGINEERINGAUDIT LOG

Project valuesDisciplinesResource typesMilestonesDesign elementsScheduleTeamsResourcesAccount code setCause codes

Account code set

Account code set enabled

Account code set

T1

Include selected account code set in project settings?

Account code

Account code description

Design element

Primary UoM

Alternate System UoM

Ground

Accour

00

Overhead

HH2

PLS

PLS

Under

2

A1

TEST

INDIRECTS (PLS)

PLS

PLS


Above

2

Subtotals

Count: 2

Update account codes - The Update account codes feature alerts you of any account code updates made to the master account code library in Platform that impacts any account code in an ACS, such as deleted account codes or modified UoMs.

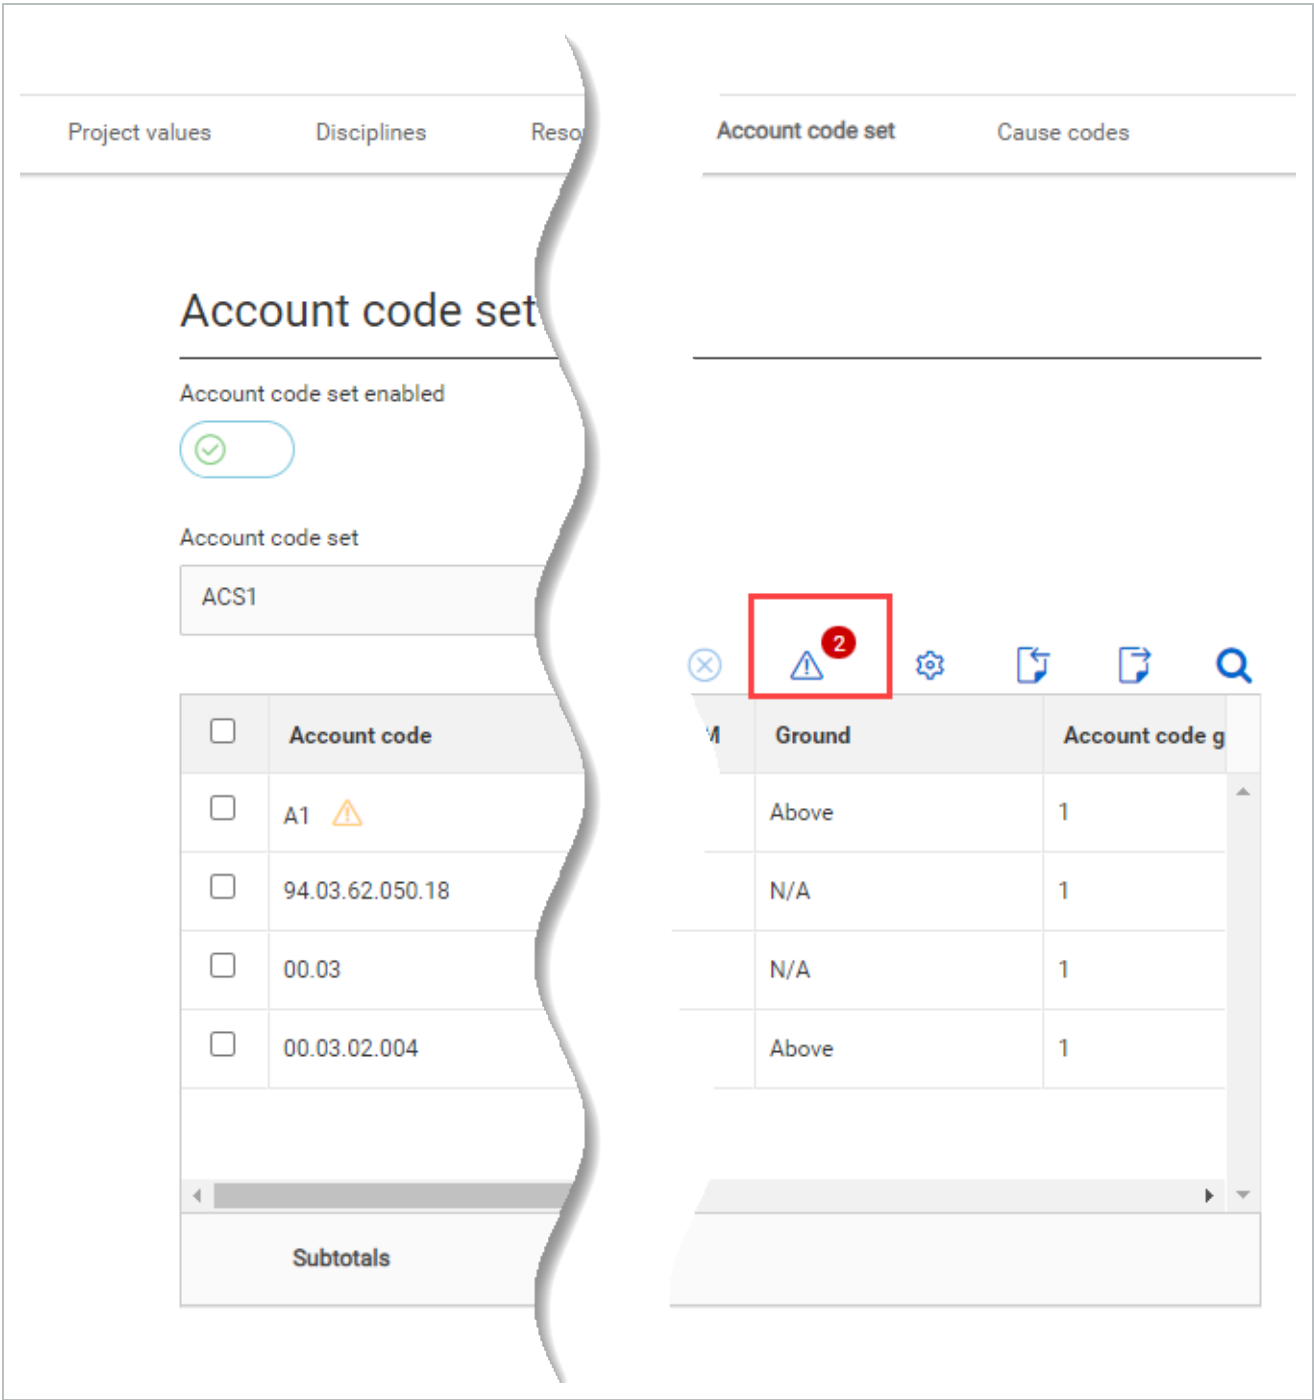

2.9.1 Steps

You can do the following actions:

- **Create a new account code set** - Click the **Account code set** drop-down list, and then select **New account code set** from the list. Enter a new name, and then click **Create**.
- **Add account code set values to an account code set group** - Click the **Configure account code group** icon, enter an ID and description, and then click **Add** icon. Account code groups are account code set specific. Account code groups can be added individually or in bulk using the import process. You cannot add or import account codes to a set without at least one account code group maintained. You cannot delete account code groups tagged to an Account code in the set. Account code values assigned to an account code in the set cannot be removed.

Account code set

Account code set enabled

Account code set: KEGI AC Set

Include selected: ☒

☐	Account code	Account code description	Design element
☐	88.01.02	Design Engineering Indirects - Pr...	FIE...
☐	88.01.04	Design Engineering Indirects - En...	IND...
☐	88.01.06	Design Engineering Indirects - De...	LEA...
☐	88.01.08	Design Engineering Indirects - Sp...	IND...
☐	88.01.12	Design Engineering Indirects - Ar...	IND...
Subtotals		Count: 3,144	

Configure account code set values

ACCOUNT CODE GROUP | DRAWING CODES

☐	Position	*ID	*Description	
☐	1005	Enter ID	Enter description	
☐	01	MQA	Ind - Project Mgmt	☒
☐	02	MQB	Ind - Eng Mgmt	☒
☐	03	MQC	Mech Pipe Plans	☒
☐	04	MQD	Ind - Sponsor	☒
☐	05	MQE	Ind - Area Manager	☒
☐	06	MQF	Ind - DBI Manager	☒
☐	07	MQG	Ind - Opp Support	☒
☐	08	MQH	Ind - Project Controls	☒
☐	09	MQI	Ind - Doc Control	☒
☐	10	MQJ	Ind - PG	☒
☐	11	MQK	Ind - Admin	☒
☐	12	SQL	Ind - Quality Team	☒
☐	13	MQM	Ind - Other MISC	☒
☐	14	MQN	Ind - Interface	☒
☐	15	MQO	Expenses	☒
☐	16	MQP	Consultants	☒

- **Add account codes to an Account code set** - Click the **Add account code** icon, select an account code from the list, and then click **Assign**. Select the required and optional attributes for the account code, and then click **Add**. After an account code is assigned to a project it cannot be removed.
- **Remove an account code or an account code group** - To remove an account code, select the account code, and then click the **Remove account code** icon. To remove an account code group,

click the **Remove account code group** icon on the right. You cannot remove an account code group assigned to an account code set in the set or an account code assigned to a project.

- **Edit an account code group or account code** – To edit an account code group, click in the fields, and then enter text. To edit an account code, select an account code, and then click the **Edit account code** icon. In the Edit account code slide-out panel, make your changes, and then click **Save**.
- **Sort account codes or groups** - Select the item, and then click the up and down arrows to the right of the table to adjust the position of account code groups.
- **Update account codes that have been modified in InEight Platform** - Click the **Update account codes** icon to open the Update account codes dialog box.

Update account codes

The following account codes have either been deleted or had a UoM modified in Core. Please select which account codes you would like to update in the account code set.

☐	Update type	Account code	Account code description	Design Element	Design Element UoM	Primary UoM	Alternate System UoM	Modified Primary UoM	Modified Primary UoM
☐	Modified UoM	A1	A1	PAA	PAA	PAA		PLS	PLS
☐	Deleted account code	A1	A1	PAA	PAA				

0 item selected

Select the account codes to update, and then click **Update**.

- **Add drawing codes** – Click the **Configure account code group** icon, enter an ID and description, and then click **Add** icon. Drawing codes can be added individually or in bulk using the import process.
- **Remove a drawing code** - Click the **Remove drawing code** icon to the right. You cannot remove drawing codes that have been assigned to a project.
- **Sort drawing codes** - Select the item, and then click the up and down arrows to the right of the table to adjust the position of the drawing code.

At the project level, you can tie an account code set to your project. For more information, see [Account code set](#) in project level settings.

2.9.2 Considerations

- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Engineering.
- To enable or disable the Tie to account code set toggle for a project, the scope items grid must be empty.
- Only account codes that are available in InEight Platform Master data libraries > Account codes can be added to an account code set.
- You cannot delete an account code from an account code set assigned to a scope item.

2.10 CAUSE CODES

In the Engineering module, cause codes are required when a quantity change occurs. For more information, see [Update scope item quantities](#).

You can manage cause codes for your organization in Settings > Design > Engineering > **Cause codes**.

C-XYZ / Settings

QUANTITY FORECASTINGENGINEERINGAUDIT LOG

Project ValuesDisciplinesResource typesMilestonesDesign elementsSchedule creationTeamsResourcesAccount code setCause codes

Cause codes

↑↓

07

Enter ID

Enter description

☐	01	PrimeContractChange	Prime Contract Change	⊗
☐	02	ClientRequest	Client Request	⊗
☐	03	ConstructionChangeRequest	Construction Change Request	⊗
☐	04	VendorDesignorMaterialChan...	Vendor Design or Material Change	⊗
☐	05	EngineeringErrororOmission	Engineering Error or Omission	⊗
☐	06	DesignProgression	Design Progression	⊗

2.10.1 Steps

You can do the following actions:

- **Add** - Enter and ID description, and then click the **Add cause code** icon.
- **Remove** - Click the **Remove cause code** icon to the right. You cannot remove a cause code assigned to a scope item on a project.
- **Edit** - Click in the fields, and then enter text or select an option.
- **Sort** - Select a cause code, and then click the up and down arrows to the right of the table to adjust the position of the cause code.

Cause codes configured at the organization level are available to all projects.

2.10.2 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Engineering.

2.11 PROJECT SETTINGS FOR ENGINEERING

As an administrator, you can configure settings for the Engineering module at the project level. Settings at the organization level are inherited by associated child organizations and projects. At the project level, you can further refine some settings to customize how they are applied in each project.

You can manage engineering settings for your projects in Settings > Design > **Engineering**.

The Design project settings gives you access to the following project configurations:

[Project values](#)

[Account code set](#)

[Resource types](#)

[Milestones](#)

[Teams](#)

[Resources](#)

[Control settings](#)

[Dates](#)

[Documents](#)


For general information on InEight cloud platform settings, see [Project Settings](#).

2.12 PROJECT VALUES

2.12.1 Summary


You can select which project values can be associated to engineering scope items and if they are required in a project. The values are configured at the organization level in Settings > Design > Engineering > **Project values**. Project values configured at the organization level are available in all projects.

To configure project values, go to Engineering > **Project values**.

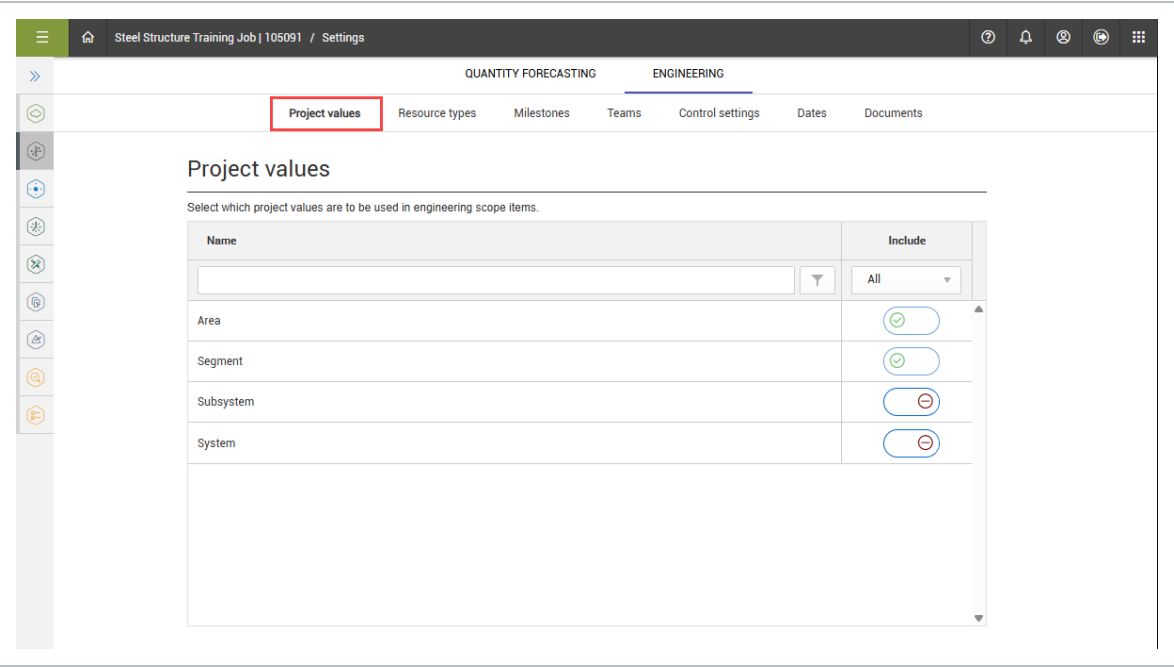


When you include project values, those values are available for selection in Settings at the project level. You can select or deselect the values that are not required for the project.

When you require a project value, the value is required at the project level. The project-level toggles for these values are automatically disabled.

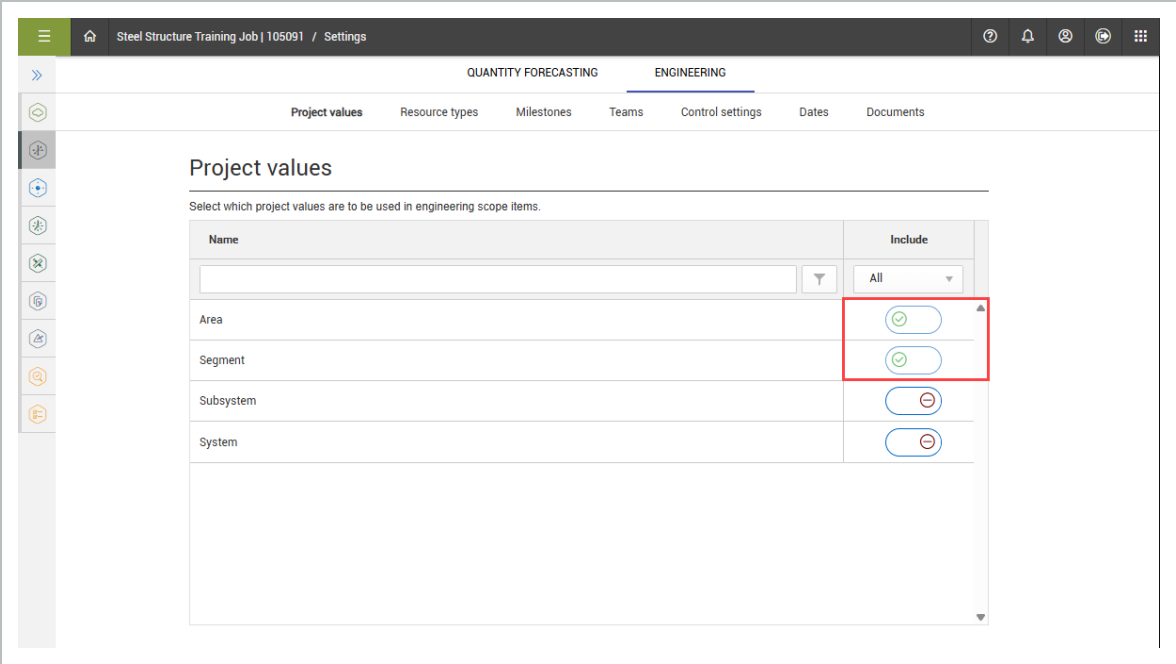

The selected project values are shown in the Scope item grid and slide-out panel. You can also export and import them in a Microsoft Excel spreadsheet.

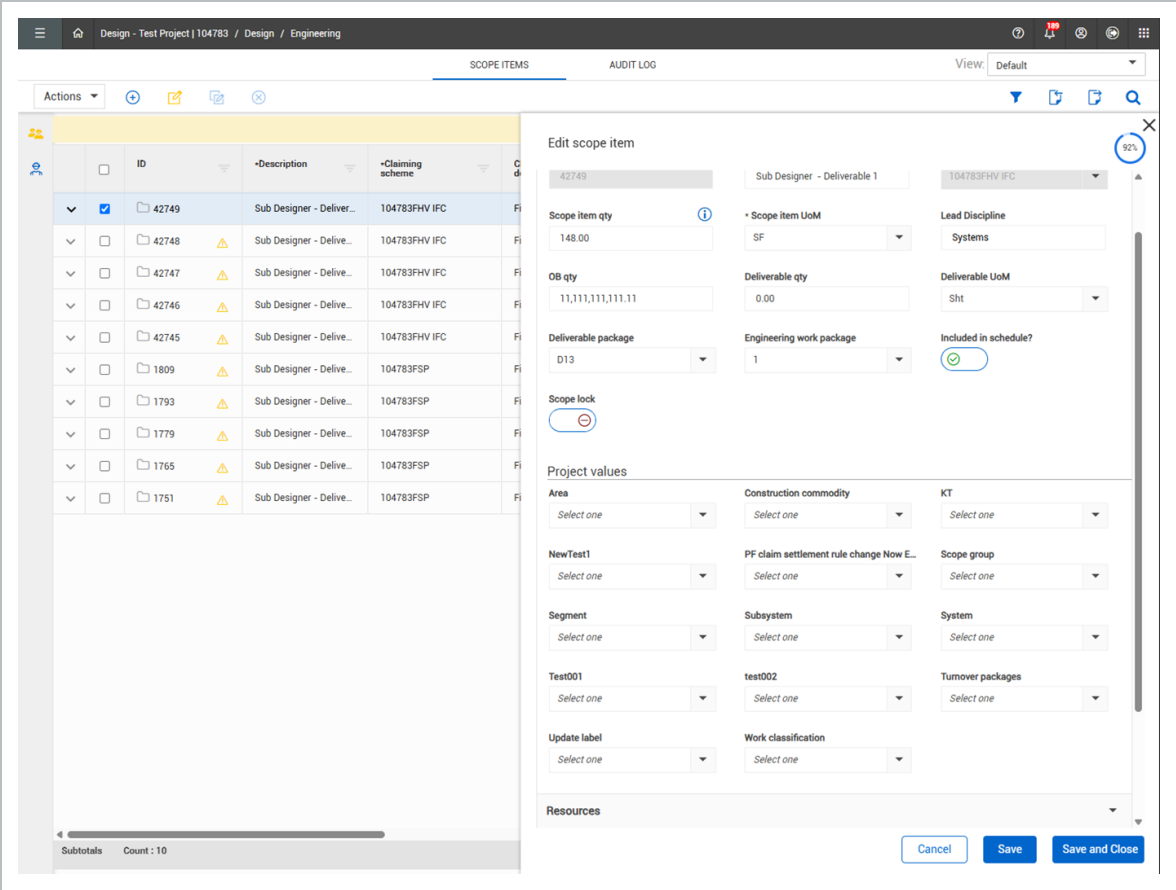

2.12.2 Considerations

- You must have the Edit engineering settings permission.

2.12.3 Related links

After project values are set up, you can configure **disciplines**. For more information on how to configure disciplines, see [Disciplines](#).

2.13 ACCOUNT CODE SET

Account code sets are used to group together account codes and tag them for use with scope items. This lets you narrow down the account codes in the master data library to only those necessary for use in Design for specific projects.

Account code sets are created at the organization level. To make an account code set available in project settings, select an account code set at the organization level. For more information, see [Account code set](#) in organization settings.

You can manage account code set settings for your project in Settings > Design > Engineering > **Account code set**.

QUANTITY FORECASTING ENGINEERING

Project values **Account code set** Resource types Milestones Schedule Teams Resources Control settings Dates Documents

Account code set

Tied to account code set? ☒ *Account code set locks on upload of scope item structure

Select UoM from Account Code Set:

☒ Primary UoM ☐ Alternate System UoM

Validate UoM for claiming? [?](#)

Tied to account code set - You can tie an account code set to your project by setting the Tied to account code set toggle to *On*. You can then select an account code set. Only account codes in that set are available to assign to scope items in the project.

Select UoM from Account Code Set - You can set either the primary or alternate system UoM to be used throughout the project. The primary and alternate system UoM are configured at the organizational level.

Validate UoM for claiming toggle – You can choose to validate the account code primary UOM from the master library. When the Validate UoM for claiming toggle is set to *On*, the UoM in account code, scope item, and WBS must match to enable claiming. By setting the Validate UoM for claiming toggle to *Off*, only the UoM for the scope item and WBS must match.

2.13.1 Considerations

- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Engineering.
- To set the **Tied to account code set** toggle to *On* or *Off*, the scope items grid for the project must be empty.

2.14 RESOURCE TYPES

Resource types are associated with disciplines and must be managed in your project to add claiming schemes. For more information, see [Configure claiming schemes](#). Resource types are created at the organization level.

You can manage resource types for your project in settings > Design > Engineering > **Resource types**.

Resource type

	Position	ID	Description	Discipline	
19			Select resource type		
☐	01	EL	Electrical Lead	Electrical	
☐	02	EE	Electrical Engineer	Electrical	
☐	03	ED	Electrical Designer	Electrical	
☐	04	PM	Project Management	Indirect	
☐	05	ML	Mechanical Lead	Mechanical	
☐	06	ME	Mechanical Engineer	Mechanical	
☐	07	MD	Mechanical Designer	Mechanical	
☐	08	SL	Structural Lead	Structural	
☐	09	SE	Structural Engineer	Structural	

2.14.1 Steps

You can do any of the following actions:

- **Add** – Click the **Select resource type** drop-down list, select a resource type, and then click the **Add resource** icon.
- **Remove** - Click the **Remove resource type** icon to the right. You cannot remove a resource type that has been assigned to a project.
- **Sort** - Select a resource type, and then click the up and down arrows to the right of the table to adjust the position of the resource type.

All resource types are created at the organization level and are automatically inherited in projects. For more information, see [Resource types in organization settings](#).

2.14.2 Considerations

- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Engineering.
- When you assign a resource type to a claiming scheme step, its associated ID and discipline is automatically populated.

2.15 MILESTONES


You can define completion milestones in the Engineering module to assign to claiming scheme steps. Examples of completion milestones might be Issue for Review or Issue for Construction.

A system-generated milestone named Scope Complete is automatically assigned to every project ensuring that all scope item's scope can be planned with dates.

Milestones are created at the organization level in Settings > Design > Engineering > **Milestones**. After creation, you can assign milestones at the suborganization level.

At the project level, all milestones from the parent organization are automatically inherited and you can assign or remove resource types as necessary.

To add a new milestone at the organization level, enter an ID, a description, and a discipline, and then click the **Add resource** icon. To edit resource types, click in the fields, and then enter text. To remove a resource type, click the **Remove resource type** icon to the right. To adjust the position of a resource type in the list, select the resource type, and then click the up or down arrows to the right of the table.

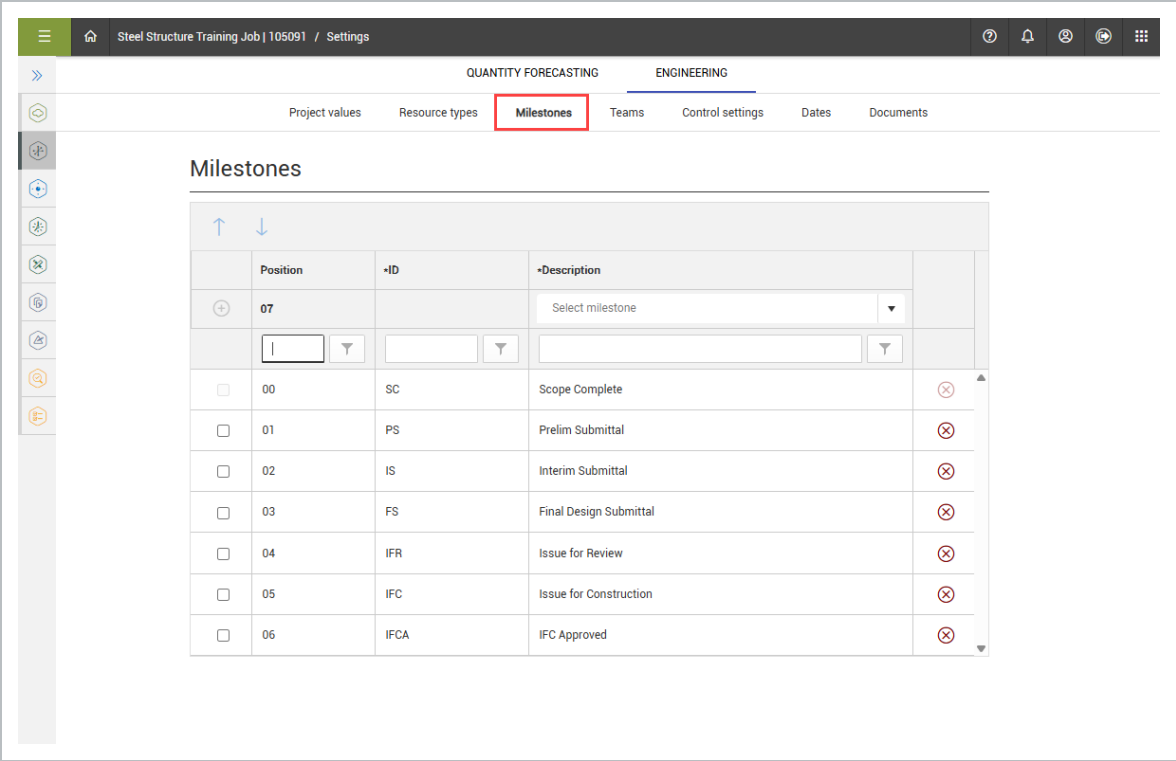

To add a milestone at the project level from the parent organization, select a description from the drop-down list, and then click the **Add milestone** icon.

2.15.1 Considerations

- You must have the permission Edit engineering settings.
- You cannot edit or remove a milestone when it is assigned to a project.

2.15.2 Related links

After milestones are set up, you can assign them to claiming scheme steps. For more information, see [Claiming schemes overview](#).

2.16 TEAMS

You can manage teams and resource assignments settings in Teams.

2.16.1 Manage teams

Teams are used to group resources to assign to claiming steps for scope items. Teams created at the organization level are inherited by all projects in the organization. For more information, see [Teams](#) in organization settings.

To manage teams for your project, go to Settings > Design > Engineering > **Teams**.

The screenshot displays the 'Teams' tab within the 'ENGINEERING' settings. The top navigation bar includes 'Project values', 'Account code set', 'Resource types', 'Milestones', 'Schedule creation', 'Teams' (highlighted with a red box), 'Control settings', 'Dates', and 'Documents'. The main content area is titled 'Team' and contains a table with columns: 'Posi...', 'ID', 'Team', 'Is Ve...', 'Organization', and 'Vendor'. The table has one row with '01' in the 'ID' column and 'Enter te...' in the 'Team' column. Above the table are up and down arrows for sorting. Below the table, it states 'No records available'. Below the table is the 'Resource assignment' section, which includes two toggle switches: 'Enable Organization team/user planning' and 'Enable Vendor team/user planning'. Each toggle has a tooltip explaining its function.

Posi...	ID	Team	Is Ve...	Organization	Vendor
	01	Enter te...	☐		

No records available

Resource assignment

Enable Organization team/user planning ⓘ When enabled, user assignment will be restricted to configured organization users where Organization teams are assigned to scope items.


Enable Vendor team/user planning ⓘ When enabled, user assignment will be restricted to configured vendor users where Vendor teams are assigned to scope items.

You can do the following actions:

- **Add** – Click in the Enter team drop-down list, select a team, and then click the **Add team** icon.
- **Remove** - Click the **Remove team** icon to the right. You cannot remove a team assigned in a project.
- **Sort** - Select a team, and then click the up and down arrows to the right of the table to change the position of the team.

2.16.2 Resource assignment

In the Resource assignment section of the Teams tab, you can enable or disable organization and/or vendor teams for scope planning. The option to enable and/or disable organization and vendor planning teams gives you control on scope item visibility for team users.

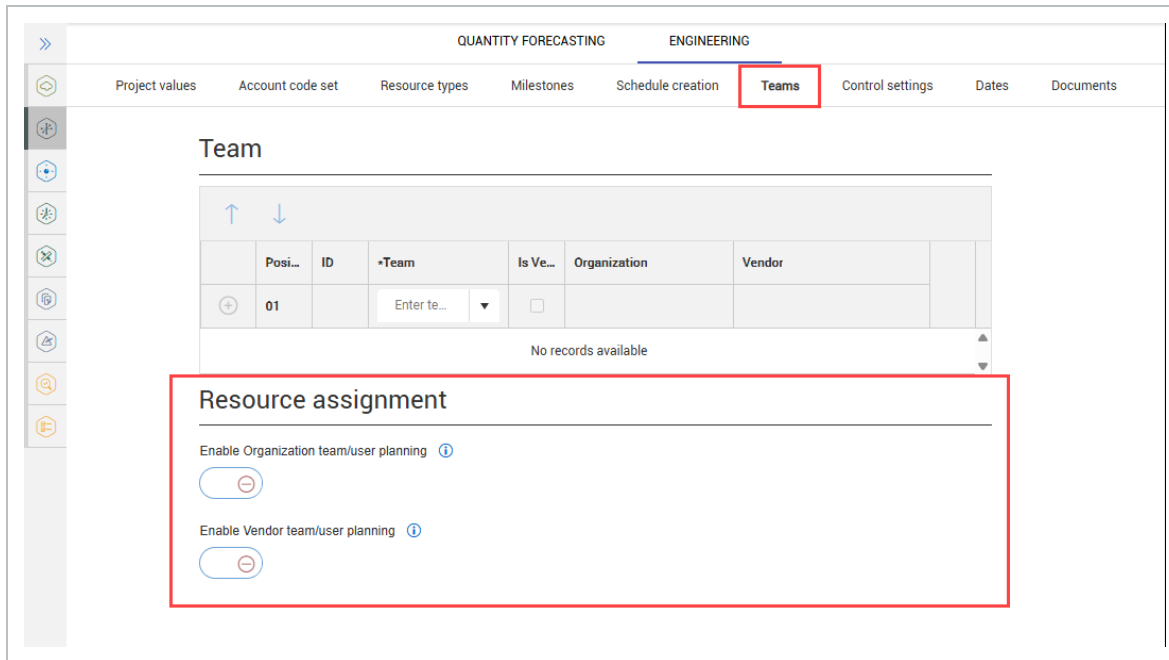

You can enable the following options:

- **Enable Organization team/user planning** — When set to *ON*, user assignment is restricted to the organization teams and their assigned users when assigning them to scope items during planning.
- **Enable Vendor team/user planning** — When set to *ON*, user assignment is restricted to the vendor teams and their assigned users when assigning them to scope items during planning.

When only Enable Vendor team/user planning is set to *ON*, only vendor users are shown when a vendor is selected in a scope item. In planning, you can assign a vendor team to scope items. For example, when team Subcontract Designer is assigned to scope items and users from that team log in to the Engineering module, they are restricted to only their assigned team scope items in the Assigned Team tab.

SCOPE ITEMS

AUDIT LOG

View: Unsaved (Default)

Actions

Project scope is unlocked

	ID	Description	Claiming scheme	Claiming scheme description	% Complete	Team	Assigned to	Lead discipline	Scope qty
✓	42749	Sub Designer - Delive...	104783FHV IFC	Fire Hose Valve additio...	92.00	Subcontract Designer	Julio Salguero	Systems	
✓	42748	Sub Designer - Delive...	104783FHV IFC	Fire Hose Valve additio...	100.00	Subcontract Designer		Systems	
✓	42747	Sub Designer - Delive...	104783FHV IFC	Fire Hose Valve additio...	100.00	Subcontract Designer		Systems	
✓	42746	Sub Designer - Delive...	104783FHV IFC	Fire Hose Valve additio...	100.00	Subcontract Designer		Systems	
✓	42745	Sub Designer - Delive...	104783FHV IFC	Fire Hose Valve additio...	100.00	Subcontract Designer		Systems	
✓	1809	Sub Designer - Delive...	104783FSP	Fire Standpipe 3 Step	100.00	Subcontract Designer		Systems	
✓	1793	Sub Designer - Delive...	104783FSP	Fire Standpipe 3 Step	100.00	Subcontract Designer		Systems	
✓	1779	Sub Designer - Delive...	104783FSP	Fire Standpipe 3 Step	100.00	Subcontract Designer		Systems	
✓	1765	Sub Designer - Delive...	104783FSP	Fire Standpipe 3 Step	100.00	Subcontract Designer		Systems	
✓	1751	Sub Designer - Delive...	104783FSP	Fire Standpipe 3 Step	100.00	Subcontract Designer		Systems	

Subtotals

Count : 10

When a user from Subcontract Designer is assigned to a scope item, the user can view their assigned team scope items in the Assigned to Me tab.

SCOPE ITEMS

AUDIT LOG

View: Unsaved (Default)

Actions

Project scope is unlocked

	ID	Description	Claiming scheme	Claiming scheme description	% Complete	Assigned to	Lead discipline
✓	42749	Sub Designer - Delive...	104783FHV IFC	Fire Hose Valve additio...	92.00	Julio Salguero	Systems

Subtotals

Count : 1

For more information about assigning vendor users, see [Vendors](#) in InEight Platform.


2.16.3 Considerations

- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Engineering.

2.17 RESOURCES

Resources users are used in the Engineering module to for assignment to claiming steps on scope items. Resources configured at the organization level are available to all projects in the organization. For more information, see [Resources](#) in organization settings.

You can manage resources user assignment limits for your project in Settings > Design > Engineering > **Resources**.

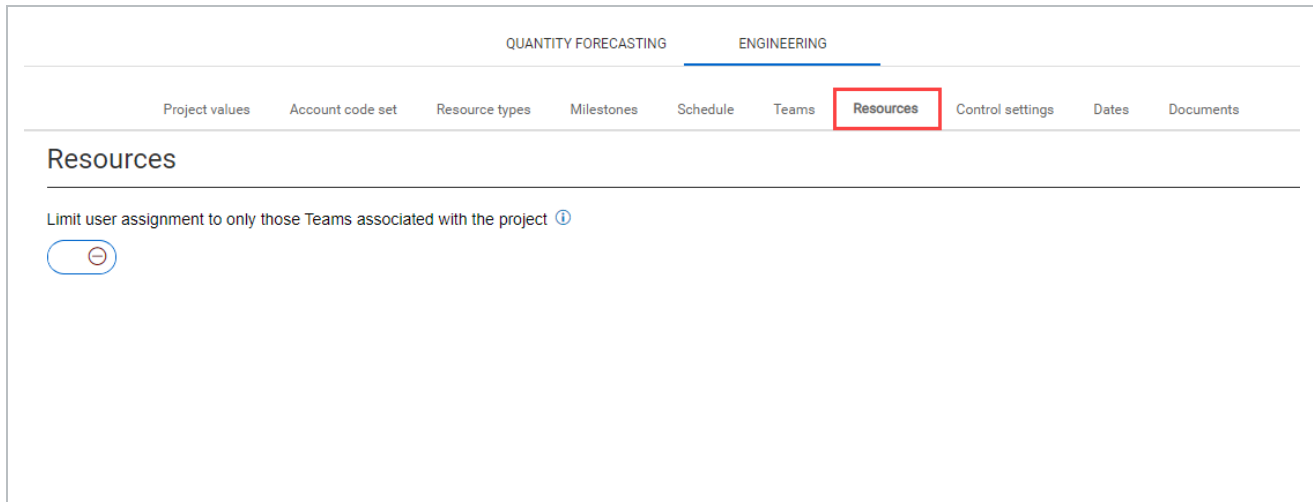

Limit user assignments to only those Teams associated with the project - When set to *Off*, any user with project permissions will be available to assign on the project. When set to *On*, only those users who are associated to Teams assigned on the project will be available to assign on the project.


By default, this toggle is set to *Off*. To set the toggle to *On*, at least one team must be added to the project.

2.17.1 Considerations

- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Engineering.
- When you set the Limit user assignment to only those Teams associated with the project toggle to *On* after the project has started, the system validates that all users assigned to incomplete claiming steps are associated with teams added to the project.

2.18 CONTROL SETTINGS

As a project administrator, you can enable InEight Control integration and functionality for your project in Settings > Engineering > **Control** settings tab.

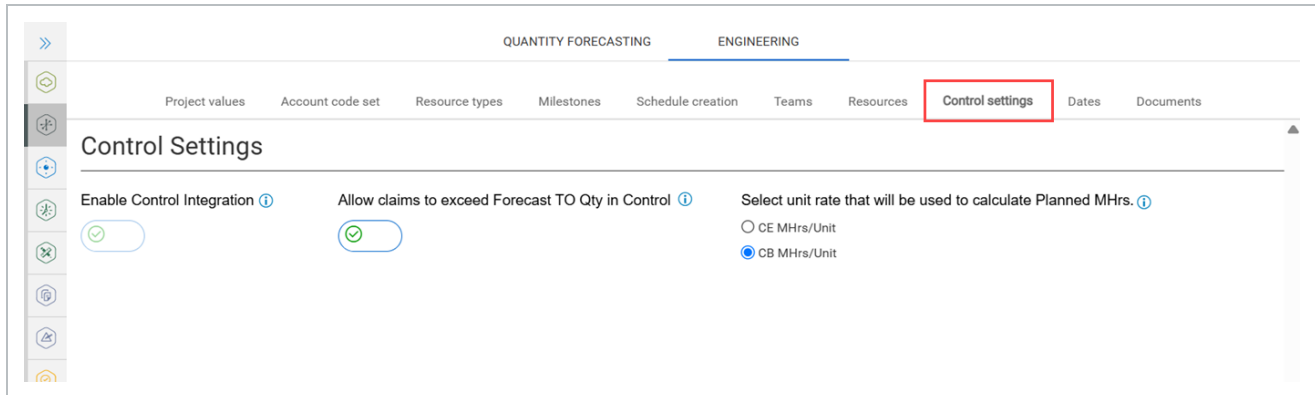

The setting is set to *On* by default for all new projects. The setting can only be updated when no scope items exist on the project. The setting is locked once a scope item is added on the project. All scope items must be deleted to update the setting.

When the Enable Control Integration toggle is set to *On*, a WBS code must be assigned for each Resource Type on a scope item to enable claiming on the scope item. This allows for WBS phase codes to be assigned to scope items. Also, scope item's steps are claimed and synced with Control to track the quantity completion progress on the associated WBS phase codes.

The Get TC Remaining MHrs/Unit action is also made available. For more information, see [Actions overview](#) in the Engineering module.

When the Enable Control Integration toggle is set to *Off*, the WBS assignment is not needed to enable claiming on a scope item. Claims made in Engineering are not sent to Control. Also, all WBS related columns and fields are hidden.

2.18.1 Allow claims to exceed Forecast TO quantity in Control

You can configure whether to allow claims to exceed the forecast TO quantity in Control. When the Allow claims to exceed Forecast TO Qty in Control setting is set to *On*, Design validates whether any claims exceed the remaining Forecast TO quantity on the associated WBS in Control. A warning banner shows to indicate that a claim exceeds the forecast TO quantity in Control before sending the claim to Control.

When set to *Off*, Design will not allow any claim to save when it exceeds the remaining Forecast TO Qty on the associated WBS in Control. A warning banner shows to indicate that the claim exceeds the remaining Forecast TO Qty.

The Allow claims to exceed Forecast TO Qty in Control setting shows only when the Enable Control Integration setting is set to *On*. Otherwise, the setting will be hidden. This setting is set to *Off* by default and can be set to *On* at any point during the project. The setting will apply to the claims thereafter.

2.18.2 Select a unit rate that will be used to calculate planned man-hours

You can select to calculate planned man-hours using CB MHrs/Unit or CE MHrs/Unit from Control. The planned man-hour setting gives you flexibility to manage how planned man-hours are calculated.


When the CE MHrs/Unit option is selected, the planned man-hours are calculated using the CE unit rate from Control. When CB MHrs/Unit is selected, the planned man-hours are calculated using the CB unit rate from Control. The planned man-hours will continue to roll up to the WBS, Work Packages, or Documents associated to a quantity item.

2.18.3 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Engineering.


2.19 DATES

As a project administrator, you can configure scope item dates values for your project in Settings > Engineering > **Dates** tab.

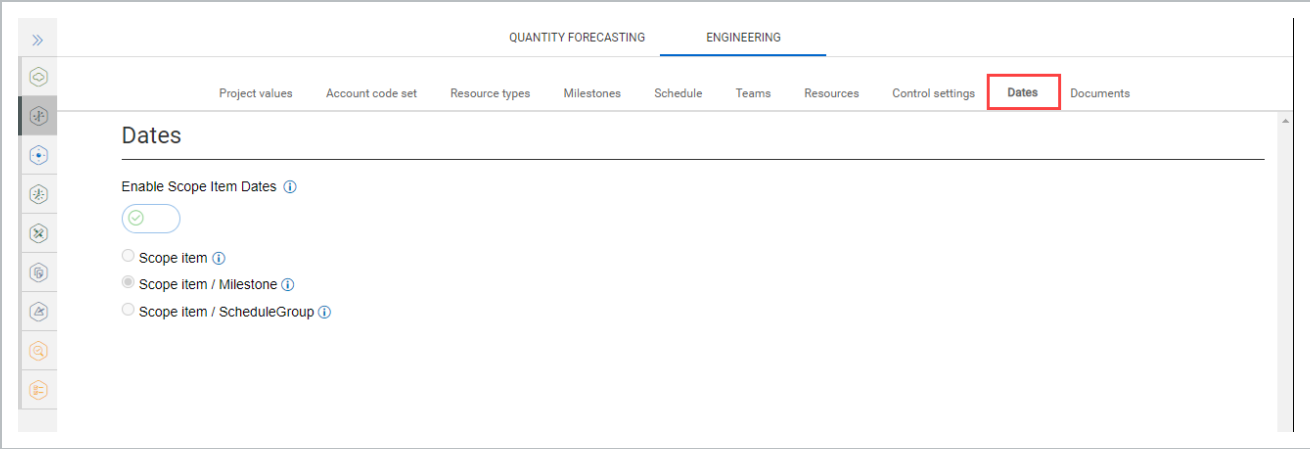

2.19.0.1 Enable scope item dates

When you set the Enable Scope Item Dates toggle to *On*, you must select from the three available options for dates. The Dates panel also shows for scope items.

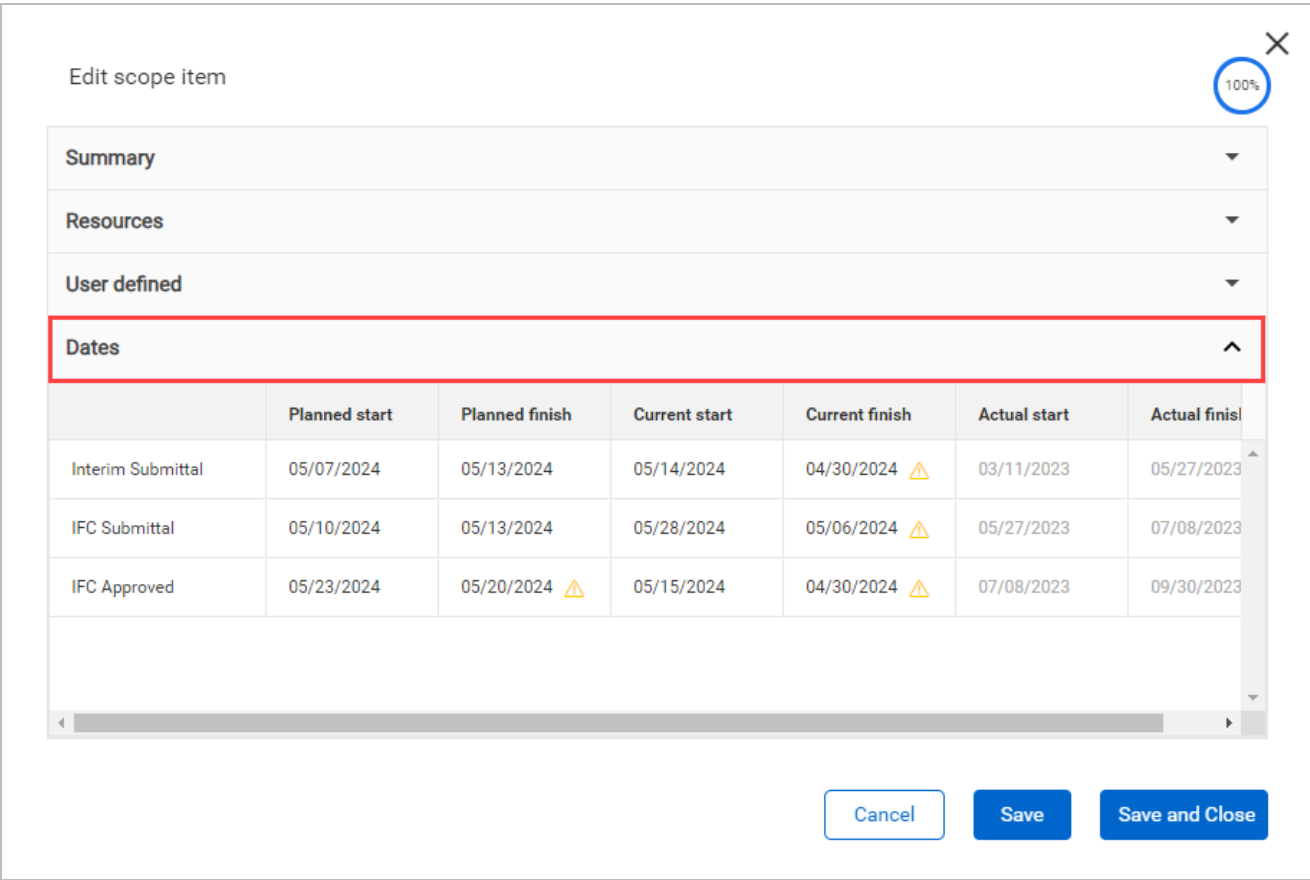

Actual start dates are an aggregated value based on the claim date that you specify when you begin claiming. The Actual start date is based on the Dates settings shown in the following table:

Setting	Description
Scope item	Generates one set of Planned, Current, and Actual Start and Finish Dates per scope item. The system captures the first claim date made on the scope item in the Actual Start Date field.
Scope item / Milestone	Generates one set of Planned, Current, and Actual Start and Finish Dates per unique milestone associated with the assigned claiming scheme. The system captures the first claim date made on each milestone on a claiming scheme in the Actual Start Date field.
Scope item / ScheduleGroup	Generates one set of Planned, Current, and Actual Start and Finish Dates per unique Scheduled Group associated with the assigned claiming scheme. The system captures the first claim date made on each schedule group on a claiming scheme in the Actual Start Date field.

2.19.1 Consideration

- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Engineering.
- Scope item Dates values can only be updated when no dates are present on any scope item.

2.20 DOCUMENTS

You can configure the integration of scope items with documents from InEight Document for your project in Settings Engineering > **Documents**.

The screenshot shows the 'Documents' settings page in the InEight Design application. The page is titled 'Documents' and is part of the 'Design - Document claiming / Settings' section. The 'ENGINEERING' tab is selected, and the 'Documents' sub-tab is highlighted in the top navigation bar.

Key settings and actions visible include:

- Enable Document integration:** Toggled 'On' (green checkmark).
- Enable Document claiming:** Toggled 'On' (green checkmark).
- Refresh document types:** A blue button with a refresh icon.
- Refresh document status:** A blue button with a refresh icon.
- Full document refresh:** A blue button with a refresh icon.
- Delta document refresh:** A blue button with a refresh icon.
- Completed status:** Two 'Completed' status indicators.
- Data last refreshed:** Two timestamps: '08/20/2025 04:22:17 AM' and '09/09/2025 12:55:40 PM'.

Below the settings, a note states: 'Select which document types are to be shown in document association. By default all document types are included.'

Two grids are present for selecting document types:

- Document Types:** A search bar and a list with one item, 'Document Types', which is currently selected. Below the list, it says 'No records available.'
- Selected Document Types:** A search bar and a list of document types, each with a checkbox. The types listed are: REG, DRAWING, SPEC, MAN, PHOTO, REPORT, SCHED, SHOPDWG, SKETCH, TESTDEL, TYPE1, TYPE2, and TYPE3.

Blue arrows indicate the relationship between the two grids.

2.20.1 Document integration

To associate documents from Document with scope items, you must do the following:

- Set up the project in InEight Platform > Suite Administration > **Application integrations**.
- Under project settings, on the Engineering > **Documents** tab, set the **Enable Document integration** toggle to *On*.

When Document integration is set to *On*, the Document Types and Selected Document Types grids show at the bottom of the page. The grids are where you can manage the document types. The Associate documents action is also made available in the Engineering > Scope Items > **Actions** drop-down menu.

To sync documents with Document, click **Full document refresh** or **Delta document refresh**. You can view the last date and time the data was refreshed.

2.20.1.1 Document types

The Document Types grid shows all available document types from the mapped Document project. You can select which document types from the Document register are shown in the Associate documents page when associating documents to scope items.

2.20.1.2 Selected Document Types

The Selected Document Types grid shows the document types to be synced to Document. Document types that have an active association cannot be removed unless you remove their associations.

To add a document type, select it from the Document Types list, and then click **Move right**. To remove a document type, select it from the Selected Document Types list, and then click **Move left**.

Associate documents

You can associate documents by:

- Navigating to Scope items > Actions > **Associate documents**, and then selecting the **Mapping** tab to manually map individual scope items, or use the **Auto map** feature to map in bulk.
- The Document section of the scope item slide-out panel.
- Using the scope item's template to import document associations.

2.20.2 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform, a role with the applicable permissions in Engineering, and applicable permissions in InEight Document.

2.21 ORGANIZATIONAL SETTINGS FOR QUANTITY FORECASTING

The organization Quantity forecasting settings gives you access to the following configurations:

- [Project values](#)
- [Account code set](#) and [Discipline set](#)

- [Design tracking stages](#)
- [Design elements](#)
- [Notes](#)
- [Cause codes](#)

The configured settings are available for each project in the organization. You can manage quantity forecasting settings for your organization in Settings > Design > **Quantity Forecasting**.

For general information about InEight cloud platform settings, see [Organization Settings](#).

2.21.1 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

2.22 PROJECT VALUES

You can configure the criteria for how project value types are associated to a quantity item and if they are required in projects in the organization in org > Settings > Design > Quantity Forecasting > **Project values**.

The values are managed in InEight cloud platform. For more information, see [Project values](#).

The values that have Include set to *On* show as optional in all projects within the organization. The values that have Required set to *On* show as required in all projects in the organization.

C-XYZ / Settings

QUANTITY FORECASTINGENGINEERINGAUDIT LOG

CancelSave

Project values

Select which project values are to be used in quantity items.

Name	Include	Required
Area	☒	☒
Construction commodity	☒	☒
Segment	☒	☒
Subsystem	☒	☒
System	☒	☒
Turnover	☒	☒

Enable Account code set and Discipline set☐

Design tracking stages

	Position	*Design stage title	
☒	04	Enter design stage title	
☐	01	30%	☒
☐	02	60%	☒
☐	03	90%	☒

In the project > Settings > Quantity Forecasting > Attribute and project values > **Project values** section, you only see the project values that are included at the organization level.

Include – When you set the Include option to *On* for a project value, the project value becomes available as an attribute in the quantity item. By default, the value is set to *Off* in the project. You have the option to set the Include option to *On*.

Required - When you set the Required option to *On* for a project value, the project value type is a required attribute on the quantity item. The project-level toggles for these values are automatically set to *On* and cannot be changed. The system will check that these required fields are maintained when adding or editing quantity items in the project. Required fields will show with an asterisk in the project to let you know which fields are required when adding or editing quantity items.

2.22.1 Considerations

- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.
- Include will be disabled if any quantity item has data maintained or if Required is set to *On*. Required becomes disabled if quantity item data exists but there are quantity items that do not have that project value type maintained.

2.23 ACCOUNT CODE AND DISCIPLINE SETS

You can enable the option to use account code and discipline sets by setting the **Enable Account code set and Discipline set** toggle to *On*.

The screenshot shows the 'QUANTITY FORECASTING' settings page. At the top, there are tabs for 'QUANTITY FORECASTING', 'ENGINEERING', and 'AUDIT LOG'. Below the tabs, there are 'Cancel' and 'Save' buttons. A red box highlights the 'Enable Account code set and Discipline set' toggle, which is currently turned on. Below this, there are sections for 'Discipline set' and 'Account code set'. The 'Account code set' section includes a dropdown menu labeled 'Select one'. At the bottom of the page, there are several icons for navigation and actions.

When the feature is set to *On*, you can manage disciplines sets and account code sets. You must first create discipline sets to create account code sets.

2.23.1 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

2.24 DISCIPLINE SET

Discipline sets are used to link to an account code set, which will limit the account code set to use only those disciplines in the set. When the **Enable Account code set and Discipline set** toggle is set to *On*, you can manage disciplines for your organization in Settings > Design > Quantity Forecasting > **Discipline set**.

QUANTITY FORECASTINGENGINEERINGAUDIT LOG

CancelSave

Discipline set

Discipline set

Discipline one

	Position	*Discipline	*Discipline group	
+	04	Select discipline	Select discipline group	
☐	01	Aggregates and Paving	1	⊗
☐	02	Building	1	⊗
☐	03	Bulk Commodities	2	⊗

The standard disciplines can be added or removed from a set to limit which disciplines are available. When disciplines are added to a set, they must be associated to a Discipline Group.

2.24.1 Steps

You can do any of the following actions:

- **Create a new discipline set** - Click the **Discipline set** drop-down list, and then select **New discipline set**. Enter a new name, and then click **Create**.
- **Add discipline group** – Select a discipline set from the list, click the **Configure discipline group** icon, enter an ID and description, and then click **Add** icon. You cannot delete a discipline group assigned to a discipline in the set.

Discipline set

Discipline set

MR1

	Position	*Discipline	*Disciplin
+	11	Select discipline	Select dis
☐	01	Aggregates and Paving	1
☐	02	Building	1
☐	03	Bulk Commodities	2
☐	04	Change Orders, Contract All...	2
☐	05	Commercial Cost	4
☐	06	Engineering	3

Configure discipline group

	Position	*ID	*Description	
+	07	Enter ID	Enter description	
☐	01	1	1	⊗
☐	02	2	2	⊗
☐	03	3	3	⊗
☐	04	4	4	⊗
☐	05	5	5	⊗
☐	06	7	7	⊗

- **Add discipline to a discipline set group** – Click the **Discipline set** drop-down list, and then select a discipline set. Click the **Select discipline** drop-down list, and then select a discipline. Click the **Select discipline group** drop-down list, and then select a discipline group. Click the **Add discipline to set** icon. You cannot delete a discipline assigned to an account code in an account code set.
- **Remove a discipline or a discipline group** - Click the **Remove discipline from the set** or the **Remove discipline group** icon to the right. You cannot delete a discipline group assigned to a discipline in the set or a discipline assigned to an account code in an Account Code set.
- **Edit a discipline group or a discipline** - Click in the fields, and then enter text.
- **Sort** - Select the item, and then click the up and down arrows to the right of the table to adjust the position of a discipline or discipline group.

2.24.2 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

2.25 ACCOUNT CODE SET

Account code sets (ACS) are used to configure metadata in an account code to better drive data reliability when leveraging account codes on quantity items. Account code sets also help you narrow down account codes to only those you need to use in Design for specific projects. You can only add account codes that exist in Main menu > Master data libraries > **Account codes**.

When the **Enable Account code set and Discipline set** toggle is set to *On*, you can manage account code sets for your organization in Settings > Design > Quantity Forecasting > **Account code set**.

QUANTITY FORECASTINGENGINEERINGAUDIT LOG

CancelSave

Account code set

Account code set

SASA

Discipline set

TKiewit

Include selected account code set in project settings?

☒

☐

Account code

☐

30.06.02.002

☐

30.06.02.006

☐

30.06.02.009

☐

30.06.02.012

☐

30.06.02.012.02

Account code description

Mobilization and Demobilization ...

Equipment Setup, Dismantle, Rec...

Overland Major Crane Moves - La...

Tower Crane Setup and Dismantle

Tower Crane Setup - Foundation ...

Design element

Mobilization / Demobili...

Mobilization / Demobili...

Crane Walk

Mobilization / Demobili...

Mobilization / Demobili...

Primary UoM

Ea

Ea

LF

Ea

Ea

Alternate System UoM

Ea

Ea

m

Ea

Ea

Ground

Above

Under

Above

Above

Above

Disci

Operi

Overh

Operi

Operi

Operi

Subtotals

Count: 17,263

2.25.1 Steps

You can do any of the following actions:

- **Create a new account code set** - Click the **Account code set** drop-down list, and then select **New account code set** from the list. Enter a new name, and then click **Create**.
- **Add account code set values to an account code set group** - Click the **Configure account code group** icon, enter an ID and description, and then click **Add** icon. Account code groups are account code set specific. Account code groups can be added individually or in bulk using the import process. You cannot add or import account codes to a set without at least one account code group maintained. You cannot delete account code groups tagged to an Account code in

Page 56 of 183

InEight Inc. | Release 26.7

the set. Account code values assigned to an account code in the set cannot be removed.

The screenshot displays the 'Account code set' configuration interface. The main window shows a list of account codes for set 'S11'. A modal window titled 'Configure account code set values' is open, showing a table of account code groups. The table has columns for Position, *ID, and *Description. The first row is for Position 06, with *ID and *Description fields for entry. Subsequent rows are for Positions 01 through 05, each with a checkbox and a red 'X' icon in the final column. The modal also includes a title bar with a close button and a subtitle 'ACCOUNT CODE GROUP'.

- **Add account codes to an Account code set** - Click the **Add account code** icon, select an account code from the list, and then click **Assign**. Select the required and optional attributes for the account code, and then click **Add**.
- **Remove an account code or an account code group** - To remove an account code, select the account code, and then click the **Remove account code** icon. To remove an account code group, click the **Remove account code group** icon to the right. You cannot remove an account code group assigned to an account code set in the set or an account code assigned to a project.
- **Edit an account code group or account code** – To edit an account code group, click in the fields, and then enter text. To edit an account code, select an account code, and then click the **Edit account code** icon. In the Edit account code slide-out panel, make your changes, and then click **Save**.
- **Sort** - Select the item, and then click the up and down arrows to the right of the table to adjust the position of account code groups.
- **Update account codes that have been modified in InEight Platform** - The Update account codes feature alerts you of any account code updates made to the master account code library in Platform that impacts any account code in an ACS, such as deleted account codes or modified UoMs.

Account code set

Account code set

SASA

Discipline set

1K

Include selected account code set in project settings?

☒
☐
☐
☒
☐

☐	Account code	Account code description	Design element	Primary UoM	Alternate System UoM	Ground	D
☐	61.09.14 ⚠️	Concrete on Metal Deck	Concrete on Metal Dec...	SF	m2	Above	Ci
☐	61.09.14.002 ⚠️	Concrete on Metal Deck	Concrete on Metal Dec...	SF	m2	Above	Ci
☐	61.09.14.002.02	Concrete on Metal Deck - Fab Fo...	Fab Forms	SF	m2	Above	Ci
☐	61.09.14.002.04	Concrete on Metal Deck - Edge o...	Concrete on Metal Dec...	LF	m	Above	Ci
☐	61.09.14.002.06	Concrete on Metal Deck - Deck P...	Concrete on Metal Dec...	SF	m2	Above	Ci
Subtotals		Count: 17,263					

You can review and update the account codes using the Update account codes wizard. Click the **Update account codes** icon to launch wizard and sync account codes in the set with the master data account code in Platform.

QUANTITY FORECASTINGENGINEERINGAUDIT LOG

CancelSave

Account code set

Update account codes

The following account codes have either been deleted or had a UoM modified in Core. Please select which account codes you would like to update in the account code set.

☐

Update type

☐

Modified UoM

☐

Modified UoM

☐

Modified UoM

⚠

⚠

⚠

61.09.14

61.09.14.002

70.25.24

Concrete on Metal Deck

Concrete on Metal Deck

Pipeline Tie-In

Concrete on Metal...

Concrete on Metal...

Pipeline Tie-In - LF

SF

SF

LF

SF

SF

LF

CY

CY

Ea

m3

m3

Ea

0 item selected

Cancel

Update

Any account codes that are updated in the ACS are also updated in projects that have the ACS assigned. To update modified UoM update types, the Design element UoM assigned on the account code in the ACS must match the modified UoM. You cannot select the account code

without the UoM match. You can edit the Design element assignment directly in the wizard to assist with the UoM alignment.

- **Make an ACS available in project settings** - Select an account code, and then turn the **Include selected account code set in project settings** toggle to *On*.

At the project level, you can tie an account code set to your project. For more information, see **Account code set** in the [General](#) settings.

2.25.2 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

2.26 DESIGN TRACKING STAGES

Design tracking stages are used to track how scope quantities change across an organization's design's milestones. You can manage Design tracking stages for your organization in Settings > Design > Quantity Forecasting > **Design tracking stages**.

QUANTITY FORECASTING

ENGINEERING

AUDIT LOG

Cancel

Save

Design tracking stages

	Position	*Design stage title	
+	12	Enter design stage title	
☐	01	30% Qty	⊗
☐	02	60% Qty	⊗
☐	03	90% Qty	⊗
☐	04	100% Qty	⊗
☐	05	Option A Qty	⊗
☐	06	Current IFC Qty	⊗
☐	07	Option B Qty	⊗
☐	08	add	⊗
☐	09	Stage 1	⊗

2.26.1 Steps

You can do any of the following actions:

- **Add** - Enter a Design stage title, and then click the **Add** icon. Design stage titles must be unique.
- **Edit** - Click in the fields, and then enter text.
- **Delete** - Click the **Delete Design tracking stage** icon to the right. You cannot delete tracking stages assigned to a project.
- **Sort** - Select the Design tracking stage, and then click the up and down arrows to the right of the table to adjust the position of a Design stage.

When Design tracking stages are created, they become available to add in the settings for projects in the organization. For more information, see [Design tracking stages](#) in project level settings.

2.26.2 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

2.27 DESIGN ELEMENTS


Design elements are used to group like scope into specific coding that you can associate to a quantity item and roll up quantity, hours, and cost to the design element level to drive decision making information on a project.

You can manage design elements for your organization in Settings > Design > Quantity forecasting > **Design elements**.

Cancel

Save

Design elements

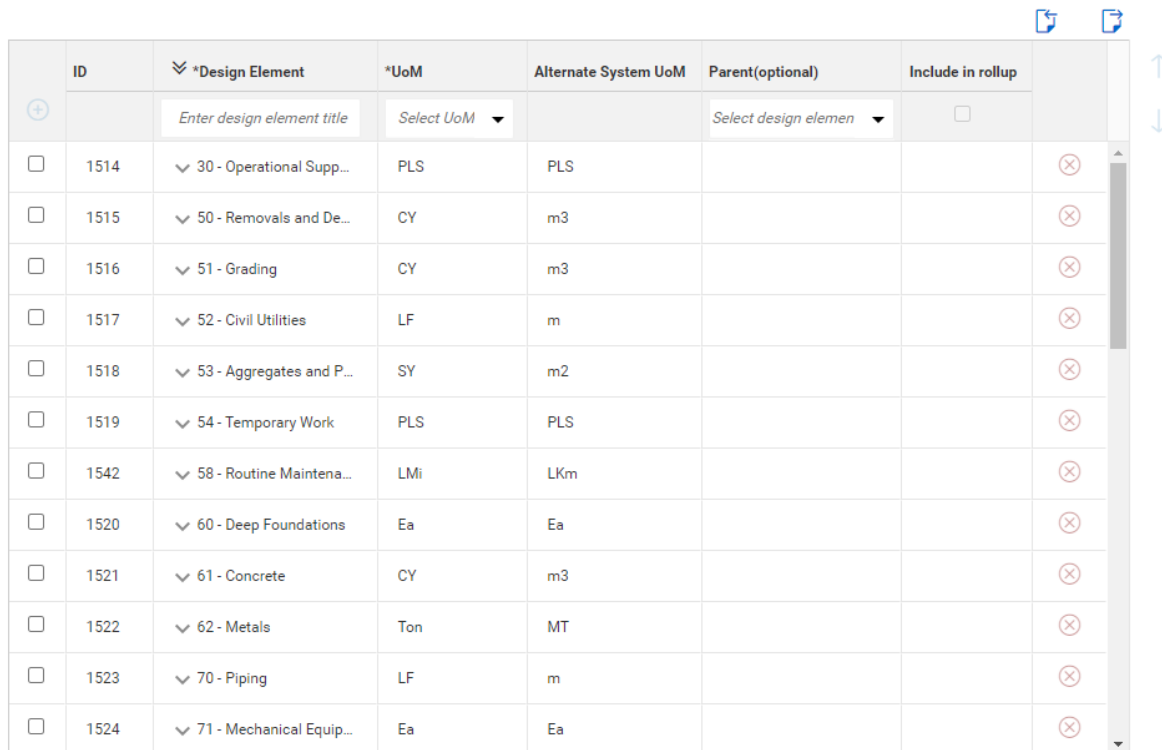

	ID	*Design Element	*UoM	Alternate System UoM	Parent(optional)	Include in rollup	
		Enter design element title	Select UoM		Select design elemen	☐	
☐	1514	30 - Operational Supp...	PLS	PLS			⊗
☐	1515	50 - Removals and De...	CY	m3			⊗
☐	1516	51 - Grading	CY	m3			⊗
☐	1517	52 - Civil Utilities	LF	m			⊗
☐	1518	53 - Aggregates and P...	SY	m2			⊗
☐	1519	54 - Temporary Work	PLS	PLS			⊗
☐	1542	58 - Routine Maintena...	LMI	LKm			⊗
☐	1520	60 - Deep Foundations	Ea	Ea			⊗
☐	1521	61 - Concrete	CY	m3			⊗
☐	1522	62 - Metals	Ton	MT			⊗
☐	1523	70 - Piping	LF	m			⊗
☐	1524	71 - Mechanical Equip...	Ea	Ea			⊗

2.27.1 Steps

You can do any of the following actions:

- **Add** - Enter a unique name, select a UoM, and optionally select a parent Design element to group elements together, and then click the **Add design element** icon. The Alternate System UoM will be automatically populated based UoM selected. You can also use the import process to import Design elements using the Export and Import icons.
- **Edit** - Click in the fields, and then enter text.
- **Delete** - Click the **Delete Design element** icon on the right. You cannot delete terminal Design elements assigned to a quantity item.
- **Sort** - Select the Design element, and then click the up and down arrows to the right of the table to adjust the position of a Design element.

- **Include in rollup** - The Include in rollup option is only applicable to terminal Design elements. The setting can only be selected when the terminal Design element UoM matches its parent Design element UoM.

When Design elements are created, they become available to add in the settings for projects in the organization. For more information, see [Design element setup](#) in project settings.

2.27.2 Considerations

- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.
- Only terminal Design elements can be associated to a quantity item.
- A parent Design element cannot be deleted when associated with a terminal Design element.
- Design element names must be unique and are required to have a UoM.

2.28 NOTES

2.28.1 Tags

Tags are used when entering notes or quantity item change log entries. You can manage tags for your organization in Settings > Design > Quantity forecasting > Notes > **Tags**.

QUANTITY FORECASTING
ENGINEERING
AUDIT LOG

Cancel
Save

Notes

Tags

	Position	*ID	*Description	Required	
+	06	Enter ID	Enter Description	⊖	
☐	01	QR	Quantity Reduction	⊖	⊗
☐	02	QG	Quantity Growth	⊖	⊗
☐	03	EA	Estimating Aware	✓	⊗
☐	04	A1	A1	✓	⊗
☐	05	A2	A2	✓	⊗

2.28.2 Steps

You can do any of the following actions:

- **Add** - Enter a tag ID, description, set the Required toggle, and then click the **Add tag** icon.
- **Edit** - Click in the fields, and then enter text.
- **Delete** - Click the **Delete tag** icon on the right of the table. Tags assigned to a quantity item cannot be deleted.
- **Sort** - Select the tag, and then click the up and down arrows to the right of the table to adjust the position of a tag.

When the required toggle is set to *On*, the tag is added to all the projects in the organization. Tags not set as required are available to add to all projects in Project Settings. For more information about Tags, see **Notes** in [General](#) project settings.

2.28.3 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

2.29 CAUSE CODES

Cause codes are a standard set of coding you can configure for your organization to highlight reasons why change was observed on the project. When a quantity item change occurs, you are required to use cause codes.

You can manage cause codes for your organization in Settings > Design > Quantity Forecasting > **Cause codes**.

QUANTITY FORECASTINGENGINEERINGAUDIT LOG

CancelSave

Cause codes

	Position	*ID	*Description	
	13	Enter ID	Enter description	
☐	04	DP	Design Progression	
☐	05	DG	Design Growth	
☐	06	EE0	Engineering Error or Omission	
☐	07	ESE0	Estimating Error or Omission	
☐	08	VDMC	Vendor Design or Material Change	
☐	09	PCC	Prime Contract Change	
☐	10	C1	C1	
☐	11	C2	C2	
☐	12	C3	C3	

2.29.1 Steps

You can do any of the following actions:

- **Add** - Enter an ID and a description, and then click the **Add Cause code** icon.
- **Edit** - Click in the fields, and then enter text.
- **Delete** - Click the **Delete cause code icon** to the right. You cannot delete cause codes assigned to a quantity change note on a project.
- **Sort** - Select the cause code, and then click the up and down arrows to the right of the table to adjust the position of a cause code.

When cause codes are created, they become available to all projects in the organization. For more information, see [Quantity change notes](#).

2.29.2 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

2.30 PROJECT SETTINGS FOR QUANTITY FORECASTING

As an administrator, you can configure settings for the Quantity Forecasting module at the project level. Settings at the organization level are inherited by associated child organizations and projects. At the project level, you can further refine some settings to customize how they are applied in each project.

You can manage project settings in project > settings > **Design**.

The Design project settings gives you access to the following project configurations:

[General](#)

[Design element setup](#)

[Design tracking stages](#)

[Attributes and project values](#)

[Component integration](#)

[Linked engineering projects](#)

For general information on InEight cloud platform settings, see [Project Settings](#).

2.31 GENERAL

The general settings gives you access to general project configurations. From your project's home page, you can manage the general settings in Settings > Design > Quantity Forecasting > **General**.

The image and table below is an overview of the General settings tab:

QUANTITY FORECASTINGENGINEERING

General

Design element setup

Design tracking stages

Attributes and project values

Component integration

Schedule

Linked engineering projects

Cancel

Save

1

Auto ID configuration

Automatically generate a new quantity item's ID?
☒

2

Account code set

Tied to account code set?
☒

*Account code set locks on upload of quantity item structure
1Kievitt

Select UoM from Account Code Set:
☒ Primary UoM
☐ Alternate System UoM

3

Control Integration

Inherit WBS attributes? (Account code, Cost segment, UoM, Play item, Assigned vendors)
☒

4

Manual Unit Rate Configuration

Enable editing of OB Mhrs/Unit or CB Mhrs/Unit fields?
Original Budget ☒ Current Budget ☐

5

CE Mhrs Configuration

Select unit rate that will drive CE Mhrs:
☒ CE Mhrs/Unit
☐ CB Mhrs/Unit

6

Notes

Tags

	Position	ID	*Description	
☒	10		Select tag	
☐	01	adddddddd	add	☒
☐	02	QG	Quality Growth	☒
☐	03	QR	Quantity Reduction	☒
☐	04	A1	A1	☒
☐	05	A2	A2	☒
☐	06	A3	A3	☒
☐	07	aaa	aaa	☒
☐	08	AB	Absolute b	☒
☐	09	aaaaaaaaa	aaa55555	☒

General settings tab

	Title	Description
1	Auto ID configuration	Allows project admins to set whether an ID is system generated or user specified when a new Quantity Item is added to the project.

2

Account code set

Allows project admins to enable the use of Account Code Sets on a

General settings tab (continued)

	Title	Description
		project and select which Account Code Set to use. Account Code Sets are created in the Org Settings and consist of many Account Codes that are tagged with Design Element, UoM, Ground, Discipline, Qty Source information. When an Account Code Set is tied to a project, the tagged attribute fields will be auto populated on the Quantity Item when an Account Code is assigned. The Quantity Items grid must be empty to enable/disable the Account Code Set project setting. When an Account Code Set is tied to a project, only those Account Codes in the set will be available to assign to the Quantity Item. This setting gives project admins the option to use either the Primary UoMs or Alternate System UoMs on the project when an Account Code is assigned to a Quantity Item. Project admins can also enable the ability to edit the inherited UoMs and their usage in the column, add or edit in the slide-out panel, and via import. To disable the feature, all Quantity Item UoMs must align to the assigned Account Code's UoM from the associated Account Code Set.
3	Control Integration	Enable integration of InEight Control's WBS attributes for the project. Quantity items will inherit the

General settings tab (continued)

	Title	Description
		Account code, Cost segment, UoM, Pay item, and Assigned attributes. The inherited attributes are disabled in the quantity item fields. To enable Control Integration, the WBS phase code must be selected as Required and Unique in the Quantity Forecasting > Fields and component integration settings tab and existing data must align with Control's WBS attributes.
4	Manual Unit Rate Configuration	Allows project admins to manually set the OB MHrs/Unit and/or CB MHrs/Unit on all the Quantity Items in the project. When the setting is enabled, the OB and/or CB MHrs will not be generated using the unit rates from InEight Control. With the setting enabled, the "Get OB MHrs/Unit" and/or the "Get CB MHrs/Unit" will be removed from the Actions menu and the OB MHrs/Unit and/or CB MHrs/Unit fields will become editable. The system requires all OB MHrs/Unit and/or CB MHrs/Unit fields to be empty to turn this setting Off. If you were functioning off Control OB and/or CB Unit Rates, then the system will allow you to turn this setting On, but all the OB and/or CB Unit Rate fields will be cleared.
5	CE MHrs Configuration	Allows project admins to specify which unit rate should be used to

General settings tab (continued)

	Title	Description
		calculate the CE MHrs on each Quantity Item in the project. The setting allows for either the CE unit rate or the CB unit rate to be used to drive the CE MHrs. This setting will be applied to all Quantity Items in the project. The setting can be changed in the middle of a project. If the setting is changed, the user will be prompted with a warning message and the system will automatically update the CE MHrs on every Quantity Item using the updated unit rate.
6	Notes	Tags - Allows project admins to add and remove tags on project which can be added to the individual notes maintained on a Quantity Item. Once a tag is created in the Organization Settings, then it will become available to add to a project through this project settings.

2.31.1 Considerations


You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

2.32 DESIGN ELEMENT SETUP

Design elements are used to group like scope into specific coding and associate it to a quantity item. The quantity, hours, and cost can then be rolled up to the design element level to drive decision making information on a project. Design elements are configured in organization settings and are

available to all projects in the organization. For more information, see **Design elements** in organization settings.

You can manage Design elements in the project’s Settings > Design > Quantity forecasting > **Design element setup** tab. You can select which Design elements are available on the project.

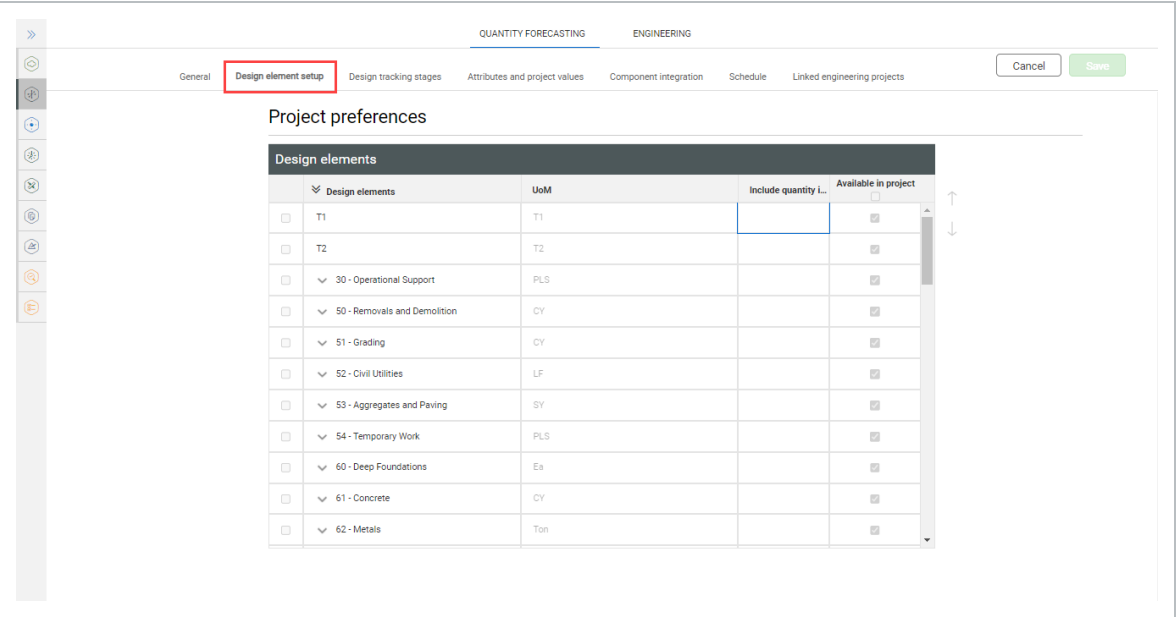

Design elements configured at the organization level are available to all projects in the organization. For more information, see [Design elements](#) in organization settings.

When an Account code set is enabled on the project, the Include quantity in the rollup calculation and Available in project options are disabled in the Design elements grid, as the project uses the Design elements tagged to the account codes in the Account code set. For more information, see **Account code set** in the project’s [General](#) settings.

2.32.1 Steps

You can perform the following actions for Design element setup:

- **Available in project** - Select which Design elements to make available in the project.
- **Sort** - Select the Design elements, and then click the up or down arrows to the right of the table to adjust the position of a Design element.


2.32.2 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

2.33 DESIGN TRACKING STAGES

Design tracking stages are used to track how scope quantities change throughout the design process. Design tracking stages are created in organization settings and are available to add to all projects in the organization. For more information, see **Design tracking stages** in organization settings.

You can manage Design tracking stages in the project's settings (Design > Quantity forecasting > **Design tracking stages** tab).

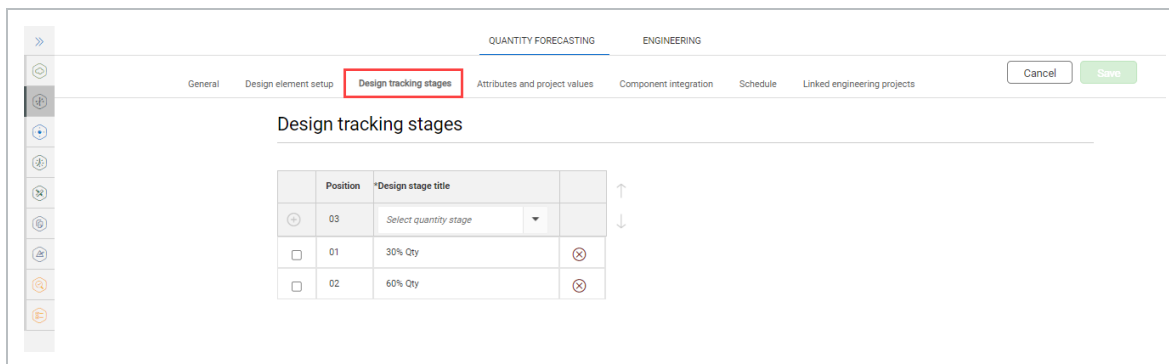

By adding a design tracking stage to a project, a field is added to the Quantity Items grid and quantity item slide-out panel. Tracking stages can then be imported into the project.

2.33.1 Steps

You can perform the following actions for Design tracking stages:

Add – Click the Select quantity stage drop-down, select a stage from the list, and then click the Add icon.

Remove - Click the Remove icon to the right. You cannot remove Design stages that have been assigned to quantity items.

Sort - Select the Design tracking stage, and then click the up or down arrows to the right of the table to adjust the position of a Design stage.

Design tracking stages created in organization settings become available to add in the project settings for every project in the organization. For more information, see [Design tracking stages](#) in organization settings.

2.33.2 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

You cannot delete Design tracking stages that are assigned to a project.

2.34 ATTRIBUTES AND PROJECT VALUES

You can configure the criteria for how attributes and project value types are associated to a quantity item and if they are required in a project in project > Settings > Design > Quantity Forecasting > **Attributes and project values** tab. For each attribute and project value, you can configure which one is included, required, and unique.

The following image shows the Attributes and project values tab:

QUANTITY FORECASTING ENGINEERING

General Design element setup Design tracking stages **Attributes and project values** Component integration Schedule Linked engineering projects

Required and unique fields

Identify the required field for a quantity item, and the combination of fields that will make the quantity item unique.

Name	Include	Required	Unique	Component
Attributes				
ID	☒	☒	☐	☐
Account code	☒	☒	☒	☒
WBS phase code	☒	☒	☒	☒
Discipline	☒	☒	☐	☐
Work type	☒	☐	☐	☐
Cost segment	☒	☐	☐	☐
Design element	☒	☒	☐	☐
UoM	☒	☒	☐	☐
Ground	☒	☒	☐	☐
Construction work package	☒	☐	☐	☐
Engineering work package	☒	☐	☐	☐
Deliverable package	☒	☐	☐	☐
Project values				
Area	☒	☐	☐	☐
Construction commodity	☒	☒	☒	☒
DemoProject1221	☐	☐	☐	☐
Segment	☒	☐	☐	☐
Subsystem	☒	☐	☐	☐
System	☒	☐	☐	☐
test JS	☐	☐	☐	☐
TestProjValueType	☐	☐	☐	☐
TestRavali12	☐	☐	☐	☐
Turnover	☒	☐	☐	☐
Work classification	☒	☒	☐	☐

Include – When you turn the Include option to *On* for a value, the value is made available to select from as optional in quantity items.

Required - When you turn the Required option to *On* for a value, the value is a required attribute on the quantity item. Required fields will show with an asterisk in the project to let you know which fields are required when adding or editing quantity items. Design checks that these required fields are maintained when adding or editing quantity items in the project.

Unique - The Unique toggle lets you set to *On* a combination of fields for setting quantity items uniqueness. For example, if you select System, Area, and Turnover in the Unique setting, then Design does not allow two quantity items to exist in that project with the same System, Area, and Turnover combination. Design checks this unique setting every time a quantity item is added or edited in the project. The field must first be set as required to set it as a unique field. The setting is primarily needed for the integration with InEight Plan to automatically associate Plan components to the quantity items

in Design. The uniqueness of the field eliminates a potential conflict with quantity items during the Plan component sync and association process.

Component - When the Plan component integration is enabled for the project in the [Component integration](#) tab, you can configure which values will integrate with Plan components. To turn the Component field to *On*, you must first set the field as required and unique. Unique and Component fields must match.

2.34.1 Attributes

The attribute values are part of the Design application and are used to configure the project's quantity items. All attributes have Include set to *On* by default. You can change the values for each project.

2.34.2 Project values

You can select which project value types can be associated to quantity items and if they are required in a project. The Project value types have Include set to *Off* by default. The project values are supplemental attributes configured at the organization level. For more information, see [Project values](#) in organization settings.


2.34.3 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

2.35 COMPONENT INTEGRATION

2.35.1 Plan Component Integration

In the Component integration tab, you can enable the integration with InEight Plan components.

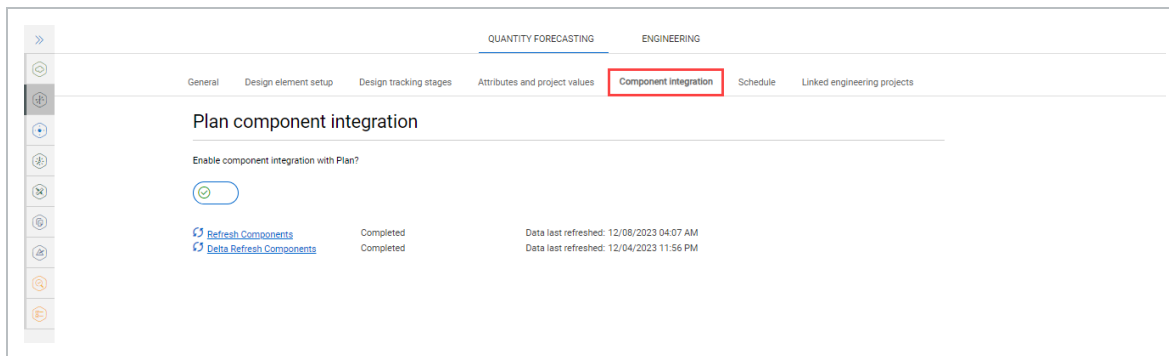

Setting the Enable component integration with Plan toggle to *On* enables the following:

- The Get Plan Components option in the project > Design > Quantity Items > **Actions** menu.
- The Component column in project > Settings > Design > Quantity Forecasting > **Attributes and project values** tab. You can configure criteria for how component data is assigned to a quantity item.

Sync components by clicking **Refresh Components** or **Delta Refresh Components**. The status and last refresh date are shown next to the refresh options so you can be informed of when the last refresh was completed.

When you enable component integration with Plan, at least one attribute must be set to *On* in the project > Settings > Quantity Forecasting > Attributes and project values > **Component** column. For more information, see [Attributes and project values](#).

When components with these attributes are synced from Plan, Design automatically associates the components to the quantity item when a quantity item exists with matching attributes.

The component attributes must match the unique configured attributes. Changes to Component integration settings cannot be saved until these are selected.


2.35.2 Considerations

- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

2.36 LINKED ENGINEERING PROJECTS

You can link projects with the goal of sharing deliverable and engineering work packages from the Engineering module to the Quantity forecasting module and show Engineering Work Packages in

InEight Plan. You can manage linked engineering projects in project settings (Design > Quantity Forecasting > **Linked engineering projects** tab).



To share engineering work packages between different projects and Plan, you must link the projects.

By default, each project is already linked to itself, so you can always share deliverable and engineering work packages in the same project.

In the Quantity forecasting module, there are two fields that are linked and populated from the Engineering module:

- **Deliverable package:** This field draws data from Actions > Configure work packages > **Deliverable Package** in the Engineering module for linked projects.
- **Engineering work package:** This field draws data from Actions > Configure work packages > **Engineering Work Package** in the Engineering module for linked projects.

Edit quantity item

DETAILS

QUANTITIES

COMPONENTS

NOTES

Select one

Select one

OB MHrs/Unit

CB MHrs/Unit

650.00

Commodity

Select one

Construction work package

Select one

Deliverable package

PWD

Engineering work package

Bridge

User defined field 1

C1001.01010

User defined field 2

User defined field 3

User defined field 4

User defined field 5

User defined field 6

Design Complete

Cancel

Save

These fields are also available as columns in the quantity items grid.

After you associate a deliverable or engineering work package with a quantity item, you cannot delete the package or unlink the project.

2.36.0.1 Integration with Plan

In Plan's Work packaging module, you can associate EWPs from Design to Construction work packages (CWP). For more information on associating EWPs, see Engineering work package (EWP) in Plan's [Work package creation](#) topic.

2.36.1 Steps

Link projects

1. From the Linked engineering projects tab, click **Link project**
2. In the dialog box, select one or more projects, and then click **Add**

You will only see projects you have permission for.

To unlink a project, click the **Unlink** project button next to the project.

CHAPTER 3 – ENGINEERING MODULE OVERVIEW

3.0.1 Summary

The Engineering module lets you perform design planning, resourcing, and progress tracking. The module lets you take off your design scope in a standardized method and associate configurable master and project-level data. The design scope is taken off as a combination of claiming schemes and scope items. Resources can be allocated to the scope items.

The Engineering module is integrated with InEight Control to let you assign WBS phase codes to a scope item. This lets earned quantity value flow to integrated WBS phase codes in Control, where you can manage budgets, earned value, and earned revenue.

3.1 SCOPE ITEMS

3.2 SCOPE ITEMS OVERVIEW

The Scope items page is the main page of the Engineering module. All individual engineering deliverables are created and tracked as scope items in the grid on this page. You must have the permission View scope items.

The following image and table provide an overview of each section of the Scope items page.

The screenshot shows the 'SCOPE ITEMS' page with the following callouts:

- 1: Actions dropdown menu
- 2: Filter and sort icons
- 3: View: Default dropdown menu
- 4: Table header row
- 5: Filter, Add, Edit, and Search icons
- 6: Table body row
- 7: User profile icon
- 8: Table body row

ID	Description	Claiming scheme	Claiming scheme description	% Complete	Lead discipline
262893	P&ID_128	PIDS		0.00	Mechanical
262892	P&ID_127	PIDS		0.00	Mechanical
261919	P&ID_131 upd er	PIDS		13.00	Mechanical
261687	P&ID_1301	PIDS		0.00	Mechanical
261686	P&ID_129	PIDS		65.00	Mechanical
261683	P&ID_126	PIDS		0.00	Mechanical

Subtotals Count: 296

Overview - Scope items page


Title		Description
1	Actions menu	Do any of the following: • Manage documents • Configure claiming schemes • Configure work packages • Configure project values • Get FC Remaining MHrs/Unit • Lock or Unlock Budget • Role assignment • Run reports
2	Scope item buttons	Add, edit, and delete scope items.
3	View	Manage project-specific views by saving, renaming, importing, and deleting views. For more information, see the Project views section below.
4	Scope items	Grid showing scope items and related information organized by columns.
5	Upper-right toolbar	• Create query filter - Opens the query builder • Import and Export - Import and export sets of data • Find - Search scope items
6	Column chooser	Select which columns are shown or hidden.
7	Show/Hide claiming steps	Shows claiming scheme steps, details, and history. It also lets you claim completion for each scope item.
8	Additional views	Select from the following views: • All Scope Items • WBS rollup • Assigned to Me.

3.2.1 Project views


You can add, remove, and filter columns to customize your view on the Scope Items page. You can save the customized view in your project for future use. When you save a custom view, the view is saved

and stored in the project and is not automatically available in other projects.

After you customize your view, click the **View** drop-down menu, and then select **Save view as** to save it as a new project view. When you update an existing custom view, you have the option to save the updated custom view by selecting **Save view**, or save it as a new view by selecting **Save view as**.

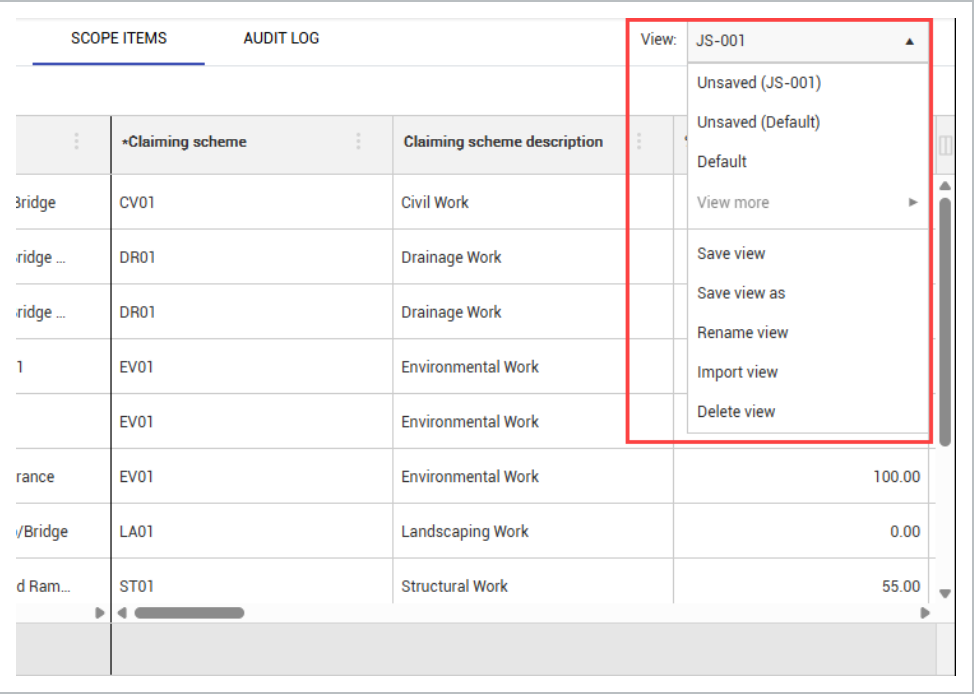

You can import saved views to your project by clicking View > **Import View**, and then select a project to import its views.

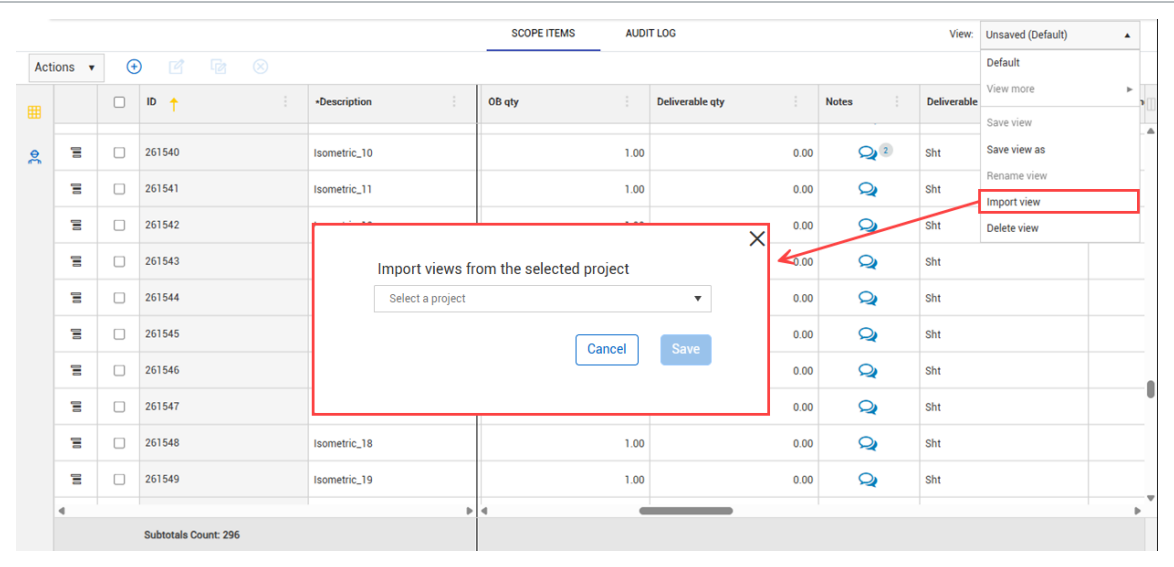


When you import a project, the project imports with all its saved views.

3.2.2 Column filter menus

You can use the column filter menus to better view and filter data. Click the **Column Menu** icon, and then select from the following:

- Sort Ascending
- Sort Descending
- Lock or Unlock
- Filter

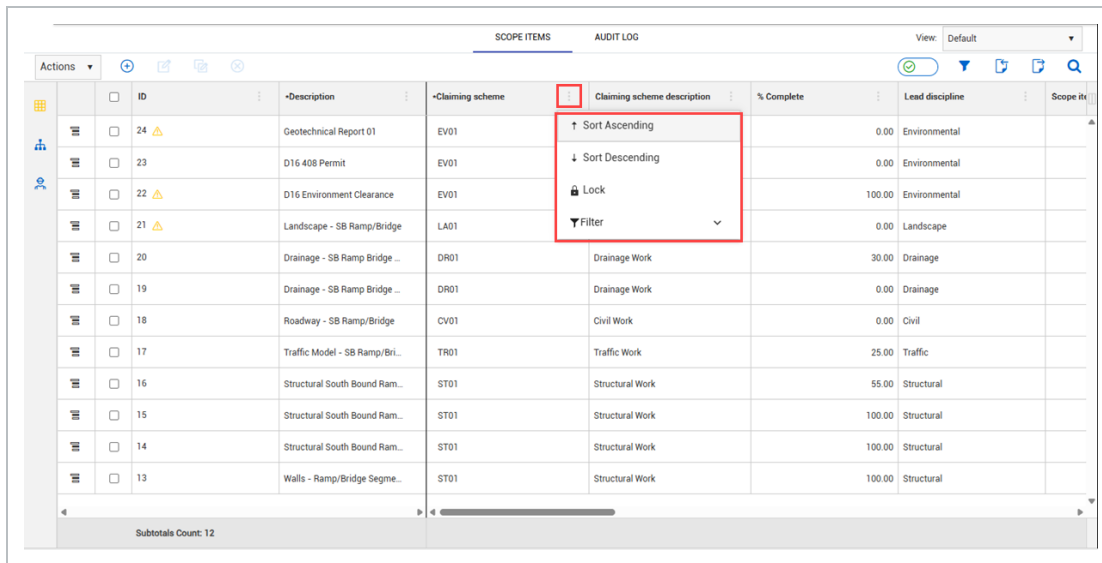

The screenshot shows a table titled 'SCOPE ITEMS' with columns: ID, Description, Claiming scheme, Claiming scheme description, % Complete, Lead discipline, and Scope item. A red box highlights the 'Claiming scheme description' column header, where a dropdown menu is open. The menu options are: '↑ Sort Ascending', '↓ Sort Descending', '🔒 Lock', and '🔍 Filter'. The table contains 12 rows of data, including items like 'Geotechnical Report 01', 'D16 408 Permit', and 'D16 Environment Clearance'.

ID	Description	Claiming scheme	Claiming scheme description	% Complete	Lead discipline	Scope item
24	Geotechnical Report 01	EV01		0.00	Environmental	
23	D16 408 Permit	EV01		0.00	Environmental	
22	D16 Environment Clearance	EV01		100.00	Environmental	
21	Landscape - SB Ramp/Bridge	LA01		0.00	Landscape	
20	Drainage - SB Ramp Bridge ...	DR01	Drainage Work	30.00	Drainage	
19	Drainage - SB Ramp Bridge ...	DR01	Drainage Work	0.00	Drainage	
18	Roadway - SB Ramp/Bridge	CV01	Civil Work	0.00	Civil	
17	Traffic Model - SB Ramp/Bri...	TR01	Traffic Work	25.00	Traffic	
16	Structural South Bound Ram...	ST01	Structural Work	55.00	Structural	
15	Structural South Bound Ram...	ST01	Structural Work	100.00	Structural	
14	Structural South Bound Ram...	ST01	Structural Work	100.00	Structural	
13	Walls - Ramp/Bridge Segme...	ST01	Structural Work	100.00	Structural	

3.2.3 Lock columns

You can lock columns to view key information when reviewing large amounts of data. You can lock one to multiple columns at one time. Locking columns allows you to scroll horizontally while keeping the column or columns locked in place on the left side of the page.

To lock a column in place, click the **Column Menu** icon next to a column, and then select **Lock** from the drop-down menu. To unlock a locked column, select **Unlock** from the drop-down menu.


3.2.4 Scope Item page audit columns

You can view the following columns which provide direct access to audit-related data without requiring you to review auto-log entries or open individual records.

- Created by
- Created date
- Modified by
- Modified date
- Document count
- Issue count

3.3 SCOPE ITEMS

In the Scope items page, you can manage scope items by performing actions such as adding and editing scope items. When you add or edit a scope item, a dialog box shows where you can enter data for the following sections shown in the image and table depending on your settings.

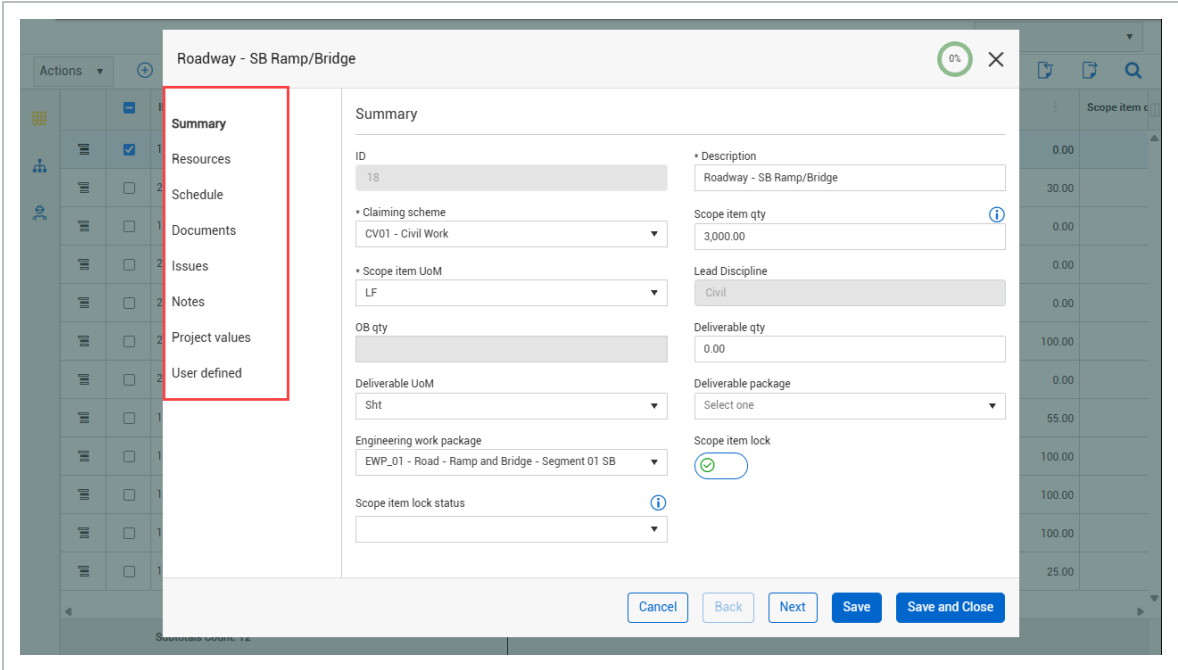

Section	Description
Summary	Shows details of the scope item, including ID, description, claiming scheme, and scope item quantity and UoM. For more information, see the Summary section below.
Resources	Shows the resources assigned to the selected claiming scheme so you can

Section	Description
	know what percentage of scope needs to be done by each resource. For more information, see Scope item resources .
Schedule	View Baseline, Current, and Actual schedule dates. To view the Schedule section, you must set one of the following Schedule setting to <i>On</i> : • Enable schedule integration toggle which allows you to manage activities. • Enable manual date entry toggle which allows you to manually select schedule dates.
Documents	When integrated with InEight Document, the Documents section shows documents associated with the scope item. For more information, see Documents overview .
Issues	Shows a distinct list of issues associated to the scope item. For more information, see Change integration – Associate scope items to issues .
Notes	Add notes to communicate scope item related information. The Notes section shows only when you edit a scope item. For more information, see the Notes section below.
Project values	Add and edit standardized project values configured in InEight Platform.
User defined	These are free-form text fields with a maximum of 250 characters each.

3.3.1 Summary section

The following fields show on the Summary section:

- **ID** - This field is automatically populated.
- **Description** - Must be unique.
- **Claiming scheme** - Must be set up on the Configure claiming schemes page.
- **Scope item qty and UoM** - If an account code set in enabled for the project, the UoM must match the UoM of the resource type's associated account code in the Resources tab, which is automatically populated after you select a claiming scheme. Scope item UoM must also match WBS phase code UoM to claim progress.
- **Lead Discipline** - This field is automatically populated based on the claiming scheme.

- **OB qty** - This field is initially populated by the Scope Item qty field when the budget is locked. It is not editable but is shown for tracking purposes. If you edit the scope item qty, you must enter a reason to explain the difference. See [Update scope item quantity](#) for more information.
- **Deliverable qty and UoM** - The quantities and units of the design deliverables, such as sheets. Deliverable package – You can use this field to group your scope of work.
- **Engineering work package** - This field can be used to group your scope of work separately from deliverable packages. For example, you might group multiple deliverable packages under one engineering work package.
- **Scope item lock** - You can lock the scope item and prevent further claiming. A yellow warning icon shows that claiming is disabled because the scope item is locked. You can lock or unlock a scope item at any time during the process.
- **Scope item lock status** - Associate a lock status value when you enable Scope item lock. Additional context is provided explaining why the scope item is locked. Lock statuses are optional and not required when locking a scope item. You can select from the following statuses:
 - Not started
 - On hold
 - Removed
 - Completed

The Forecast Remaining MHrs/Unit rate is automatically set to 0 when a lock status of *Removed* or *Completed* is selected. As a result, the scope item no longer shows remaining forecasted hours. The scope item lock statuses can be included in import and export functions. During import, lock status values are only processed when the scope item locked flag is enabled.


- **Project values** - Project values are standardized data configured in InEight Platform. For more information, see [Project values in scope items](#).

3.3.2 Notes section

When you edit a scope item, you can add notes in the Notes tab to communicate any information related to the scope item. The notes show in a conversation-style format. Notes show in chronological order and consist of the following information:

- The user who created the note
- The date and time the note was added

- The note content itself

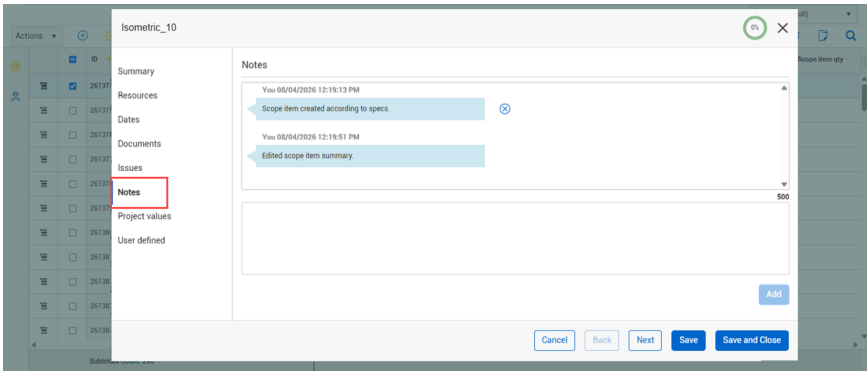

You can access notes from the Notes tab in the scope item dialog box and from the Notes icon shown on the Scope Items page.

SCOPE ITEMS									
AUDIT LOG									
View: Unsaved (Default)									
Actions	ID	Description	OB qty	Deliverable qty	Notes	Deliverable UoM	Engineering work package	Deliverer	
☒	261540	Isometric_10	1.00	0.00		Sht			
☐	261541	Isometric_11	1.00	0.00		Sht			
☐	261542	Isometric_12	1.00	0.00		Sht			
☐	261543	Isometric_13	1.00	0.00		Sht			
☐	261544	Isometric_14	1.00	0.00		Sht			
☐	261545	Isometric_15	1.00	0.00		Sht			
☐	261546	Isometric_16	1.00	0.00		Sht			
☐	261547	Isometric_17	1.00	0.00		Sht			
☐	261548	Isometric_18	1.00	0.00		Sht			
☐	261549	Isometric_19	1.00	0.00		Sht			
Subtotals Count: 296									

Users with the View scope items permission can add notes even when they do not have permission to edit the scope item.

3.4 ADD SCOPE ITEMS

3.4.1 Add a scope item

Scope items can be added manually or by importing them in bulk into the Scope items page. To add scope items, you must have the permission Add scope items and have added claiming schemes to associate with scope items. For more information, see [Claiming schemes overview](#).

Adding a scope item

1. Click the **Add scope item** icon in the upper left. The Add scope item dialog box opens.
2. Fill out the following required fields and any optional fields:
 - **Description**
 - **Claiming scheme**
 - **Scope item UoM**
3. Click **Add**. The Update scope item qty dialog box opens.

Update scope item qty

Please select a cause code and optional note as to why the scope item qty is being updated.

Cause code

Prime Contract Change

Note

☐ Associate to change issue

	Issue ID	Issue name
☐	19	One-Issue
☐	18	Design-issue
☐	17	q2
☐	16	q2
☐	15	q5

Cancel Update


4. Select a cause code from the **Cause code** drop-down list, and then optionally enter a note.
When integrated with InEight Change, you can optionally select the **Associate to change issue** check box, and then select an issue from the grid.
5. Click **Update**.

3.4.2 Import new scope items


Importing lets you add scope items in bulk. All imported scope items that pass validations are added to the Scope items page. The imported scope items that fail validations are added to the Error resolution page. All imports are shown in Audit log > **Import history**. To import cost items, you must have the permission Import scope items.

3.4 Step by Step 1 – Import scope items

1. On the Scope items page, click the **Export** icon, and then select **Export scope item template**. A Microsoft Excel spreadsheet is downloaded.

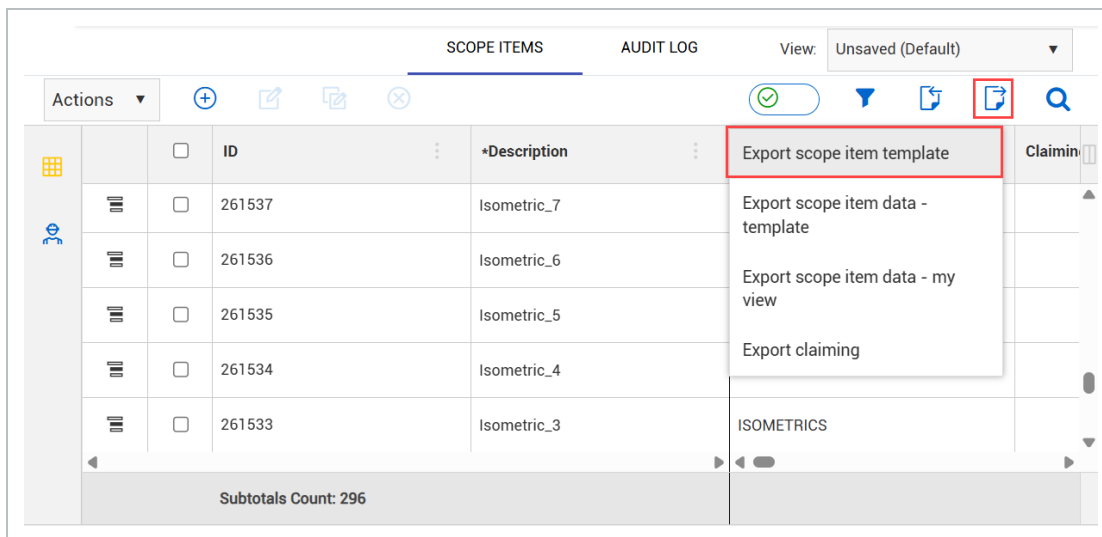

2. Complete the fields in the spreadsheet, and then save it.
3. On the Scope items page, click the **Import** icon, and then select **Import scope items**.

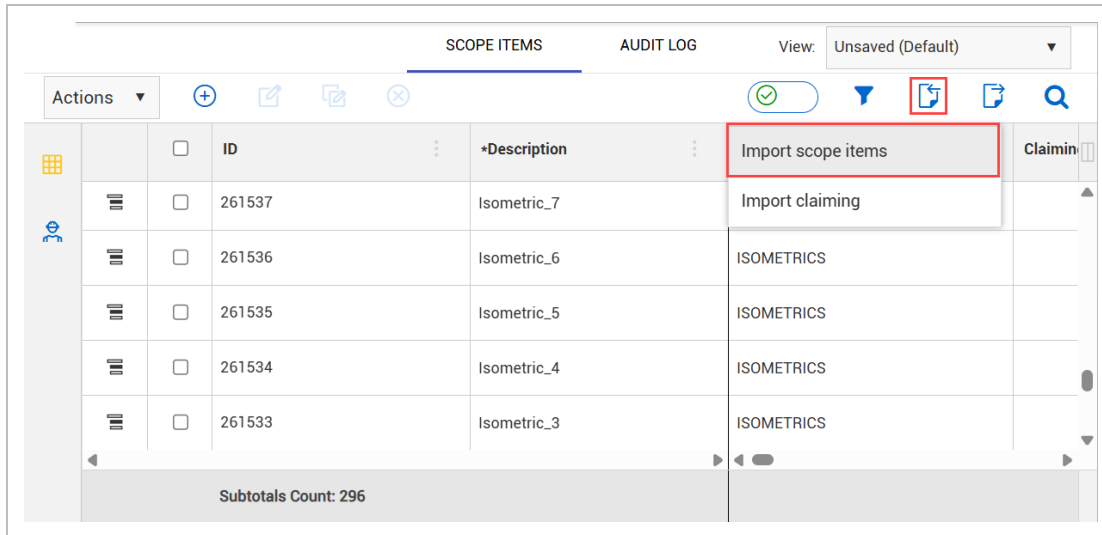

4. Click **Browse**, and then select the saved spreadsheet.
5. Click **Import**. The import status is shown, and then the Import history page opens. If there are any errors, they are shown in the table.
6. If there are issues, click **Completed with issues** in the Status column to open Scope item error resolution, and then click the scope item ID to view and resolve issues before saving.

3.5 EDIT SCOPE ITEMS

In the Scope item page, you can edit a single scope item or multiple scope items in bulk. You must have the permission Edit scope items.

When you select to edit scope items, the Edit scope item dialog box opens and shows the scope item details.

3.5.1 Edit a scope item

Editing a scope item

1. Select the check box to the left of one scope item and then click the **Edit scope item** icon in the upper left. The Edit scope item slide-out panel opens.

The screenshot shows the 'Edit scope items' dialog box for item 'Isometric_7'. The dialog is divided into two main sections: 'Summary' and 'Details'. The 'Summary' section contains fields for ID (261537), Description (Isometric_7), Scope item qty (1.00), Lead Discipline (Mechanical), OB qty (1.00), Deliverable qty (0.00), Deliverable UoM (Sht), Deliverable package (Select one), and Engineering work package (Select one). The 'Details' section contains fields for Claiming scheme (ISOMETRICS), Scope item UoM (Each), and Scope item lock (a toggle switch). The dialog also features a 'Cancel' button, a 'Back' button, a 'Next' button, a 'Save' button, and a 'Save and Close' button. A red box highlights the 'Save' and 'Save and Close' buttons.


2. Edit the fields you want to update.
3. Click **Save** or **Save and Close**.

When you update the Scope item qty on a scope item that has no claiming, the Update scope item qty dialog box will guide you through the process of the update. You have the option to associate the quantity change to InEight Change. For more information, see [Update scope item quantities](#).


3.5.2 Edit scope items in bulk

Bulk editing provides a quick and easy way to update multiple scope items. You can bulk edit scope items and assign WBS codes, teams, areas, and many other scope item values. You can then filter scope items using the updated column fields. For example, when you want to filter scope items to a team or area, you can select the applicable scope items in bulk, and then assign to a team or an area. You can then filter by teams or area to view the scope items. You no longer have to import bulk updates.


When you choose to edit multiple scope items, the Edit scope items dialog box shows. You can select from Scope Item and Resources column values to update the selected scope items.

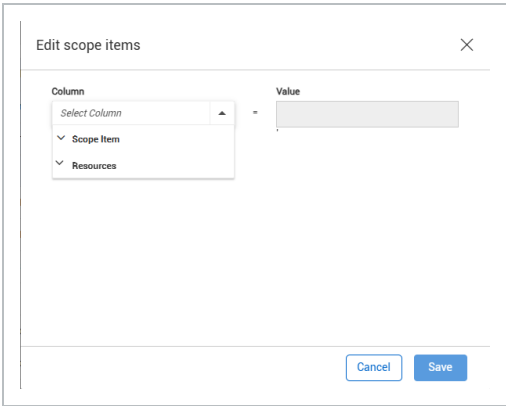

For example, when you set up a new project and WBS codes have not been assigned to scope items, you can select in bulk the applicable scope items, and then assign WBS codes to the scope items.

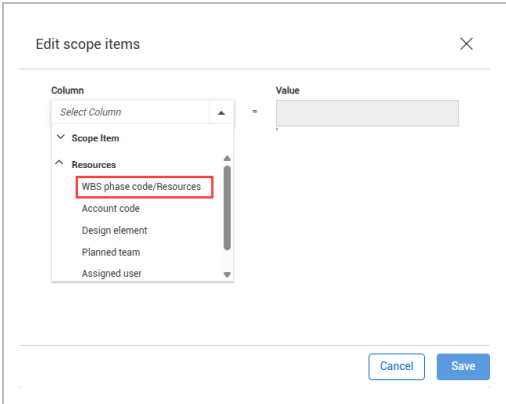

If the columns you selected have fields that cannot be updated, a message in red text alerts you that the field is not editable for at least one of the scope items. For example, you cannot edit a locked WBS or a locked claiming scheme.

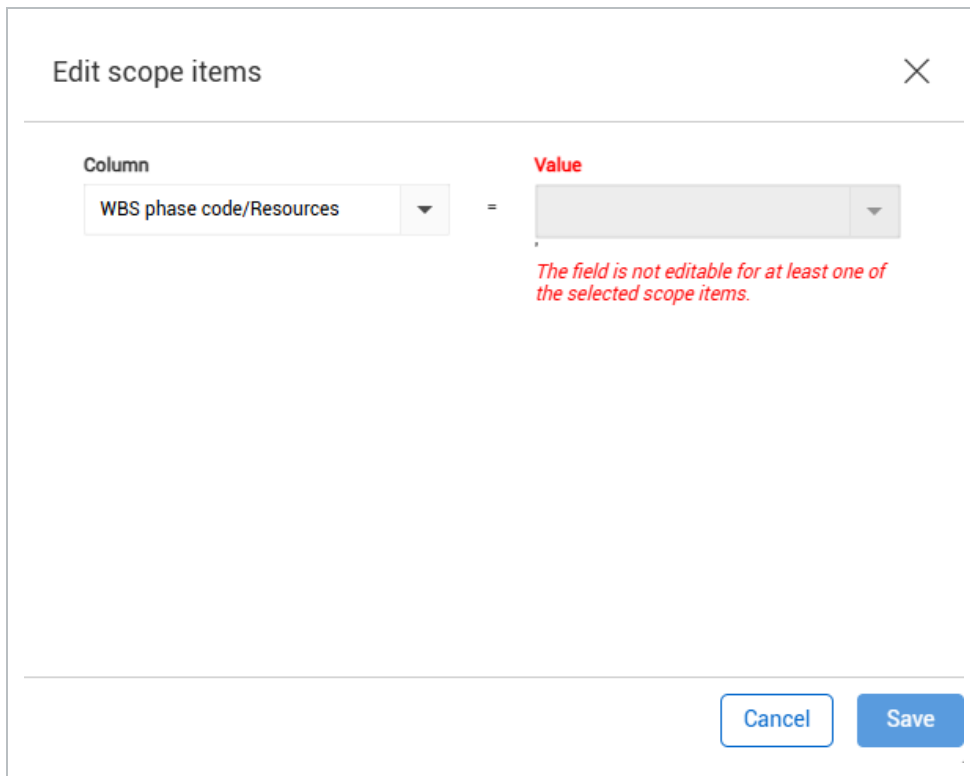

The dialog box is titled "Edit scope items" with a close button (X) in the top right corner. It contains a "Column" dropdown menu with "WBS phase code/Resources" selected, followed by an equals sign and a "Value" dropdown menu. A red error message is displayed below the "Value" dropdown: "The field is not editable for at least one of the selected scope items." At the bottom right, there are "Cancel" and "Save" buttons.

Click **Save** to apply your changes.

3.6 UPDATE SCOPE ITEM QUANTITIES

You can update a scope item quantity to adjust the claiming on any previously claimed steps to reflect the new scope item quantity. You can update quantities manually or by importing them. You must have the permission Edit scope items.

3.6.1 Update scope item quantities with no claiming

The Update scope item qty dialog box guides you through the process when you update the scope item quantity for an item that has no claiming.

In the Update scope item qty dialog box, you must select a Cause code and optionally enter a note as to why the scope item quantity is being updated.

×

Update scope item qty

Please select a cause code and optional note as to why the scope item qty is being updated.

Cause code

Prime Contract Change

Note

☐ Associate to change issue

Issue ID

Issue name

Cancel

Update

InEight Change integration

When you integrate with Change, you have the option to select the **Associate to change issue** check box to associate the quantity change to an issue in Change. You must select an issue from the grid to update the scope item.

3.6.2 Update scope item quantities with claiming

When you edit a scope item that has claiming and update the claimed quantities, the Update scope item qty wizard guides you through adjusting the claiming.

Update scope item qty

1

2

3

Select steps

Assign issue

Review steps

This action will update the claimed qty on each of the previously claimed steps for this scope item. An additional claim will be made on each step to capture the qty delta.

For partial claiming steps the "New claim qty" will be editable for further claiming adjustments. If the partial claiming step was previously complete, then the New claim qty will be defaulted to the New scope item qty amount. If the partial claiming step was not previously complete, then the New claim qty will be defaulted to the Claimed to date amount. The "New claim qty %" reflects the percentage of the step that will be complete based on qty specified in the "New claim qty" field.

☒ Last claim date

☐ Manual claim date

Claim date

*Cause code

Note

Client Request

Step

Step name

Partial claimin

New scope item q

Claimed to dat

Claimed to date

New claim qty

New claim qty %

Claim qty deltr

Claim date

Actual Team

Claimed by

1

Work Complete - 100%

☒

80.00

2.00

5.00%

2.00

2.50%

0.00

03/17/2022

Andrew Gr...

Count: 1

☐ Associate to change issue

Cancel

Next

The Update scope item qty wizard shows a grid of all steps with claiming history. The earned value is automatically adjusted to the new quantity value for complete steps. You can export all claimed steps for additional review by clicking the **Export** icon in the upper right of the grid.

InEight Change integration

When you integrate with Change and update the scope item quantity, you have the option to select the **Associate to change issue** check box to associate the quantity change to an issue in Change. In Assign issue (step 2), select an issue from the grid.

Update scope item qty

1

2

3

Select steps

Assign issue

Review steps

Associate to Change issue

	Issue ID	Issue name
☒	19	One-Issue
☐	18	Design-issue
☐	17	q2
☐	16	q2
☐	15	a5

Cancel

Back

Next

After the Update scope item qty wizard is completed, the issue is associated to the remaining steps of the scope item.

3.6 Step by Step 1 – Updating scope item quantity

- 1. Select the check box to the left of one scope item and then click the **Edit scope item** icon in the upper left. The Edit scope item slide-out panel opens.
- 2. Change the value in the Scope item qty field, and then click **Save** or **Save and Close**. The Update scope item qty wizard dialog box opens.

Update scope item qty

1

2

3

Select steps

Assign issue

Review steps

This action will update the claimed qty on each of the previously claimed steps for this scope item. An additional claim will be made on each step to capture the qty delta.

For partial claiming steps the "New claim qty" will be editable for further claiming adjustments. If the partial claiming step was previously complete, then the New claim qty will be defaulted to the New scope item qty amount. If the partial claiming step was not previously complete, then the New claim qty will be defaulted to the Claimed to date amount. The "New claim qty %" reflects the percentage of the step that will be complete based on qty specified in the "New claim qty" field.

☒ Last claim date

☐ Manual claim date

Claim date

*Cause code

Note

Client Request

Step	Step name	Partial claimin	New scope item q	Claimed to dat	Claimed to date %	New claim qty	New claim qty %	Claim qty deltz	Claim date	Actual Team	Claimed by
1	Work Complete - 100%	☒	80.00	2.00	5.00%	2.00	2.50%	0.00	03/17/2022		Andrew Gr...

Count: 1

☐ Associate to change issue

Cancel

Next

3. Select **Last claim date** or **Manual claim date**.

The Last claim date option lets you attribute the updated claims to the date the last claims were made on each step, reflecting more accurately in your reporting. Manual claim date is selected to today's date by default. The claim date selected is reflected for all steps.

4. Select a cause code from the **Cause code** drop-down list, and then optionally add a note.

5. Edit the **New claim qty**, **New claim qty percentage**, or **Actual Team** when applicable.

When integrated with InEight Change, you can select the **Associate to change issue** check box to associate the quantity change to a Change issue.

6. Click **Next**.

When associated to a change issue, select the Change issue in **Assign issue** (step 2).

7. Review the changes (step 3), and then click **Update**.

Administrators can configure cause codes at the organization level. For more information, see [Cause codes \(Engineering\)](#).


3.6.3 Update scope item quantities by import

When you update the Scope item qty field of multiple scope items through the import process after claims have been made, the Update all scope item qty dialog box guides you through adjusting the claiming on any previously claimed steps to reflect the new scope item quantities.


The Update all scope item qty dialog box shows grids of all selected scope items and steps with claiming history. You can export all scope items and claimed steps for additional review by clicking the **Export** icon in the upper right of the grid.

3.6 Step by Step 2 – Updating scope item quantity by import

1. Import a file with changes to the quantities for more than one scope item. The import process results in an error.
2. In Import history > **Scope item error resolution**, click the **Update all scope item qty** icon at the top of the grid. The Update all scope item qty dialog box opens.



3. Select the scope items whose claiming you want to adjust.

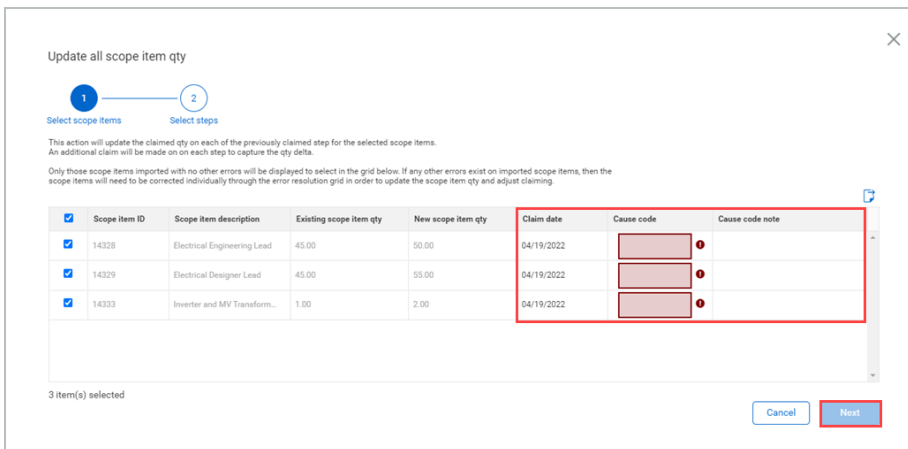

4. Select a cause code. Optionally, add a note.
5. Optionally, edit the Claim date. By default, it is set to today's date. This claim date is reflected for all steps.

6. Click **Next**. The Select steps page opens.

Update all scope item qty

1

2

Select scope itemsSelect steps

This action will update the claimed qty on each of the previously claimed step for the selected scope items. An additional claim will be made on on each step to capture the qty delta.

For partial claiming steps the "New claim qty" will be editable for further claiming adjustments. If the partial claiming step was previously complete, then the New claim qty will be defaulted to the New scope item qty amount. If the partial claiming step was not previously complete, then the New claim qty will be defaulted to the Claimed to date amount. The "New claim qty %" reflects the percentage of the step that will be complete based on qty specified in the "New claim qty" field.

Scope item ID	Scope item d...	Step	Step name	Partial claiming	New scope...	Claimed to date	Claimed to date %	New claim qty	New claim qty %	Claim qty delta	Actual Team	Claimed by
14328	Electrical En...	1	FTE Week	☒	50.00	15.16	33.70%	15.17	30.33%	0.00		
14329	Electrical De...	1	FTE Week	☒	55.00	15.16	33.70%	15.17	27.58%	0.00		
14333	Inverter and ...	1	Start Activity	☐	2.00	1.00	100.00%	2.00	100.00%	1.00		
14333	Inverter and ...	2	Generate Deliv...	☐	2.00	1.00	100.00%	2.00	100.00%	1.00		
14333	Inverter and ...	3	Generate Deliv...	☒	2.00	1.00	100.00%	2.00	100.00%	1.00		
14333	Inverter and ...	4	Check for IFR	☐	2.00	1.00	100.00%	2.00	100.00%	1.00		

Count: 7

Cancel

Back

Update

7. Optionally, edit the Actual Team and Claimed by fields in the grid. By default, these fields are set to the team and user specified on the last claim.

8. Review the changes, and then click **Update**.

3.6.4 Scope item quantity history

You can view previous scope item quantity changes in the Scope Items page by hovering over the **Information** icon in the Scope item qty column. Click **More details** to view the Scope item quantity history in the **Audit Log** tab.

SCOPE ITEMS

AUDIT LOG

View: Unsaved (Default)

Actions	ID	Description	Lead discipline	Scope item qty	Scope item UoM	OB qty	Deliverable qty
	261661	P&ID_104			Each	1.00	
	261660	P&ID_103			Each	1.00	
	261659	P&ID_102			Each	1.00	
	261658	P&ID_101			Each	1.00	
	261657	P&ID_100			Each	1.00	
	261656	P&ID_99			Each	1.00	
	261655	P&ID_98			Each	1.00	
	261654	P&ID_97	0.00 Mechanical	1.00	Each	1.00	
	261653	P&ID_96	0.00 Mechanical	1.00	Each	1.00	
Subtotals Count: 296							


Scope item qty changes (2 total)

More details

Scope item qty	Cause code	Changed by	Changed date
2.00	Client Request plv	Vijaya LakshmiDa...	05/26/2025 06:03:45 AM
1.00	*	Jakob Sjuts1	07/30/2025 01:58:30 PM

3.7 SCOPE ITEM RESOURCES

On the Add and Edit scope item dialog box, the Resources section lists the resource types associated to steps in the claiming scheme assigned to the scope item.

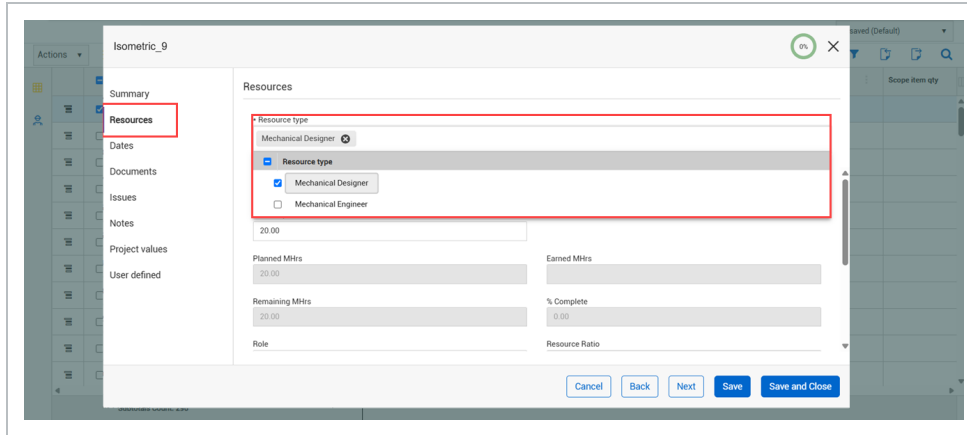

You can associate multiple resources to a scope item. Click in the **Resource type** field, and then select resource types from the list. When multiple resources are associated, you can view a summary of the selected resources. You can view a summary of resource items such as man hours, resource ratio, and percent complete of the selected resources.

Selecting a single resource continues to show information specific to that individual resource.

The following columns are automatically populated based on the selected claiming scheme:

- % Complete – Percent claimed by the resource type on the scope item.
- WBS % Claim Ratio – Sum of % Claim across claiming steps with the associated WBS.
- CE Mhrs/Unit – CE unit rate from Control of the associated WBS. See [Considerations](#) for more information.
- Scope item qty – Automatically populated from the Summary section.
- Scope item Mhrs – (CE Mhrs/Unit) × Scope item qty.

The following columns can be assigned for each resource type:

- WBS
- Account code
- Design element - See [Design elements](#) for more information.
- Role - Only roles configured in the Role assignment dialog box are available. See [Role assignment](#) for more information.

- Planned team - If roles are enabled, this field is automatically populated based on role assignment. If roles are disabled, you can assign any team according to resource project settings.
- Assigned user - If roles are enabled, this field is automatically populated based on role assignment. If roles are disabled, you can assign any user according to resource project settings.
- CE Mhrs/Unit – See [Considerations](#) for more information.

These assignments are inherited by claiming steps with the associated resource type in the claiming scheme.

3.7.1 Considerations

- If account code sets are enabled for the project, only account codes from the assigned account code set are available to assign to a resource type on the scope item. The design element is automatically populated based on the account code assigned. The account code UoM must match the Scope item UoM in the Summary section.
- When you assign a WBS phase code, the account code is automatically populated with the account code associated with the WBS in InEight Control. If an account code has already been assigned to the scope item's resource type, then the system checks if the account code matches Control. If the account code does not match, a warning message is shown, and the account code assignment is overridden to match Control.
- You cannot edit the WBS phase code if percent complete is above zero. If you claim up and then back down to zero, you can edit the WBS phase code.
- The CE Mhrs/Unit column can be manually edited when a WBS phase code has not been assigned. After you assign a WBS phase code, CE Mhrs/Unit is inherited from the WBS phase code.
- After the CE Mhrs/Unit column is filled, the Scope item Mhrs is automatically calculated.
- When you assign a role to a scope item, the role, planned team, and assigned user are inherited by the claiming steps. You can still update the role on individual steps if the step has not been claimed.

3.8 SCOPE ITEM CLAIMING

3.8.1 Summary

You can claim earned quantity against a scope item directly on the Scope items page. Claiming is done in the Claiming tab of the dialog box that shows for each scope item in the grid.

3.8.2 Considerations

- To claim, you must have the permission Edit claiming.
- To claim against a scope item, a WBS phase code must be assigned to all resource types associated with the scope item.
- If any compliance issues exist on a scope item, you cannot claim against it.
- For partial claiming using the Claim qty field, you can enter any quantity less than or equal to the scope item quantity. If Claim qty equals Scope item qty, the Complete check box is automatically selected.
- If you enter a partial quantity, and then later claim additional quantity in the same step, you must enter the total amount up to that point, not an incremental amount. For example, if a step is partially claimed for 10, and you want the current claimed quantity to be 100, you must enter 100, not 90.
- You can enter a value in the Claim qty % column if partial claiming is enabled. After you enter the percentage value, the Claim qty field is automatically filled with the corresponding quantity value.
- Claiming history can be seen in the History tab of the scope item slide-out panel and in the Claiming history tab of the Audit log.

3.8.3 Claim on a scope item

You can claim earned quantity against scope items directly from the Scope items page.

3.8 Step by Step 1 – Claim a step on a scope item

1. On the Scope items page, click the **Claiming** icon to the left of the scope item. A dialog box opens to the Claiming tab.

The screenshot shows the 'SCOPE ITEMS' page with a table of items. Item 261442, 'Foundations_6', is selected. A red box highlights the 'Claiming' icon (a document with a checkmark) to the left of the item. A red arrow points from this icon to the 'CLAIMING' tab in the dialog box that opens. The dialog box has a 'Complete' column with a checked checkbox for Step 1. The 'Date' field is populated with '08/27/2026' and the 'Claimed by' field with 'Julio Salgado'. The 'Claim qty' is 1.00 and 'Claim qty %' is 100.00. The 'Actual Team' is 'Structural De...'. The 'Save and Close' button is highlighted in blue.

Step	Complete	Step name	% Claim	Partial cl.	Claim qty	Claim qty %	Undo claim	Date	Milestone co.	Issue	Resource type	Actual Team	Claimed by
1	☒	Document created	0.00%	☐	1.00	100.00		08/27/2026			Structural De...		Julio Salgado
2	☐	Step - 2	39.00%	☐							Structural De...		
3	☐	Step - 3	39.00%	☐							Structural De...		
4	☐	Issue for Review	0.00%	☐						Issue for R...	Structural De...		
5	☐	Step - 5	0.00%	☐							Structural De...		
6	☐	Step - 6	10.00%	☐							Structural De...		
7	☐	Step - 7	10.00%	☐							Structural De...		
8	☐	Issue for Construction	2.00%	☐						Issue for C...	Structural De...		
9	☐	Upview	0.00%	☐						Upview	Structural De...		

% Complete: 0.00%

Cancel Save Save and Close

2. Select the check box in the Complete column for the step.
3. You can edit the Date and Claimed by fields. By default, these fields are automatically populated with today's date and the user who selected the check box.

You cannot select a future date.

4. You can enter a partial quantity in the Claim qty column.

Partial claiming must be enabled for the associated claiming scheme step to use this feature.

5. Click **Save** or **Save and Close**. The claim is locked and the Date, Actual team, and Claimed by fields cannot be edited.


To make changes to a claim, the step must be unclaimed, and then reclaimed.

3.8.4 Import claiming in bulk

Importing lets you claim against scope items in bulk. All imported claiming that passes validations is added to the Scope items page. The imported claims that fail validations are added to the Error resolution page. All imports are shown in Audit log > **Import history**. You must have the permission Import claiming. You can import all claiming based on either quantity or percentage. See the procedure below for more information.

3.8 Step by Step 2 – Importing claiming

1. To import claiming, on the Scope items page, click the **Export** icon, and then select **Export claiming**. A Microsoft Excel spreadsheet is downloaded.

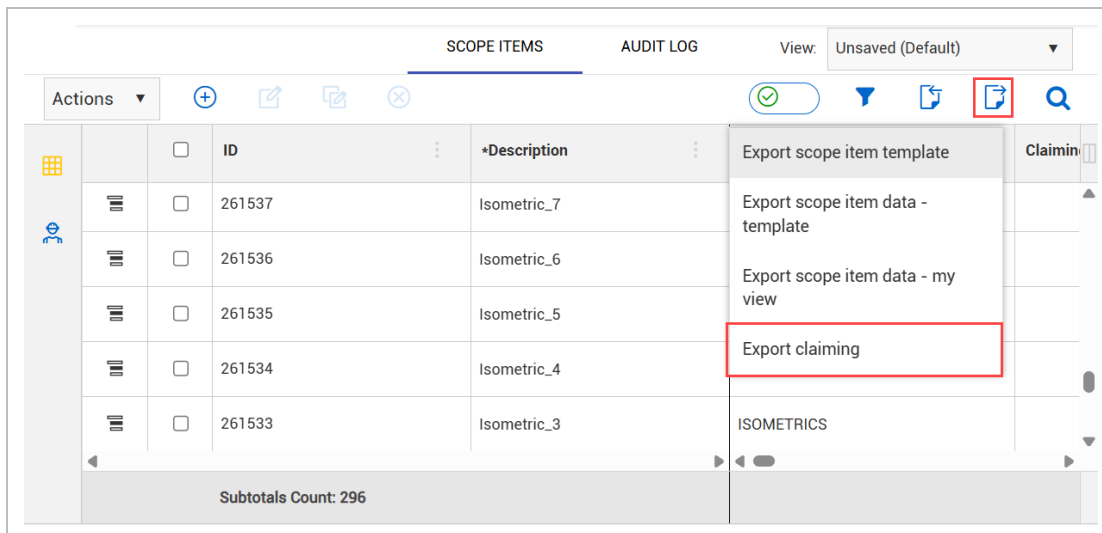

2. Fill in values in either the Claim qty % or Claim qty columns in the spreadsheet, and then save it.
3. On the Scope items page, click the **Import** icon, and then select **Import claiming**.

SCOPE ITEMS			AUDIT LOG		View: Unsaved (Default)
Actions					
	☐	ID	*Description	Import scope items	Claiming
	☐	261537	Isometric_7	Import claiming	
	☐	261536	Isometric_6	ISOMETRICS	
	☐	261535	Isometric_5	ISOMETRICS	
	☐	261534	Isometric_4	ISOMETRICS	
	☐	261533	Isometric_3	ISOMETRICS	
Subtotals Count: 296					

- Click **Browse**, and then select the saved spreadsheet.
- Select either **Claim by quantity** to import only values in the Claim qty column or **Claim by percentage** to import only values in the Claim qty % column.
- Click **Import**. The import status is shown, and then the Import history page opens. If there are any errors, they are shown in the table.
- If there are issues, click **Completed with issues** in the Status column to open Claiming error resolution, and then resolve issues before saving.

3.8.5 Undo claiming


Undo claim wizard lets you undo claims for a step or scope item, which reduces the claiming back to 0% complete. This reverses all claims for the specific step or scope item to the day the original claim occurred. You must have the permission Edit claiming.

You can undo claiming for a step or an entire scope item. When a step or scope item has not been claimed and is at 0%, the undo claiming icons do not show. All original claims and claim reversal are captured for audit purposes.

3.8 Step by Step 3 – Undo claim for a step

- 1. On the Scope items page, click the **Undo claim** icon.

A dialog box shows all claims for the step.

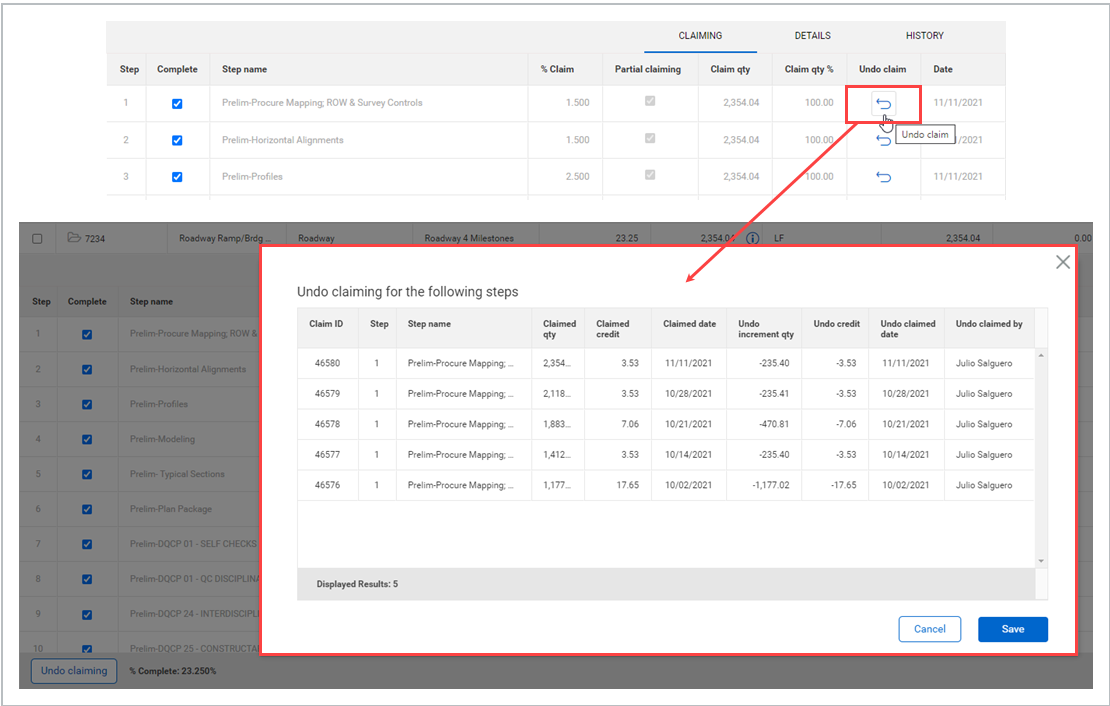


- 2. Click **Save** to undo claiming for the steps shown.

3.8 Step by Step 4 – Undo claim for a scope item

- 1. On the Claiming tab, click the **Undo** claiming button at the bottom left.

A dialog box shows claims for all the steps in the scope item.

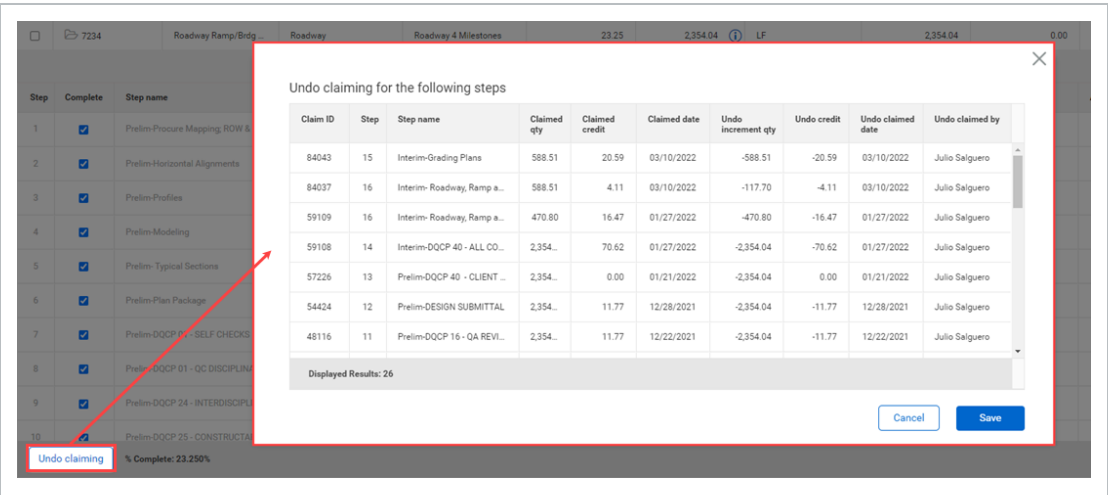


2. Click **Save** to undo claiming for the all the steps in the scope item.

When InEight Control integration is enabled, the undo claims are sent to the assigned WBS in Control.

3.9 PROJECT VALUES IN SCOPE ITEMS

Project values are standardized data configured in InEight Platform . Project values can be shared and used in Design. You can configure which project values to use for projects in the Settings, and then assign project values such as Area, Segment, System, Subsystem, Work classification, and others depending on your business requirements.


To assign project values, go to the Project values section of the Add or Edit scope item dialog box.

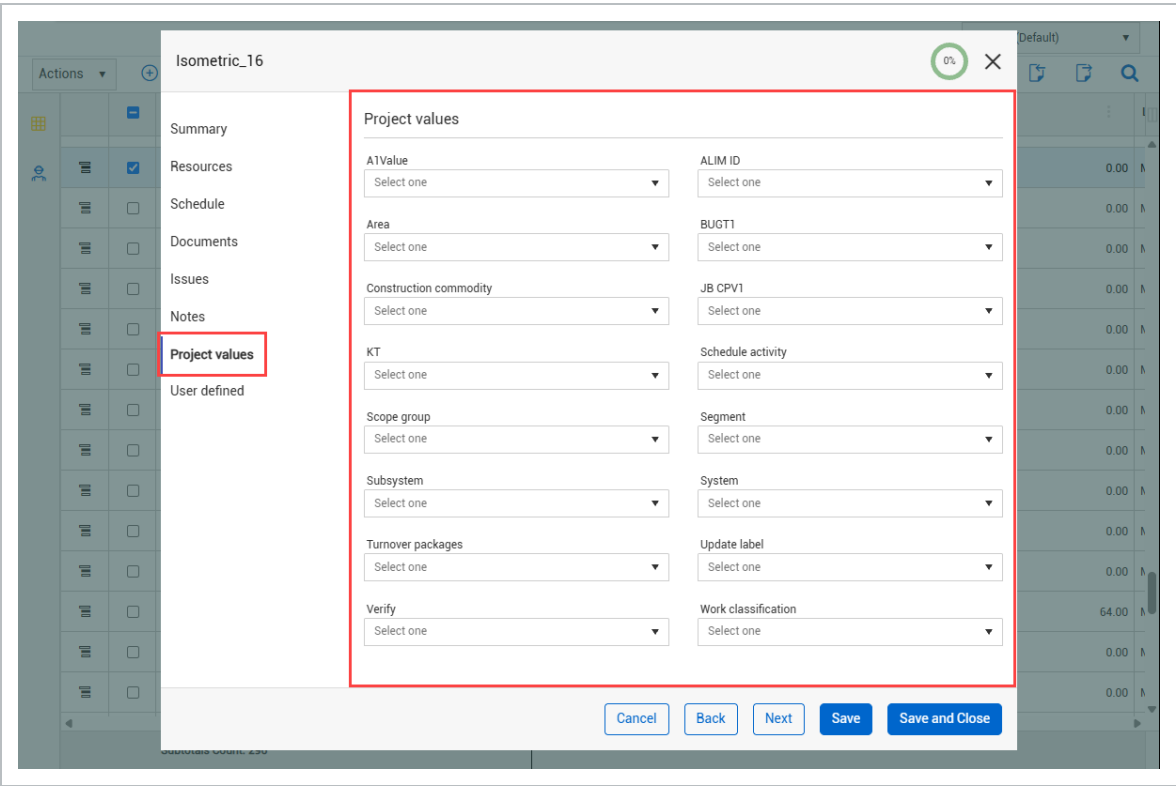

Select from the project value field drop-down lists, and then click **Save**.

3.9.1 Project value status

When the status of a project value is changed to *Unavailable* in Platform, a yellow caution icon shows in the project value field for assigned values. The project value field in the scope item’s dialog box is highlighted red and shows *Project value is unavailable* below the value field.

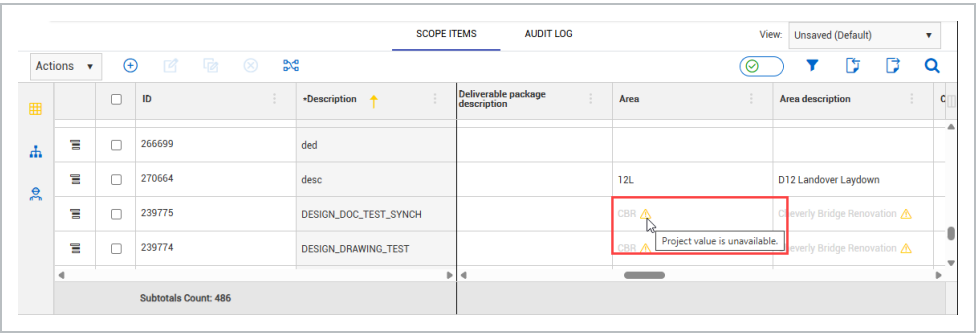

You can update the scope item to an available project value in the scope item's dialog box. When you select to update the project value in the scope item, only project values marked as available in Platform show in the drop-down list.

To save the scope item, you must select an available project value.

Update a project value

- 1. Select the scope item, and then click the **Edit scope item** icon.
- 2. Select an available project value from the project value drop-down list, and then click **Save**.

DESIGN_DOC_TEST_SYNCH

0%

×

Summary

Resources

Schedule

Documents

Issues

Notes

Project values

1

User defined

Project values

A1TESTProjectValue1

Select one

Area

CBR

Project value is unavailable.

BUGT1

Select one

D1AutoPV1

Select one

JB CPV1

Select one

Model

Select one

Scope group

ALIM ID

Select one

B1AutoPV1

Select one

Construction commodity

Select one

HVT1

Select one

KT

Select one

Schedule activity

Select one

Segment

Cancel

Back

Next

Save

Save and Close

3.10 COMPLIANCE ISSUES

Compliance yellow caution icons show on scope items where claiming is disabled due to missing data or cost item data discrepancies with the scope item. The caution icon shows in the ID column and the Compliance column on the Scope Items page.

SCOPE ITEMS

AUDIT LOG

View: Unsaved (Default)

Actions

		ID	Description	Scope item UoM	Compliance	OB qty
		279698	2 steps 1 resource	Each	True	
		279697	Claiming is disabled. Please resolve issues on the scope item to enable claiming.		True	
		279696	2 steps 2 resource 2 costite...	Each	True	
		279694	testing q23	Each	True	
		279692	test211211	Each	True	
		279691	PL	Each	True	
Subtotals Count: 486						

The Compliance column is not part of the default view but can be added to the page as an available column through the column chooser.

To see which fields are causing a compliance issue, select the scope item with the issue, and then click the **Edit scope item** icon. In the Edit scope dialog box, fields with issues show caution icons. When you hover over a caution icon, a message is shown with issue details and how to resolve the issue. You must resolve all compliance issues to enable claiming on a scope item.

2 steps 1 resource

Summary

Resources

Schedule

Documents

Issues

Notes

Project values

User defined

Resources

WBS UoM of MWk does not align with the scope item UoM. Please resolve to enable claiming

WBS phase code

4956 - WSX1

UoM

Each

CE Mhrs/Unit

10.00

FC Remaining Mhrs/Unit

1.00

Planned Mhrs

100.00

Earned Mhrs

Cancel

Back

Next

Save

Save and Close

The following list details of compliance issues and how to resolve them:

- Claiming is disabled when a scope item qty value is 0.00. Add quantity to the scope item to enable claiming.
- WBS phase code assignment is missing on the resource type. Assign a WBS phase code to the resource type to enable claiming.
- WBS UoM does not align with the scope item UoM. Update the scope item UoM to match the WBS UoM or assign a different WBS with an associated UoM that matches the scope item UoM.

The following compliance issues show only when ACS is enabled on the project:

- Account code UoM does not match the scope item UoM. Update the scope item UoM to match the account code UoM or assign a different account code with an associated UoM that matches the scope item UoM.
- Account code UoM does not match the scope item UoM. Update the scope item UoM to match the account code UoM or assign a different account code with an associated UoM that matches the scope item UoM. This is applicable only if account code sets are enabled for the project.

3.11 AUDIT LOG

The Audit log gives you visibility to scope item changes, claiming history, import history, and scope item quantity history on a project.

The Scope item page shows changes made to any attribute field on a scope item, scope item resource type, or step details. This log also records the creation and deletion of scope items. For each change, the values before and after, the user who made the change, and the time and date the change was made are also shown.

SCOPE ITEMS											
AUDIT LOG											
Scope item	Audit type	Scope item ID	Scope item description	Resource type	Step	Step name	Attribute	Value before	Value after	Changed by	Changed date
Claiming history											
Import history											
Scope item quantity history	Scope item	264967	AQ6	*	*	*	Cause code		Prime Contrac...	Julio	08/27/2026 09:0...
	Scope item	264967	AQ6	*	*	*	Scope item qty	0.0000000000	100.00000000...	Julio	08/27/2026 09:0...
	Resources	264967	AQ6	Electrical Engineer	*	*	Design element		INDIRECTS (M...	Julio	08/27/2026 09:0...
	Resources	264967	AQ6	Electrical Engineer	*	*	Account code		88.01.22	Julio	08/27/2026 09:0...

The Claiming history page shows all the claims made on scope items in the project. On this page, you can resend individual claims to InEight Control. When a claim is saved in the Engineering module, the claiming record is immediately sent to Control to consume the claim quantity on the associated WBS. If the claim does not make it to Control successfully, this feature can be used to resend the claim. To

resend claims to Control, select one or more claim records in the grid, and then click the **Resend selected claims to Control** icon in the upper left.

SCOPE ITEMS									
AUDIT LOG									
									
Scope item	☒	Claim ID	Scope item ID	Step	Step name	WBS phase code	Resource type	Claim qty	Claim qty %
Claiming history									
Import history	☒	1097858	273959	41	IFC Approval	4958	ENGDESIGN	2.00000000000	100.000000000
Scope item quantity history	☐	1097857	273959	40	IFC DQCP 40 All Comme...	4958	ENGDESIGN	2.00000000000	100.000000000
	☐	1097856	273959	39	IFC DQCP 40 Client/Thir...	4958	ENGDESIGN	2.00000000000	100.000000000
Subtotals									

The Import history page shows all the imports initiated on the project. If a file has any errors when it is imported, then the Failed record count column shows the number of records in error and the Status column has a value of Completed with errors, in a link.

To view and correct errors, click **Completed with errors** to open the error resolution page. For claiming schemes and scope items, click either the claiming scheme or scope item ID to view and resolve issues before saving. For claiming, resolve the issues in the grid before saving.

SCOPE ITEMS									
AUDIT LOG									
Scope item	Import type	File name	Status	Total record count	Successful record count	Failed record count	Fixed record count	Deleted record count	
Claiming history									
Import history		Scopeltem	Export Scop...	0	0	0	0	0	
Scope item quantity history		Engineering...	Export Engin...	1	1	0	0	0	
		DeliverableP...	Export Deliv...	3	3	0	0	0	
		Scopeltem	Export Scop...	1	0	1	0	0	
		Scopeltem	Export Scop...	1	0	1	0	0	

To view and correct errors, click **Completed with errors** to open the error resolution page. For claiming schemes and scope items, click the claiming scheme or scope item ID to view and resolve issues before saving. For claiming, resolve the issues in the grid before saving.

Import history

Claiming scheme error resolution

Claiming scheme ID

0123 EW BSTR

Resolve claiming scheme

• ID

0123 EW BSTR

• Description

Bridge Structures - Early Works

• Lead Discipline

Structural

STEPS

•Step	•Step name	•% Claim	Partial claim	•Resource type	•Resource Discipline	Milestone Completion	•Schedule group	•Activity ID format
12	Enter step name	Enter % ci	☐	Select resource...		Select milestone	Select sche...	Select acti...
☐ 1	Final Design Development ...	S 1	☒	Structural Engineer	Structural		RD	AccountCode/...
☐ 2	Final Design Development ...	S 1	☐	Structural Engineer	Structural		RD	AccountCode/...
☐ 3	Final Design Development ...	S 1	☒	Structural Engineer	Structural		RD	AccountCode/...
☐ 4	Final Design Development ...	S 1	☐	Structural Engineer	Structural		RD	AccountCode/...
☐ 5	Final Design Development ...	S 1	☒	Structural Engineer	Structural		RD	AccountCode/...
☐ 6	Final Design Development ...	S 1	☐	Structural Engineer	Structural		RD	AccountCode/...
☐ 7	Final Design Development ...	S 1	☒	Structural Engineer	Structural		RD	AccountCode/...
Subtotal: 50.000%								

12 errors remaining

Cancel

Save

The Scope item quantity history page shows all scope item quantity updates on a project.

SCOPE ITEMS		AUDIT LOG							
Scope Item	Scope item ID	Scope item description	Scope item qty before	Scope item qty after	Cause code	Note	Changed by	Changed date	
Claiming history	261658	P&ID_101	1.000000000000	2.000000000000	Client Request pkv		Vijaya LakshmiDa-PTR	05/26/2026 06:03:45...	
Import history	262892	P&ID_127	0.000000000000	1.000000000000			Radhika Kondabala-PK	10/06/2025 07:57:23...	
Scope item quantity history	262893	P&ID_128	0.000000000000	1.000000000000			Radhika Kondabala-PK	10/06/2025 07:57:23...	
	261010	DRIP 121 - cond air	1.000000000000	11.000000000000			radhikab kondabala	10/16/2025 04:19:26	

3.12 VENDOR ACCESS TO SCOPE ITEMS

If you are using Design for engineering work, you could be collaborating with third party vendors, such as an Engineering firm, to design work on a project. As design work progresses, you might need vendors to participate in the review or development of the designs, and you can give them access to claim against the design steps they are working on.

In the Engineering module of Design, vendors can be given access to claim against the items they are participating in, known as engineering scope items.

To provide vendor access, all the following conditions must be met:

- In Platform:
 - The vendor must be assigned to a user.
 - The vendor must be assigned to the applicable project.
 - The vendor must be assigned to a team in Project Settings > Design > **Engineering**.
- In Design > **Engineering**:
 - The applicable scope items must be edited to assign the vendor team to the resources on the scope item.

After these conditions are met, the vendor can log into Design for the project they are assigned to. On the Scope items page of the Engineering module, the vendor can only view the scope items their team is assigned to.

For more information, see the following topics:


- [Teams](#)
- [Scope item resources](#)

3.13 ACTIONS

3.14 ACTIONS OVERVIEW

In the Scope items page, you can perform various actions on an engineering project. The list of items in the Actions menu is dependent on your configuration. You must have applicable permissions in Engineering.

The following image and table provide an overview of each action.

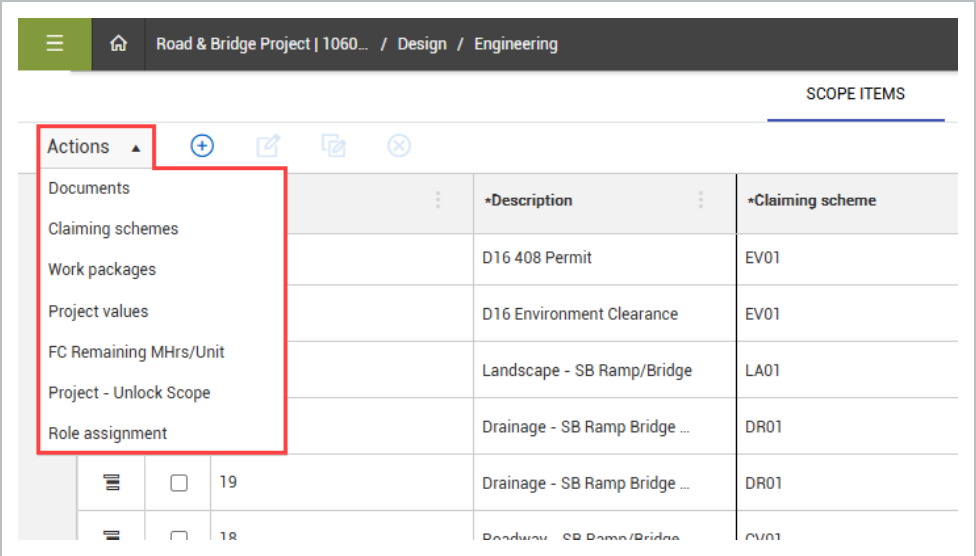


Action	Description
Documents	Manage the mapping and claiming of scope items with documents from InEight Document.
Claiming schemes	You can manage claiming schemes as the first step in setting up a project in the Engineering module. Claiming schemes are required to be configured prior to creating a scope item.
Work packages	Manage work packages in the Engineering or Deliverable package tabs. After a work package is created on a project, it will become available to assign on a Scope Item within the project.
Project values	Create project values for Segment, Construction commodity, System, Turnover packages, Subsystem, Work classification, Assigned disciplines, and Assigned commodities on a project. You can assign these to scope items.
Project - Lock or Unlock scope	When you initially lock scope on a project, a snapshot is taken of the original quantity for each existing scope item. Cause codes are required for any scope item quantity changes. When unlocked, the OB qty field is editable on all existing scope items. A warning will show when scope is unlocked that reads <i>Scope is unlocked</i> .
FC Remaining MHrs/Unit	You can get the current Forecast Remaining unit rate from Control for the WBS phase codes on the project and calculate the remaining

Action	Description
	forecasted man hours on the related scope items where the WBS is assigned. Control Integration must be enabled in project settings.
Role assignment	Manage role assignments in a project in the Current and Future Assignments tab and view its history in the User Assignment History tab.


3.15 DOCUMENTS

3.16 DOCUMENTS OVERVIEW

You can associate scope items and documents from InEight Document to support status and progress reporting on deliverables. Go to project > Engineering > Scope Items > **Actions**, and then click **Documents** to open the Documents page.

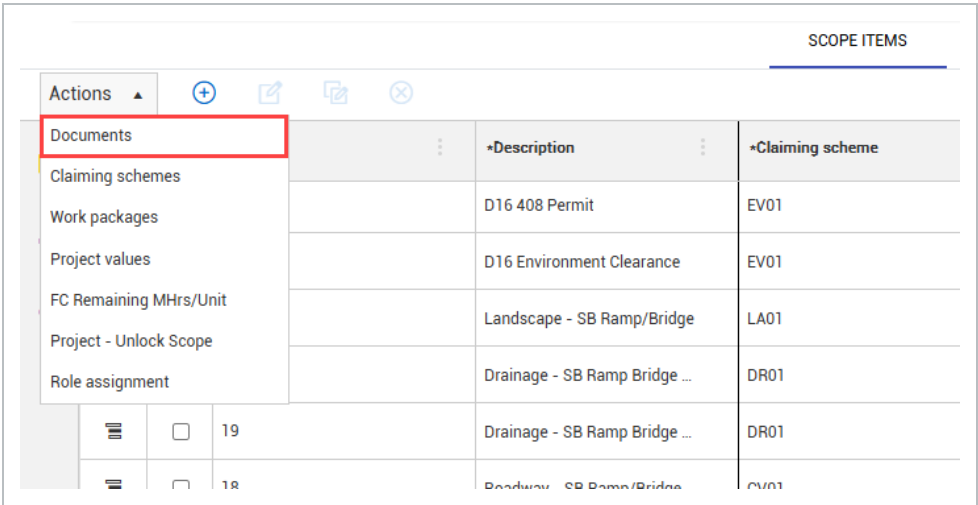

In the Associate documents page, you can view and manage the Claiming, Mapping, and Summary tabs.




- **Claiming tab** — You can progress earned value based on document status.
- **Mapping tab**— You can view and associate documents to scope items.
- **Summary tab**— You can view a document summary of hours, percent complete, and dates.

3.16.1 Column filters

You can use the column filter menus in the Claiming and Mappings tabs to better view and filter data. Click the **Filter** icon, and then select from the following:

- Sort Ascending
- Sort Descending
- Lock or Unlock
- Filter

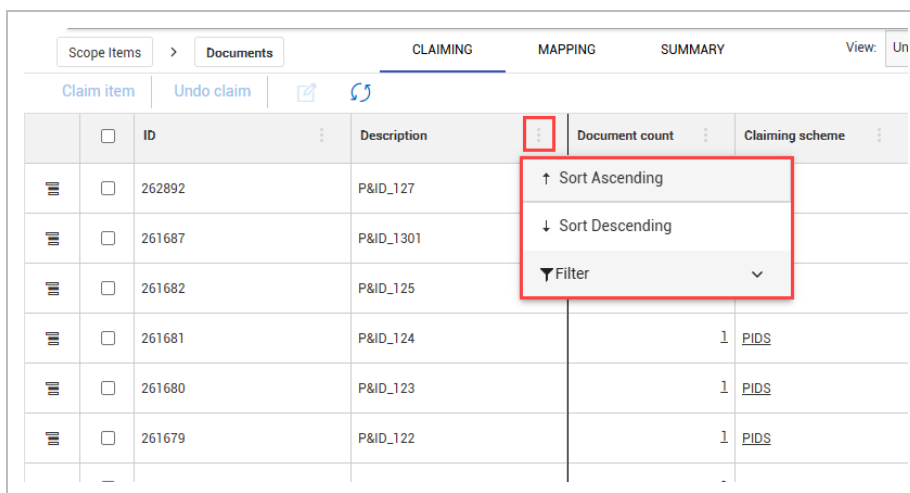

Scope Items	>	Documents	CLAIMING	MAPPING	SUMMARY	View: Un
Claim item	Undo claim					
	☐	ID	Description	Document count	Claiming scheme	
	☐	262892	P&ID_127			
	☐	261687	P&ID_1301			
	☐	261682	P&ID_125			
	☐	261681	P&ID_124	1	PIDS	
	☐	261680	P&ID_123	1	PIDS	
	☐	261679	P&ID_122	1	PIDS	
	☐	-		-		

3.16.2 Lock and unlock columns

You can lock columns in the Claiming and Mappings tabs to view key information when reviewing large amounts of data. You can lock one to multiple columns at one time. Locking columns allows you to scroll horizontally while keeping the column or columns locked in place on the left side of the page.

To lock a column in place, click the **Filter** icon next to a column name, and then select **Lock** from the drop-down menu. To unlock a locked column, select **Unlock** from the drop-down menu.

Scope Items > Documents

CLAIMING MAPPING SUMMARY

View: Unsaved (Default)

Claim item Undo claim

☐	ID	Description	Document count	Claiming scheme	Scope item claimed status	Document status
☐	262892	P&ID_127			Not Started	Not Started
☐	261687	P&ID_1301			Not Started	Not Started
☐	261682	P&ID_125			Not Started	Not Started
☐	261681	P&ID_124			Not Started	Not Started
☐	261680	P&ID_123	1	PIDS	Not Started	Not Started
☐	261679	P&ID_122	1	PIDS	Not Started	Not Started
☐	261678	P&ID_121	1	PIDS	Not Started	Not Started
☐	261677	P&ID_120	1	PIDS	Not Started	Not Started

Subtotals Count: 48

Selected Items: 0

3.16.3 Considerations

- To enable Document integration, you must first set up the project in InEight Platform > Suite Administration > **Application integrations**.
- To access the Associate documents feature you must select the *Enable Document integration* setting for your project in the Engineering **Documents** tab.
- To view the Claiming tab, you must select the *Enable Document claiming* setting for your project in the Engineering **Documents** tab.

3.17 CLAIMING

3.18 CLAIMING OVERVIEW

You can manage document claiming in the Claiming tab of the Documents page. Claiming allows the scope managed in Design to earn automated claiming based on the associated document’s status from the document repository in InEight Document. A new Document claiming permission has been added for Engineering to specifically control access to the Claim Item and Undo Claim Item actions. You must have the permission Document claiming to claim a document or undo a document claim.

To enable claiming, you must do the following:

- Set up the project in InEight Platform > Suite Administration > **Application integrations**.
- Set the **Enable Document integration** and **Enable Document claiming** toggles to *On* in the project's Settings > Engineering > **Documents** tab.

When the Enable Document claiming setting is selected, Design syncs the document statuses from the project in Document mapped in InEight Platform and the following occurs:

- A Document status column shows on the claiming scheme.
- A Claiming tab shows on the Documents page.
- Design compares the claimed document status on a scope item's claiming scheme to the associated document's status to systematically track and progress earned value.

The image and table below show an overview of the Claiming tab:

	Option	Description
1	Claim item	Opens the Ready to be claimed wizard to begin the claiming process.
2	Undo claim	Opens the Undo claiming wizard to begin the process to reverse claiming.
3	Edit scope item	Open the Edit scope item panel where you can edit scope item details.
4	Document sync	Sync claiming data with InEight Document.
5	Document count	Click the document count hyperlink to open a submenu to show the scope item's associated documents.
6	Claiming	Click the claiming scheme hyperlink to open the claiming scheme in a

	Option	Description
	scheme	new tab.
7	View	You can select saved and default views and save, rename, or delete views.
8	Search	Use to search data in the claiming register.
9	Column options	Opens the Column options dialog box to add and remove columns from your view.

3.18.1 Claiming tab columns

You can use the Column options icon at the top right of the scroll bar to customize the view of the Claiming tab. After customizing the view, you can save your view by clicking the **View** drop-down and then selecting the **Save view as** option.

The following are key columns in the Claiming tab:

- **Scope item status** — Shows the completed claimed status that correlates with the status set in Document.
- **Document status** — Shows the current set status from Document. The status may match the scope item status or the next status set in Document you can claim items to.

The Document status column syncs the statuses from Document and show in the Claiming tab and in the claiming scheme slide-out panel. This allows claiming scheme steps to be directly correlated to your business process workflow for document management.

A document status can only be associated to one step.

- **Claiming state** — There are four Design claiming states:
 - Pending review — The document status has progressed further than the scope item's claimed status and is eligible to have progress earned.
 - Pending undo review — The document status has regressed to a state before the scope item's claimed status and is eligible to have progress undone.
 - Idle — The document status matches the scope item's claimed status.

- **Error** — There is an error with the document statuses, the document to scope item association, or the scope item has a compliance issue preventing claiming from occurring.
- **Document count** — Shows the number of documents associated with the scope item. You can click the number link to open the Document tab within the scope item to view details of the associated documents.

3.18.2 Lock columns

You can lock columns to view key information when reviewing large amounts of data. You can lock one to multiple columns at one time. Locking columns allows you to scroll horizontally while keeping the column or columns locked in place on the left side of the page.

To lock a column in place, click the **Column Menu** icon next to a column, and then select **Lock** from the drop-down menu. To unlock a locked column, select **Unlock** from the drop-down menu.

3.18.3 Column filter menus

You can use the column filter menus to better view and filter data. Click the **Column Menu** icon, and then select from the following:

- Sort Ascending
- Sort Descending
- Lock or Unlock
- Filter

3.19 MANAGE CLAIMING

In InEight Document, statuses can be configured for a document. On claiming schemes in Design, these statuses are correlated with the progress of claiming steps associated with that status. When the set of claiming steps associated with the status are completed, the scope item automatically progresses to the mapped step configured in Document. You must have the Document claiming permission in Engineering to claim a document or reverse a document claim.

3.19.1 Claim items

On the Claiming tab, you can claim items by selecting scope items that have a claiming state of *Pending review*.

Click **Claim item** to open the Ready to be claimed wizard to begin the claiming process for the scope item claiming steps.

In step 1 (Claim items) of the Ready to be claimed dialog box, you can view the selected scope items for claiming.

The screenshot shows a dialog box titled "Ready to be claimed" with a close button (X) in the top right corner. Below the title is a progress indicator with two steps: "1 Claim items" (active) and "2 Claimed steps". Below the progress indicator, it says "Items selected below will be marked for claiming". There are two radio buttons: "Status change date" (selected) and "Manual claim date". Below this is a table with the following columns: "Scope item ID", "Scope item description", "Scope item claim status", "Document claim status", and "Claiming state". The table has a header row with filters (dropdown arrows) and a data row with one item selected (checkbox checked). Below the table is a scrollbar and a summary bar showing "Items : 1" and "Selected items : 1". At the bottom right are four buttons: "Cancel", "Back", "Next", and "Save".

	Scope item ID	Scope item description	Scope item claim status	Document claim status	Claiming state
			All	All	All
☒	261687	P&ID_130		Issued for Review	Pending review

Items : 1 Selected items : 1

Cancel Back Next Save

After confirming the scope item selection, click **Next** to go to step 2 (Claiming steps).

In step 2 (Claiming steps), you can view the steps for the scope item to be claimed. Click **Save** to complete claiming.

Ready to be claimed

1

2

Claim items

Claimed steps

Steps for the selected scope items to be claimed are shown.

Scope item ID	Scope item description	Step	Complete	Step name	% Claim
			All		
261687	P&ID_130	35	☒	Step - 35	
261687	P&ID_130	36	☒	Step - 36	
261687	P&ID_130	37	☒	Step - 37	
261687	P&ID_130	38	☒	Step - 38	
261687	P&ID_130	39	☒	Step - 39	
261687	P&ID_130	40	☒	Step - 40	
261687	P&ID_130	41	☒	Issue for Review	

Items : 41

Cancel

Back

Next

Save

After claiming, the scope item claimed status progresses to the status set in Document and the Claiming state now shows *Idle*.

ScopeItems > Documents

CLAIMING MAPPING SUMMARY

View: Default

Claim item


Undo claim

	ID	Description	Document count	Claiming scheme	Scope item claimed status	Document status	Claiming state	% Complete	Scope id
☐									
☐	261687	P&ID_1301	1	PIDS	Issued for Review	Issued for Review	Idle	65.00	
☐	261686	P&ID_129	1	PIDS	Issued for Review	Issued for Review	Idle	65.00	
☐	261685	P&ID_128	1	PIDS	Not Started	Not Started	Idle	0.00	
☐	261684	P&ID_127	1	PIDS	Not Started	Not Started	Idle	0.00	
☐	261683	P&ID_126	1	PIDS	Not Started	Not Started	Idle	0.00	
☐	261682	P&ID_125	1	PIDS	Not Started	Not Started	Idle	0.00	
☐	261681	P&ID_124	1	PIDS	Not Started	Not Started	Idle	0.00	
☐	261680	P&ID_123	1	PIDS	Not Started	Not Started	Idle	0.00	
☐	261679	P&ID_122	1	PIDS	Not Started	Not Started	Idle	0.00	

Subtotals Count: 296 Selected items: 0

3.19.1.1 Sync to document

You can use the Sync to document option to sync data with Document.



To update or refresh Design and Document data, simply click the **Sync to document** icon to sync data with Document. After the sync completes, a **Document sync completed message** shows at the top of the page.

You must refresh the Design page for any updates to show.

3.19.2 Undo claiming

After you perform claiming, claiming is synced with Document, and the statuses are updated in both Design and Document. To undo claiming, you must initiate it in Document.

In Document, open the document, and then reverse the status to the previous one.

STAT1

DETAILLINKSCOMMENTSFILE VIEWERUSER ACCESSTRANSMITTAL HISTORY

document details

CancelSave

* Document No. ⓘ

ISOMETRIC_27

* Title

Isometric_27

Tags:

Select a tag...

Version

B.01

* Revision

B - Revision B

* Status

STAT1 - STAT1

Select one

IFI - Issued for Information

IFR - Issued for Review

IFT - Issued for Review

NEWDS - NEWDS

NS - Not Started

PD - Preliminary Design

STAT1 - STAT1

Date released

Received

mm-dd-yy

* Discipline

ADMIN - Administration

* Type

DRAWING - Drawing

From

Jakob Sjuts, INEIGHT

Review status

Un-Restrained

Date recorded

08-19-25

Sender company

Select one

Sender

Select one

Area

In Design, the Claiming state for the scope item changes to *Pending undo review*. Select the scope item, and then click the **Undo claim** button. The Undo claiming wizard opens.

In Claim items (step 1), the scope items are automatically selected. You can deselect scope items to exclude them from the process. Click **Next** to confirm selections.

Page 124 of 183

InEight Inc. | Release 26.7

Undo claiming

1

2

Claim items

Undo claiming

Items selected below will be marked to undo the claiming.

	Scope item ID	Scope item description	Scope item claim status	Document claim status	Claiming state
			All	All	All
☒	261557	Isometric_27	Issued For Construction	Issued for Review	Pending undo review

Items : 1Selected items : 1

Cancel

Back

Next

Save

In Undo claiming (step 2), the list of steps are shown for your review. Click **Save** to complete the process.

Undo claiming

1

2

Claim items

Undo claiming

Steps for undoing the claiming on selected scope items are shown below.

	Step	Step name	Undo increment qty	Undo credit	Undo date	Undo claimed by
	27	Issue for Construction	-1.00	-0.02	08/12/2025	Jakob Sjuts1
	26	Step - 26	-1.00	-0.27	08/12/2025	Jakob Sjuts1
	25	Step - 25	-1.00	-0.04	08/12/2025	Jakob Sjuts1
	24	Step - 24	-1.00	-0.01	08/12/2025	Jakob Sjuts1
	23	Step - 23	-1.00	-0.05	08/12/2025	Jakob Sjuts1
	22	Step - 22	-1.00	-0.27	08/12/2025	Jakob Sjuts1
	21	Step - 21	-1.00	-0.05	08/12/2025	Jakob Sjuts1
	20	Step - 20	-1.00	-0.07	08/12/2025	Jakob Sjuts1
	19	Step - 19	-1.00	-0.06	08/12/2025	Jakob Sjuts1
	18	Step - 18	-1.00	0.00	08/12/2025	Jakob Sjuts1

Cancel

Back


Next

Save

3.19.3 Navigate to claiming schemes

On the Claiming scheme column of the Documents > Claiming tab, click the claiming scheme link to open the claiming scheme dialog box in the Scope items > **Configure claiming schemes** page, in a new tab.

On the Edit claiming scheme dialog box, you can view the synced status and click in the **Document status** field to select from a drop-down list of available statuses synced from the mapped project in Document.

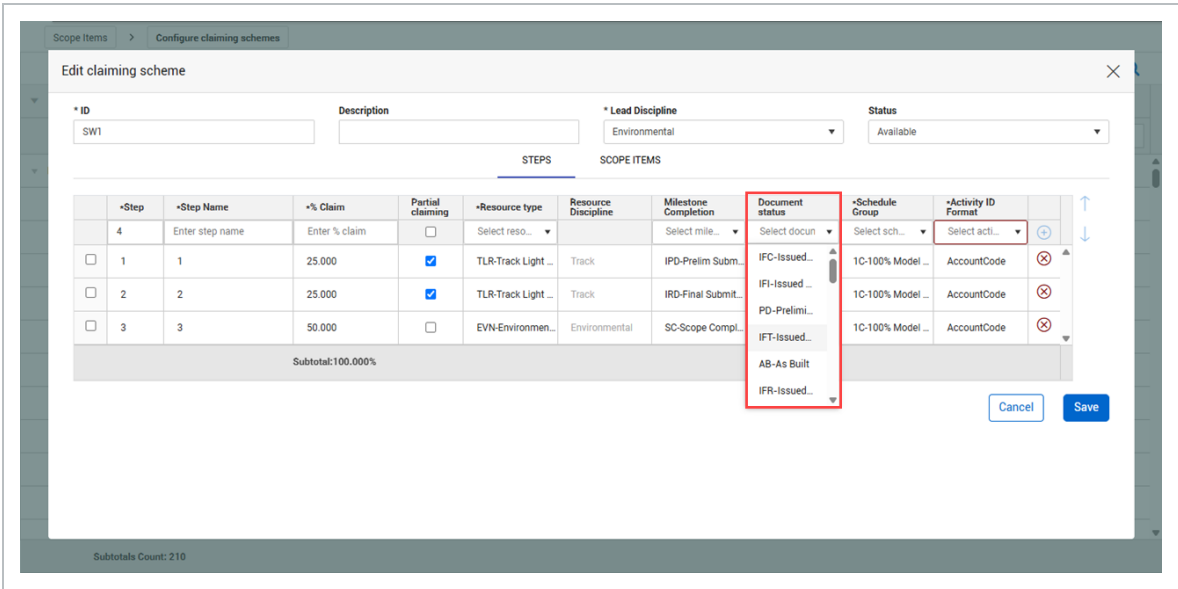


3.20 MANAGE SCOPE ITEMS IN CLAIMING

On the Documents Claiming tab, you can view and edit scope items. You can also view scope item claim details and document associations.

3.20.1 Edit scope items

To view and edit scope item details, select a scope item, and then click the **Edit scope item** icon.

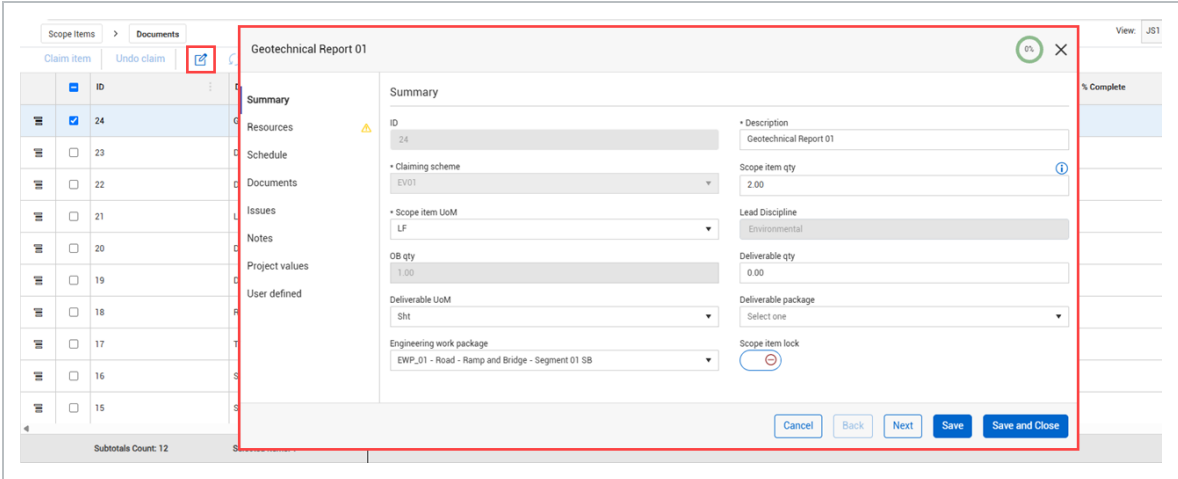

On the Edit scope item dialog box, you can view and edit all the details of a scope item, including viewing and associating documents in the Documents section.

3.20.2 View scope item claim details and document associations

You can view a scope item's claiming details and document associations. Click the **Claiming** icon next to the scope item. The Claiming dialog box opens.

The screenshot shows the 'Claiming' dialog box for 'Geotechnical Report 01'. The dialog box has a title bar with a close button. Below the title bar, there are tabs for 'CLAIMING' and 'DOCUMENTS'. The 'CLAIMING' tab is active, showing a table with columns: Step, Com..., Step name, % Claim, Partial cla..., Claim qty, Claim qty %, Date, Document stat..., Issue, Resource type, and Claimed by. The table contains 6 rows of data. The 'DOCUMENTS' tab is also visible, showing a table with columns: Document No, Document Name, Document Date, Document Status, and Document Link. The 'Geotechnical Report 01' dialog box is open, and the 'Geotechnical Report 01' scope item is selected in the main table.

Step	Com...	Step name	% Claim	Partial cla...	Claim qty	Claim qty %	Date	Document stat...	Issue	Resource type	Claimed by
1	☐	Interim Design Development	42.000	☐	0.00	0.00	10/04/2023			Geotechnical En...	Susan cappelloni
2	☐	Interim QA and Submittal	18.000	☐	0.00	0.00	10/04/2023			Geotechnical En...	Susan cappelloni
3	☐	Receive and Address Final Comments	10.000	☐	0.00	0.00	10/04/2023		1	Geotechnical En...	Paul bennion
4	☐	Prepare IFC Package	15.000	☐	0.00	0.00	10/04/2023		2	Geotechnical En...	Paul bennion
5	☐	Submit IFC	5.000	☐	0.00	0.00	10/04/2023		1	Geotechnical En...	Paul bennion
6	☐	IFC Approved	10.000	☐	0.00	0.00	10/04/2023			Geotechnical En...	Paul bennion

Subtotals Cour

% Complete: 0.000%

- **Claiming** - View claiming details, including the document status. In the Issue column, you can view and associate steps to Change management issues.
- **Documents** – View associated document details, including links to associated documents in the *Document No* column. With the applicable permissions, you can click the hyperlink to open the linked document in the InEight Document application.

3.21 MAPPING


3.22 MAPPING OVERVIEW

On the Mapping tab, you can manage the association of scope items and documents from InEight Document. You can associate scope items and documents in the Mapping page by:

- Manually mapping individual scope items to documents
- Using the Map many documents to a single scope item or Map many scope items to single document option. This option is available when the *Enable Document claiming* project setting is disabled.
- Using the Auto map feature to quickly map all scope items and documents that share the same document number in bulk. This option is available when the *Enable Document claiming* project setting is selected.

You can use other ways to map scope items and documents, such as using a Microsoft Excel template to associate scope items and documents and import them in bulk, and in the Documents section of the scope item’s slide-out.

The image and table below show a summary of the Mapping tab:

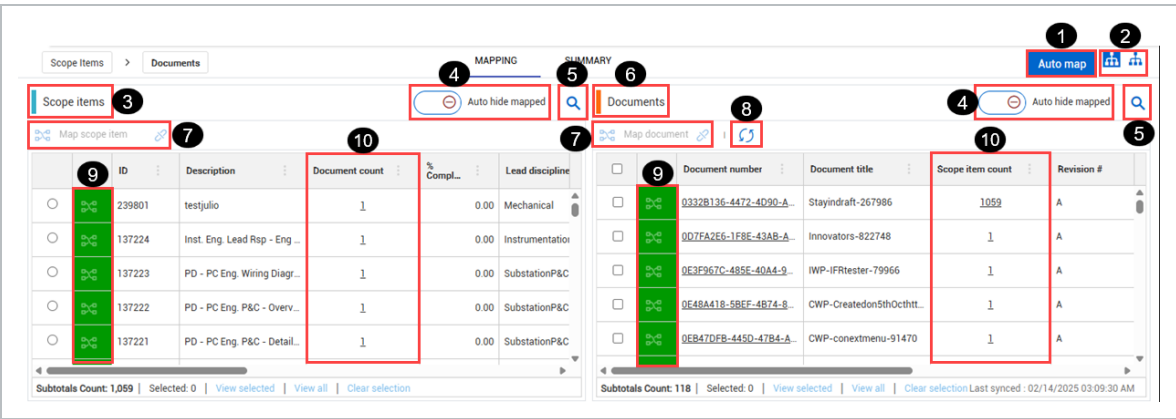

	Item	Description
1	Auto map	When both the <i>Enable Document integration</i> and <i>Enable Document claiming</i> project settings are selected, you can use the auto-mapping feature to quickly associate all scope items and documents that share the same scope item description and document number.
2	Map many scope items to single document option	When only the <i>Enable Document integration</i> setting is selected, you can use both the map many documents or map many scope items feature to manually select to map many documents to a single scope item, or many scope items to a single document. You can also use the Auto map feature.
3	Scope Items grid	The left grid shows the project’s list of scope items.
4	Auto hide	Auto hide mapped scope items or documents to filter them out from

	Item	Description
	mapped	the grid.
5	Search	Use to search for scope items in the Scope items grid or search documents in the Documents grid.
6	Documents grid	The right grid shows the list of documents synced from Document.
7	Map scope item and Map document Unlink scope items or documents	After making your selection, you can map documents to a scope item or map scope items to a document. After making your selection, unlink scope items or documents.
8	Document sync	Sync existing, new, and updated documents from the Document application. Synced documents will show in the Associated documents page. The Last synced status is shown on the lower right side of the panel.
9	Mapped and unlinked items column	View of mapped and unlinked items. Mapped items show a green mapped icon. Unlinked items show the Unlink icon.
10	Document count Scope item count	In the Scope items grid, the Document count column shows the number of documents mapped to a scope item. In the Documents grid, the Scope item count shows the number of scope items mapped to the document. The number is a hyperlink you can click to open a dialog box that shows the list of associated items.

3.23 MAP DOCUMENTS AND SCOPE ITEMS

There are multiple ways to map scope items and documents. The mapping options give you flexibility to map documents and scope items quickly and easily.

You can associate documents to scope items by:

- Manually mapping many documents to one scope item or mapping many scope items to one document.


If the *Enable Document claiming* project setting is set to *On*, a document can only be mapped to one scope item.

- Using the Auto map feature.
- Importing mapped scope items and documents from a template in bulk.
- Using the Document section of the scope item's slide-out panel.

You must have the required permissions in Engineering for document association.

3.23.1 Manually map items

In the Mapping tab, you can use the Map scope item or Map document options to map one to multiple documents to a scope item and map one to multiple scope items to a document. Use the toggle at the top right of the page to switch between the two options.

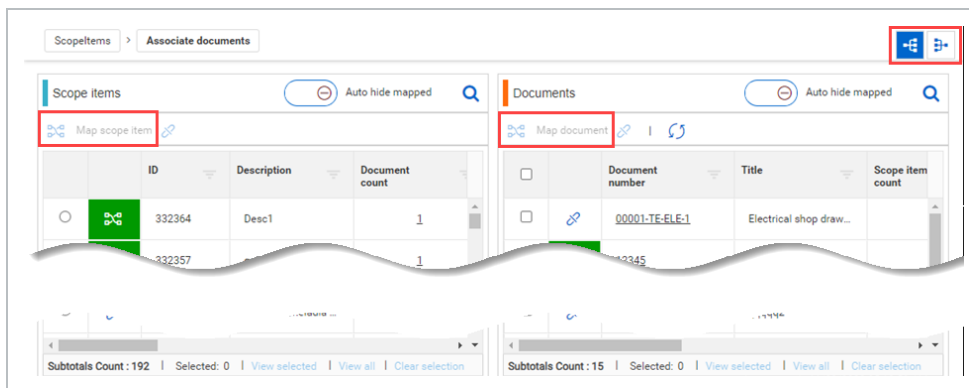

Map documents to scope items

1. Click **Map many documents to a single scope item** at the top right of the page.
2. Select a single scope item in the Scope items panel, and then select one to multiple documents in the Documents panel.
3. Click the **Map document** button in the Documents panel to complete the mappings. The green linked icon will show next to the scope item indicating that it has been mapped.


Map scope items to documents

1. Click **Map many scope items to single document** at the top right of the page.
2. Select a single document in the Documents panel, and then select one to multiple scope items in the Scope items panel.
3. Click the **Map scope item** button in the Scope items panel to complete the mappings. The green linked icon will show next to the document indicating that it has been mapped.

3.23.2 Auto map


You can use auto-mapping to quickly map many scope items to documents. If your business process is composed of having the same scope item description with matching document numbers, you can use the auto-mapping feature to map all scope items with documents using one click.

In the Mapping tab, click the **Auto map** button to quickly associate all scope items to their respective documents when the scope item's description matches the document number.




3.23.3 Import from a template

You can import associated scope items with documents using an import template. In the Scope Items page, you can use the export feature to export your scope item data to a spreadsheet template.

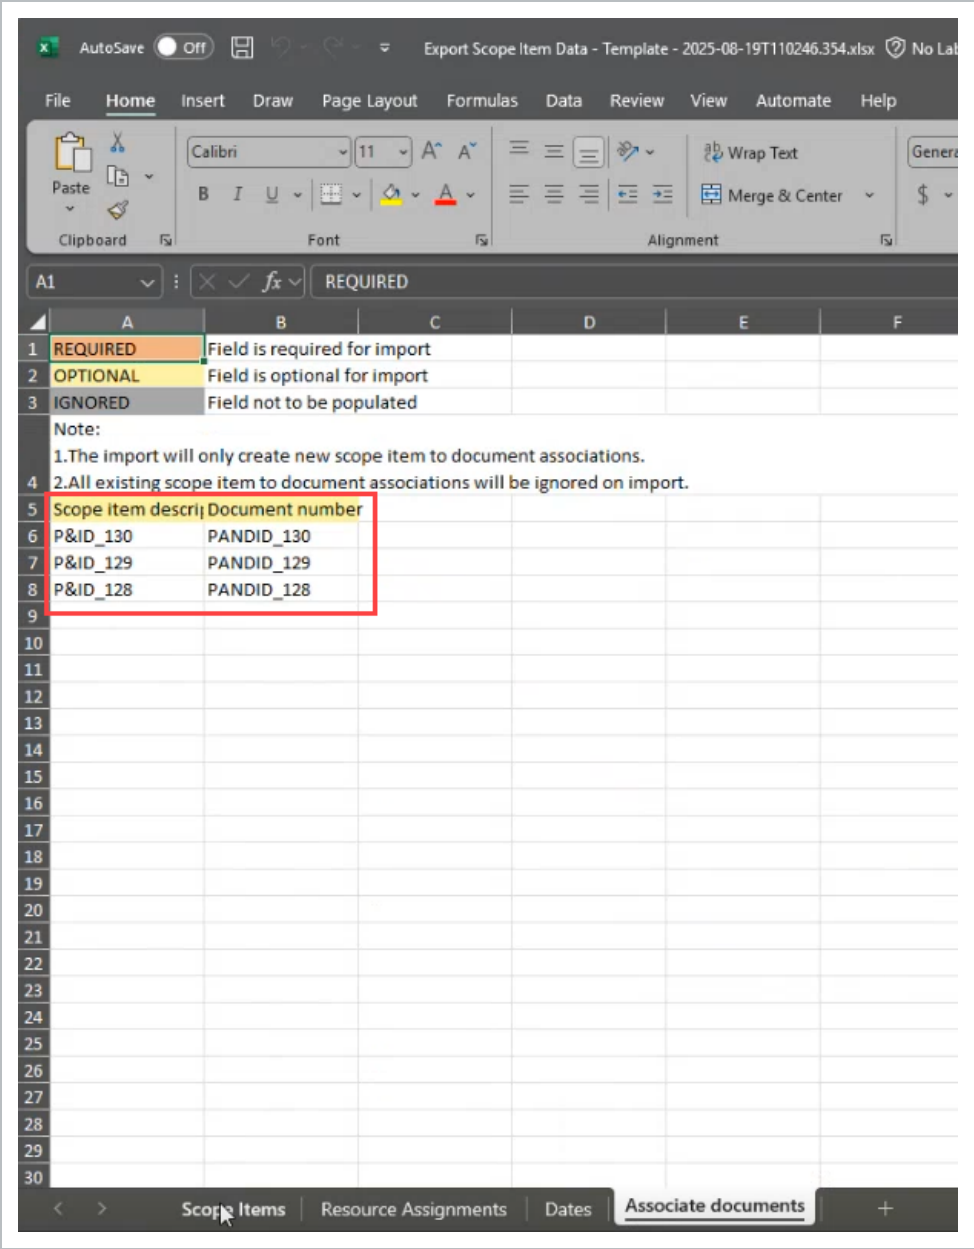

3.23.4 Scope item dialog box


On the Scope Item’s page, you can associate documents in the Documents section when you add or edit a scope item. Select the **Documents** section, and then click the **Document number** drop-down field to select the document from the list. You can select multiple documents to associate to the scope item if needed.

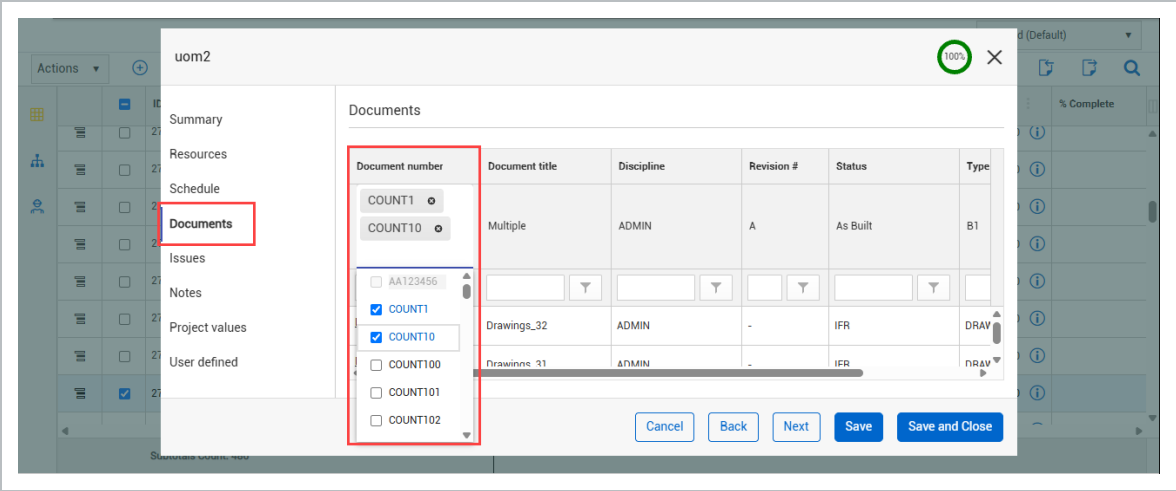

3.24 ASSOCIATED ITEMS

The columns in the Scope items and Documents grids provide valuable information about the scope items and documents. In the Scope items and Documents grid, you can view the number of associated items in the Document count and Scope item count columns.

You can click the **Document count** or **Scope item count** number hyperlink to open the Associated Items dialog box to view the associated items.

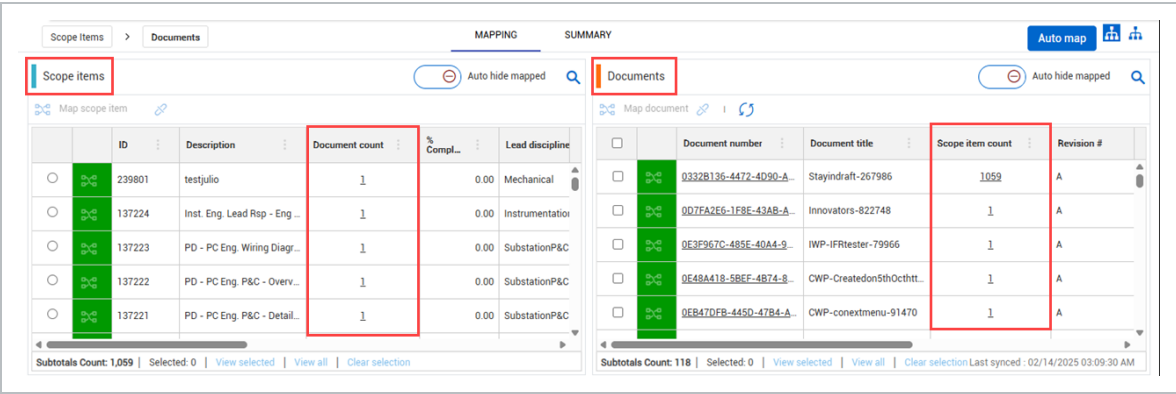


You must have the applicable permissions in Engineering for document association. To view documents in InEight Document, you must have the applicable InEight Document permissions.

3.24.1 Scope items grid

In the Scope items grid, the Document count column shows the number of documents associated to scope items as a hyperlink. You can click the Document count hyperlink to open the Associated items

dialog box to quickly view a list of associated documents.

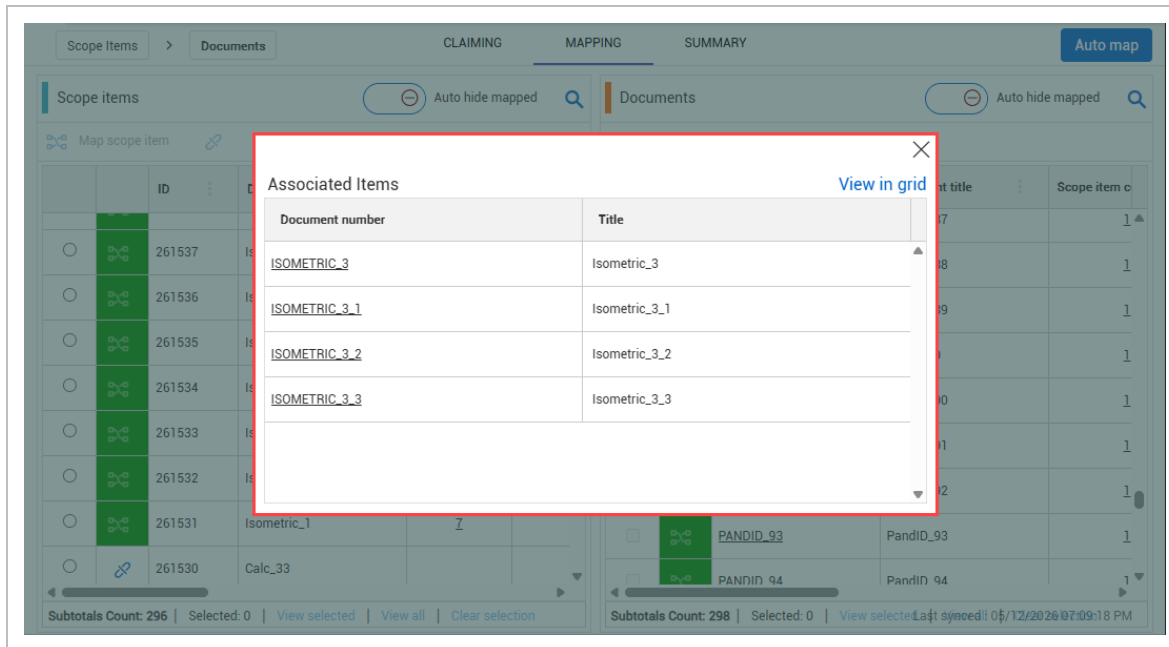

In the Associated items dialog box, you can do the following:


- **Document number** — The document number from Document as a hyperlink. Click the hyperlink to open in Document.
- **Title** — The title of the document.
- **View in grid** — Filter the scope items and view them in the Scope items grid. Click the **Document number** link to open the associated document in Document.

3.24.2 Documents grid

In the documents grid, the Document number shows the document synced from Document and the number of scope items associated to documents in hyperlinks.


- **Document number** — With applicable permissions, you can open a document in the InEight Document application. In the Document number column, click the Document number hyperlink to open the document in InEight Document.
- **Scope item count** — The Scope item count column shows the number of scope items associated to a document. You can click the scope item's hyperlink to open the Associated items dialog box to quickly view a list of associated scope items.

- View in grid — Click the **View in grid** button to view a filtered list of the associated scope items in the Scope items grid. Clear the ID column filter to reset.
- Scope Item ID — Unique identifier for the scope item.
- Description — Unique description for the scope item.

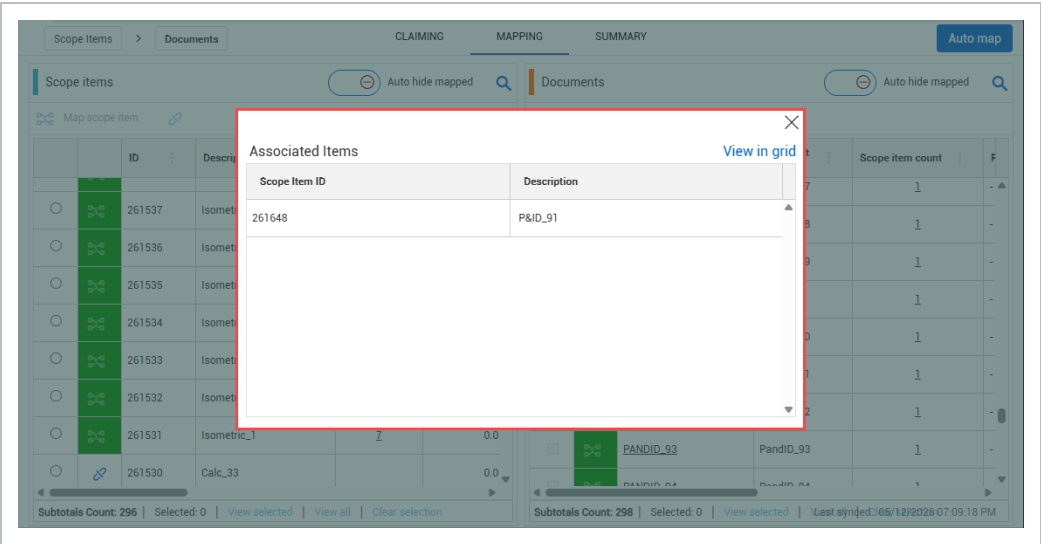

3.24.3 Unlink associated items

You can unlink associated items from scope items and documents. You must have the required permissions in Engineering for document associations.

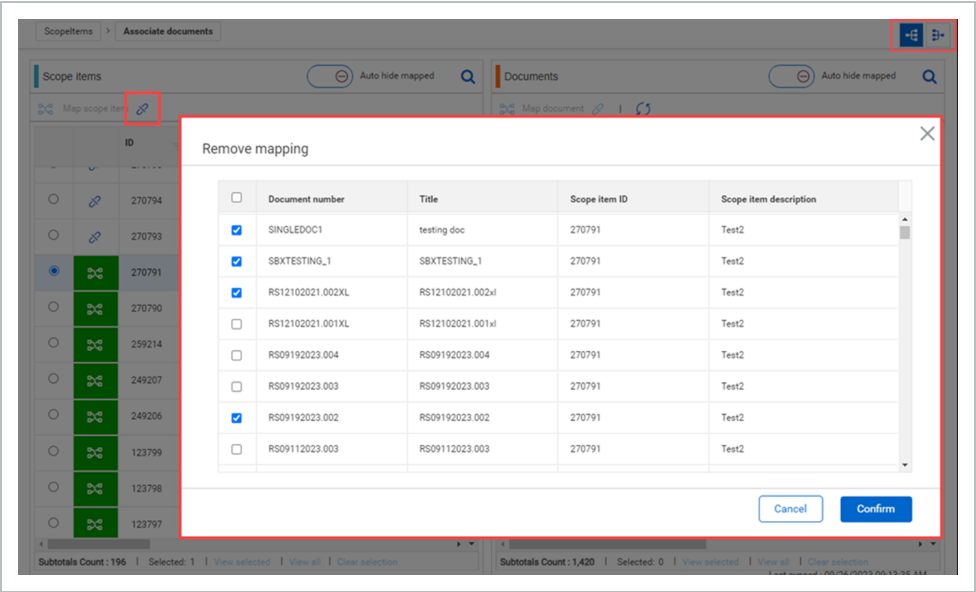


Unlink associated items

1. To unlink documents from a scope item, select **Map many documents to single scope item**. To unlink scope items from a document, select **Map many scope items to single document**.
2. Select the scope item or document.
3. Click the **Unlink** icon. The Remove mapping dialog box shows.
4. Select the item or items you want to unlink, and then click **Confirm**.

3.24.4 Mapped documents removed from InEight Document

When mapped documents are deleted in Document, a warning shows at the top of the Mapping page showing the number of documents that no longer exist.

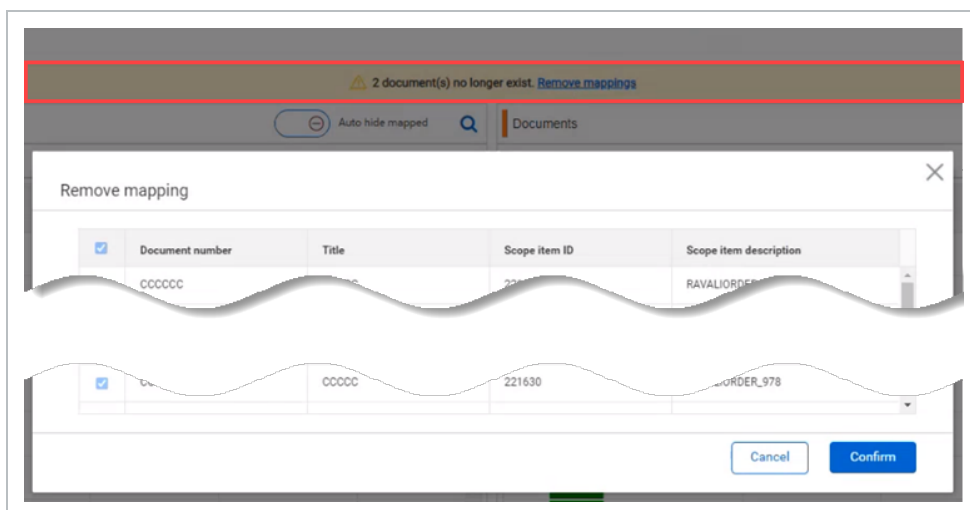

You can click the **Remove mappings** link in the warning message to view the deleted documents and remove.

3.25 SUMMARY

On the Summary tab, you can view a summary of documents associated to scope items to easily track associated items, provide real time updates, and export data.

Scope Items

>

Documents

CLAIMING

MAPPING

SUMMARY

Document / Scope item

Document status

of scope items

% Complete

Planned Mhrs

Earned Mhrs

Forecast remaining Mhrs

Baseline start

month/d...

☐	» DRAWINGS_44 - Drawings_44	IFR	1	0.00	20.00	0.00	20.00	
☐	» DRAWINGS_45 - Drawings_45	IFR	1	0.00	20.00	0.00	20.00	
☐	» DRAWINGS_46 - Drawings_46	IFR	1	0.00	20.00	0.00	20.00	
☐	» DRAWINGS_47 - Drawings_47	IFR	1	0.00	20.00	0.00	20.00	
☐	» DRAWINGS_48 - Drawings_48	IFR	1	0.00	20.00	0.00	20.00	
☐	» DRAWINGS_49 - Drawings_49	IFR	1	0.00	20.00	0.00	20.00	
☐	» DRAWINGS_5 - Drawings_5	IFR	1	0.00	20.00	0.00	20.00	
☐	» DRAWINGS_6 - Drawings_6	IFR	1	0.00	20.00	0.00	20.00	
☐	» DRAWINGS_7 - Drawings_7	IFR	1	0.00	20.00	0.00	20.00	
Subtotals Count: 298					9,285.00	630.00	8,655.00	

The Summary tab functions similarly to the work package feature, such as the percent complete column, the warning icon that shows when there are missing values, and the summary overview of all documents in the document register at the bottom of the window. The scope item's data that's associated to a document is aggregated and a summary of percent complete, hours, and min/max dates are shown per document. Additional features include:

- When scope items are associated to a document, you can expand the document to view the associated scope items.
- When multiple scope items are associated, the system aggregates the percent complete, hours, dates. The earliest start date and the latest end date are captured at the document level.


3.26 CLAIMING SCHEMES

3.27 CLAIMING SCHEMES OVERVIEW

A claiming scheme is a sequence of steps and milestones used to record progress of engineering deliverables called scope items. Steps and milestones are assigned a completion percentage based on the level of effort to complete each step. This lets you progressively track progress as phases of design are completed on a daily or weekly basis.

Claiming schemes are broken out into engineering disciplines, which are set up at the organization level. See [Disciplines](#) for more information. Configuring claiming schemes is the first step in setting up a project in the Engineering module. You must have the applicable claiming schemes permissions.

To configure claiming schemes, open the Engineering module to the Scope items page, and then click **Actions > Claiming schemes**.

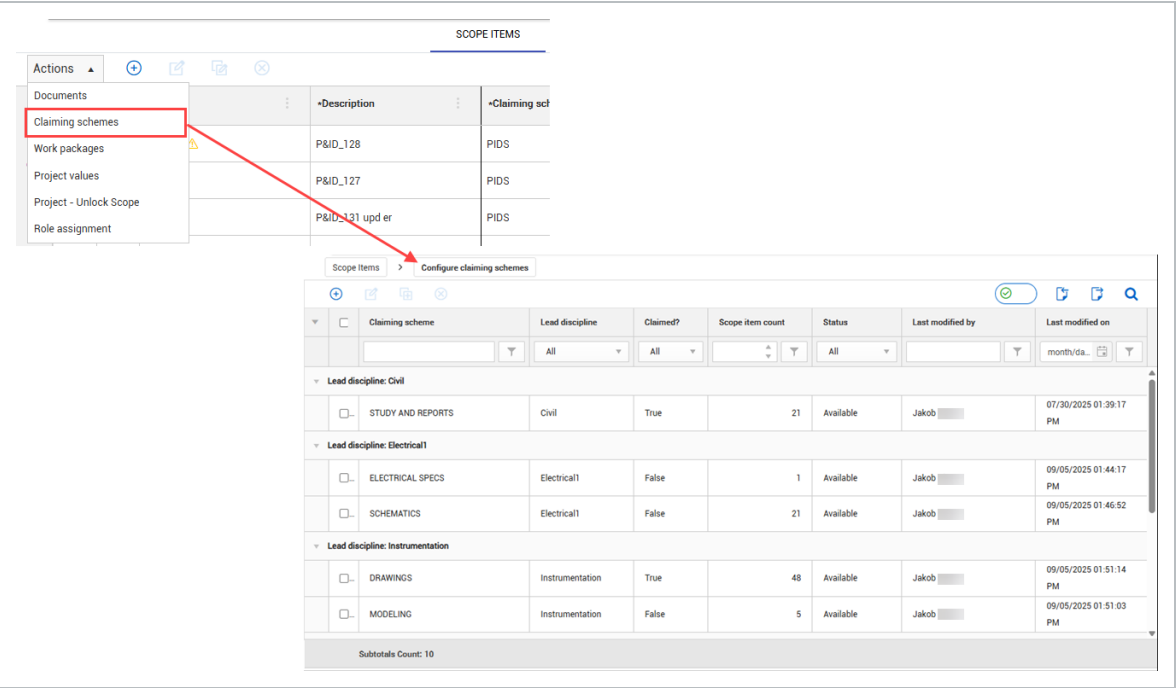

You can add claiming schemes using the following options on the Configure claiming schemes page:

- Manually add a claiming scheme using the **Add claiming scheme** option.
- Copying an existing claiming scheme using the **Copy claiming scheme** option.
- Importing claiming schemes in bulk using the export and import features.

Scope Items cannot be created on a project without a claiming scheme assigned.

3.27.1 Columns

The following table provides an overview of the available columns on the Claiming schemes page:

Column name	Description
Claiming scheme / Scope Item	Shows the name of the claiming scheme and associated scope items.
Lead discipline	Shows the associated lead discipline. Disciplines are configured in organization settings.
Last modified by	Shows the name of last user who modified the claiming scheme.
Last modified on	Shows the date and time of the last modification made to the claiming scheme.
Claimed?	Shows whether there is any claiming performed on the claiming scheme. When the status is <i>True</i> , claiming has been performed, and you are not able to edit the claiming scheme. When the status is <i>False</i> , claiming has not been performed, and you are able to edit the claiming scheme.
Scope item count	Shows scope items being used by showing the number of scope items associated to the claiming scheme.
Status	Gives you the option to set the claiming scheme status as Available or Unavailable. When set to Available, you can assign the claiming scheme to scope items. When set to Unavailable, you can no longer assign the claiming scheme to scope items. Any scope items that are already assigned to an unavailable claiming scheme will remain assigned and functional.

3.28 MANAGE CLAIMING SCHEMES

Claiming schemes can be added on the Configure claiming schemes page manually, by copying an existing claiming scheme, or in bulk by importing them using the claiming scheme template. Before you create scope items, you must create claiming schemes to assigned to scope items.

3.28.1 Add a claiming scheme manually

Claiming schemes can be manually added individually using the Add button on the Configure claiming schemes page. When you add a claiming scheme, you must also set up at least one step in the claiming scheme.

A system-generated milestone named Scope Complete is automatically assigned to a claiming scheme's last step if the last step is a null value when configured.


Claiming schemes can also be added individually using the Copy button and in bulk using the Import claiming scheme button.

3.28.2 Considerations

- You must have resource types and disciplines added to the organization and project to be able to add claiming schemes. See [Disciplines](#) for more information.
- The Resource discipline field of a claiming scheme step is automatically populated based on the selected resource type.
- You must assign a Lead Discipline to each claiming scheme. This discipline is separate from the resource disciplines assigned to each individual steps, which do not need to match the lead discipline. This is useful when a claiming scheme generally falls under one discipline even if individual steps' assigned resource types fall under different disciplines.
- You can optionally set up a step for partial claiming, which lets you claim only partial completion for that individual step.
- You can optionally assign a single project milestone to a step. You must have milestones set up and assigned to the project.
- The sum of % Claim across all steps must equal 100% to save a claiming scheme.
- You must have the permission Add claiming schemes.

3.28 Step by Step 1 – Adding a claiming scheme manually

1. To add a claiming scheme manually, click the **Add claiming scheme** button. The Add claiming scheme dialog box opens.

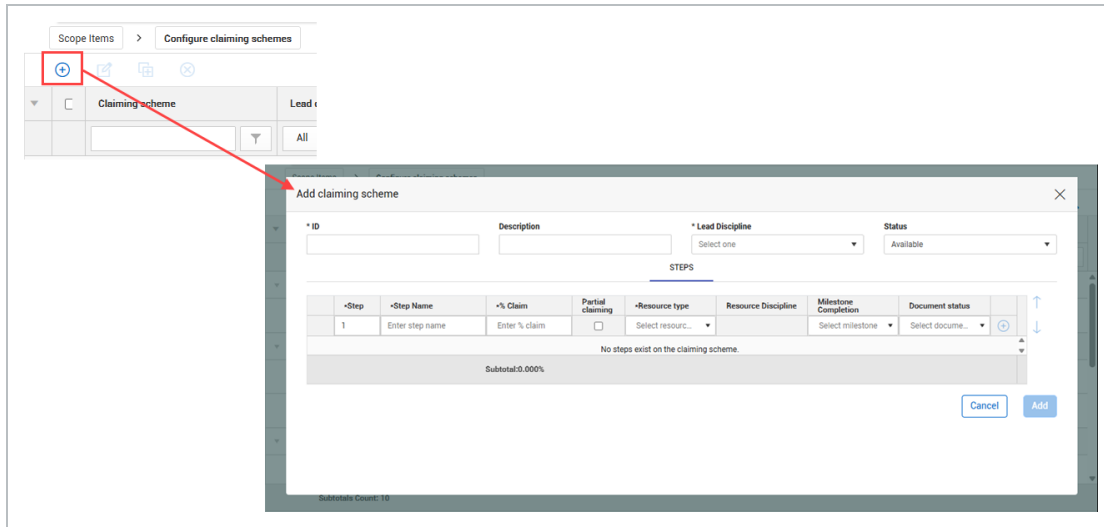

2. Complete the required fields:
 - ID – The ID value must be unique
 - Lead Discipline
3. Fill out the required fields for the first step:
 - Step number
 - Step name
 - % Claim – The percentage completed by this individual step.
 - Resource type
 - Schedule group
 - Activity ID format
4. Optionally, select the **Partial claiming** check box if you want to be able to claim only partial completion of this step.
5. Optionally, select a milestone under Milestone Completion for the step.
6. To add additional steps, click the **Add** icon on the right, and then repeat steps 3-5.

To delete a step at any time, click the **Delete** claiming scheme step icon on the right.

7. Click **Add**.

3.28.3 Copy a claiming scheme

You can copy an existing claiming scheme and its steps from the Configure claiming schemes page. You also have an opportunity to modify details of the claiming scheme and its steps before saving. You must have the permission Add claiming schemes.

Copying an existing claiming scheme is useful when you want to create multiple claiming schemes whose steps are similar to each other and that only require minor modifications instead of creating each claiming scheme from scratch. You can only copy one claiming scheme at a time.

3.28 Step by Step 2 – Copying an existing claiming scheme

1. Open the Configure claiming schemes page, and then select one claiming scheme in the grid. The Copy claiming scheme button is enabled in the upper left.
2. Click the **Copy claiming scheme** button. The Copy claiming scheme dialog box opens.

The screenshot shows the 'Copy claiming scheme' dialog box. The dialog is titled 'Copy claiming scheme' and has a close button (X) in the top right. It contains the following fields and controls:

- * ID: A text input field.
- Description: A text input field.
- * Lead Discipline: A dropdown menu with 'Select one' as the placeholder.
- Status: A dropdown menu with 'Available' as the placeholder.
- STEPS: A table with the following columns:

*Step	*Step Name	*% Claim	Partial claiming	*Resource type	Resource Discipline	Milestone Completion	Document status
3	Enter step name	Enter % claim	☐	Select resource...		Select milesto...	Select docum...
☐ 1	Document created	0.000	☐	CEN-Civil Engineer	Civil		NS-Not Started
☐ 2	Issue for Construction	100.000	☒	CEN-Civil Engineer	Civil	SC-Scope Complete	IFC-Issued For...
- Subtotal: 100.000%
- Buttons: 'Cancel' and 'Save'.

3. Enter a unique ID, and then select a Lead Discipline.
4. Modify or delete existing steps, or add new steps, as necessary.
5. Click **Save**.

3.28.4 Import claiming schemes

Importing lets you add claiming schemes in bulk using a Microsoft Excel spreadsheet. Each row in the spreadsheet represents one step in a claiming scheme.

All imported claiming schemes that pass validations are added to the Configure claiming schemes page. The imported claiming schemes that fail validations are added to the Error resolution page. All imports are shown in Audit log > **Import history**. To import claiming schemes, you must have the permission Import claiming schemes.

To import claiming schemes, export a claiming scheme template. When you click Export, there are two export options:


- **Template** — This option exports a blank Excel template that you fill out to add new claiming schemes.
- **Data export** — This option exports an Excel file of all selected claiming schemes. To select all claiming schemes, select the check box in the upper left of the Configure claiming schemes page before the data export.

You can only import new claiming schemes, not edit existing ones. To edit an existing claiming scheme on the Configure claiming schemes page, select a claiming scheme, and then click the **Edit claiming scheme** icon.

A system-generated milestone named Scope Complete is automatically assigned to a claiming scheme's last step if the last step is a null value when configured.

3.28 Step by Step 3 – Import claiming schemes using the Excel template

1. In the Configure claiming schemes page, click the **Export claiming scheme** icon, and then select **Template** from the drop-down menu. The Export Claiming Scheme Template.xlsx spreadsheet is downloaded.




2. Open the template in Excel.

- Fill out the required fields for each claiming scheme and step. Each row represents one step. The ID column is the name of the claiming scheme.

	A	B	C	D	E	F	G	H
1	REQUIRED	Field is required for import						
2	OPTIONAL	Field is optional for import						
3	IGNORED	Field not to be populated						
Note: 1.Import functionality only allows for new Claiming Schemes to be created. Existing Claiming Schemes can be updated using the edit button. 2. Partial claiming field should be specified as either True or False. 3. Resource Discipline field will be ignored on import as the Discipline gets inherited from the Resource type assignment.								
4	ID	Description	Lead Discipli	Step	Step name	% Claim	Partial claiming	Resource type
6	0123 EW BSTR	Bridge Structures - Early Works Structural	1		Final Design Development Bridge Structures- 5% Step	5,000	True	Structural Engineer
7	0123 EW BSTR	Bridge Structures - Early Works Structural	2		Final Design Development Bridge Structures- Receive As Builts & Digitize Complete	5,000	False	Structural Engineer
8	0123 EW BSTR	Bridge Structures - Early Works Structural	3		Final Design Development Bridge Structures- 15% Step	5,000	True	Structural Engineer
9	0123 EW BSTR	Bridge Structures - Early Works Structural	4		Final Design Development Bridge Structures- Analytical Model Geometry Complete	5,000	False	Structural Engineer
10	0123 EW BSTR	Bridge Structures - Early Works Structural	5		Final Design Development Bridge Structures- 45% Step	5,000	True	Structural Engineer
11	0123 EW BSTR	Bridge Structures - Early Works Structural	6		Final Design Development Bridge Structures- Coordination with Track and Systems	5,000	False	Structural Engineer
12	0123 EW BSTR	Bridge Structures - Early Works Structural	7		Final Design Development Bridge Structures- 65% Step	5,000	True	Structural Engineer
13	0123 EW BSTR	Bridge Structures - Early Works Structural	8		Final Design Development Bridge Structures- Jacking Sequence Finalized	5,000	False	Structural Engineer
14	0123 EW BSTR	Bridge Structures - Early Works Structural	9		Final Design Development Bridge Structures- 95% Step	5,000	True	Structural Engineer
15	0123 EW BSTR	Bridge Structures - Early Works Structural	10		Final DQCP 01 - Self Checks Complete	3,000	False	Structural Engineer
16	0123 EW BSTR	Bridge Structures - Early Works Structural	11		Final DQCP 01. QC Disciplinary Review	2,000	True	Structural Engineer

- Save the Excel file.
- In the Configure claiming schemes page, click the **Import** icon.
- In the Import data from template dialog box, click **Browse**, and then select the Excel file. Click **Import**. The Import history page opens with the status of the import.

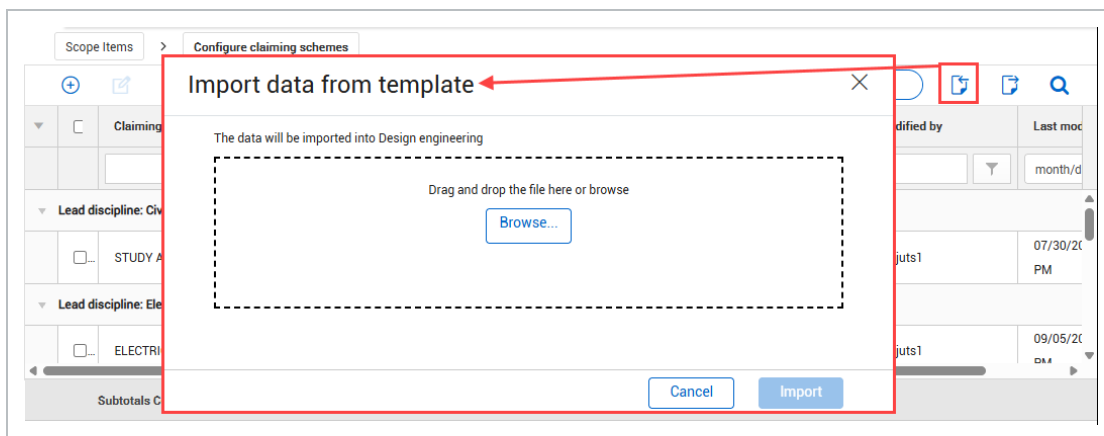


- If there are issues, click **Completed with issues** in the Status column to open Claiming scheme error resolution, and then click the claiming scheme ID to view and resolve issues before saving.

3.29 DOCUMENT INTEGRATION - CLAIMING SCHEMES

When integrated with InEight Document, a Document status column shows on the claiming scheme that syncs with the Document project.

The Document status field shows the synced status from the mapped project in Document. You can also click in the **Document status** field, and then click the drop-down icon to select an available status from the list.

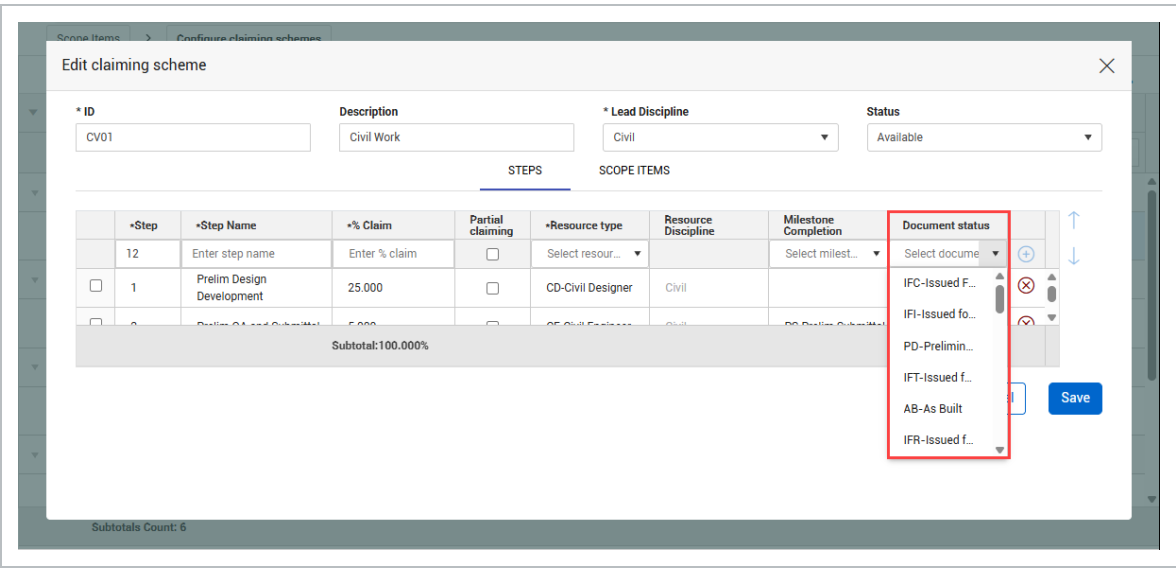

3.30 WORK PACKAGES

3.31 WORK PACKAGES

A work package is a small, manageable scope of work that can be assigned for supervision, execution, and tracking.

In the Configure work packages page, the Engineering Work Package and Deliverable Package tabs are where you can create a list of work packages associated with the project. You must have the applicable permissions in Engineering.

To open Configure work packages, go to Engineering > Scope Items > Actions > **Work packages**.

Scope Items > Work packages		ENGINEERING WORK PACKAGE		DELIVERABLE PACKAGE	
Display ID	Description	Construction need by date	Discipline	# of scope items	% Complete
		month/day/year			
☐ EWP04	Road - Ramp and Bridge - Segm...	10/10/2023	Civil		
☐ EWP_03	Road - Ramp and Bridge - Segm...	12/01/2023	Civil		
☐ EWP_02	Road - Ramp and Bridge - Segm...	11/03/2023	Civil		
☐ EWP_01	Road - Ramp and Bridge - Segm...	10/06/2023	Civil	11	1€
☐ Civil2	Roadway		Civil		
☐ Civil_04	Roadway		Civil		
☐ Civil	roadway		Transportation Structures	1	3€
Subtotals Count: 7					

The Engineering Work Package and Deliverable Package have the same functions. For example, you can create the same work packages in each tab, and then group them so they roll up differently. You can choose to define and group the work packages based on your business process.

You can add, edit, and delete engineering work package and deliverable package items.

The work package grid shows the aggregated work package data for all scope items associated to the work packages on the project. When you add or remove a scope item from a package, the work package summary information is updated. When you update a scope item's hours, dates, or claiming, the summary information is also updated to reflect the changes.

Data validations are built into a work package's summary information for percent complete, hours, and dates. When a scope item associated with a package has missing or null values for hours or dates, a warning icon shows next to the values that depend on the missing or null values to calculate. For example, if a scope item has the MHRs null due to a missing CE MHRs/qty unit rate, the warning icons show in the % Complete, Planned MHRs and Earned MHRs. You can hover over the warning icon for more information.


Scope Items > Work packages		ENGINEERING WORK PACKAGE		DELIVERABLE PACKAGE	
% Complete	Planned MHRs	Earned MHRs	Forecast remaining MHRs	Baseline start	Baseline finish
				month/day/year	month/day/year
40.00 ⚠	2,260.00 ⚠	8,120.00 ⚠	0.00		
28.33 ⚠	8.00 ⚠	2.26 ⚠	0.00		
33.33	120.00	40.00	8.00		

3.32 WORK PACKAGES OVERVIEW PAGE

The Work packages Overview page provides transparency of various work package related items. You must have applicable permissions in Engineering.

To open a work package overview page, click the **Display ID** column link of an Engineering or Deliverable work package in Scope Items > Actions > **Work packages**.

The image and table below are an overview of the Work and Deliverable work package overview page:

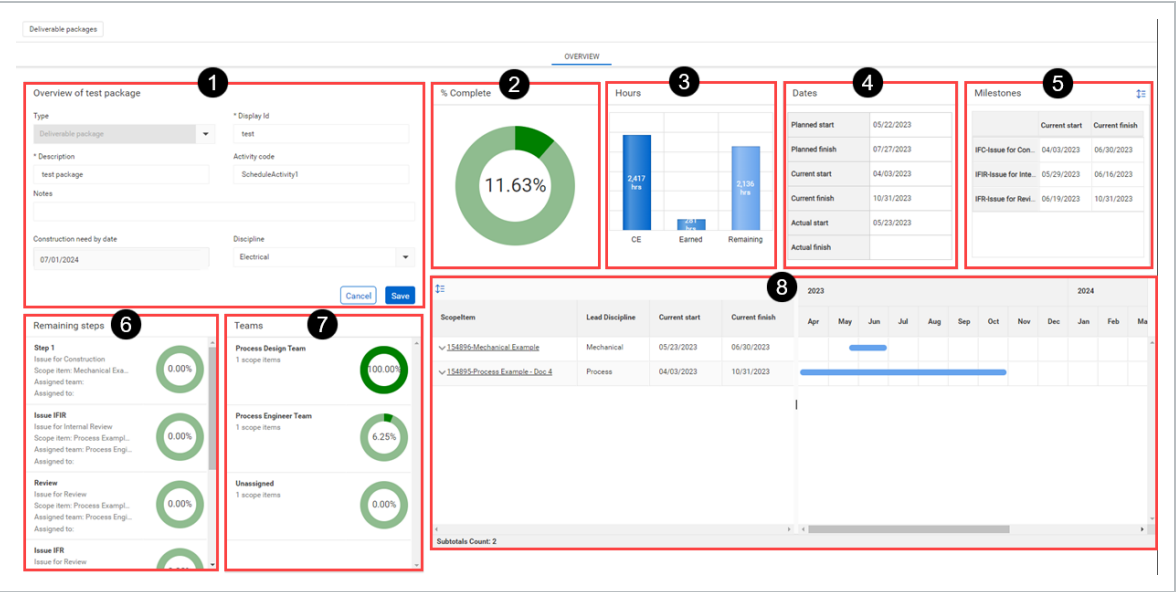


	Title	Description
1	Overview of test package	View and edit the current work package attributes.
2	% Complete	% complete is based on the scope item hours and earned progress on scope items within the work package. ((Earned Qty x CE MHRs ÷ Unit) ÷ CE Hours).
3	Hours	- CE - Sum of the scope item man hours for all scope items within a package (Scope Item Qty x CE MHRs ÷ Unit). - Earned - Sum of the scope item earned hours for all scope items within a package (Earned Qty x

	Title	Description
		CE MHRs ÷ Unit). • Remaining - Sum of the scope item forecast remaining man hours for all scope items within a package (CE Hours - Earned Hours) if Control integration is off and ((Scope Item Qty - Earned Qty) x CE MHRs ÷ Unit) if Control integration is on.
4	Dates	Start dates show the earliest date, and finish date will show the latest date from the related scope items.
5	Milestones	When the Project Settings - Dates setting is configured with Scope Item/Milestone, the milestones window will show. You can use the Dates Chooser icon to toggle between the following dates: • Planned start/finish • Current start/finish • Actual start/finish • Completion
6	Remaining steps	View non-completed steps and their percent complete for all related scope items to the package. Remaining steps will be shown ascending based on step order.
7	Teams	Shows all teams associated to the work package and the teams' percent complete. The teams' percent complete is based on scope item hours and earned progress the team is assigned to on the scope items within the work package (Earned Hours ÷ Scope Item Hours). An unassigned team will show for scope items that does not have a team assigned.
8	Gantt	List of scope items with their related work packages. In the Gantt chart, you can view the start and finish dates for the scope items within the work package. You can use the Dates Chooser icon to toggle between the following dates: • Planned start/finish

Title	Description
	• Current start/finish • Actual start/finish When the Project Settings, Dates setting is configured with Scope Item/Milestone, you can expand the scope items and view the milestone dates below the scope item.

In the scope item list, when you click on a scope item link, the Edit scope item dialog box opens. You can view and make changes to scope items. When changes are saved, the overview page is updated to reflect the new changes.

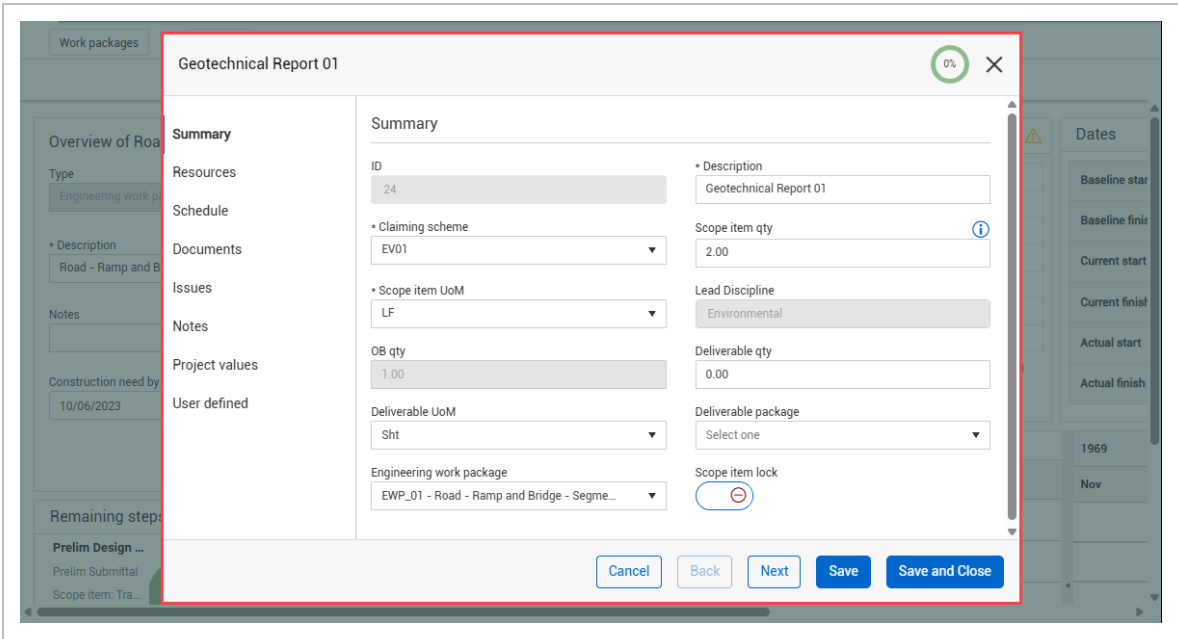

3.33 PROJECT VALUES

You can define project-specific values to assign to scope items in the project. Types of project values are construction work areas, segments, and work classifications. You define the values for each of these in InEight Platform. For example, a construction work area might be named Main St NE bridge, a work classification might be named Drainage, and a deliverable package might be Drainage package. You must have the following InEight Platform permissions:

- Edit engineering settings in Organization project
- Add project value types in Add project value types

You can configure project values manually or by importing a Microsoft Excel file.

3.33 Step by Step 1 – Add a project value manually

1. From the Scope items page, click **Actions**, and then select **Project values** from the drop-down menu. The Platform Project values page opens in a new tab.

Area	ID	Name	Description	Status	Mapped Value
Segment	SEG_03	Segment 03		Available	
	SEG_02	Segment 02		Available	
	SEG_01	Segment 01		Available	

2. Click the type of project value you want to add (For example, Area or Segment).
3. In the table, click the **Add** icon to add a new value.
4. Enter a unique ID and applicable data in the available fields.
5. Click the **Add** icon.
6. Click the **Add** icon to the left of the new fields.

Area	ID	Name	Description	Status	Mapped Value
Segment	SEG_04	Segment 04		Available	
	SEG_03	Segment 03		Available	
	SEG_02	Segment 02		Available	
	SEG_01	Segment 01		Available	

At the organizational level, you can select which project values can be associated with engineering scope items and if they are required in a project. For more information, see [Project values in organizational settings](#).

At the project level, you can select which project values you want to associate with scope items, and if they are required from the Include list. For more information, see [Project values in project settings](#).


3.34 LOCK AND UNLOCK PROJECT SCOPE

On the Scope items page, you can lock and unlock the scope on a project. The scope is unlocked by default for new projects. To lock the scope, you must have the permission Lock project. To unlock the scope, you must have the permission Unlock project.

When the scope is locked for the first time on a project, the current Scope item qty value is automatically used as the OB qty value for each existing scope Item in the project. When you update the scope item quantity while the scope is locked, a cause code is required. Any new scope items added after the scope is locked do not have an OB quantity.

When the scope is unlocked, then the OB qty field is editable on all existing scope items in the project.

To lock or unlock the scope from the Scope items page, click **Actions**, and then select **Project - Unlock Scope** or **Project - Lock Scope** from the drop-down list.

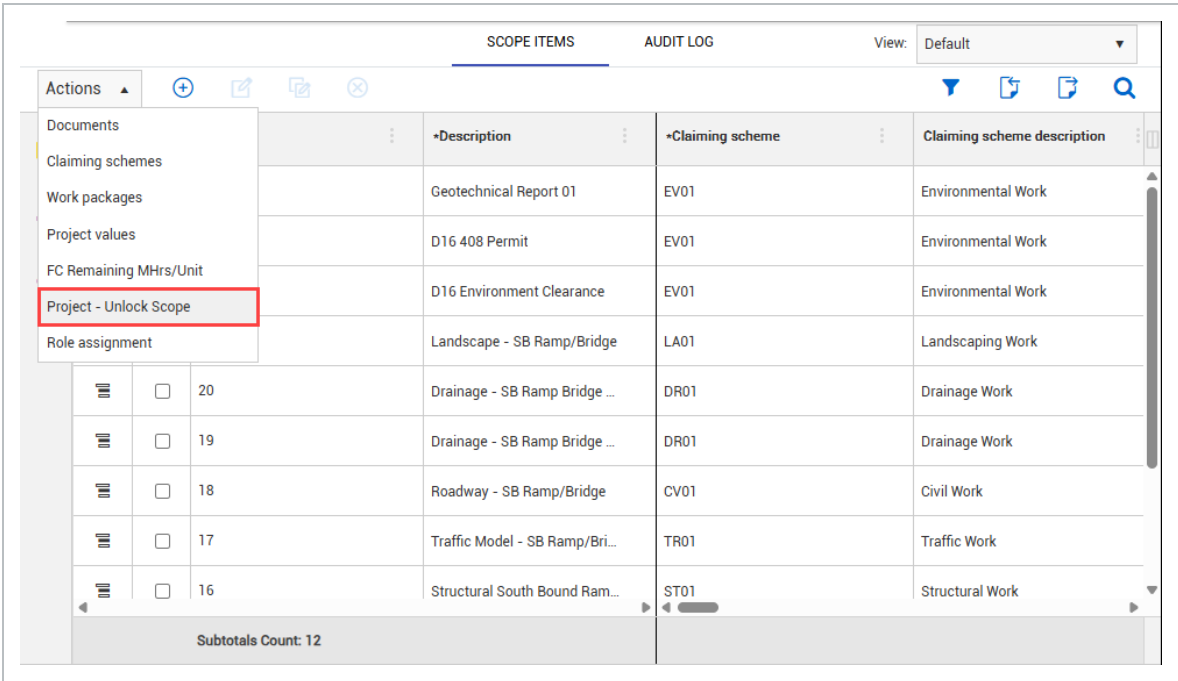

To lock scope, you must have permission Lock project. To unlock scope, you must have the permission Unlock project.

3.35 ROLE ASSIGNMENT

The Role assignment dialog box lets you create roles by resource type, and assign teams and users to roles. You can create roles for any resource type added to your project. When you add a claiming

scheme to a scope item, a default role is automatically added for the associated resource type and claiming scheme if a role does not already exist.

The Role assignment dialog box shows the Current and future assignments tab by default when opened. On this tab, you can add roles and assign teams and users. There is also a User assignment history tab, which shows a record of all user assignment changes made.

The Current and future assignments tab shows counts of current assignments to scope items and steps.

After a role is created, you can assign it to a scope item in the Resources section of the Add and Edit scope items dialog boxes and in the Resource Assignments sheet of the Microsoft Excel import template. When you assign a role to a scope item, the Planned team and Assigned user fields are automatically populated with assignments from the Role assignment dialog box and become read-only.

3.35.1 Considerations

- To see role assignments, you must have the permission View role assignment. To perform actions on role assignments, you must have the permissions Edit role assignment, Add role assignment, and Delete role assignment.
- When you assign a role to a scope item, the role, planned team, and assigned user are inherited by the claiming steps. You can still update the role on individual steps if the step has not been claimed.
- You can delete a role only if it is not assigned to a scope item.
- When you update a planned team or assigned user on a role, those fields are updated on all incomplete scope items and steps with that role assigned. Any completed roles with the role assigned keep the previous planned team and assigned user.
- There is no limit on the number of roles that can be created for a resource type.
- For each existing role, you can add a future user by clicking the **Add future user** icon next to the role name. This allows another user to be assigned on a role on a future start date. The start date defaults to today's date, and can be updated to a future date. On the start date, the current user is replaced by the future user and each incomplete step is updated with the future user.
 - After a future user is added to a role, the end date of the current user on the role defaults to the day before the future user's start date.

	Resource type / Role	Planned team	Assigned user	Start date	End date
+	Drainage Engineer				
+	Drainage Engineer 1	Water	Brian	06/07/2021	06/28/2022
+	Drainage Engineer 1	Water	Dominic	06/29/2022	
+	CES				

- Each role can have only one future user at a time.

3.35 Step by Step 1 – Assign a role, planned team, and user to a resource type

- From the Scope items page, click **Actions**, and then select **Role assignment** from the drop-down menu. The Role assignment dialog box opens to the Current and future assignments tab.
- Click the **Add role** icon next to a resource type. A new row is created below with a default name.

To change the name, click on the role name, edit the name, and then press **Enter**.

Role assignment									
CURRENT AND FUTURE ASSIGNMENTS					USER ASSIGNMENT HISTORY				
Resource type / Role	Planned team	Assigned user	Start date	End date	Total scope items	Scope items remaining	Total steps	Steps remaining	Note
+	Systems Communications								
+	Systems Communications 1		06/07/2021		0	0	0	0	
+	Structural Engineer								
+	Structural Engineer 1		06/07/2021		0	0	0	0	
+	Architectural Landscaping								
+	Architectural Landscaping 1		06/07/2021		0	0	0	0	
+	Systems Traction Power								
+	Systems Traction Power 1		06/08/2021		0	0	0	0	
+	Systems PLS								
+	Systems PLS 1		06/07/2021		0	0	0	0	
+	Drainage Engineer								
+	Drainage Engineer 1	Water	Brian	06/07/2021	0	0	0	0	
+	CES								
+	CES 1		06/11/2021		0	0	0	0	

- Click in the Planned team field for the new role, and then select a team from the drop-down list. Any team added to project settings is available to be selected.
- Click in the Assigned user field, and then select a user from the drop-down list. Any user with access to the project is available to select.
- Click **Save**.


For more information about assigning a resource type to a scope item, see [Scope item resources](#).

3.36 CHANGE INTEGRATION – ASSOCIATE SCOPE ITEMS TO ISSUES

You can associate scope items to issues in Change to mitigate risks in deliverables. Issues can be associated on the Scope Items page, and also when you add a scope item or update a scope item's quantity. For more information about adding or updating the quantities of a scope item, see [Add scope items](#).

3.36.1 Associate a Change issue

To associate an issue, click the **Claiming** icon to the left of the scope item, and then in the Issue column click the **Associate to Change issue** icon. This opens the Associate to Change issue dialog box.

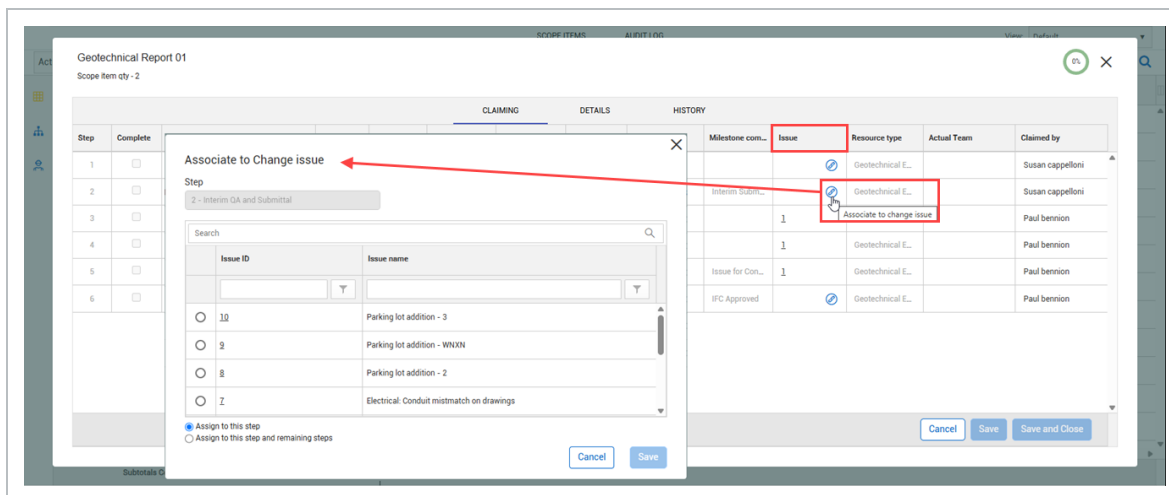

In the Associate to Change issue dialog box, you can select Change issues to assign to the scope item. You can select a single issue at a time and then assign it to the current step or to the current step and the remaining non-completed steps of the scope item.

After your issue selection, select **Assign to this step** or **Assign to this step and remaining steps**, and then click **Save**. Click the number link to view the associated issues. In the dialog box you can remove issues or return to the Associate to Change issue dialog box to manage issues.

3.36.2 View number of assigned issues

After you associate issues to a scope item, a number count link shows in the Issue column with the number of issues assigned to the scope item. Click the number link to view the associated issues. In the

dialog box you can remove issues or return to the Associate to Change issue dialog box to manage issues.

Geotechnical Report 01
Scope item qty - 2

0% X

CLAIMING				DETAILS		HISTORY			
Partial cl...	Claim qty	Claim qty %	Undo claim	Date	Milestone c...	Issue	Resource type	Actual Team	Claimed by
☐	0.00	0.00		10/04/2023		2	Geotechnic...		Susan cappelloni
☐	0.00	0.00		10/04/2023	Interim Su...	2	Geotechnic...		Susan cappelloni
☐	0.00	0.00		10/04/2023		1	Geotechnic...		Paul bennion
☐	0.00	0.00		10/04/2023		2	Geotechnic...		Paul bennion
☐	0.00	0.00		10/04/2023	Issue for ...	1	Geotechnic...		Paul bennion
☐	0.00	0.00		10/04/2023	IFC Appro...				

Associated issues

Issue ID	Issue name
10	Parking lot addition - 3

Associate to Change issue


Click the *number* link to view the associated issues. In the dialog box you can remove issues or return to the Associate to Change issue dialog box to manage issues.

Associated issues

Issue ID	Issue name	
2	Internal wiring repair 2	
1	Frame adjustments 1	

Associate to Change issue

To remove the issues, click the **Disassociate Change issue** icon, and then select **Disassociate from this step** or **Disassociate from all steps on this scope item**.

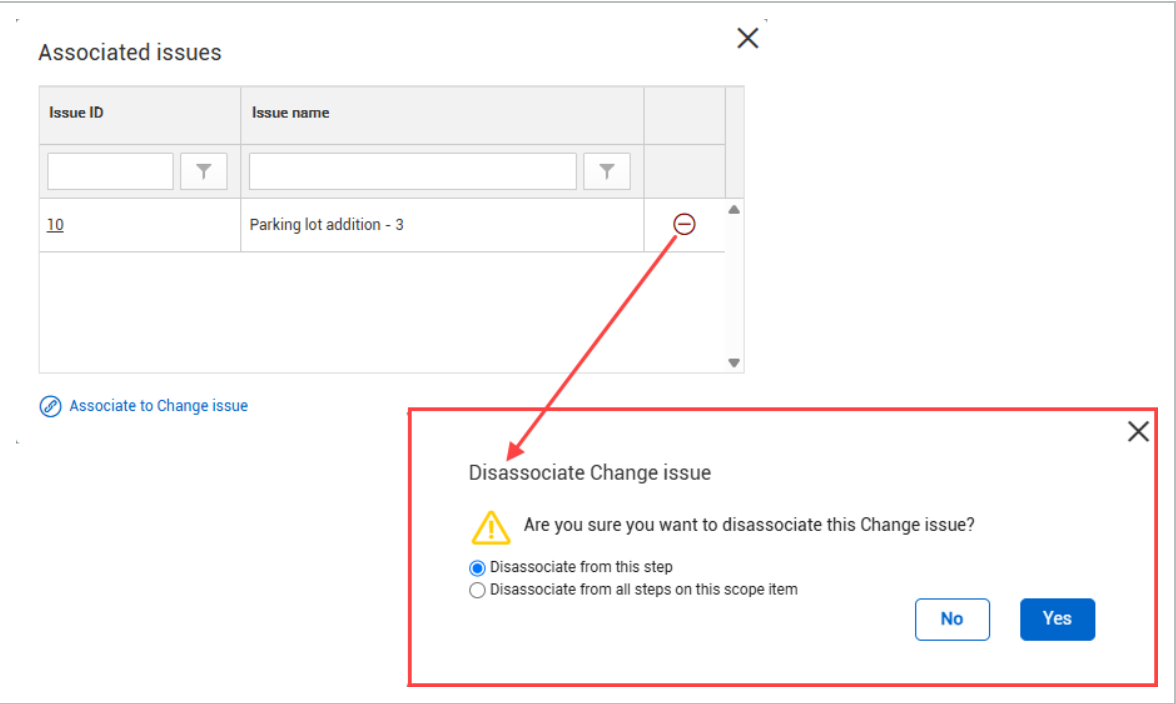

CHAPTER 4 – QUANTITY FORECASTING MODULE OVERVIEW

4.0.1 Summary

The Quantity forecasting module lets you maintain a continuous integration of quantities, man-hours, and schedule for design-build and EPC work. Quantity forecasting lets you configure a project to track quantities that are being driven by estimate, design, and construction phases on a project.

Quantity forecasting is integrated with the InEight Control and InEight Plan applications, which allows for seamless transition of data between the systems.

4.1 QUANTITY ITEMS

The Quantity items page contains the main grid for managing all quantity items and progressing quantities on a project.

The following image and table give an overview of each section of the Quantity items page:

1

2

QUANTITY ITEMS

ROLLUP VIEW

AUDIT LOG

5

3

4

6

7

Actions

ID	Description	UoM	Forecast (T0) qty	Discipline	Design element	Account code	Account code description	WBS phase code
3729367		LF	423.00	Electrical	Ductbank	81.03.08.016.02	Underground Duct b...	1005
3392370		CY	423.00	Grading	Mechanical & Electri...	51.18.02.002	Mechanical and Elec...	1005
3392366		PLS	122,784.00	Metals	Specialty Metals Wo...	62.99.02	Specialty and Uniqu...	1005
3392365		LF	122,784.00	Electrical	Grounding - Cable	81.30.02.002	Underground Groun...	1005
3392364		PLS	1,820.00	Electrical	Substation Bus - PLS	81.63.12	Substation Bus	1005
3392363		LF	2,350.00	Electrical	Overhead T/D String...	81.60.01.004.04	Overhead Transmiss...	1005
3391039		LF	41,272.00	Electrical	Wires and Cabling	81.09.02	Wire and Cable Pull...	1005
2510248	test	CY	403.00	Concrete	Place/Wet Finish/Cu...	61.06.02.006.08	Cast in Place Wall...	1005

Subtotals Count: 8

Overview - Quantity items page

Title		Description
1	Actions menu	Do any of the following: • Get Control unit rates • Run report • Lock and unlock scope • Quantity change notes
2	Quantity item buttons	Add, edit, and delete quantity items.
3	Hide archived	When a quantity item is set to archived and the toggle is set to <i>On</i> , the quantity item no longer loads nor shows in the grid to improve project load performance. You can make the archived items show by turning the Hide Archived toggle to <i>Off</i> . After turning the toggle to <i>Off</i> , the items marked as archived load. The toggle is set to <i>On</i> by default.
4	View	Select, save, rename, and delete views.
5	Upper right toolbar icons	• Data conflicts - Show whether conflicts exist. • Create Query Filters - Open the query builder. • Import and Export - Import and export sets of data. • Row density lets you adjust the spacing of grid rows • Find lets you search quantity items.
6	Quantity items	Grid showing quantity items and related information organized by column.
7	Column chooser	Select which columns are shown or hidden.

4.1.1 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.

4.2 ADD A QUANTITY ITEM

4.2.1 Summary

You can add a quantity item manually in the Quantity items page.

The Add quantity item slide-out panel contains the Details and Quantities tabs.

On the Details tab, the fields required to make a quantity item depend on how your project is set up. Whether each field is required or must have a unique value is set in the Fields and component integration subtab of Quantity forecasting project settings.

When a quantity item is added, and the quantity item is associated to a cost item, the quantity is sent to InEight Control. Any quantity where the UoM does not align between a cost item and a quantity item is not sent to Control.

On the Quantities tab, you can set the Quantity driver for the quantity item. The quantity driver designates which design stage drives the quantity item's forecast (TO) qty. When you select a stage as the quantity driver, the forecast (TO) qty is automatically updated with the quantity maintained on that stage. Design stages are used to group and collect quantities as the design changes. Design stages are created at the organization level and added at the project level.

You are not required to set the quantity driver when adding the quantity item, and can change it later. The quantity driver is set to CB qty by default. For more information, see [Quantity driver](#).


4.2.2 Considerations

You must have the permission Add quantity items.

4.2.3 Steps

To add a quantity item:

1. Click the **Add quantity item** button in the upper left. The Add quantity item slide-out panel opens.

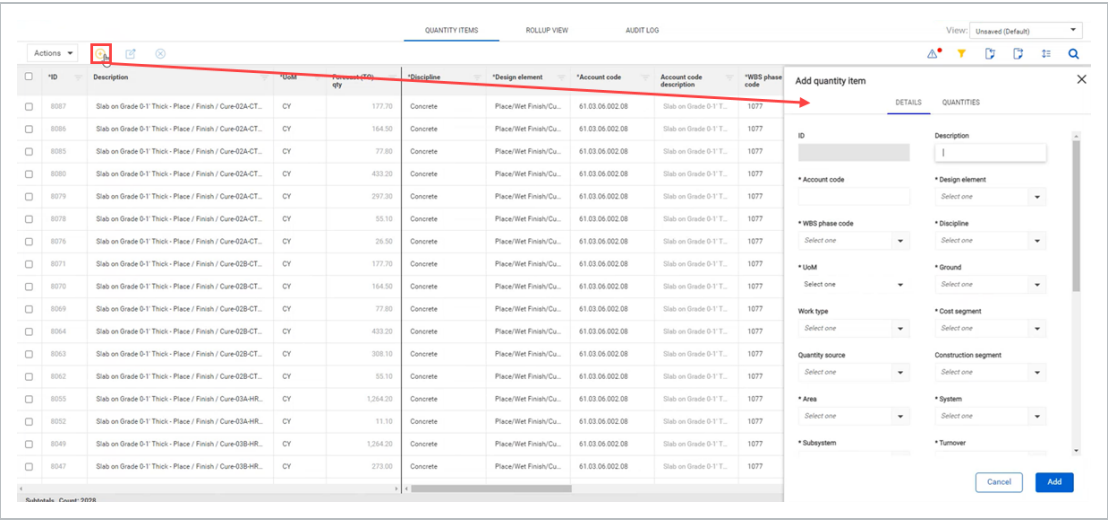

- 2. Fill in any required fields, as indicated by an asterisk.
- 3. Click **Add**.

4.3 PROJECT VALUES

Project values are standardized data configured in InEight Platform. Project values can be shared and used in Design. You can configure which project values to use for projects in the Settings, and then assign project values such as Area, Segment, System, Subsystem, Work classification, and others depending on your business requirements.

To assign project values go to the Add or Edit quantity item slide-out panel's **Project values** section.

Edit quantity item

DETAILS

NOTES

* Design element

Site Restoration - Acre

* WBS phase code

1006

* Discipline

Overhead

* UoM

Acre

* Ground

Under

* Work type

Direct

* Cost segment

Business Overhead

Quantity source

Construction

Construction work package

Select one

Deliverable package

Select one

Engineering work package

Select one

OB MHrs/Unit

CB MHrs/Unit

Design Complete

Include quantity in roll up calculation?

Include in schedule?

Archived?

Project values

* Area

13L

Construction commodity

Segment

Subsystem

System

Turnover packages

Quantities

Components

Observations

Cancel

Save

Select from the project value fields drop-down lists, and then click **Save**.


4.3.1 Project value status

When the status of a project value is changed to *Unavailable* in Platform, a yellow caution icon shows in the project value field for assigned values. The project value field in the quantity item’s slide-out

InEight Inc. | Release 26.7

Page 163 of 183

panel is highlighted red and shows *Project value is unavailable* below the value field.

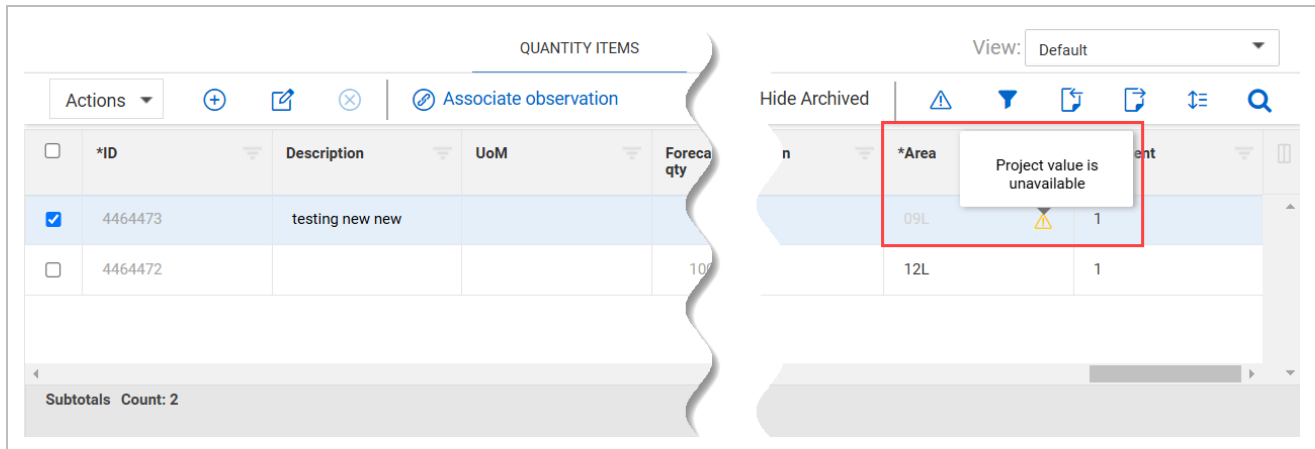


You can update the quantity item to an available project value in the quantity item slide-out panel. When you select to update the project value in the quantity item, only project values marked as available in Platform show in the drop-down list.

To save the quantity item, you must select an available project value .

To update to an available project value, select to edit the quantity item, and then select an available project value from the drop-down list.

Update a project value

1. Select the quantity item, and then click the **Edit quantity item** icon.
2. Select an available project value from the project value drop-down list, and then click **Save**.

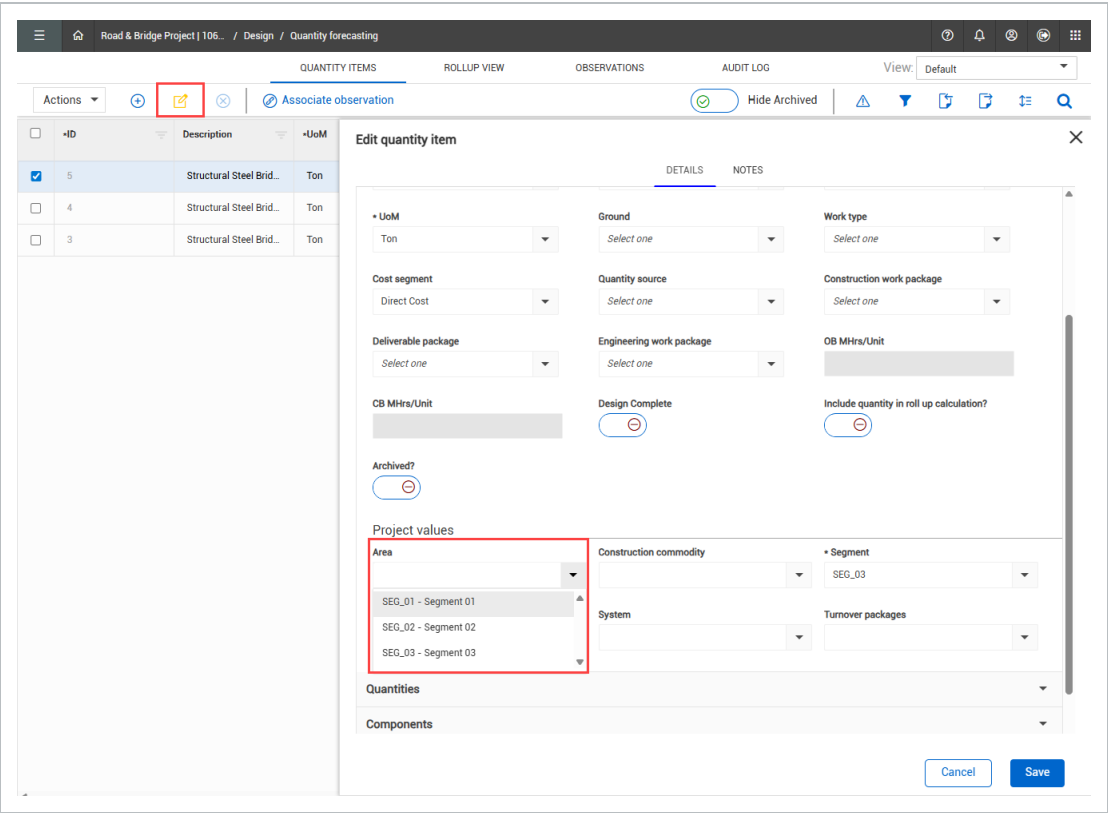

4.4 COMPONENTS SECTION

The components section of a quantity item shows the associated InEight Plan components. When project administrators enable the integration and configure the criteria for how Plan components associate to quantity items, Plan components are automatically associated to quantity items.

Edit quantity item

DETAILS

NOTES

Summary

Quantities

Components


Component ID	Component qty	Installed qty	Modified Date
Erect Structural Steel 03	415.00000	0.00000	11/25/2024 11:20:34 AM
Subtotals		415.00	

Cancel

Save

4.4.1 Component ID link

Click the **Component ID** link to open the component in Plan. A new tab opens where you can manage the component in Plan’s Quantity tracking module.

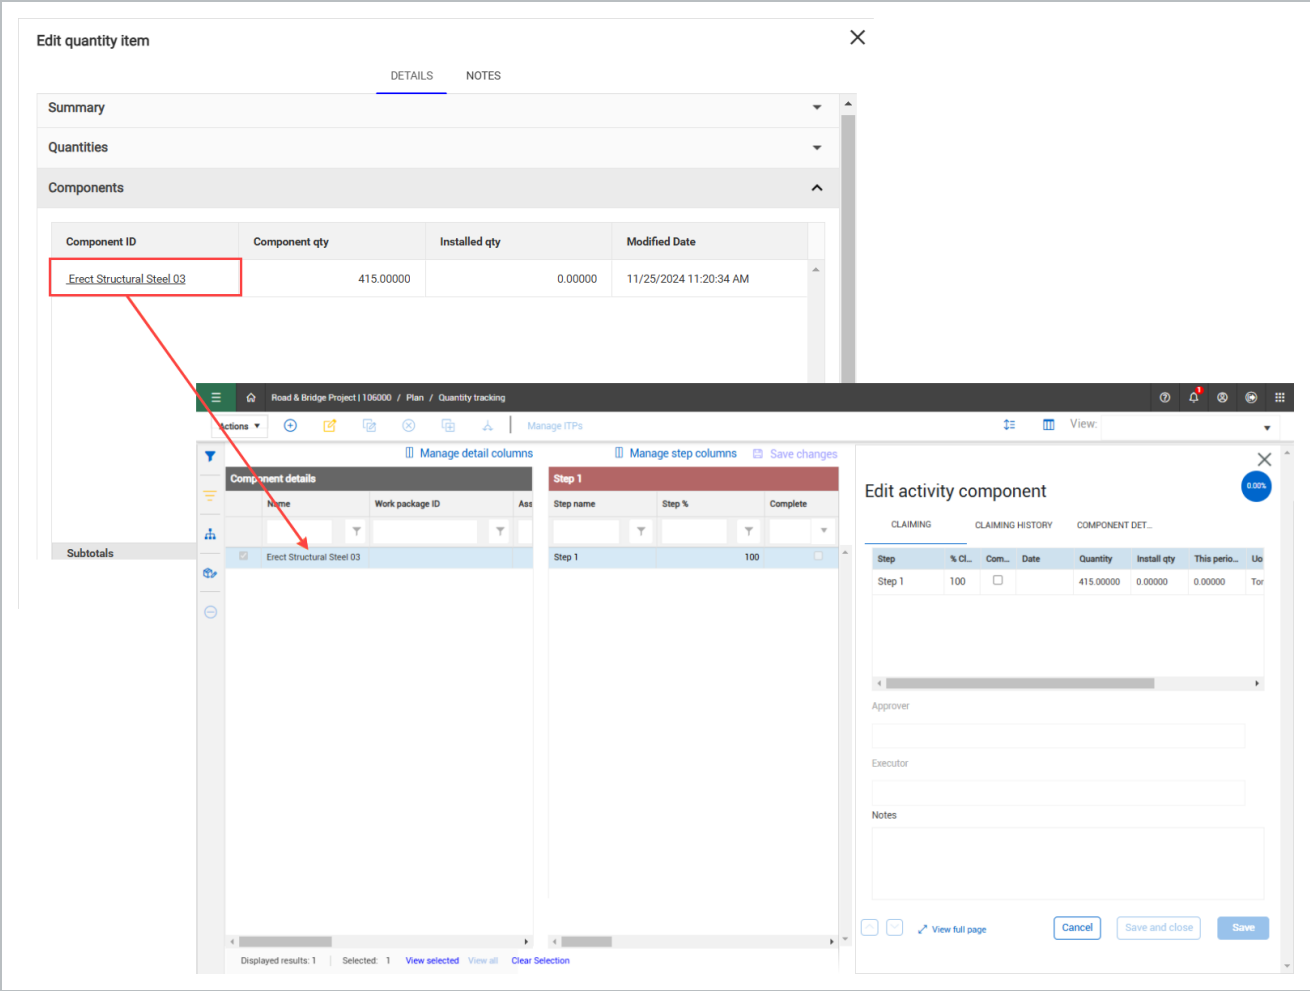

4.5 OBSERVATIONS SECTION

In the Observations section, you can view observations assigned to quantity items.

QUANTITY ITEMS

ROLLUP VIEW

OBSERVATIONS

AUDIT LOG

View:

Unsaved (Default)

Actions

Associate observation

Hide Archived

☐	*ID	Description	*UoM
☐	4464483		Gal
☒	2200248		LF
☐	2200247		Ea
☐	2200246		LF
☐	2200245		LF
☐	2030534		LF
☐	2030533		Ea
☐	2030532		Ea
☐	2030531		Ea
☐	2030530		Ea
☐	2030529		Ea
☐	2030528		Ea
☐	2030527		Ea

Subtotals Count: 13,142

Edit quantity item

DETAILS

NOTES

Summary

Quantities

Components

Observations

Observation id	Observation name	Observation date
<u>704</u>	Failed gauge testing inside	10/16/2024
<u>703</u>	Hardness testing verification	10/16/2024
<u>665</u>	Excavation slope observation	09/18/2024
<u>664</u>	Incorrect quantities in materials	09/17/2024
<u>662</u>	Wrong construction size in materials	09/17/2024


Cancel

Save

You can view the observation ID, observation name, and observation date.

4.5.1 Observation ID link

Click the **Observation ID** link to open the observation in the Observations tab. A new tab opens where you can manage the observation.

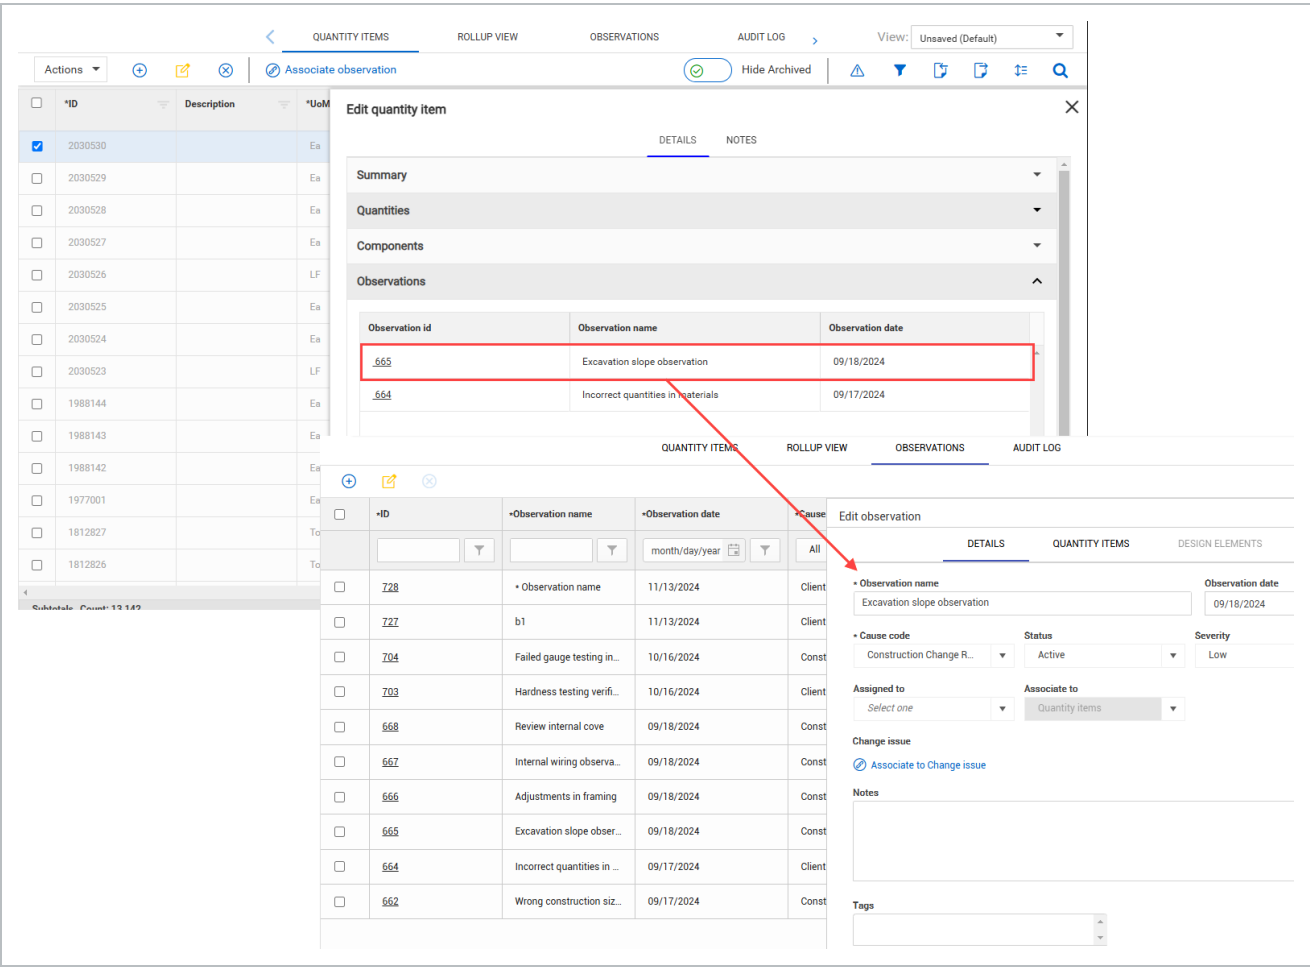

4.6 QUANTITY DRIVER

4.6.1 Summary

The quantity driver designates which design stage drives a quantity item’s forecast (TO) qty. Design stages are used to group and collect quantities as the design changes. Design stages are created at the organization level and added at the project level.

You can update the quantity driver using the Edit quantity item slide-out panel, the Quantity items grid, or the import process. When you select a stage to be the quantity driver, the Forecast (TO) qty field is automatically updated and a blue pushpin icon is added to the design stage.

When the quantity is updated and the quantity item is associated to a cost item, the quantity is sent to InEight Control. Any quantity where the UoM does not align between a cost item and a quantity item is not sent to Control.

You can set the quantity driver to be the CB quantity, any of your project's design stages, or component quantity. Component quantity is the sum of quantities of components from InEight Plan associated to the quantity item.

ID	Description	Unit	Forecast (TO) qty	Quantity driver	CB qty	20% Qty	90% Qty	Design Complete	Component Qty	Installed qty
45509		CY	158.00	Component Qty				☒	158.00	0.00
45505		Ex	24.00	Component Qty				☒	24.00	0.00
45504		LF	19.37	Component Qty				☒	19.37	0.00
45503		LF	13.73	Component Qty				☒	13.73	0.00
45502		Ex	1,905.00	90% Qty	0.00		☒ 1,905.00	☐	1,905.00	0.00
45501		SP	20.16	Component Qty				☒	20.16	0.00

4.6.2 Considerations

- You can select Component qty as the quantity driver only if the Design Complete check box is selected for the quantity item.
- You can set a stage as the quantity driver even if no quantity is maintained on that stage. In this case, the Forecast (TO) qty field is set to 0.00.

4.7 DATA EXPORT

4.7.1 Summary

You can export quantity items in the Quantity forecasting > **Quantity Items** page using the export tool. You can export all items or selected items using the tool.

After you start the export, the Audit log > **Export History** page opens to show you the export status and history information. The export status shows as *In progress*. The export processes run in the background, and when completed, the status changes to *Completed* and the Download export file icon becomes available.

You can then download the file by clicking the **Download export file** icon. The file is downloaded as a Microsoft Excel file to your Downloads folder.

4.7.2 Considerations


- You must have View quantity forecasting settings permission.
- Other users of Design with the same permission can download the file.
- The file will be available for 60 days. After 60 days, the Download export file icon is disabled.

4.7.3 Steps


To export all quantity items:

- 1. Click the **Export quantity items** icon, and then select **Data export**.

To export selected items, click the check box next to the item or items, and then select **Data export**.

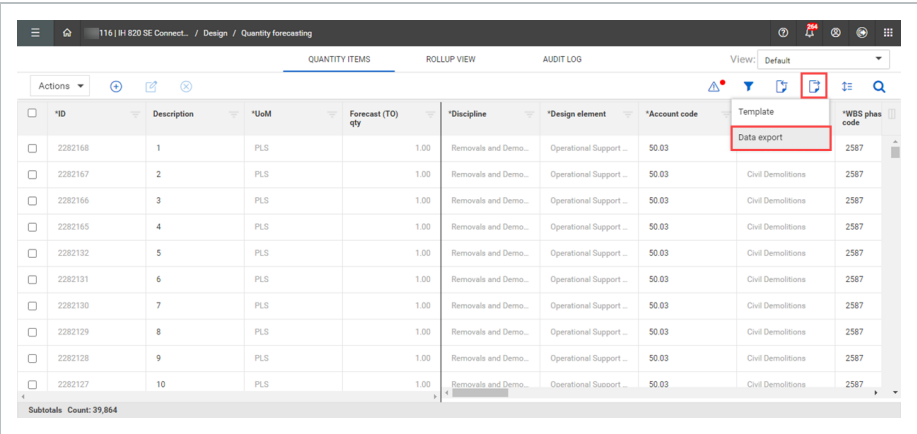

The Audit log > **Export History** page opens.

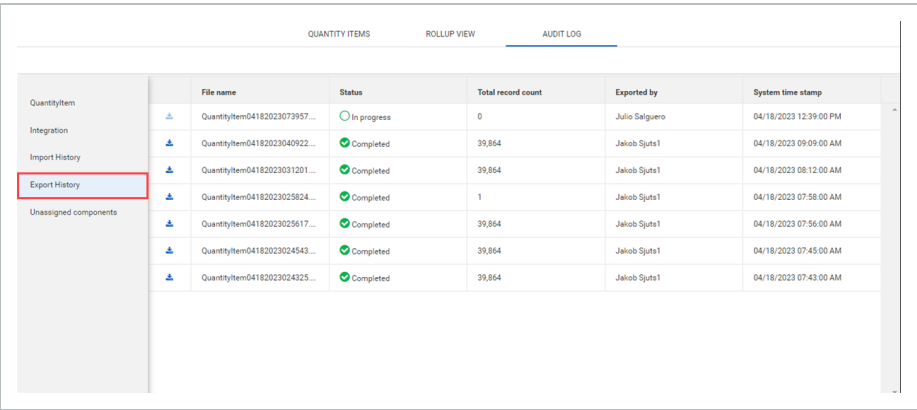

- 2. In Export History, click the **Download export file** icon to download the file.

4.8 ACTIONS

In the Quantity Items page, you can perform various actions on a project. The table and image below shows the available actions:

Overview - Actions

Action	Description
Get Control unit rates	Update the OB MHrs/Unit, CB MHrs/Unit, CE MHrs/Unit, and Forecast Remaining MHrs/Unit on the Quantity Items with current rates from InEight Control. For more information, see Get Control unit rates.
Run report	Run the Design Activity Report in a new tab. For more information, see Run report.
Get Plan components	Sync the components from InEight Plan to Design and then have the system auto-associate the Plan components to the Quantity Items in Design based on the Component Rollup configured in the project settings.For more information, see Get Plan components.
Lock and Unlock scope	Lock and unlock scope on a project.A warning will show when scope is unlocked that reads " <i>Scope is unlocked</i> ". For more information, see Lock and unlock scope.

4.8.1 Considerations

- You must have applicable permissions in Quantity forecasting.
- OB MHrs/Unit, CB MHrs/Unit must be setup in Project settings.

4.9 GET CONTROL UNIT RATES

You can update the OB MHrs/Unit, CB MHrs/Unit, CE MHrs/Unit, and Forecast Remaining MHrs/Unit for quantity items with current rates from InEight Control. This lets you use the latest budget unit rates from Control multiplied by the latest forecasted Design quantity to understand the impacts to man hours on the project.

QUANTITY ITEMS											
ROLLUP VIEW											
AUDIT LOG											
View: Default											
Actions	Forecast (TO) qty	Discipline	Design element	Account code	Account code description	WBS phase code	WBS description	OB qty	Quantity driver	CB	
Get Control unit rates									Component Qty		
Run report									CB qty		
Get Plan components									Component Qty		
Unlock budget									CB qty		
10101			Backfill Flatwork								
10154			test component	00	Overhead						
10153			test								

With Quantity Items tagged with a WBS from Control, the action lets you select which cost items to update the unit rates in Design. Control then shows the current unit rate applied in Design, the pending unit rate from Control, when the unit rate was last updated, and who performed the last update. Unit rates are never updated automatically with InEight Control unit rates. You must go through the Get Control unit rates action to update the rate applied to a Quantity Item.

4.9.1 MHrs Delta columns

The MHrs/Unit delta and MHrs Delta columns let you see any MHrs/Unit or MHrs change before applying the Pending Control Unit Rate. This is a read-only field that shows the difference between the total MHrs of quantity items with like WBS calculated using the current Quantity Forecasting rate and the total MHrs calculated using the Pending Control rate.

Get CE MHrs/Unit

1 Select Cost Items 2 Get Unit Rates

WBS phase code	Description	Current Rate	Pending control rate	Manual Rate	MHrs/Unit Delta	MHrs Delta	Last update	Updated by
1007	KIE-Design ...	39.34769230...	39.34769230769		0.00000000...	0.00000000...	03/22/2024...	Mamatha R
1013	KIE-Project ...	38.12413793...	38.12413793103		0.00000000...	0.00000000...	02/09/2024...	Jakob Sjuts1
1014	KIE-Enginee...	37.66146993...	37.66146993318		0.00000000...	0.00000000...	02/09/2024...	Jakob Sjuts1
1016	QTO-Manag...	0.00000000000	0.00000000000		0.00000000...		02/09/2024...	Jakob Sjuts1
1017	QTO-Demo/...	0.00000000000	0.00000000000		0.00000000...	0.00000000...	02/09/2024...	Jakob Sjuts1

Cancel Back Update

The Manual Rate column lets you specify a manual CE MHrs unit rate for a WBS phase code, while still allowing other WBS phase codes to function off the unit rate from Control.

Get CE MHrs/Unit

1 Select Cost Items 2 Get Unit Rates

WBS phase code	Description	Current Rate	Pending control rate	Manual Rate	MHrs/Unit Delta	MHrs Delta	Last update	Updated by
1007	KIE-Design ...	39.34769230...	39.34769230769	45	5.65230769...	0.00000000...	02/09/2024...	Jakob Sjuts1
1013	KIE-Project ...	38.12413793...	38.12413793103		0.00000000...	0.00000000...	02/09/2024...	Jakob Sjuts1
1014	KIE-Enginee...	37.66146993...	37.66146993318		0.00000000...	0.00000000...	02/09/2024...	Jakob Sjuts1
1016	QTO-Manag...	0.00000000000	0.00000000000		0.00000000...		02/09/2024...	Jakob Sjuts1
1017	QTO-Demo/...	0.00000000000	0.00000000000		0.00000000...		02/09/2024...	Jakob Sjuts1

Cancel Back Update

4.9.2 Get FC Remaining MHrs/Unit - Manual Rate column

The Manual Rate column in the Get FC Remining MHrs/Unit dialog box. This column lets you specify a manual FC Remaining unit rate for a WBS phase code, while still allowing other WBS phase codes to function off the unit rate from Control.

Get FC Remaining MHrs/Unit

1

2

Select Cost Items

Get Unit Rates

WBS phase code	Description	Current Rate	Pending control rate	Manual Rate	MHrs/Unit Delta	MHrs Delta	Last update	Updated by
1006	Mech/Elec ...	0.08493639466	0.00000000000		-0.0849363...	0.00000000...	05/04/2022...	Mason Green

Cancel

Back

Update


4.9.3 Considerations

- You must have Level 3 – Account Admin permissions in InEight Platform or a role with the applicable permissions in Quantity Forecasting.
- Get OB MHrs/Unit and CB MHrs/Unit options must be setup in Project settings.

4.10 GET PLAN COMPONENTS

You can sync the components from InEight Plan to Design to let your Quantity Item Forecast (TO) quantity to be driven by the component quantity directly from Plan. The system automatically associates the integrated Plan components to the quantity items in Design based on the project settings for required and unique attributes and project values.


To navigate to Get Plan components, go to the projects home page > Design > Quantity forecasting > Quantity Items > **Actions**.

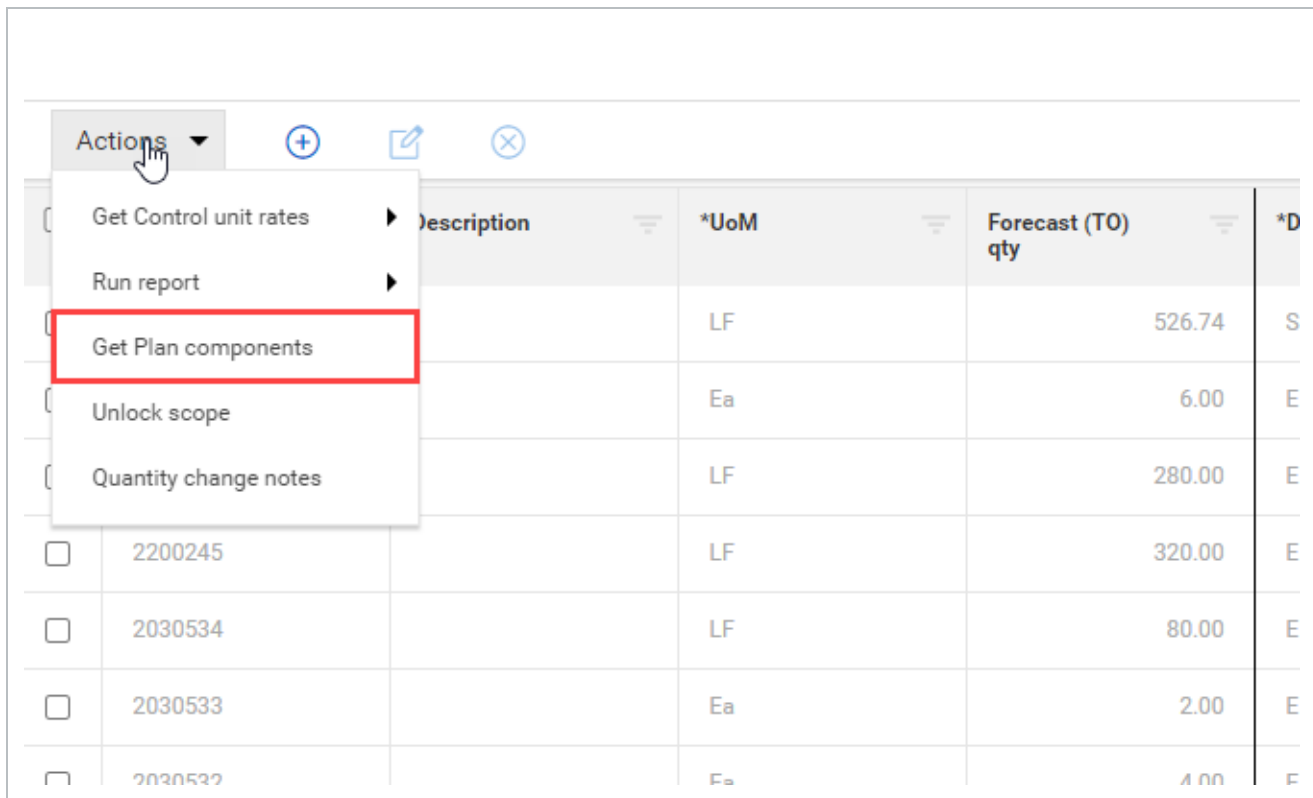

The screenshot shows a table with columns: *ID, Description, *UoM, Forecast (TO) qty, and *D. A dropdown menu is open from the 'Actions' button, with 'Get Plan components' highlighted by a red rectangle. Other options in the menu include 'Get Control unit rates', 'Run report', 'Unlock scope', and 'Quantity change notes'.

*ID	Description	*UoM	Forecast (TO) qty	*D
		LF	526.74	S
		Ea	6.00	E
		LF	280.00	E
☐ 2200245		LF	320.00	E
☐ 2030534		LF	80.00	E
☐ 2030533		Ea	2.00	E
☐ 2030532		Ea	4.00	E

A banner shows when the sync is in progress after you select **Get Plan components**.



The screenshot shows a banner at the top that reads 'Component sync in progress.' Below the banner, the table has columns: *ID, Description, *UoM, Forecast (TO) qty, *Discipline, *Design element, *Account code, Account code description, and *WBS phase code. The first row shows data for ID 3422429.

*ID	Description	*UoM	Forecast (TO) qty	*Discipline	*Design element	*Account code	Account code description	*WBS phase code
☐ 3422429	NNN	Wk	600.00	Operational Support	Dust Control	30.06.32.004	Support Services - D...	2930

During the sync, two things occur:

- As new or updated components are brought into Design, their attributes are compared to what is defined in the project settings, and then associations that occurred are created or updated.
- The quantity item's quantity is updated based on the new quantity that is brought over from Plan, and then update any Forecast (TO) quantity where Component Qty driver is set.

These are read-only fields that show the summed amounts for the quantity and installed quantity of components assigned to the quantity item.. You can view components assigned to a quantity item by opening the Edit quantity item slide-out of a quantity item, and then selecting the **Components** tab or by selecting the link available on the Component Qty amount in the grid.

QUANTITY ITEMS

ROLLUP VIEW

AUDIT LOG

View: Default

Actions

ID	Description	UoM	Forecast (TO) qty	0% Qty	90% Qty	Design Complete	Component Qty	Installed qty
45609		CY	158.00				158.00	0.00
45605		Ea	24.00				24.00	0.00
45604		LF	19.37				19.37	0.00
45603		LF	13.73				13.73	0.00
45602		Ea	1,905.00		1,905.00		1,905.00	0.00
45601		SF	20.16				20.16	0.00
45600		SF	10.50				10.50	0.00
45599		SF	10.50				10.50	0.00
45598		SF	56.50				56.50	0.00

Edit quantity item

DETAILS

QUANTITIES

COMPONENTS

NOTES

Component ID	Component qty	Installed qty	Modified Date
Embed Concrete Heating/Inboard EC-300 (1) G.U.	4.00000	0.00000	11/21/2019 12:33:19 PM
Embed Concrete Heating/Inboard EC-300 (1) G.U.	11.00000	0.00000	11/21/2019 12:33:19 PM
Embed Concrete Heating/Inboard EC-300 (1) G.U.	23.00000	0.00000	11/21/2019 12:33:19 PM
Embed Concrete Heating/Inboard EC-300 (1) G.U.	19.00000	0.00000	11/21/2019 12:33:19 PM
Subtotals	158.00		

4.10.1 Considerations

- You must have applicable permissions in Quantity forecasting.
- The Get Plan components action is available when Enable component integration with Plan is enabled and configured in the project settings > Quantity forecasting > Component integration > **Plan component integration**.

4.11 LOCK AND UNLOCK SCOPE

On the Quantity Items page, you can lock and unlock the scope of a project. When you lock the scope, the OB Qty and OB Man Hour fields are disabled, and the design stages are enabled to allow stage quantities to be maintained and updated. Locking scope maintains a snapshot of your initial estimate quantity to help in benchmarking post-project completion.

When you unlock the scope, the OB Qty and OB Man Hour fields are enabled, and all the design stages fields are disabled.

To lock or unlock the scope from the Quantity Items page, click **Actions**, and then select **Unlock Scope** or **Lock Scope** from the drop-down list.

QUANTITY ITEMS

ROLLUP VIEW

AUDIT LOG

View: Unsaved (Default)

Actions

Get Control unit rates

Run report

Get Plan components

Unlock scope

Quantity

Test Bug 23619871

Action will enable OB Qty and OB Mhrs/Unit fields and disable Design stage fields

	Description	*UoM	Forecast (TO) qty	OB qty	OB Mhrs	CB Mhrs	CE Mhrs	Fre
	NNN	Wk	600.00				156.08	
	Test Bug 23619871	SY	0.00				0.00	
			80.00				20.81	
☐	2200248	LF	526.74				559.00	
☐	2200247	Ea	6.00				2.16	
☐	2200246	LF	280.00				8.40	
☐	2200245	LF	320.00				9.60	
☐	2030533	Ea	2.00				4.75	
☐	2030532	Ea	4.00				9.50	
☐	2030531	Ea	2.00				4.75	
☐	2030530	Ea	2.00				4.75	
Subtotals Count: 13,144				1,857,409.05	1,846,599.13		2,165,654.28	

4.11.1 Considerations

- The scope is unlocked by default for new projects.
- A warning banner shows when the scope is unlocked that reads “The scope is unlocked. Scope must be locked to add design quantities.”
- To lock the scope, you must have the permission Lock project.
- To unlock the scope, you must have the permission Unlock project.

4.12 OBSERVATIONS

When changes occur in the design’s scope, you can create observations to capture the changes and associate them to quantity items or design elements. Observations lets you document changes throughout the life of the project to capture details of those changes.

The following table shows items you can add to an observation:


Observations

Field	Description
Name	Enter a required observation name.
Date	Enter a required observation date.

Observations (continued)

Field	Description
Cause code	Select a required cause code from the list.
Status	Select an observation status of <i>Active</i> , <i>Removed</i> , or <i>Closed</i> .
Severity	Select a severity of <i>Low</i> , <i>Medium</i> , or <i>High</i> .
Assign to	Assign a user to the observation.
Associate to	Associate the observation to quantity items or design elements. You can associate multiple quantity items or design elements. Quantity items must first be associated in the Quantity items page.
Change issue	When integrated with Change, you can link the observation to a InEight Change issue.
Notes	Add notes that relate to the observation.
Tags	Select tags related to the observation.

The following image shows the Observation tab with an existing observation opened:

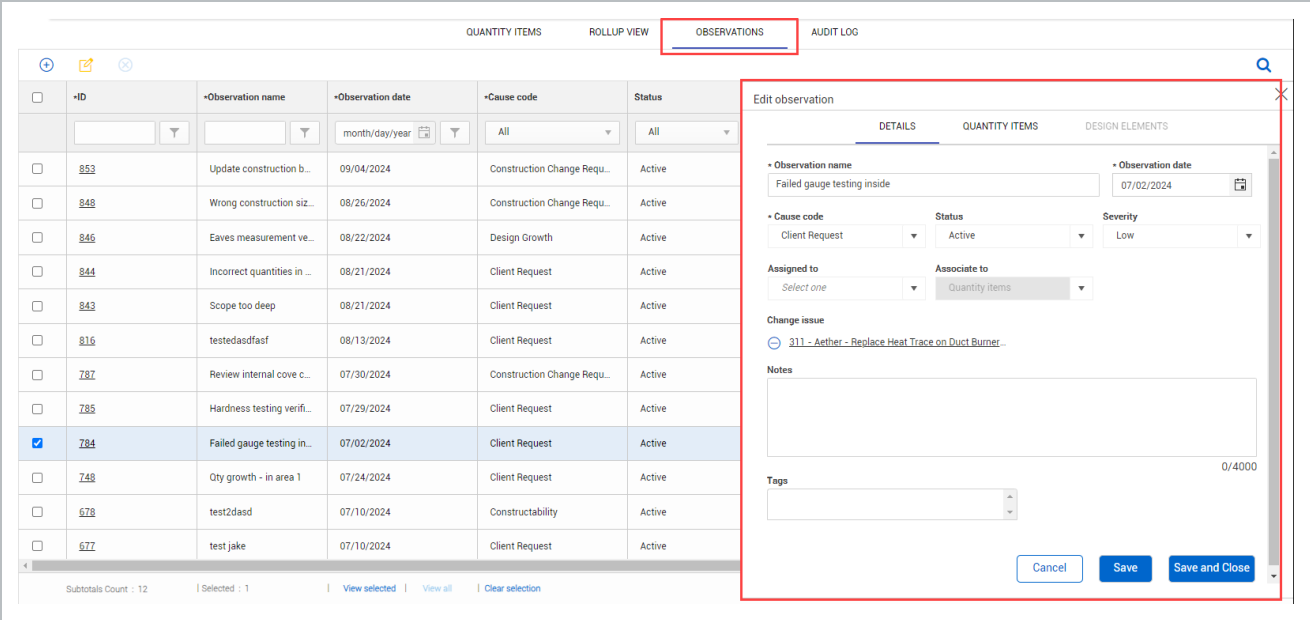

4.13 ADD OBSERVATIONS

You can add observations on the Observations page. The Add observation slide-out panel contains the Details, Quantity Items, and Design Elements tabs.

On the Details tab, in the Associate to field, you can select Quantity items or Design elements. When you select Quantity items, the Quantity Items tab is made available. When you select Design elements, the Design Elements tab is made available. The observation name must have a unique value.

Add an observation

1. Click the **Add observation** icon.
2. In the **Add observation** slide-out panel, enter the required and optional information
3. Select **Quantity items** or **Design elements** in the **Associate to** field.
 - Quantity items or design elements can be added to the observation after the observation is created.
4. Click **Add** to add the new observation.

4.13.1 Considerations

- To add quantity items, you must first add the observation, and then associate quantity items in the Quantity items page.
- You can add design elements after the observation is added.

4.14 ASSOCIATE TO QUANTITY ITEMS

You can associate multiple quantity items to an observation in the Quantity Items page.

4.14.1 Considerations

You must first add the observation and have Quantity items selected in the Associate to field to associate quantity items in the Quantity Items page.

Associate quantity items to an observation from the Quantity Items page

1. In the Quantity Items page, select the quantity items you want to associate to the observation.
2. Click **Associate observations**. The Associate observations slide-out panel opens.

The screenshot shows the 'Quantity Items' page with a table of items. Two items are selected: 1812827 and 1812826. The 'Associate observations' slide-out panel is open, showing a table of observations to associate with the selected items.

ID	Description	UoM	Forecast (TO) qty	Discipline
☐	1988142	Ea	0.00	Electrical
☐	1977001	Ea	0.00	Electrical
☒	1812827	Ton	0.00	Metals
☒	1812826	Ton	0.00	Metals
☐	1804601	LF	0.00	Electrical
☐	1804600	LF	0.00	Electrical
☐	1804599	Ea	0.00	Electrical
☐	1804598	Ea	0.00	Electrical
☐	1804489	LF	0.00	Electrical
☐	1804488	LF	0.00	Electrical

Subtotals Count: 13,144

Associate observations

Quantity items selected : 2
[View selected](#)

Select an observation to associate to the selected quantity items.

Observation name	Start date	Cause code	Note
☐	Wrong construction siz...	08/26/2024	Construction Cha...
☐	Eaves measurement ve...	08/22/2024	Design Growth
☐	Incorrect quantities in b...	08/21/2024	Client Request
☐	Scope too deep	08/21/2024	Client Request
☐	Failed gauge testing ins...	07/02/2024	Client Request

[Cancel](#) [Save](#) [Save and Close](#)

3. Select the observations to associate the quantity items to, and then click **Save**.

Associate quantity items to an existing observation

You must first associate quantity items to your observation in the Quantity Items page.

1. In the Observation page, click an observation **ID**.
2. Select the **Quantity Items** tab.
3. Select the quantity items you want to associate to the observation, and then click **Save**.

To remove quantity item associations, select the quantity items, and then click **Remove association**.

4.15 ASSOCIATE TO DESIGN ELEMENTS

You can associate multiple design elements to an observation.

4.15.1 Considerations

You must add the observation and have Design elements selected in the Associate to field to associate design elements.

Associate design elements to an existing observation

1. In the Observations page, click an observation **ID**.
2. Select the **Design elements** tab.
3. Select discipline, design element, UoM, and observation quantity to associate to the observation.

Edit observation

DETAILS

QUANTITY ITEMS

DESIGN ELEMENTS

Search...

	*Discipline	*Design element	*UoM	*Obs
	Aggregates and Paving	Concrete Paving - Reinfo...	Ea	+
	All	All	All	
☐	Building	BOP Flushes	Ea	−
☐	Bulk Commodities	Aux Boiler Flushes	Ea	−
☐	Bulk Commodities	Aux Boiler Misc Mech Checks	Ea	−
☐	Civil Utilities	Aux Boiler Misc Mech Checks	Ea	−
☐	Engineered Equipment	Aux Boiler Flushes	Ea	−

Cancel

Save

Save and Close

4. Click the **add Associate observation** icon. You can add additional design elements to associate the observation to.
5. Click **Save**.

To remove design element associations, select the design elements, and then click **Remove association**.

4.16 VIDEO INDEX

This is an index of video transcript pages. For the full video gallery, see the [main video page](#).

- [Claiming Scheme Milestones video](#)
- [Configuring Work Packages video](#)
- [Document-Claiming-video](#)
- [Engineering Settings video](#)
- [How to Claim Progress video](#)
- [How to Create a Quantity Item video](#)
- [How to Create a Scope Item video](#)
- [Integrate Design EWP's with Plan video](#)
- [Introduction to InEight Design video](#)
- [InEight Document Integration video](#)
- [Observations video](#)
- [Quantity Forecasting Settings video](#)
- [Scope Item - Change Issue Integration video](#)
- [Scope Items Bulk Editing video](#)
- [Undo Claiming in Design video](#)
- [Update Quantity and Man Hours video](#)
- [Updating Quantities video](#)
