

PROGRESS USER GUIDE

Daily Plan Mobile



Release 25.7
Last Updated: 22 August 2025

Information in this document is subject to change without notice. Companies, names and data used in examples are fictitious.

Copyright ©2025 by InEight. All rights reserved. No part of this document may be reproduced or transmitted in any form or by any means, electronic or mechanical, for any purpose, without the express permission of InEight.

Microsoft Windows, Internet Explorer and Microsoft Excel are registered trademarks of Microsoft Corporation.

Although InEight Progress has undergone extensive testing, InEight makes no warranty or representation, either express or implied, with respect to this software or documentation, its quality, performance, merchantability, or fitness for purpose. As a result, this software and documentation are licensed “as is”, and you, the licensee are assuming the entire risk as to its quality and performance. In no event will InEight be liable for direct, indirect, special, incidental or consequential damages arising out of the use or inability to use the software or documentation.

Release 25.7
Last Updated: 22 August 2025

This page intentionally left blank.

INEIGHT PROGRESS

- DAILY PLAN MOBILE

CONTENTS

1.1 InEight Progress Overview	11
1.1.1 InEight Progress Daily Planning Phases	11
1.1.2 Daily Plan Work Flow	12
1.1.3 InEight Control Integration	13
1.1.4 Daily Planning	14
1.1.5 Daily Execution	15
1.1.6 Daily Approval	15
1.1.7 Work Flow Beyond InEight Progress	16
1.1.7.1 Hours	16
1.1.7.2 Quantities and Costs	16
2.1 Mobile Overview	19
2.1.1 Login	19
Log into InEight Progress	19
2.1.2 Kiosk Mode	20
2.1.2.1 Kiosk Workflow	21
2.1.2.2 Component Search	23
2.1.3 Project List	23
2.1.4 Plan List	24
2.2 Navigate Daily Planning	26
2.2.1 Overview	26
2.2.2 Time Sheet	27
2.2.3 Quantities	29
2.2.4 Notes/Issues	31
2.2.5 Productivity	33
2.2.6 Submit & Sync	34
2.3 Navigate Execution	35
2.3.1 Plan List	36
2.3.2 Overview	36
2.3.3 Time Sheet	38
2.3.4 Quantities	39
2.3.5 Notes/Issues	41
2.3.6 Productivity	43

2.3.7 Sign Out	44
2.3.8 Submit and Sync	46
2.4 Navigate Approval	47
2.4.1 Plan List	47
2.5 Data Sync	49
2.6 Attachments on Mobile	50
2.6 Step by Step 1 – Add an attachment on mobile	50
2.6 Step by Step 2 – View an attachment on mobile	50
2.7 Daily Plan from Scratch	51
2.7.1 Plan Creation	53
2.7.1.1 Daily Plan ID	55
2.7.1.2 Overview Tab	56
2.7.2 Time sheet Tab	57
2.7.2.3 Add Tasks	57
2.7.2.4 Add Employees and Equipment	58
2.7.2.5 Add vendors	60
2.7.2.6 Temporary Employees and Equipment	60
2.7.2.7 Add Hours	61
2.7.2.8 Apply Hours to Selected Employees	62
2.7.2.9 Additional Options	63
2.7.3 Quantities Tab	64
2.7.3.10 Components	65
2.7.3.11 Planned Quantity	66
2.7.3.12 Contracts	67
Add a Contract to a Daily Plan	68
2.7.3.13 Contract components	68
Add a Contract Component to a Daily Plan	69
2.7.4 Planning Slide-Out	69
2.7.5 Notes/Issues Tab	71
2.7.5.14 Tags and Associations	72
2.7.5.15 Adding and Editing a Picture	73
2.7.6 Productivity Tab	75
2.7.7 Submit and Sync Button	76
2.7.8 Create a Plan from Scratch Walk Through	77
Create a Daily Plan from Scratch	77
2.8 Daily Plan from Copy	85
2.8.1 Create a Plan from Copy	86
Create a Daily Plan from Copy	86
2.9 Plan Review	88

2.9.1 Overview	90
Review Daily Plan Overview Tab	93
2.10 Input Actuals	95
2.10.1 Time sheet Tab	95
2.10.1.1 Remove unused tasks and resources	98
2.10.2 Quantities Tab	99
2.10.3 Notes/Issues Tab	100
2.10.3.2 Send Issue to InEight Change	101
2.10.4 Productivity Tab	102
2.10.5 Sign In/Sign Out Tab	103
2.10.5.3 Sign In Subtab	103
Shift Start Time	104
Employee Sign-in	104
Sign-in on Behalf of Employee	105
Questions	105
2.10.5.4 Breaks Subtab	106
2.10.6 Crew Break Hours	106
Shift Start/End Time	108
2.10.6.5 Sign Out Subtab	108
Shift Start/End Time	109
2.10.6.6 Employee Sign-out	110
2.10.6.7 Sign-out on Behalf of Employee	110
2.10.6.8 Client Sign-out	110
2.10.6.9 Questions	110
2.10.6.10 Time sheet Summary	111
Input Actuals	113

STEP-BY-STEP PROCEDURES

Log into InEight Progress 19

2.6 Step by Step 1 – Add an attachment on mobile 50

2.6 Step by Step 2 – View an attachment on mobile 50

Add a Contract to a Daily Plan 68

Add a Contract Component to a Daily Plan 69

Create a Daily Plan from Scratch 77

Create a Daily Plan from Copy 86

Review Daily Plan Overview Tab 93

Input Actuals 113

EXERCISES

This page intentionally left blank.

INEIGHT PROGRESS


- DAILY PLAN MOBILE

1.1 INEIGHT PROGRESS OVERVIEW

InEight Progress is one of the applications within the InEight portfolio of products. It is an integrated electronic time, equipment and quantity collection tool as well as a daily field log. The InEight Progress solution includes three submodules: Daily Planning, Weekly Time sheet and Time center. The Weekly Time sheet and Time center solutions are covered in the Progress – Advanced User Guide. This Guide will cover the Daily Planning portion of InEight Progress.

1.1.1 INEIGHT PROGRESS DAILY PLANNING PHASES

Daily planning is broken down into three distinct phases in the application: Planning, Execution, and Approval.

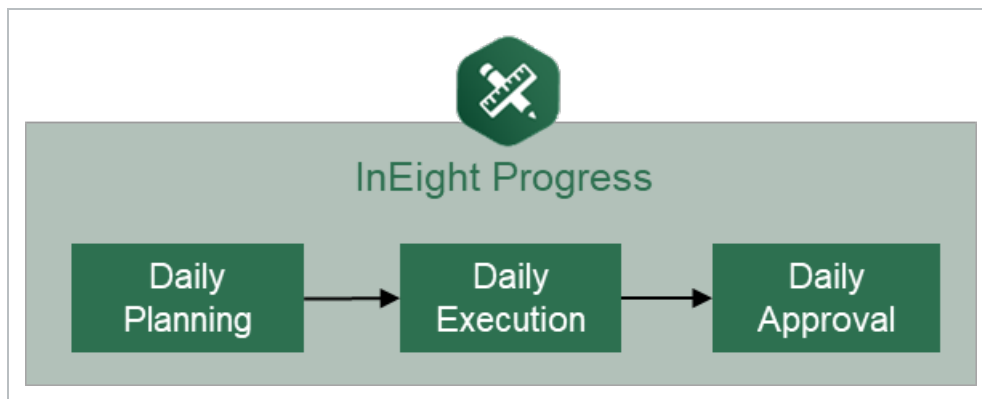


A daily plan is created by a project member to specify the tasks to be completed by a given crew, and to ensure productivity targets are met. Budget, quantity, safety, quality and other details are entered during the Planning phase to provide streamlined communication from the office to the field. Once the planner, typically a superintendent, field engineer or indirect supervisor is satisfied with the daily plan details and planned productivity, they will submit the plan to the Execution Phase.

In the Execution Phase, a project member takes the daily plan out in the field and references it throughout the day. As work is completed, the project member enters actual hours worked for employees and equipment. He or she also enters installed quantities, notes/issues and/or pictures to document issues and reviews the overall productivity. By claiming installed quantities and entering actual hours worked, the project member can view productivity in real-time. Once all employees have reviewed their hours worked and signed out of the application, the daily plan is submitted for approval.

In the Approval Phase, a project member reviews the actual tasks, employees, equipment, hours, quantities and productivity for the plan. In this phase, the hours and/or quantities can be approved as is, or if the approver would like something changed, the plan can be edited or sent back to the Execution Phase. The approver can approve the hours submitted, the quantities submitted or both. Approving the hours will send them to payroll for processing and approving the quantities will send them to the quantity tracking module of InEight Plan which syncs directly with InEight Control.

1.1.2 DAILY PLAN WORK FLOW

For all phases of the Daily Planning Process, InEight Progress Mobile communicates directly with the InEight Progress Web application, as shown in the diagram below:

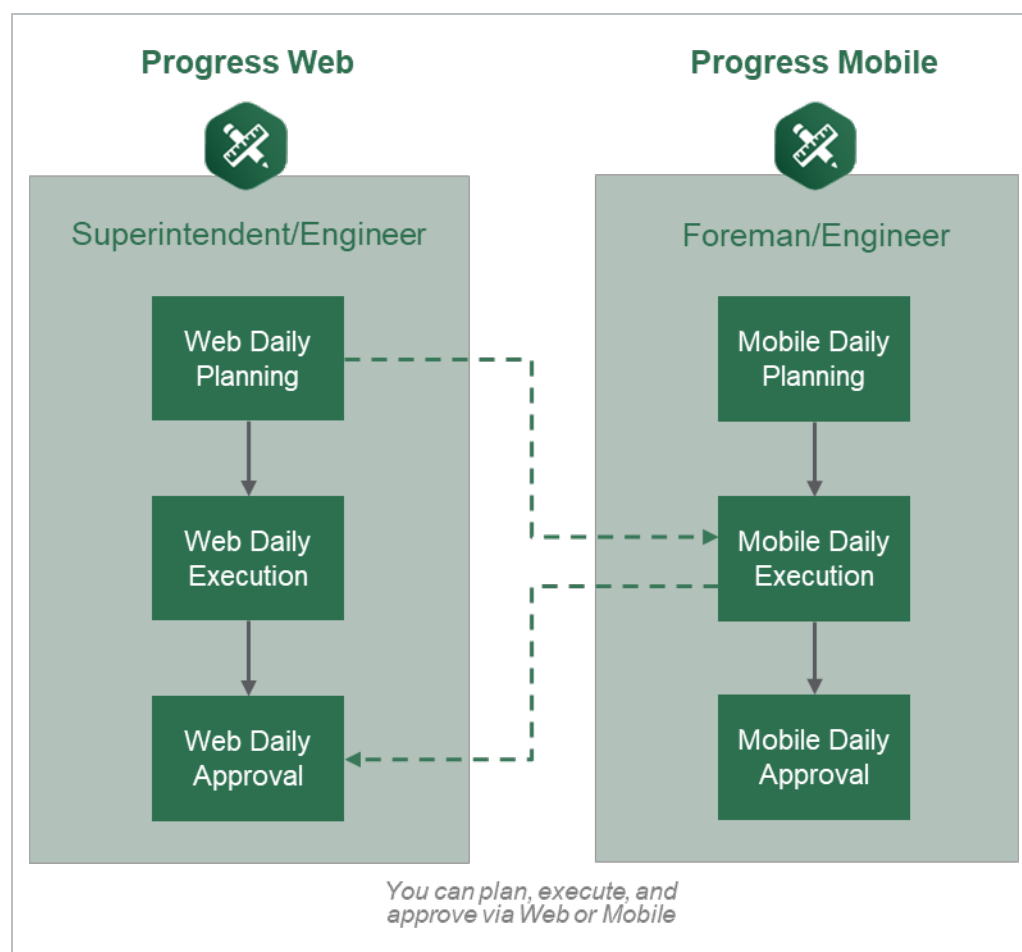

A daily plan can be accessed in either program in any of the phases of daily planning. The program used for a phase may vary from project to project and depends largely on the roles of the project members involved. For example, it may be preferable to have a staff member such as a superintendent or engineer complete daily planning in the InEight Progress web application because they prefer to


work from a computer in an office location. The Execution Phase of that same daily plan may be completed by a foreman who spends their entire workday out on the jobsite without access to a computer. In this case the Execution Phase is completed in the InEight Progress mobile application. Finally, the superintendent or engineer may also be responsible for approval of the daily plan which would again be completed in the InEight Progress Web application from their office computer.

TIP


Mobile Daily Planning has all the same functionality as Web Daily Planning for InEight Progress, but is available as a mobile-only application.

1.1.3 INEIGHT CONTROL INTEGRATION

WBS (work breakdown structure) elements are used to link the quantity, hours and cost captured in InEight Progress with the cost elements in InEight Control. InEight Control communicates the WBS Structure (including budgeted quantities, hours and cost) with InEight Plan. InEight Plan then assigns WBS elements to components.

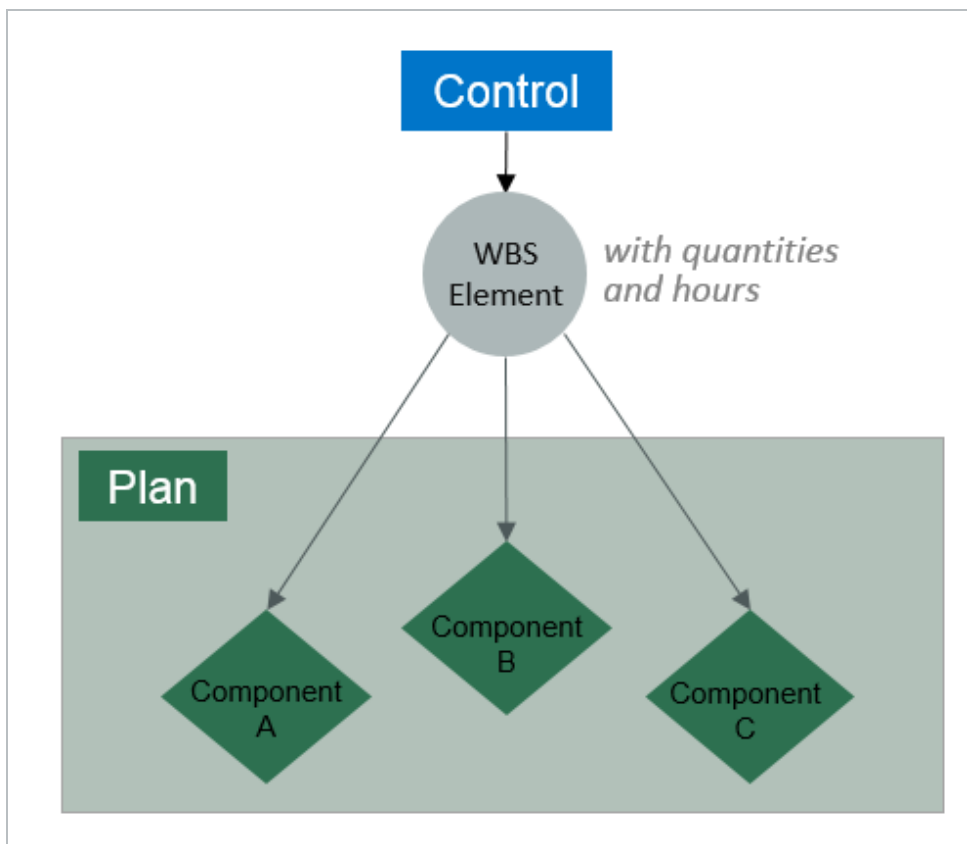

InEight Progress uses the component quantities along with actual hours to determine productivity.

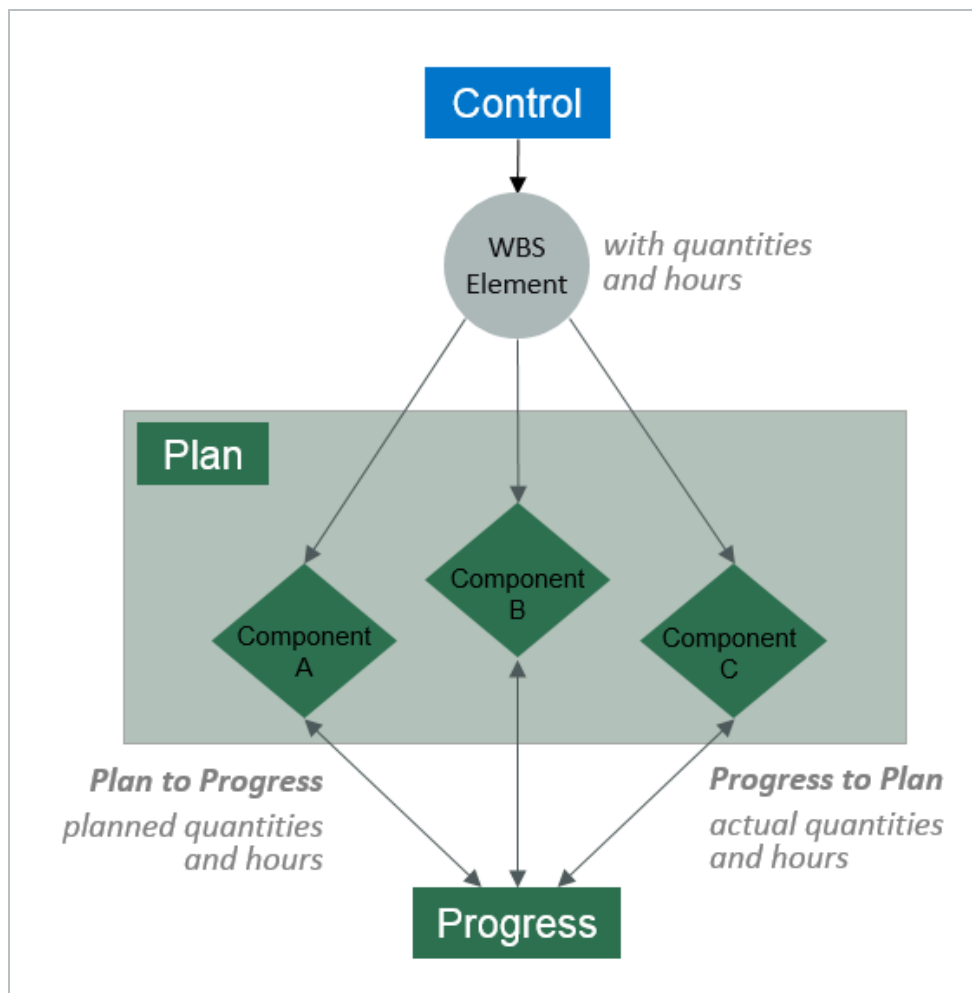

This lesson provides an overview of InEight Progress and the subsequent lessons will expand on the InEight Progress functionality in more detail.

1.1.4 DAILY PLANNING

Daily planning offers specific functionality for project members to create, view, or change daily plans as needed. Daily plans allow you to select specific components and resources (labor and equipment) from a work package and assign it in daily production increments.

Daily Planning is completed by navigating through the six tabs in the navigation bar at the top of the screen:

- **Overview** – Modify or enter plan details, approvers, and executors
- **Details** – Enter planner notes and tool box talk items
- **Time Sheet** – Select tasks and resources and assigned planned hours

- **Quantities** – Select specific components and specify planned installation quantity
- **Notes/Issues** – Enter any additional plan notes/issues including photos if needed.
- **Productivity** – Review planned productivity and compare against current budget or estimate or current estimate

NOTE

A foreman can also use mobile daily planning to change an existing daily plan. If the plan changes from the original plan, a foreman can still make changes to the daily plan.

1.1.5 DAILY EXECUTION

Daily execution allows you to capture actual hours, quantities, notes/issues, and productivity. You can document the number of hours worked for each employee and machine assigned to a specific task. (For hourly rates, you can document standard time [ST], over time [OT], or double time [DT]).

You can claim the quantity completed and see the productivity for the day. You can also add notes and pictures. Once you complete the entries, you can sign out employees and fill out compliance questionnaires. This is commonly used to ensure at sign off that employees are not injured while at work.

Daily execution is completed by navigating through the seven tabs in the navigation bar at the top of the screen:

- **Overview** – Review plan details, approvers, and executors
- **Details** – Review planned tasks, planner notes and tool box talk items
- **Time Sheet** – Enter actual hours worked and assign to tasks and resources
- **Quantities** – Enter actual components and indicate installed quantity
- **Notes/Issues** – Enter any notes/issues and photos related to execution of the work
- **Productivity** – Review actual productivity and compare with current budget, estimate and planned production rates
- **Sign Out** – Review employee hours, enter sign out pin or signature and answer compliance questions

1.1.6 DAILY APPROVAL

Daily approval allows you to review actual hours, quantities, notes/issues, and productivity that were entered during the execution phase. This gives supervisors a chance to review information before the hours are sent to the ERP payroll system and quantities are claimed in InEight Progress.

There are 3 options in the Approval Phase:

- **Approve** - Quantities and hours can be approved independently or all at once
- **Edit** – The daily plan can be further edited by the Approver to change specific details such as tasks, resources, hours and quantities
- **Reject** – Sends the daily plan back to Execution Phase to allow the Executor to revise the plan and resubmit

NOTE All tabs from the Execution Phase can be viewed in the Approval Phase.

1.1.7 WORK FLOW BEYOND INEIGHT PROGRESS

When quantities are approved in Progress, they can be brought into the InEight Control application (initiated within InEight Control).


1.1.7.1 HOURS

When hours are approved, the hours are sent to your payroll system. Once ERP payroll has processed the hours, as-built hours and costs can then be pulled into InEight Control from ERP payroll (again initiated in InEight Control).

1.1.7.2 QUANTITIES AND COSTS

Bringing actual installed quantities and as-built costs into InEight Control allows you to monitor and compare actual costs and productivity against budgets for all cost accounts. It also helps provide timely information to accurately forecast costs.

The following diagram illustrates the workflow of InEight Progress in relation to other products within the InEight portfolio and the ERP system. You will reference this diagram throughout the course.

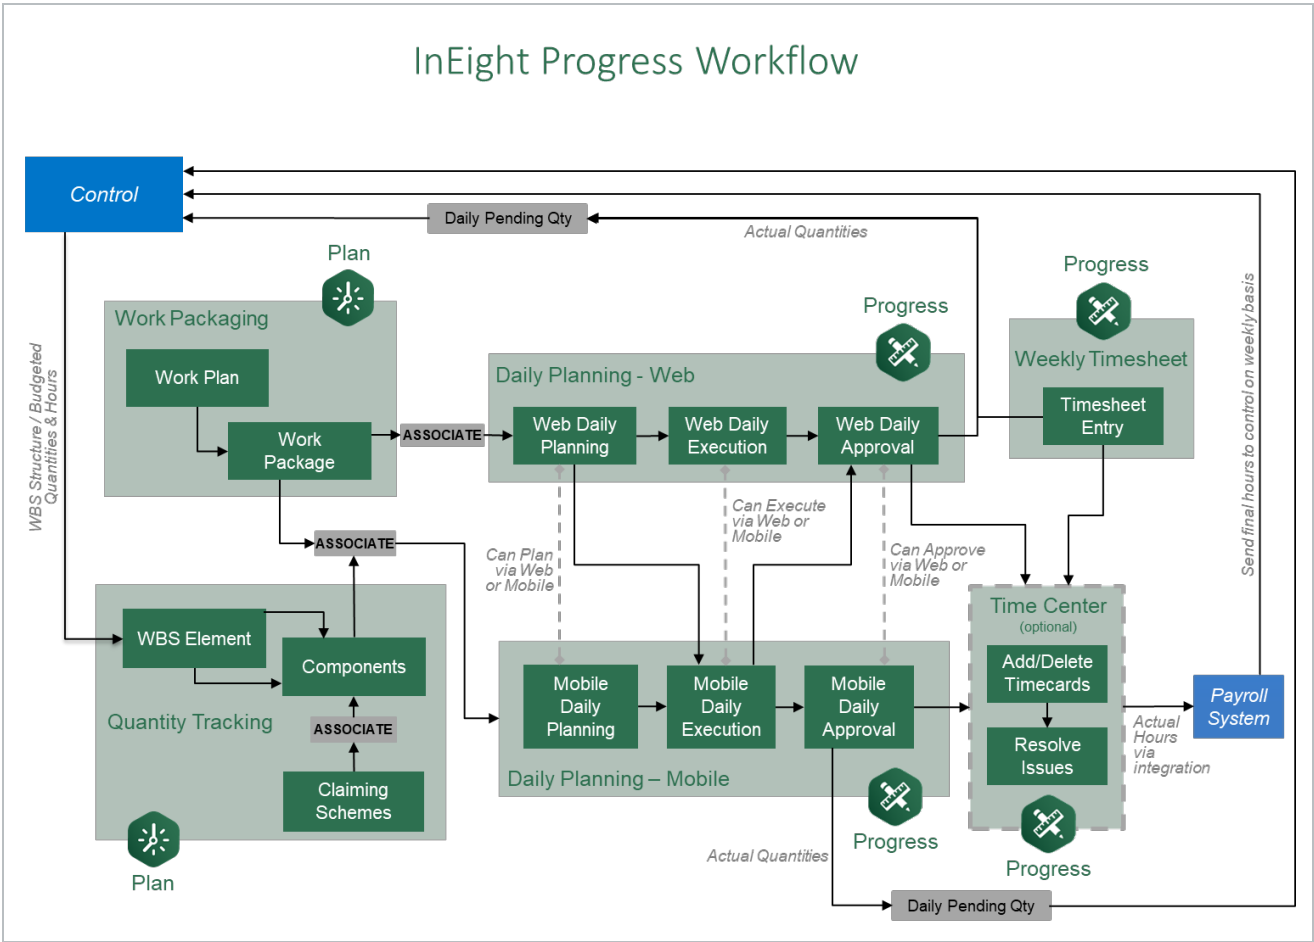

This page intentionally left blank.

INEIGHT PROGRESS - DAILY PLAN MOBILE

2.1 MOBILE OVERVIEW

2.1.1 LOGIN


InEight Progress Mobile is a mobile application only and must be installed on an Apple iPad to be used. Once installed, you take the following steps to log in to the application:

LOG INTO INEIGHT PROGRESS

1. From the home screen, open the **InEight Progress** application.



2. Enter the customer code for your organization.

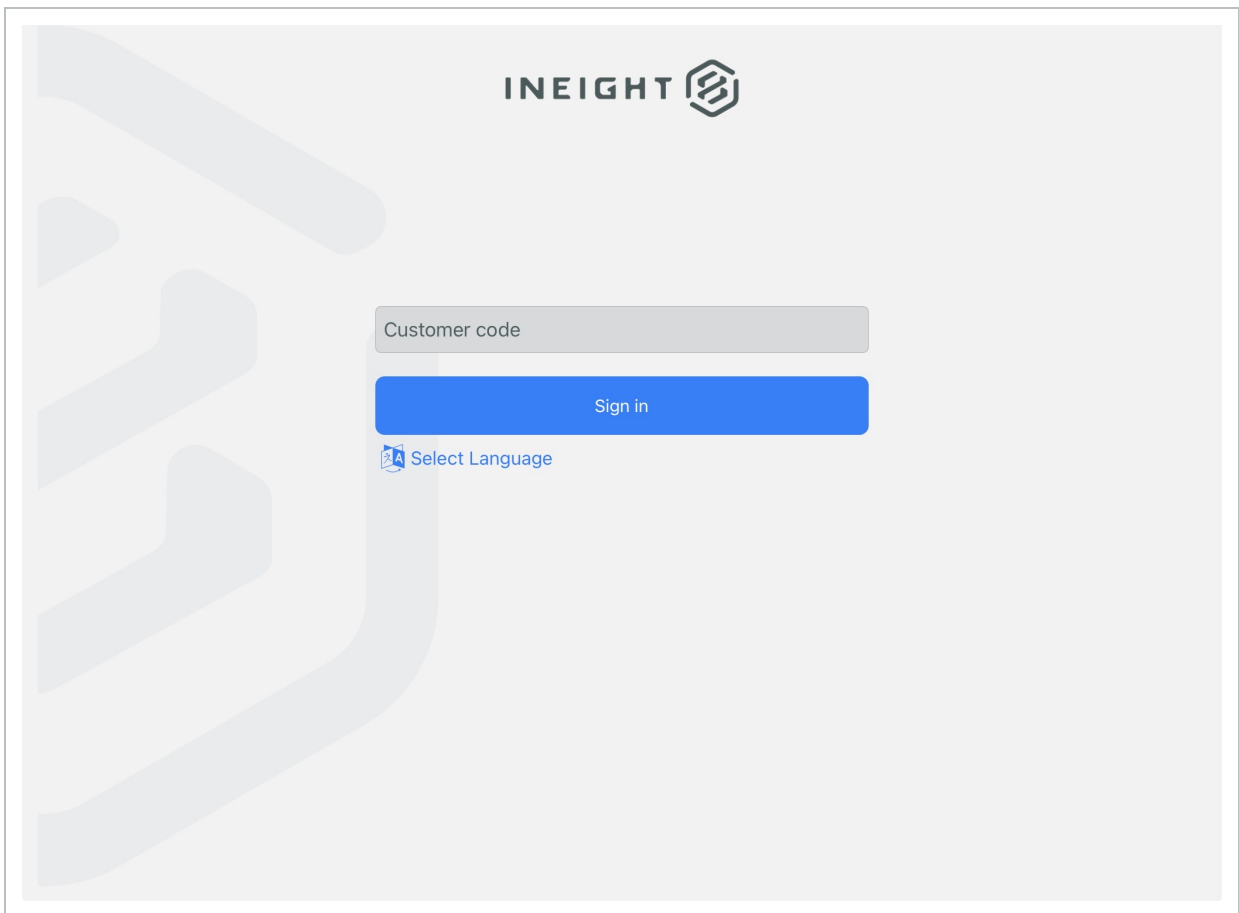

3. In the **User Pin** field, enter the password provided by your manager.

- InEight Progress automatically syncs during the initial sign in. After syncing, the available projects assigned to the user are listed

2.1.2 KIOSK MODE

Progress Mobile allows multiple users to log in on the same device using Kiosk Mode, so that only one device is needed for multiple users to perform their daily activities.


- Users can log in whether they have the same or differing roles
- When a different user logs in, it does not affect the existing logged in user
- The user logged in at the time will only see their own data

When you are using Kiosk Mode, a sync occurs automatically when you sign out.


You can also sync in the background while using the application. To sync in the background, open Settings, and then tap **Enable background sync**.

2.1.2.1 KIOSK WORKFLOW

When a previous user logs out, the new user is presented with a login screen that includes a hyperlink to **Sign in as different user**.

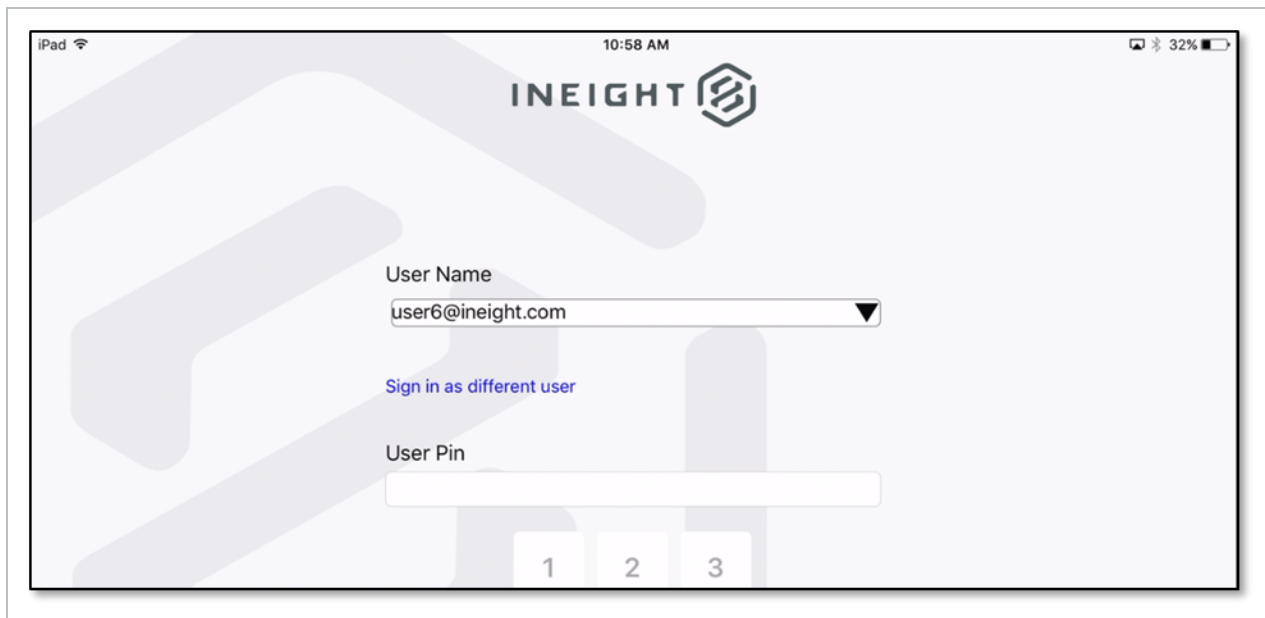

Selecting the option to sign in as a different user will take you to a new login screen where you can input your email and sign in for the first time on the device.

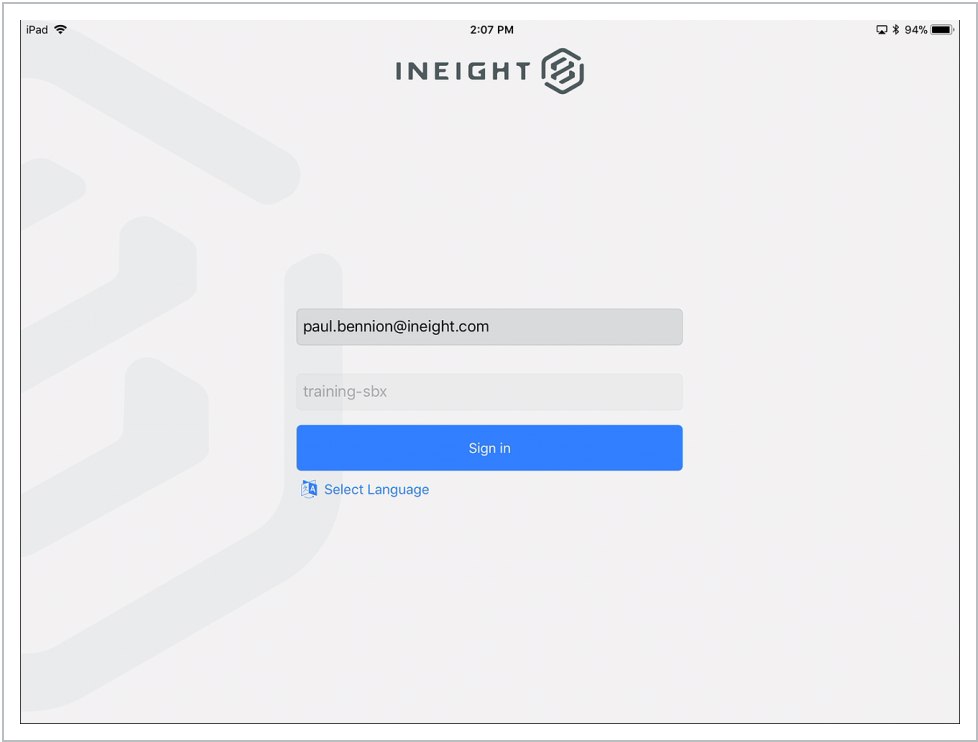


Once you have logged in, the next time you use the device you can select your email from a drop-down list and then sign in.



2.1.2.2 COMPONENT SEARCH

To search components in the mobile app, go to Quantities, and then select a task that has components. An icon labeled Recent components and the search components show. Tap Search components to search for all components under the selected task.

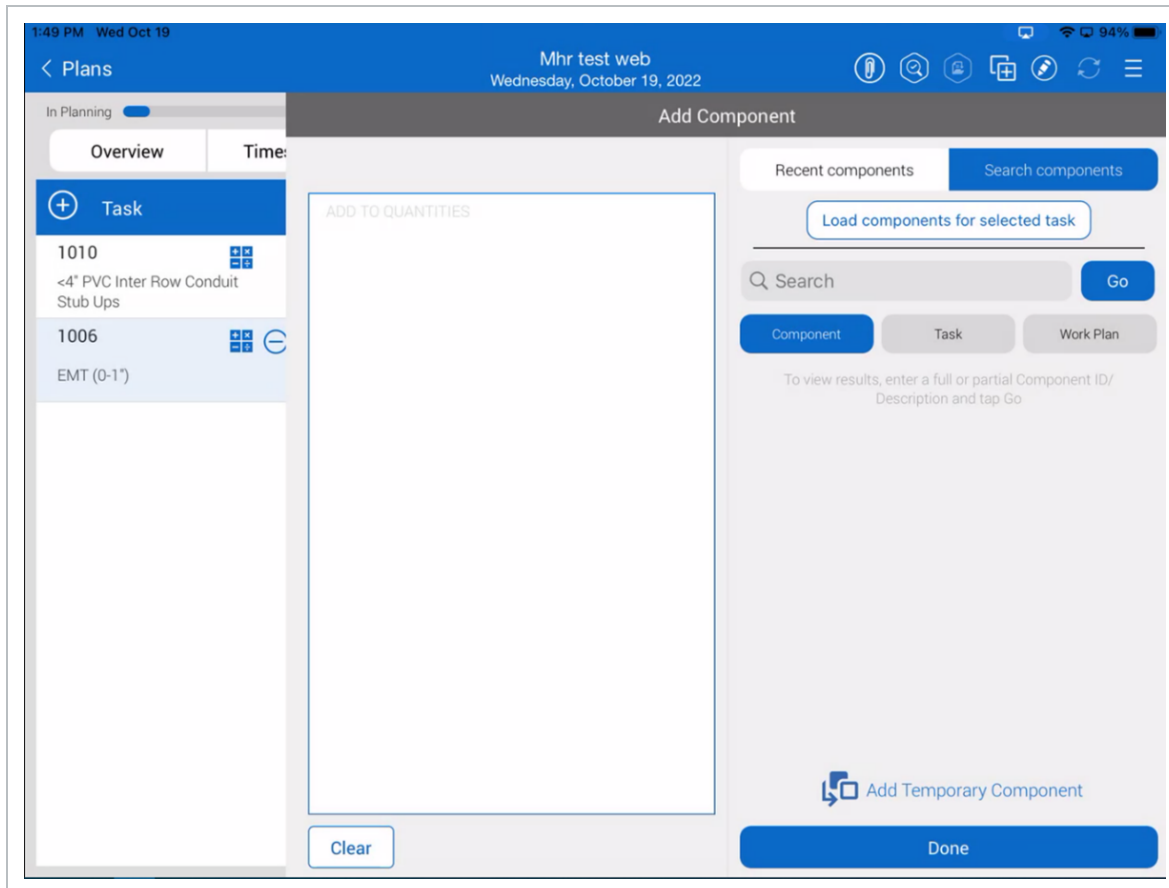

2.1.3 PROJECT LIST

Scenario


Paul is an electrical superintendent on a project. Earlier that afternoon, he asked his foreman to create a daily plan for tomorrow's work. At the end of the day Paul sits down to review the plan the foreman created.

Navigating through InEight Progress is straightforward. First, you select a project and then create and/or execute a daily plan. The following sections walk you through the process.

The project list shows all projects available for you. You must have the role of Superintendent, Engineer or Foreman assigned in the InEight cloud platform under Suite Administration > User Management, for a project to appear in the project list.

Overview - Project List

Title		Description
1	Recent Projects	Select to view all projects that you have opened recently.
2	All Projects	Select to view all projects you are assigned to.
3	Search Bar	Only appears when viewing all projects. Allows you to filter down the project list by typing any part of the project number or description in the search field.
4	Project List	List of projects to choose from. To open a project, simply tap on that project in the list.



2.1.4 PLAN LIST


The plan list shows all the daily plans already created and assigned to you within a specified date range. You can configure the date range in the project settings, but the default is ten days in the past and five days in the future. Tapping on an existing plan opens that plan.

Overview - Plan List

Title		Description
1	Project List	Takes you back to the Project List.

Overview - Plan List (continued)

	Title	Description
2	Create Daily Plan	Select this to create a new daily plan.
3	Sort	Toggles sort between ascending and descending dates.
4	View by Executor	Allows you to view plans assigned to a specific foreman.
5	Plan Header Details	Displays plan name, date, shift, location, superintendent, engineer, foreman, work plan and status. Tapping on this section will open the plan.
6	Edit / Copy / Delete	Allows you to edit, copy or delete a plan.
7	Help Overlay	Provides explanations for key items on the current screen
8	Sync	Updates the application with the latest information from InEight Cloud Platform and pushes any changes from InEight Progress Mobile back to InEight Progress Web. This is used often when working in offline mode when you return to a location with access to internet.
9	Menu	Contains quick links to the project list and sign out. Also displays the current date, app version, and date/time of last sync.
10	Search	Free text search bar to find daily plans by plan name.

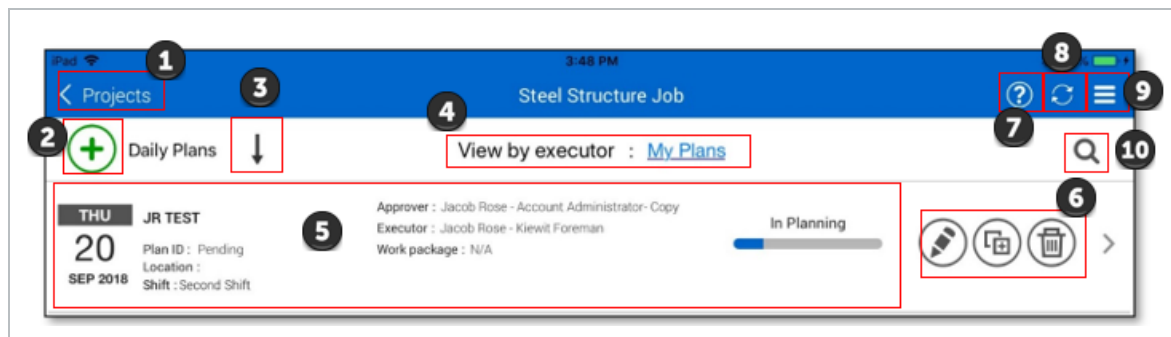**TIP**

Selecting a work plan ID will sync all components associated with that plan to the iPad for use in offline mode.

You can copy daily plans in the plan list. This is especially useful when completing repetitive work that will span multiple days.

2.2 NAVIGATE DAILY PLANNING

To navigate through the Daily Planning Phase, you will tap and complete each tab in the navigation bar.

Overview	Timesheet	Quantities	Notes/Issues	Productivity	Sign out
----------	-----------	------------	--------------	--------------	----------

TIP


While in the Planning Phase, the screen is highlighted with a blue accent. When in the Execution Phase, this changes to green. This helps to remind yourself which phase of the process you are in.

2.2.1 OVERVIEW

Once a daily plan is created, you are taken to an Overview screen. Initially this screen is blank because you have not entered any information. The Overview screen allows you to review your daily plan before starting work and includes the following information:

Overview - Overview Tab

Topic		Description
1	Tasks	Include the planned quantity, man-hours and budget gain/loss (G/L).
2	Tool Box Talks	Provide key information including general discussion, safety, quality, and environmental considerations.
3	Planner Notes	Provides space for additional notes related to the plan.

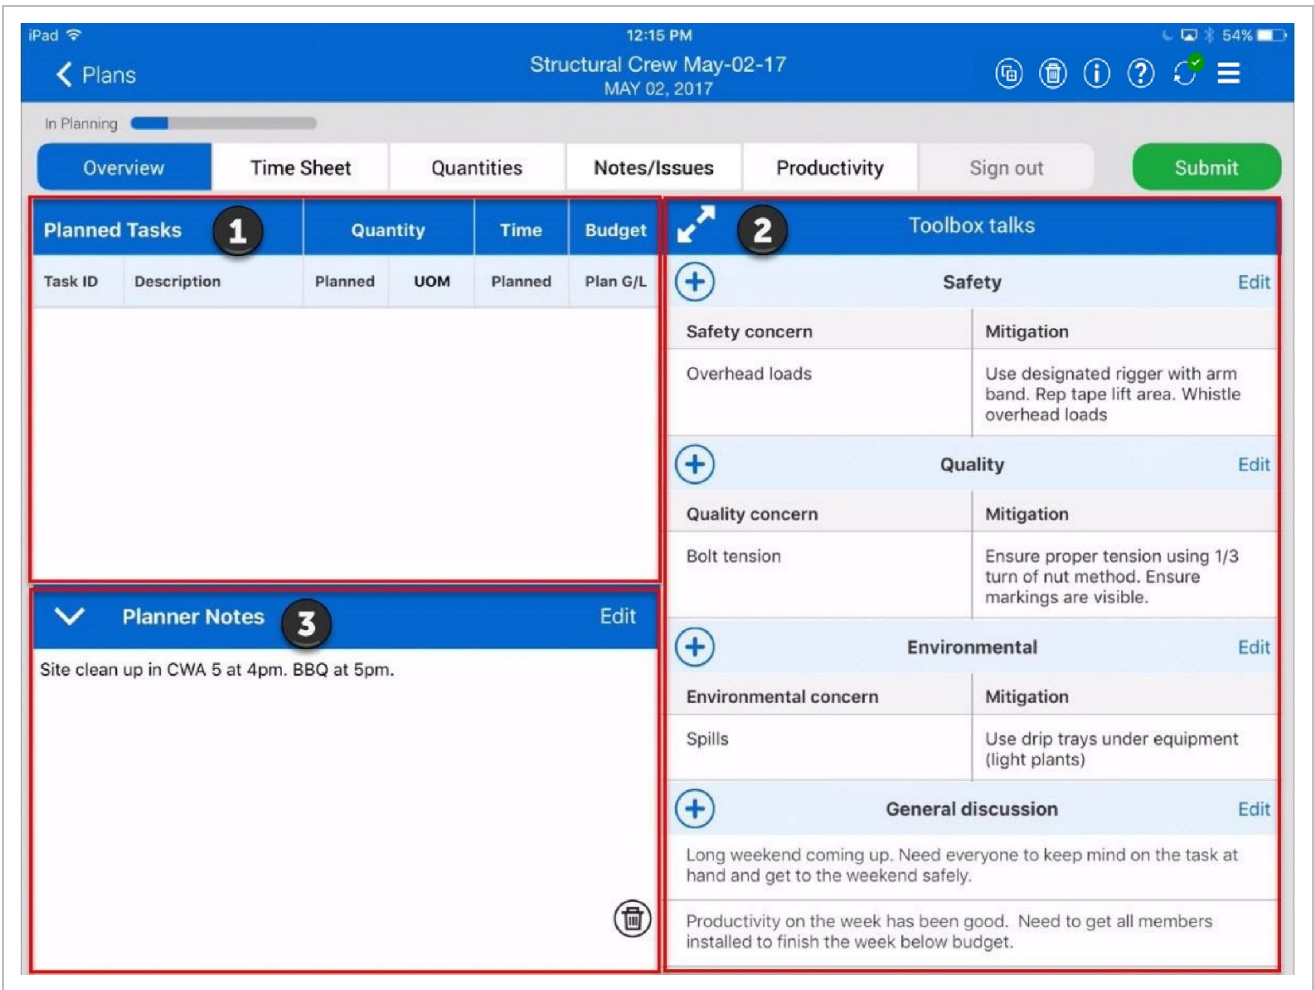

On the Overview tab, you can:


- Add tool box talk items by tapping the  icon
- Tap the  icon to expand to a larger view
- Minimize planner notes by tapping the  icon

2.2.2 TIME SHEET


On the Time Sheet tab, you can enter all your tasks, employees and equipment and assign hours to each. The table below explains key navigation points.

Overview - Time Sheet Tab

Title		Description
1	Add	Tap here to add tasks, employees and equipment. (Further explained below.)
2	Clear Hours	Tap here to clear all hours from the time sheet.
3	Reorder	Tap here to reorder tasks, employee and equipment in the time sheet.
4	Enter Hours	Tap here to enter hours (ST, OT, DT) for employees and equipment.
5	Employee / Equipment Details	Tap here to mark attendance, enter extra pay, temporarily change billing class, add notes, delete row, or clear hours.
6	Task Details	Tap here to enter total task planned hours, add notes, swap task or delete task.

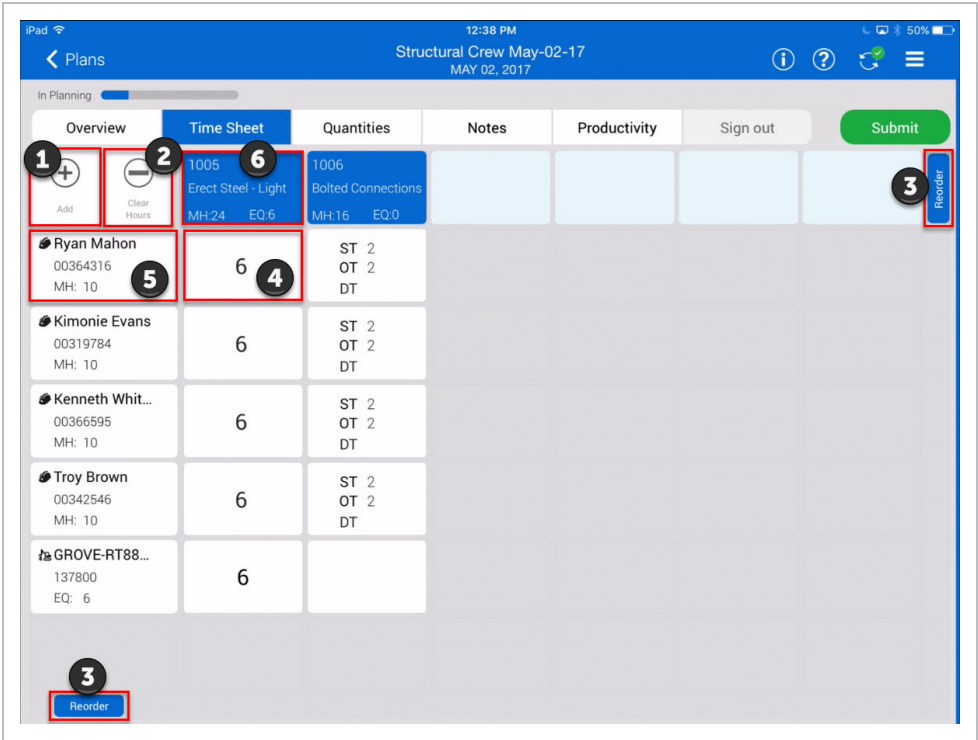

When adding tasks, employees, or equipment, the Add slide out panel appears as shown below.

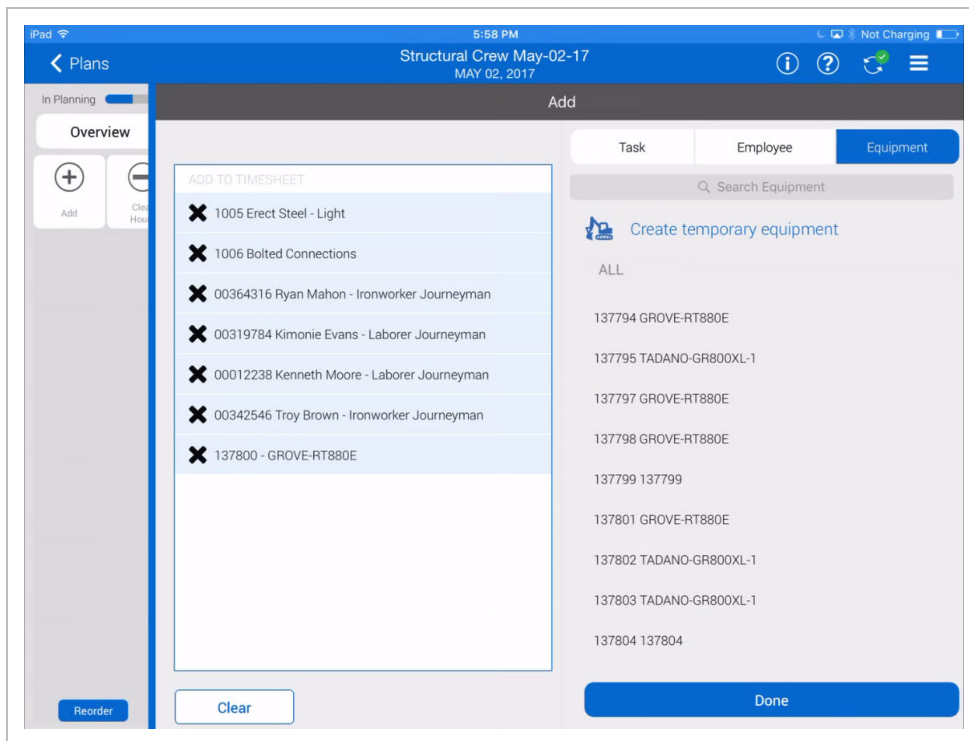


- View your lists of all available tasks, employees and equipment by tapping on the appropriate tab at the top of the window
- Once selected from a list, items appear on the left-hand side of the window under Add To Time Sheet as shown above
- Tapping on the **X** next to an item removes it from the list
- If an item you require is not available in the list, you can add a temporary task, employee or equipment by selecting **Create Temporary Task**, **Create Temporary Employee**, or **Create Temporary Equipment**
- When you are satisfied with the list to be added to the Time Sheet, tap **Done** to return to the time sheet

2.2.3 QUANTITIES

In the Quantities tab, you select components for each task. If you plan to use claiming rules with multiple steps, you can choose which steps you plan to complete. You can also indicate which components are higher priority.

Overview - Quantities Tab

Title		Description
1	Add task	Tap here to add additional tasks. Resource hours must be assigned back in the Time Sheet tab.
2	Select task	Tap here to show or add components for the selected task.
3	Add contract	Tap here to add contracts.
4	Select contract	Tap here to show or add components for the selected contract.
5	Add Components	Tap here to add components for the selected task or contract by selecting from a list.
6	Expand / Collapse	Tap here to expand and collapse individual component details.
7	Information	Tap here to show a description of the component.
8	Favorite	Tap here to add the component to your favorites.
9	Add note	Tap here to add a note or issue associated with an individual component.
10	Delete component	Tap here to delete a component.
11	Priority	Tap here to mark a component step as a priority.
12	Complete	Tap here to select a component step to complete as part of the daily plan and add the corresponding quantity to the planned quantity.
13	Planned Quantity	Tap here to enter the planned quantity for a component step, providing the planned quantity does not exceed the component quantity.
14	View Planning slide-out panel	(Not pictured. See Daily Plan from Scratch) Tap here to view the quantity needed to break even for the selected task. Or you can manually enter any quantity to see how it would affect the gain/loss for the selected task.

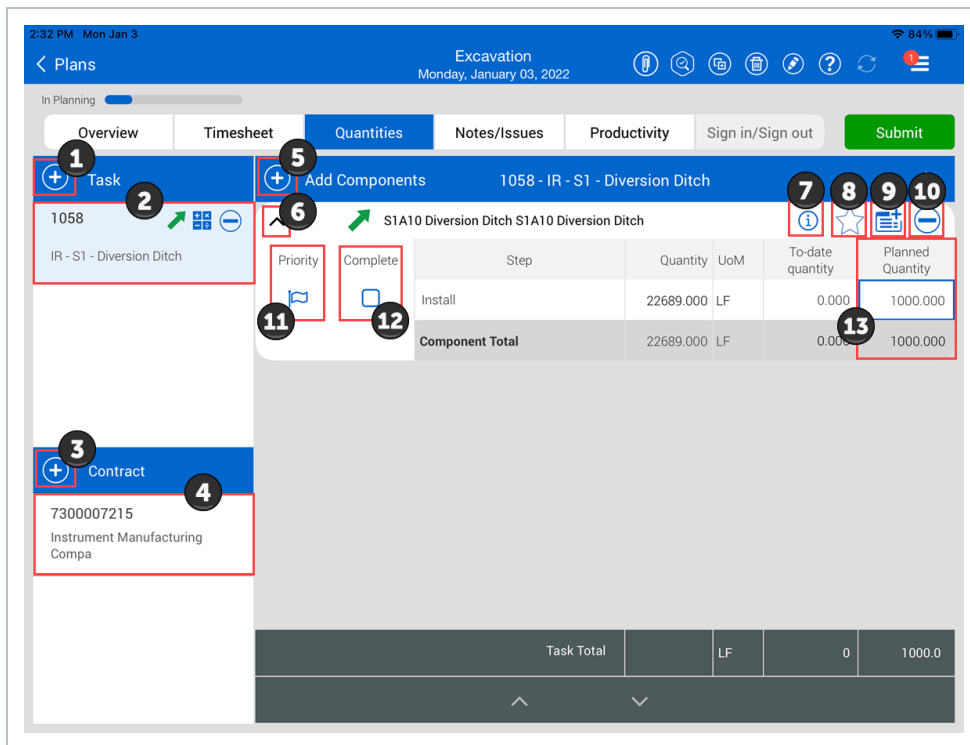

2.2.4 NOTES/ISSUES


The Notes/Issues tab is where you can enter additional information regarding a task or component for the crew to be aware of when they execute the plan. You can add safety, quality control, environmental, subcontract, and other information. If an issue is added it will automatically show up on the issue log in the InEight Change application.

Overview - Notes/Issue Tab

Title		Icon	Description
1	Add	 	The Add button allows you to add a note or issue under the Notes/Issues tab.
2	Edit		The Edit button allows you to make changes to an existing note.
3	Delete		The Delete button allows you to remove existing notes.

Overview - Notes/Issue Tab (continued)

	Title	Icon	Description
4	Arrow Up Arrow Down	 	The Arrow button allows you to navigate through the list of notes up or down.

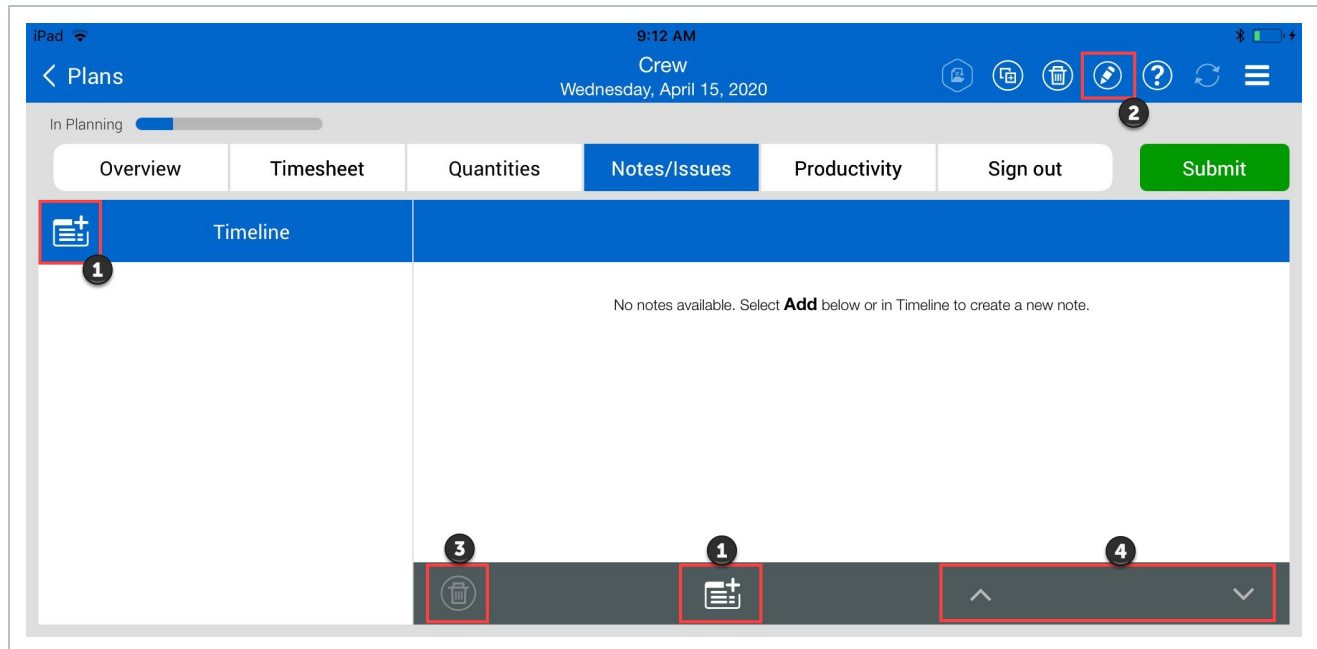


When you add a new note or issue, three icons will appear at the bottom. The following overview explains these icons.

Overview - Tags & Associations

	Title	Icon	Description
1	Tags		The Tags button allows you to add tags to your notes. The following tags are available: • Safety • Quality • Environmental • Extra Work/Changes • Delay • Production Notes

Overview - Tags & Associations (continued)

Title	Icon	Description
2 Associations		The Associations button allows you to associate the note with a specific task, employee, equipment, components, or vendors.
3		The Photo button allows you to add a picture to a note. The photo can either be taken from the device's camera or from the saved photos on the device.

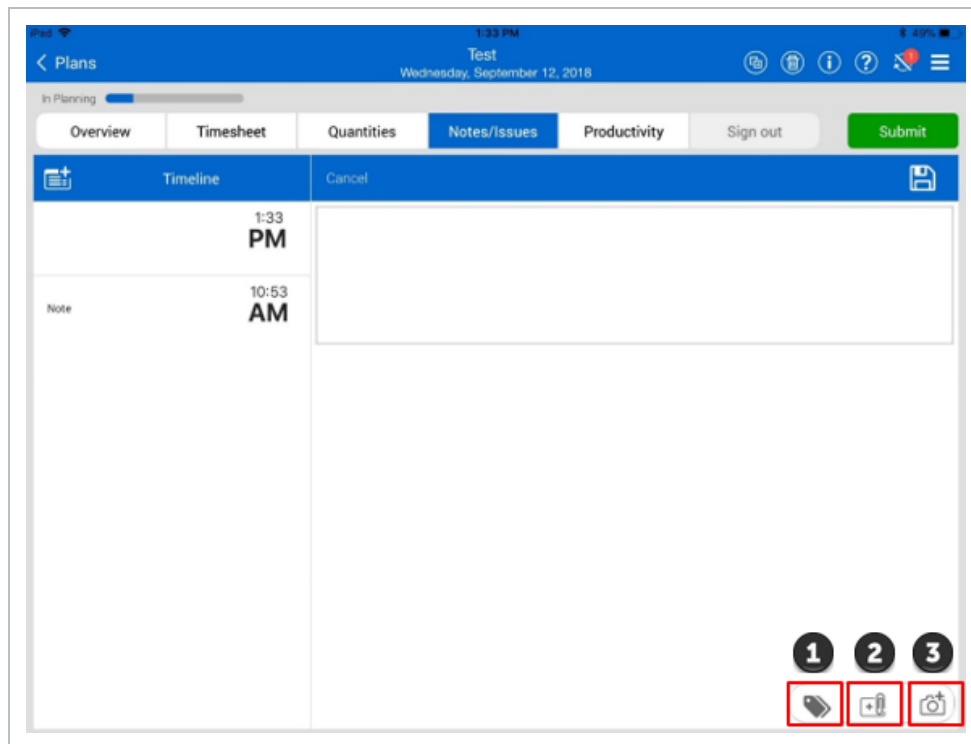

2.2.5 PRODUCTIVITY

The Productivity tab is where you can review the planned quantity and man-hours in comparison to current budget, current estimate, and forecasted or goal unit rates which shows your planned gain/loss.

Overview - Productivity Tab

Title	Description
1 Task ID and	Indicates the tasks planned for the crew to perform that day.

Overview - Productivity Tab (continued)


Title		Description
	Description	
2	Planned	Displays the plan information you entered in the Quantity tab (quantity, unit of measure, and man-hours).
3	MHRs per Qty	Compares the planned values to the current budget values.
4	Planned	Displays gain/loss for planned \$/mhrs compared to budget.

Task ID and Description		Planned			MHRs per Qty		Planned	
Task ID	Description	Quantity	UOM	MHRs	Planned	CB	Cost G/L	MHRs G/L
1511	Erect Steel (Light/Med./Hvy)	1.050	Ton	20	19.048	18.863	28	-0.2
1477	SNCR Common Steel Demo	0.175	PLS	20	114.286	151.000	351	6.4
Totals				40			379	6.0

2.2.6 SUBMIT & SYNC

After reviewing the planned information in the Productivity tab and confirming that the employees and equipment you have are accurate for the tasks, you can tap on the Submit button.

When you tap on the Submit button, a warning pop-up window appears asking if you are sure you want to move the plan to Execution.

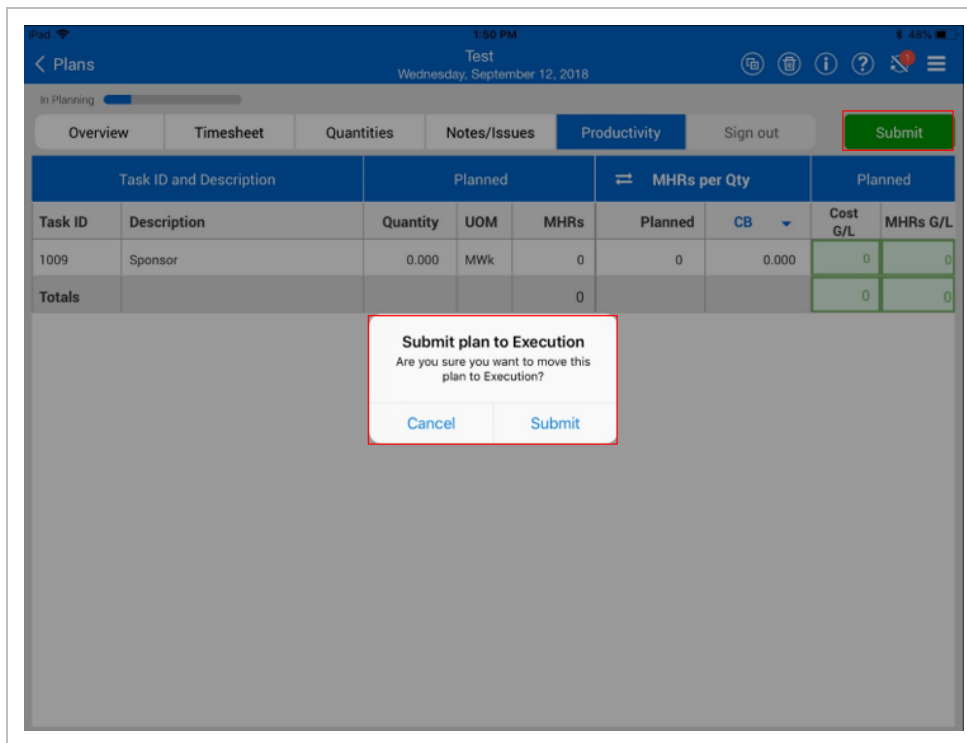

Daily Plan information will remain in the sync platform until you tap the sync button. Once you tap Sync, the Daily Plan information becomes available in the InEight Progress web application for review by the superintendent or engineer.

NOTE

A Daily Plan still in the planning phase and created in the mobile app will not be available in the web app until it's moved to the execution phase and synced. A Plan ID is assigned once the Daily Plan is in execution in the mobile app.

Scenario Recap

Paul can review the daily plan by navigating through each tab in the navigation bar and reviewing the data in each tab.

2.3 NAVIGATE EXECUTION


Scenario

Steve is an electrical foreman on a project. Yesterday he created a daily plan that was reviewed by his superintendent, Paul. He is now preparing for the morning meeting and getting ready to


execute the daily plan.

2.3.1 PLAN LIST

You access a daily plan from the list of daily plans. Note that the current status is now Execution.

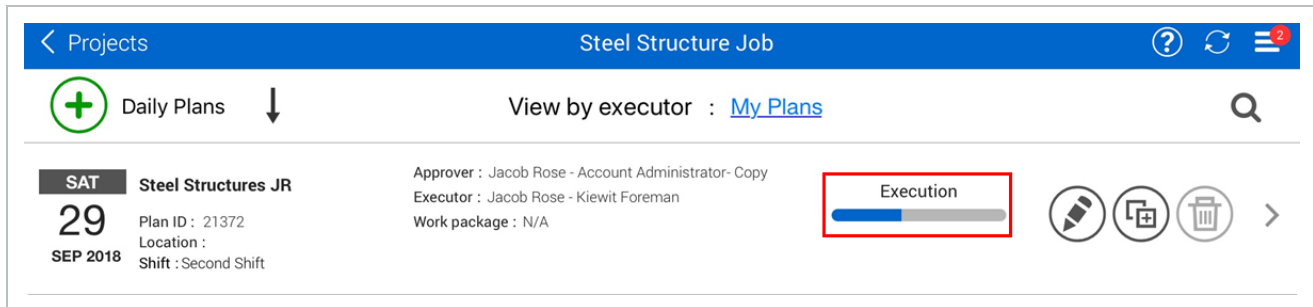

Navigating through the Daily Execution Phase is very similar to the Daily Planning Phase. The same navigation bar appears at the top of the screen and you work through each tab to review the plan information and enter actual data. The tabs in the navigation bar are the same as in the planning phase except you are now able to access the Sign Out tab.




2.3.2 OVERVIEW

The first tab that you open to is the Overview tab. The Overview tab contains key information you would want to review with your crew at the start of the shift such as:

- Planned tasks
- Planned quantity for each task
- Planned budget
- Tool Box Talks (Safety, Quality, Environmental, and General Discussion)
- Planner Notes

Overview - Overview Tab

Title		Description
1	Planned Tasks	Displays the Task ID and Description of each planned task.
2	Quantity	Displays the Planned Quantity and Unit of Measure for the task. The Planned Quantity comes from information entered during the planning phase.
3	Time	Displays the planned hours for the task.
4	Budget	Displays the planned gain or loss in manhours by comparing the planned hours and planned install quantities to the budget unit rates.
5	Tool Box Talks	Contains plan information on Safety, Quality (Quality Concern and Mitigation), Environmental (Environmental Concern and Mitigation), and General Discussion.
6	Submit	Once the plan is executed and all data has been entered, you can tap the Submit button to send the daily plan to the approval phase. You can access the submit button while working in any of the daily plans.
7	Planner Notes	Shows general notes input during the planning phase. During execution phase this block is not editable.

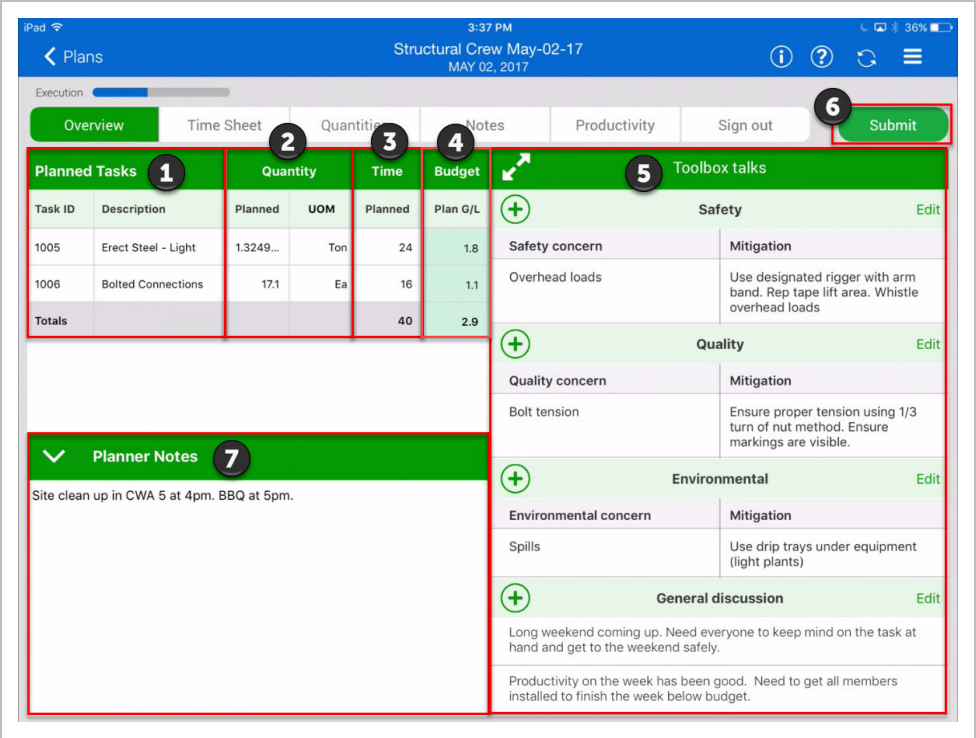

2.3.3 TIME SHEET

In the Time Sheet tab, the planned tasks, resources and hours are all displayed. As the day progresses you can enter in actual hours for each resource and task. If you need to add tasks or resources, you can do it here as well.

Time Sheet Tab

Title		Description
1	Add 	Allows you to add additional tasks, employees, and equipment to the Time Sheet. You can also create temporary tasks, employees, and equipment.
2	Clear Hours	Allows you to clear all the hours from the Time Sheet. For instance, if you copied a daily plan and copied in the hours worked by the employees you can clear it out for the new task.
3	Tasks	The work operations to be completed. These are also the cost codes you are charging employee time to.
4	Reorder	Allows you to reorder the list of items in the time sheet any way you want, by tapping and dragging the item.

Time Sheet Tab (continued)

	Title	Description
5	Employees & Equipment	Displays the employees and equipment assigned to the Time Sheet.
6	Hours	Displays the actual hours each employee worked. These fields should be edited to reflect what employees actually work on and for how long.

The screenshot displays the 'Time Sheet' tab for 'Structural Crew May-02-17'. It features a list of crew members and equipment with their respective hours. The interface includes a top navigation bar with tabs for Overview, Time Sheet, Quantities, Notes/Issues, Productivity, and Sign out. A 'Submit' button is located in the top right corner. The main content area shows a list of crew members and equipment with their associated hours. The 'Hours' column is highlighted with a red box, and a 'Reorder' button is visible on the right side of the list.

Task & resources	Hours	ST	OT	DT
Ryan Mahon 00364316 MH: 10	5	3	2	
Kimonie Evans 00319784 MH: 10	5	3	2	
Kenneth Whit... 00366595 MH: 10	5	3	2	
Troy Brown 00342546 MH: 10	5	3	2	
GROVE-RT88... 137800 EQ: 5	5			

- To enter hours for equipment and crewmembers, you click on the hour box under each task and next to the crewmembers' name
- A window appears where you can enter ST (Straight Time), OT (Over Time), or DT (Double Time)

2.3.4 QUANTITIES


In the Quantities tab, all the components that were included in the planning process for each task are shown. Actual quantities are claimed by entering the quantity or tapping the Complete check box. You can add or delete components at this point if required.

Overview - Quantities Tab

Title		Icon	Description
1	Add task		Lets you add tasks. You can also add temporary tasks.
2	Add Component		Lets you add components for the task or contract selected in the left side panels. You can also add temporary components.
3	Add contract		Lets you add contracts.
4	Expand / Collapse Icon	 	Selecting these icons will either expand or collapse the component details.
5	Complete check box		Check this box when the component of the task is complete.
6	Component breakdown		Displays the Planned Quantity and what is claimed to date. Displays the claiming steps or rules of credit for that specific component. This area is greyed out because it is not an editable field.
7	Information		Shows a description of the component.
8	Favorite		Adds the component to your favorites.
9	Notes		Allows you to add notes and issues to the components.
10	Delete		Tap this icon to remove the component.
11	Installed Quantity		Enter the numerical value of the installed quantity for each claiming step here. Checking the Complete box will auto populate this field with the total quantity.
12	Up and down		Allows you to navigate through the different tasks.

Overview - Quantities Tab (continued)

Title	Icon	Description
arrows		

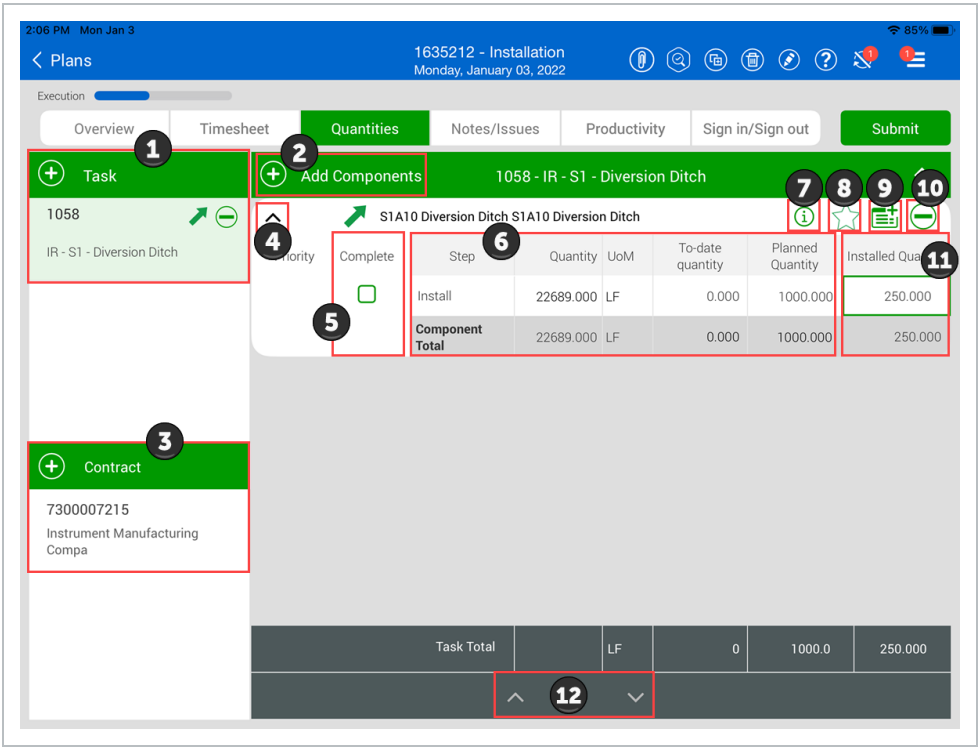


2.3.5 NOTES/ISSUES

Use the Notes/Issues tab to add notes to your components or task, for example to provide additional information regarding the operation you performed for the day, the performance results, quality issues, environmental compliance and many more.

Along with the note/issue, you can add tags to associate the notes/issues with a pre-defined category. You also can add photos with your notes/issues.

Overview - Notes/Issues Tab

Title			Description
1	Add	 	Click either icon to add a note/issues to this daily plan.
2	Name		Displays the name of the note or issue.
3	Date		The start date of the note or issue
4	Tasks		Associates the note/issue to a specific task.
5	Description		A free text field of the description of the note/issue.
6	Tags		Allows you to tag the notes/issues to a certain category such as Safety, Quality, Environmental, Extra Work/Change, Delay, or Production Notes. To see this icon, you must click on the add button.
7	Associations		Allows you to add associations to your notes, such as task, employee, equipment, components, and vendors. To see this icon, you must click on the Add button.
8	Pictures		Allows you to take a photo and attach it with your notes, or to select a photo from the photo library. To see this icon, you must click on the Add button.
9	Timeline		Thumbnail view of all notes in daily plan organized in chronological order.

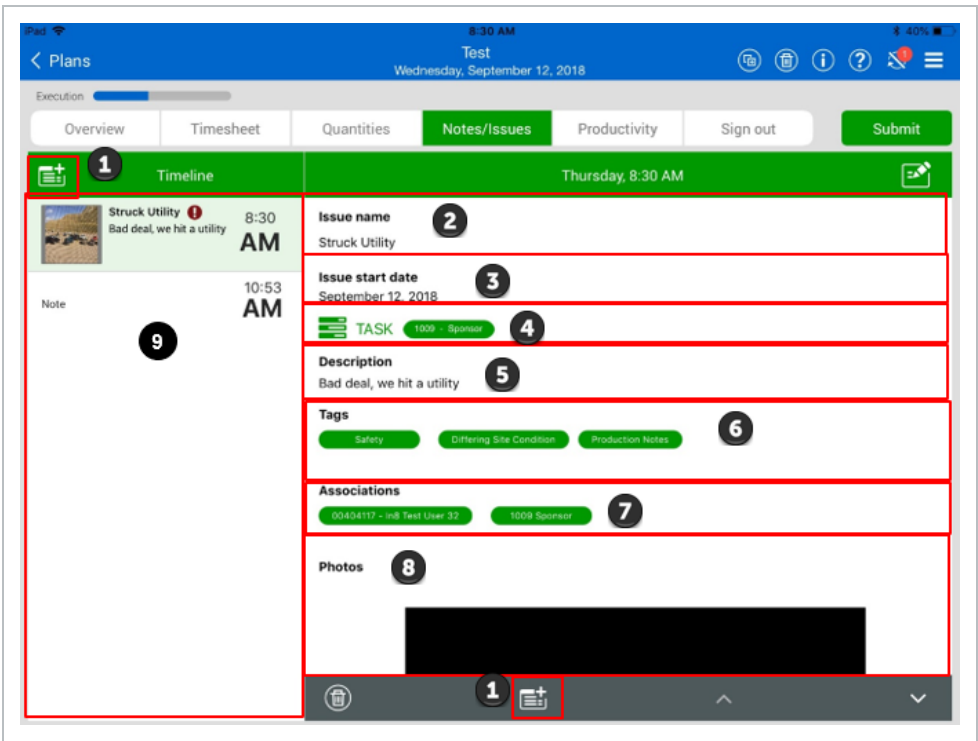

2.3.6 PRODUCTIVITY

In the Productivity tab you can review your tasks, quantities, and hours claimed for the tasks, and compare the actuals to the planned quantities and hours as well as view your actual gain/losses.

Overview - Productivity Tab

Title		Description
1	Task ID and Description	Displays the task ID and description.
2	Actuals (UoM and MHRs)	Displays the actual claimed quantities and man-hours.
3	MHRs per Qty	Compares the Planned versus Actual MHRs per Qty. You can select CE (Current Estimate) or CB (Current Budget) or Foecast or Goals.
5	Actual (G/L)	Compares actual cost or MHRs to budgeted cost or MHRs for each task and shows the gain or loss for each task.

Task ID and Description		1	Actual			MHRs per Qty			Actual	
Task ID	Description		Quantity	UOM	MHRs	Planned	Actual	CB	Cost G/L	MHRs G/L
1511	Erect Steel (Light/Med./...		1.070	Ton	20.00	19.048	18.692	18.863	45	0.2
1477	SNCR Common Steel De...		0.160	PLS	20.00	114.286	125.000	151.000	250	4.2
Totals					40.00				295	4.0

2.3.7 SIGN OUT

Before submitting a completed daily plan for approval, employees need to sign out by tapping their name. You enter the employee PIN (personal information number) which can be the birthdate of the employee or a number that the IT personnel has assigned to that employee.


The employee will be able to review the hours input by the Foreman before signing the card. At this point, they can agree or disagree with the hours and negotiate the hours before signing out.

Overview - Sign out Tab

Title		Description
1	Employee	Displays all the employees including the foreman on a specific daily plan.
2	Employee Name	Displays the name of the employee selected to sign out.
3	Employee Time Overview	Displays a summary of hours for the day and week entered for that employee.
4	As Employee/On Behalf of Employee	There are two options for signing out: the employee can sign out, or the foreman with permissions can sign out for the employee.
5	Employee Pin	Where employees enter their pin numbers.
6	Touch ID Signout	User can use iPad thumb-print to sign out rather than entering pin.

Overview - Sign out Tab (continued)

Title		Description
7	Sign out all	Allows a foreman or executor to sign out all employees by signing out only once.

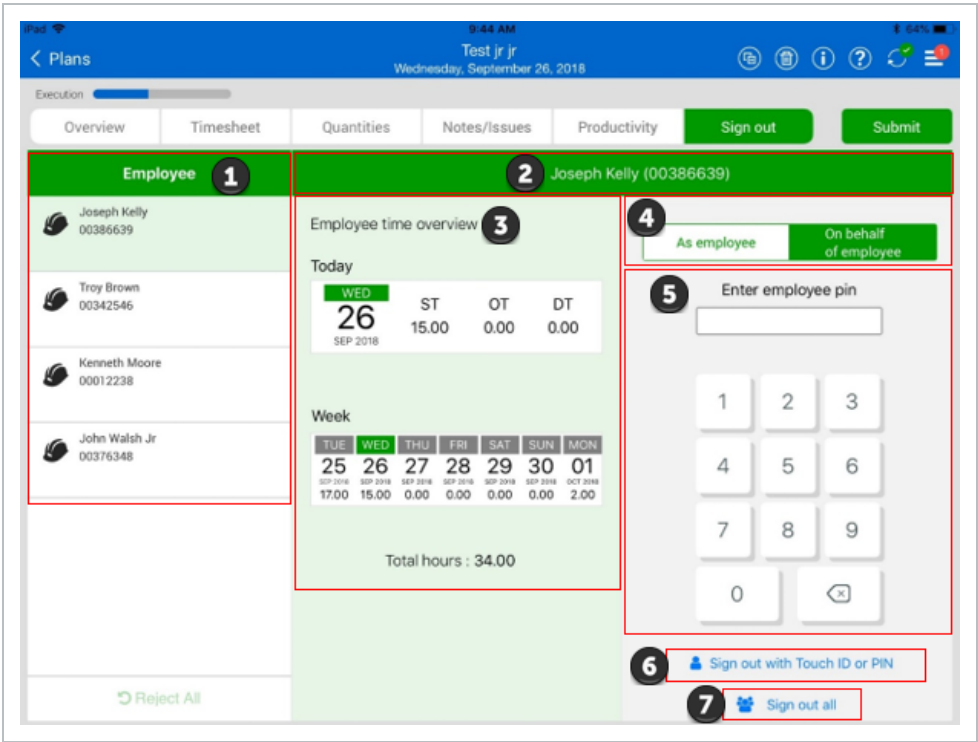

If employees sign out themselves, they have the option to either enter their pin or use an electronic signature on the iPad.

The screenshot shows the 'Plans' screen in the InEight mobile app. At the top, the status bar indicates 'iPad', signal strength, and a battery level of 64%. The app header shows 'Test jr jr' and the date 'Wednesday, September 26, 2018'. Below the header is a navigation bar with tabs: Overview, Timesheet, Quantities, Notes/Issues, and Productivity. To the right of the tabs are buttons for 'Sign out' and 'Submit'. The main content area is divided into two sections. On the left, under the 'Employee' header, is a list of employees: Joseph Kelly (00386639), Troy Brown (00342546), Kenneth Moore (00012238), and John Walsh Jr (00376348). On the right, under the 'Joseph Kelly (00386639)' header, is a signature capture area. It shows a handwritten signature and a checkbox labeled 'X' with the text 'I agree that the hours reported and answers to the compliance questionnaire are correct.' Below the signature area are two buttons: 'Clear signature' and 'Done signing'. At the bottom left of the employee list is a 'Reject All' button.

TIP

You can customize compliance questions for the specific needs of your company.

2.3.8 SUBMIT AND SYNC

Like the planning phase, you must select Submit to send the daily plan to the Approval Phase. All employees must be signed out to submit the daily plan for approval. Tap the Sync button to push any updates to the InEight Cloud Platform.


Scenario Recap

Steve and his crew could execute the work on the jobsite and he was able to complete the Execution Phase of his daily plan by navigating through each tab of the navigation bar. At the end of the shift when all employees had signed out, he submitted the daily plan for approval.

2.4 NAVIGATE APPROVAL

2.4.1 PLAN LIST


You access a daily plan from the list of daily plans. Note that the current status is now Awaiting Approval. There is also a note indicating that the quantities have not been approved.

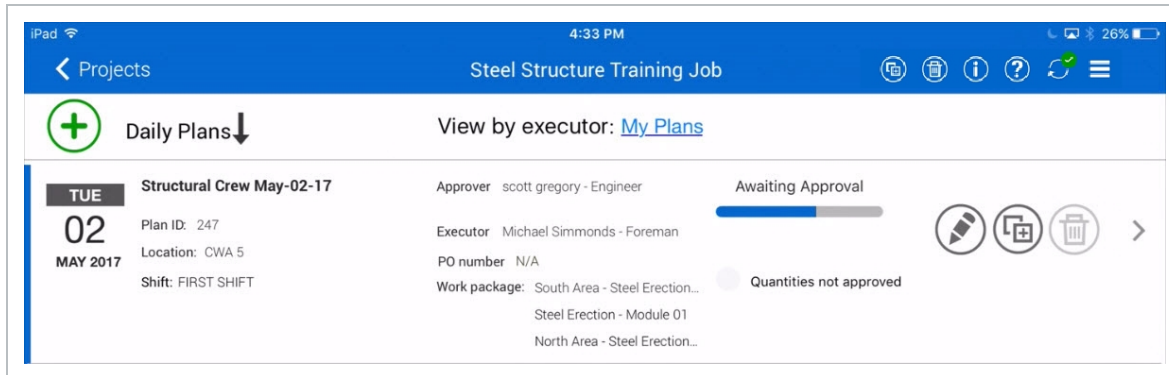


Navigating through the Approval Phase is very similar to the Planning and Execution Phases. The same navigation bar appears at the top of the screen. You can review the information in each tab to ensure everything has been entered correctly. The Submit button is now gone and is replaced by two new buttons.

Overview - Sign out Tab


Title		Description
1	Approval	Approves actual quantities, hours or both.
2	Reject	Rejects the plan and sends it back to the Execution Phase.
3	Reject Sign out	Rejects the sign out for an individual employee. This must be done before editing any hours on the Time sheet. The employee must sign out again after changes have been made or the supervisor approving the timecard can sign out on behalf of the employee.
4	Reject All	Rejects the sign out for all employees. This must be done before editing any hours in Time sheet. The employee must sign out again after changes have been made.

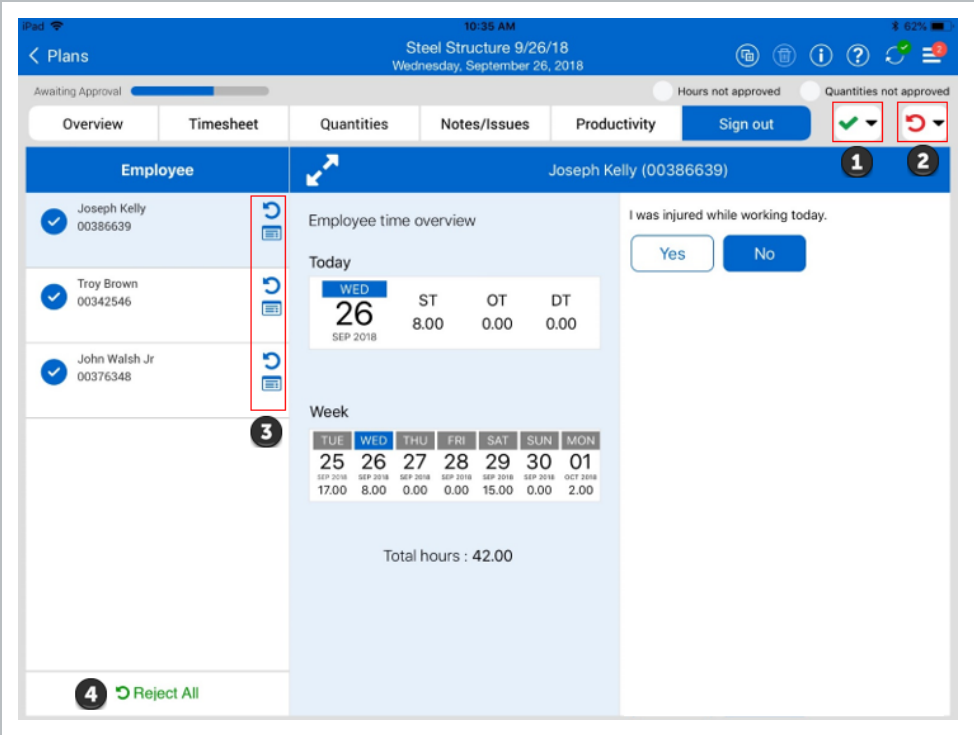

There is no requirement to enter new information in the Approval Phase. If the information is all correct, the plan can simply be approved by selecting “Approve Quantity and Hours”. If there are changes to be made that affect quantities, but the hours are correct, then you can select “Approve Hours” to send the hours to ERP payroll for processing while the changes to quantities are sorted out. The opposite is true when the quantities are correct but changes to the hours are required.

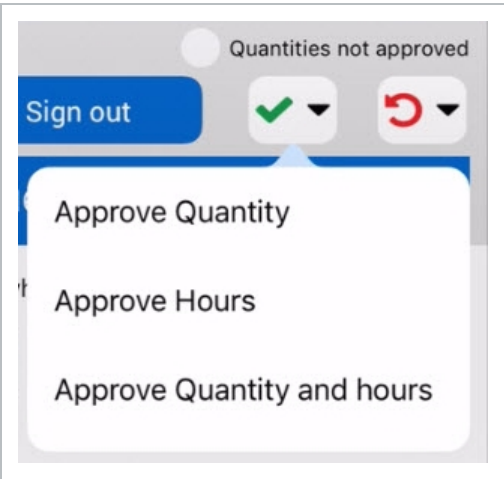

If significant changes are required, or if the Executor is the member required to make changes, it is recommended to revert the Daily Plan back to the Execution Phase before making the changes. In this case, you can select the “Reject Plan” button.

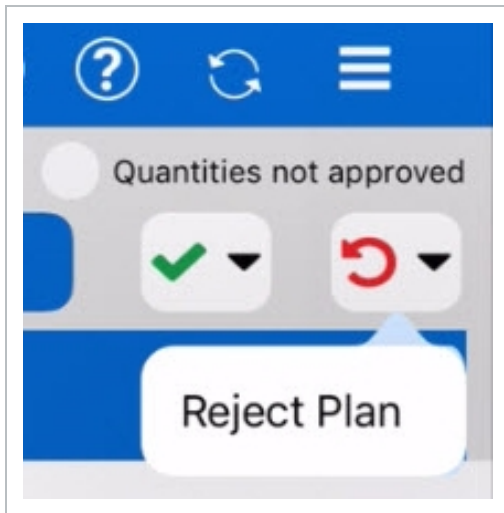

2.5 DATA SYNC

The InEight Progress application must be synced periodically receive updates from other InEight Cloud modules and vice versa. The following table explains the different sync symbols you may encounter when using InEight Progress.

Icon	Title	Description
	Available (Online)	App is online but has not been synced.
	Offline	App is offline.
	Unsynced Changes	Changes have been made to plans that haven't been synced (number of plans with unsynced changes will appear in red dot).
	Syncing	App is currently syncing (icon will spin).
	Success	Latest sync was successful.
	Failed	Latest sync was unsuccessful.

TIP

You can use InEight Progress Mobile online or offline. A Wi-Fi or cellular connection is only required to perform a sync.

2.6 ATTACHMENTS ON MOBILE


In the mobile application, you can attach files to a daily plan and view existing attachments.

NOTE You can only attach files from your device. To attach files from InEight Document to a daily plan, you must use the web application.

The following steps show you how to add an attachment from your device during any phase of daily planning.

2.6 STEP BY STEP 1 – ADD AN ATTACHMENT ON MOBILE

1. In a daily plan, tap the **Attach File** icon in the upper right of the page.
2. Select **Upload document from device** from the drop-down menu.

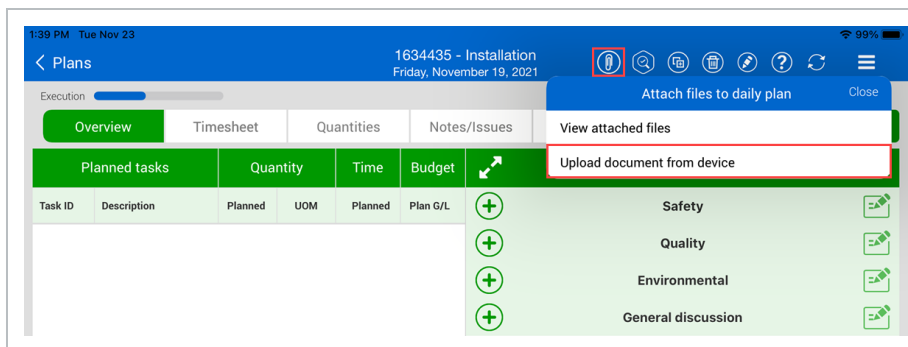

3. In the Upload Documents dialog box, tap the **Add** icon.
4. Select the file from your device, and then tap **Upload**.


NOTE An attachment must be 10 MB or less.

The following steps show you how to view an attachment during any phase of daily planning.

2.6 STEP BY STEP 2 – VIEW AN ATTACHMENT ON MOBILE

To view an attachment during any phase of daily planning, tap the **Attach File** icon in the upper right of the page, and then select **View attached files** from the drop-down menu.

1. Tap the **Attach File** icon in the upper right of the page.
2. Select **View attached files** from the drop-down menu.
3. In the Attached Files dialog box, tap a file to view it in a new window.

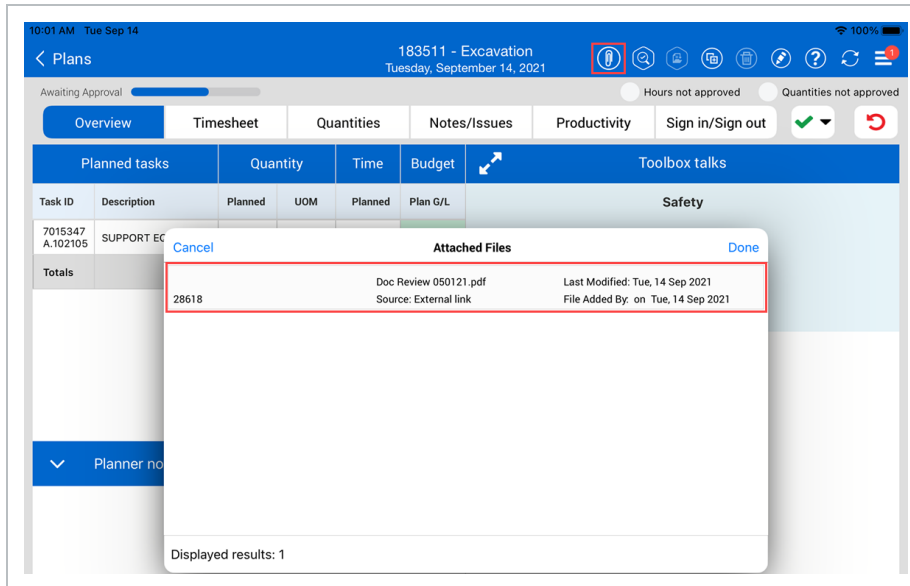
**NOTE**

You can only view attachments whose source is InEight Document in the Document mobile app if you have the app downloaded and have access to the same project in Document.

2.7 DAILY PLAN FROM SCRATCH

Scenario


Today, your crew is installing two columns of the Support Steel Structure 1 (green columns). Your plan for tomorrow is to install the horizontal and cross member assemblies (red cross bracing).

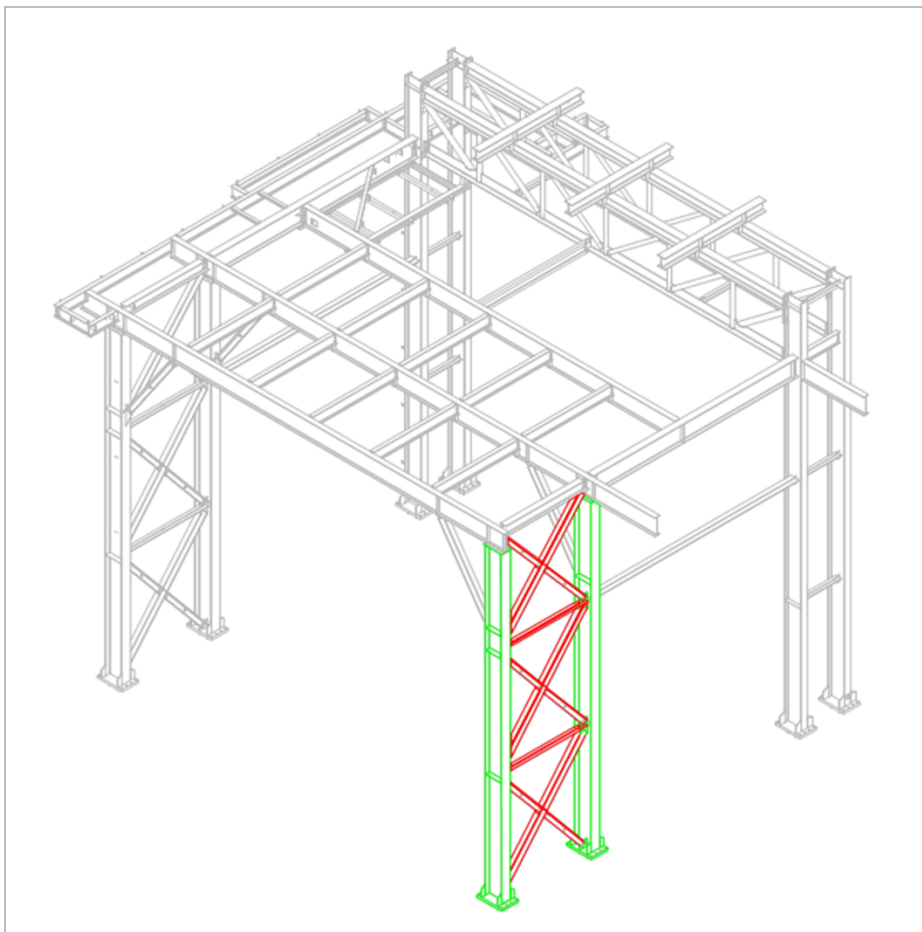

The steel members you will be installing are:

- A23
- A24
- B23
- B24
- C23
- C24
- D23
- E22
- E23

- E24
- F22

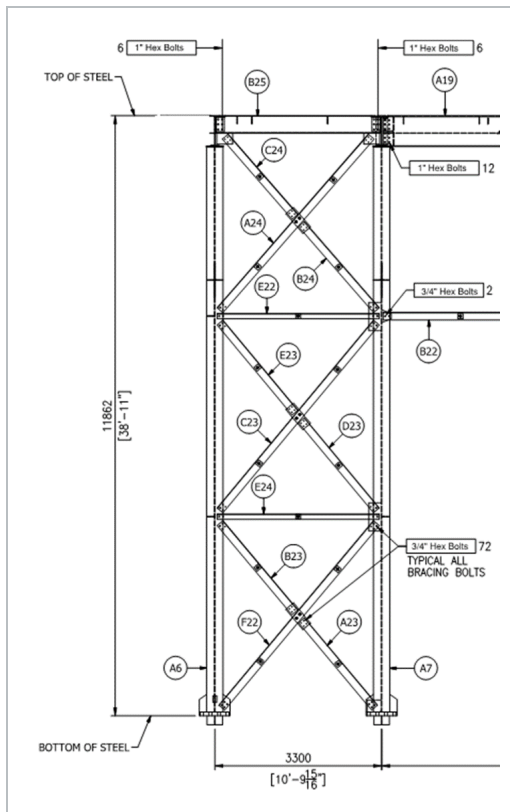

The plan for our crew tomorrow will be to shake out and transport the steel members by truck to the work area. We will also plan to erect and bolt up members C23, D23, E23, and E24. We will use a JLG to help with erection.

A plan is a list of steps that includes the time and resources (labor and equipment) that is used to achieve a goal or objective.

In InEight Progress Mobile, you can create a plan from scratch, if there is no existing plan to use that was previously created on the project. A plan can be created by either a foreman or an engineer.

2.7.1 PLAN CREATION

To create a plan from scratch, you are required to provide:

- The date the plan will be executed
- The approver of the plan (normally the originator of the plan, such as a field engineer or superintendent)
- The executor of the plan (normally the overseer of the work, such as a foreman)


NOTE

You must provide a date of when the plan will be executed, select an approver, and select an executor when you create a plan from scratch.

If an executor or approver is removed from the project, an error will appear in the Progress Mobile application prompting you to replace them on your daily plan.

Some projects or organizations may choose to not require an executor which is a setting that can be changed in the project settings. Refer to the Progress Admin User Guide for more information on settings.

After logging into the Progress Mobile app, you will land on the Projects home page where you can select one of your assigned projects.

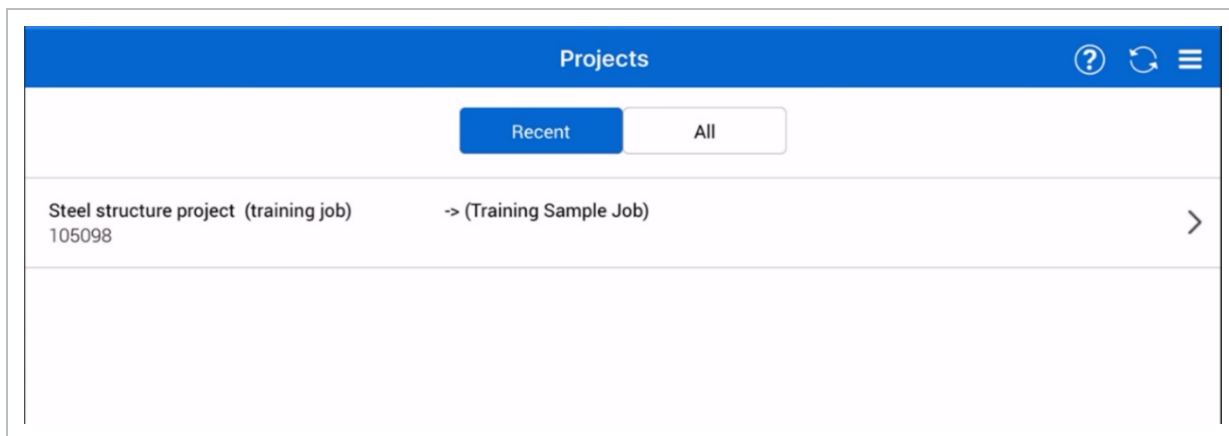


When you select the project you want to create a daily plan for, you will open the Daily plans page, where you will see the **Add**  button.

The Add button opens a slide out panel from the left where you can provide a plan description, location and date. You can also select an approver, executor, Work plan/package ID, and associated vendor. When you have completed the plan information, you create the plan by selecting **Add** in the top right corner.

The screenshot shows a mobile application interface for creating a new daily plan. At the top, there is a header bar with a green plus icon, the text 'Daily Plans', a downward arrow, and a 'View' button. Below the header, there is a 'New daily plan' form. The form has a 'Cancel' button on the left and an 'Add' button on the right. The form fields include: 'Date' (set to 'June 02, 2022'), 'New Plan Name', 'Location (optional)', 'Shift' (set to 'FIRST SHIFT'), 'Approver' (with a dropdown arrow), 'Executor' (with a dropdown arrow), 'Work plan/ package' (with a dropdown arrow), 'Associated vendor' (with a dropdown arrow), and 'Skip planning' (a toggle switch that is currently turned on).

2.7.1.1 DAILY PLAN ID

When you create a new daily plan in the Progress Mobile application, the daily plan ID will be pending until it is synced with the Progress Web application. Once a daily plan ID is assigned to the plan, it will be visible along with the plan description at the top of the screen.

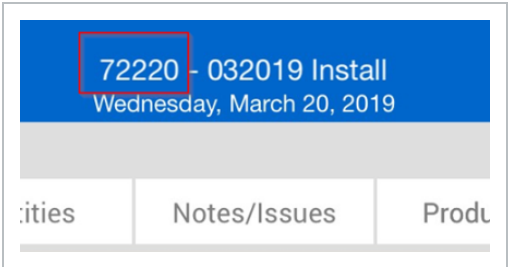

Once you create your plan, you will open to the Overview tab of the plan where you can enter information such as Planner Notes, Safety, Quality, Environmental, and General Discussion notes. To review or edit this initial information from any screen, you can select the  icon.

Light Steel Install - Structure 1

Tuesday, September 25, 2018

s

Notes

Time

Budget

anned

Plan G/L

Light Steel Install - Structure 1

Edit

Tuesday, September 25, 2018

Scottsdale

Shift

First shift9 2324

Approver

Jacob Rose - Account Administrator- Copy

Executor

Bridgette Quintero - Foreman

PO number

N/A

Work plan/ package

None

2.7.1.2 OVERVIEW TAB

After you create a plan, within the Overview page you can provide key plan information, including:

- The safety information pertaining to the Operation
- Quality concerns or required hold points
- Environmental concerns regarding your work or the area near your work
- Other notes regarding best practices

These notes become a reminder as you execute and review the plan, to ensure the required inspections for a particular section of your work are completed.

Within the General Discussion section is a note field, where you can include information to talk to your crew or foreman about, that doesn't fit in the three major categories: Safety, Quality, and Environmental. Examples include:

- A pending RFI requires a response from the engineer in order to perform a section of work due to a design conflict
- A reminder of material requisition that you need to complete for upcoming work

Aside from entering notes, you will be able to view your planned tasks information on the Overview tab after you enter your resources, quantities, and time into the other tabs.

Plans
Light Steel Install - Structure 1
Tuesday, September 25, 2018

In Planning


Overview
Timesheet
Quantities
Notes/Issues
Productivity
Sign out
Submit

Planned tasks		Quantity		Time	Budget	Toolbox talks	
Task ID	Description	Planned	UOM	Planned	Plan G/L		
Planner notes Verify steel member dimensions with updated drawings to ensure correct installation.						Safety Safety concern Mitigation Human - Equipment Interface Use spotter at all times.	
						Quality Quality concern Mitigation Material Quality Cover stockpiles	
						Environmental Environmental concern Mitigation Spills from JLG Use drip trays under equipment when not in use.	
						General discussion RFI-Metals-001 submitted to client. Allow 5 days for review and answer.	

2.7.2 TIME SHEET TAB

2.7.2.3 ADD TASKS


The key aspect to planning work is the task or objective that needs to be completed. You add tasks under the Time sheet tab. Tasks are scopes of work that equal one cost item or line in the overall project budget. They are the charge codes you will charge employee and equipment hours to. Tasks are designated by a unique WBS number which is established in InEight Control and can vary greatly from company to company based on how you standardize cost coding structures.

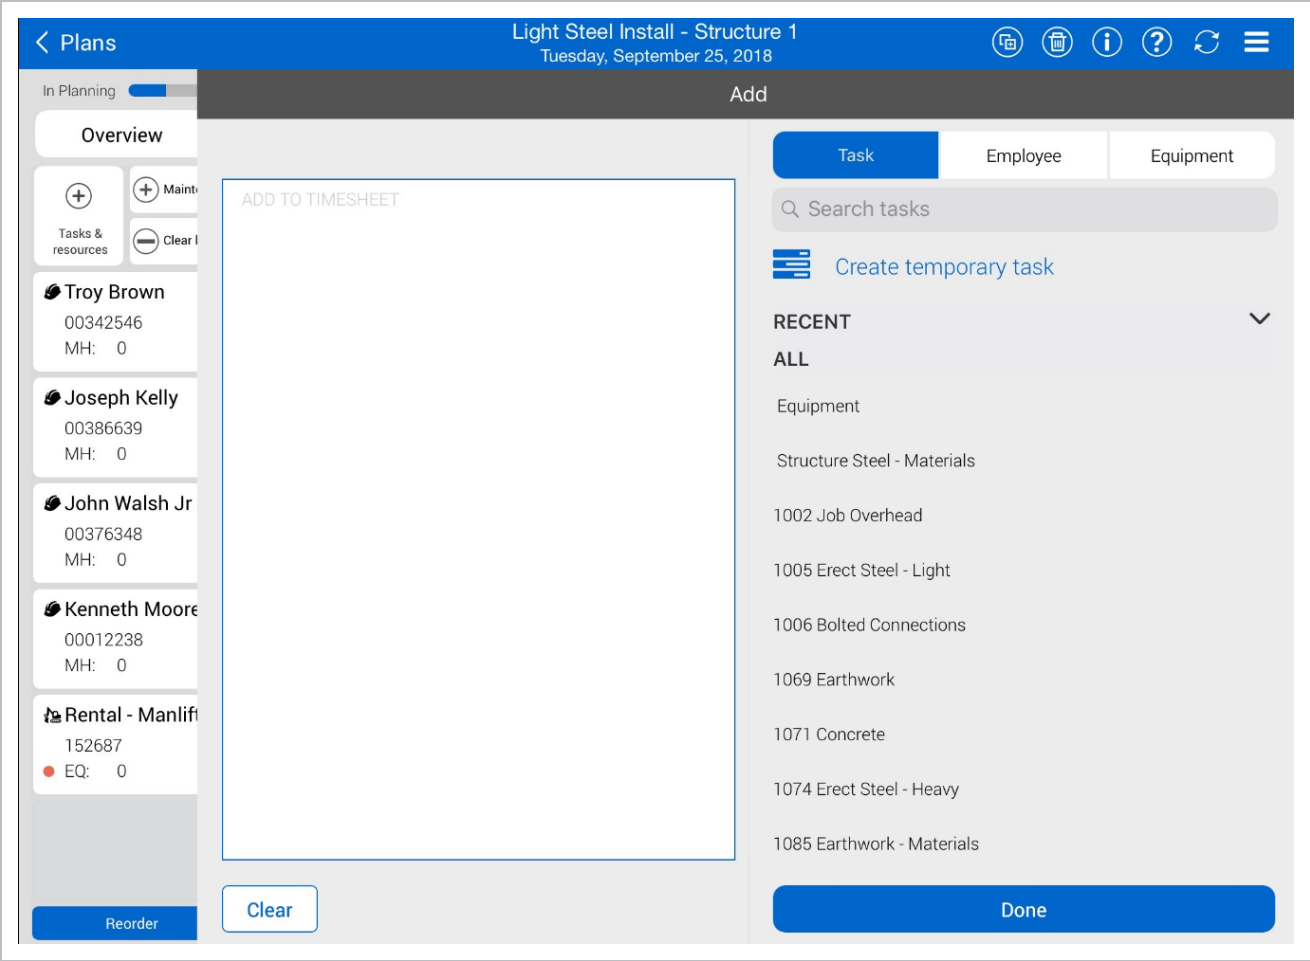

2.7.2.4 ADD EMPLOYEES AND EQUIPMENT


Part of planning the work includes planning the work hours for your labor and equipment resources to accomplish each task.

On the Time sheet tab, the foreman and/or engineer plans how long each crewmember and piece of equipment will be used to perform a specific task in your plan to maximize the crew's productivity and reduce cost, so there is no equipment standing by or crewmember roaming around with no work to perform.

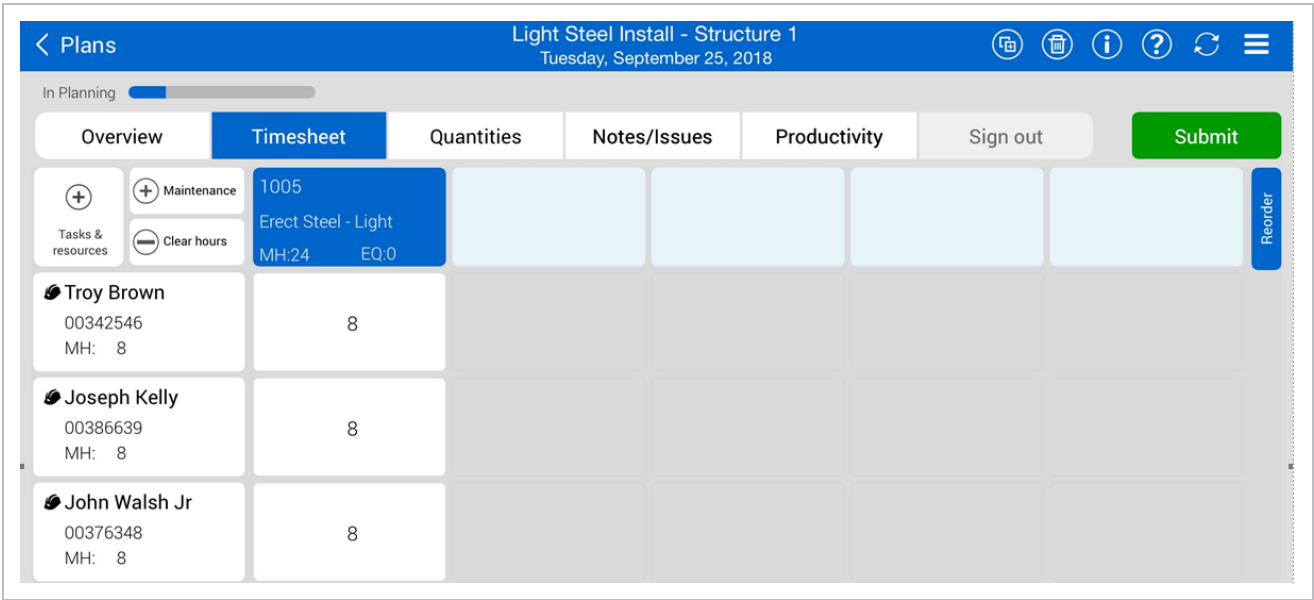

You can select employees from the projects list, add a temporary employee or scan a QR code to look up employees.

For the equipment, you can select from the projects list or add a temporary piece of equipment.

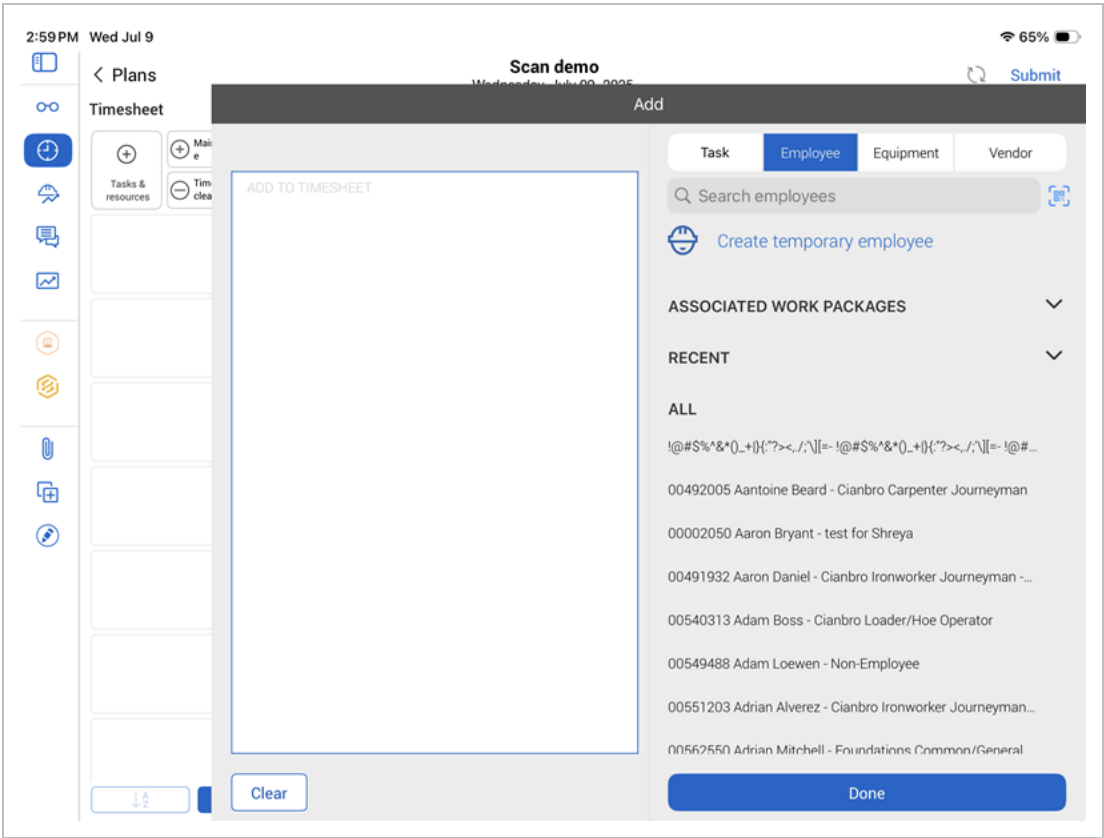

You can add employees and equipment only if the plan date is within the resources' project start and end dates. These dates are managed in your project's Assigned operational resources page.


NOTE

If you change project employee or equipment dates after they are already added, and the plan date is outside the new project employee or equipment dates, an inactive employee or equipment icon is shown.

2.7.2.5 ADD VENDORS

If your project has vendors who are completing work, you can add the vendors to a Time sheet to assign labor hours directly to the vendor and enter the number of vendor employees who worked. Vendor data comes from InEight Control, where you assign vendors to individual cost items to indicate that a certain scope of work will be completed by a third-party vendor.

To add a vendor to the Time sheet, tap **Tasks and resources**, and then tap **Vendors** in the slide-out panel. Select vendors from the left side of the panel, and then tap **Done**.

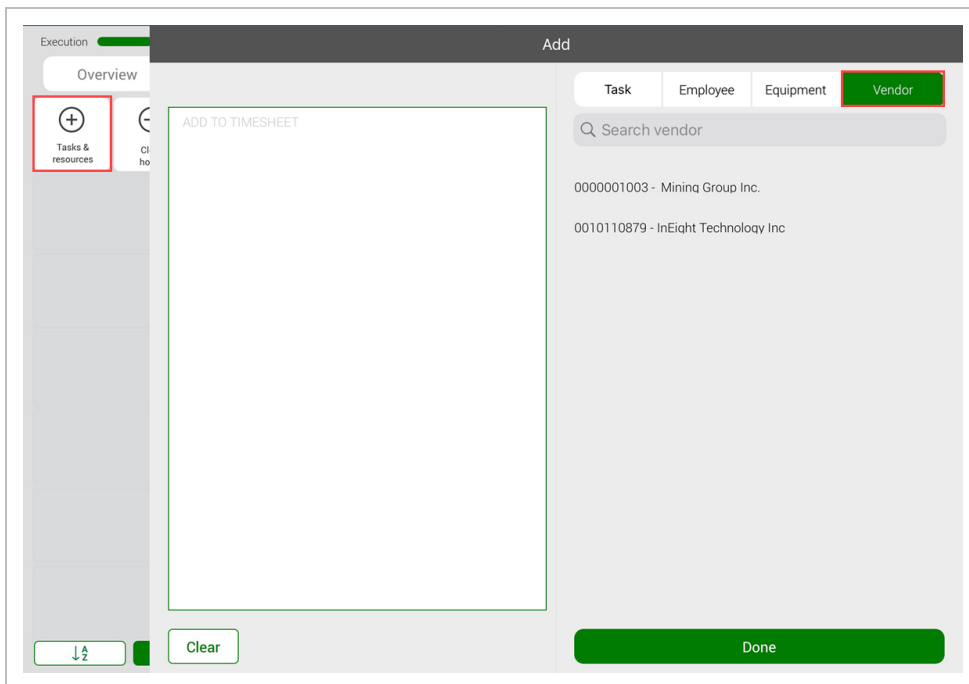

2.7.2.6 TEMPORARY EMPLOYEES AND EQUIPMENT

As you are going through the list of equipment for your project, if you cannot find the right equipment for the operation, you can create a temporary piece of equipment in InEight Progress. To create a temporary piece of equipment you will need to have a Temporary Equipment ID and Name.

2.7.2.7 ADD HOURS


After you add tasks, labor, equipment, and vendor resources to the project, you can add time to the tasks and resources.

- Time units are in hours
- You can plan the work for straight time, overtime, or double time
- To enter hours, you tap on the hour box
- If you want to apply the same hours to other selected employees, you can select the **Apply hours to selected employees** option
- If the planned hours for all employees will be the same, you can select the option **Apply hours to all employees for the task**
- If you select the ? icon, you can bring up the help screen
- If you are adding hours to a vendor resource, there is an additional Number of employees field.


The screenshot shows the InEight mobile app interface on an iPad. The top status bar indicates 2:59 PM and 67% battery. The app header shows 'Plans' and 'Structural Crew 8-27-19' for 'Tuesday, August 27, 2019'. The main screen has tabs for 'Overview', 'Timesheet', 'Quantities', 'Notes/Issues', 'Productivity', 'Sign out', and a green 'Submit' button. A list of tasks and resources is on the left, including 'Conlin C' (000000 MH: 0), 'Darrel P' (002403 MH: 0), 'Donald I' (003641 MH: 0), 'Nick J. C' (002406 MH: 0), and 'Grove-R' (MC-100 EQ: 0). The 'Timesheet' tab is active, showing a grid of tasks. Task 1005 'Erect Steel - Light' is selected. A modal dialog titled 'Task: 1005 Erect Steel - Light' is open, showing 'Employee: 00000002 Conlin Connolly - Iron Worker (Structural)'. The dialog has a 'Planned Employee Hours' section with input fields for 'ST' (8), 'OT', and 'DT'. Below this is a 'Total hours' field showing 8. At the bottom, there are two radio buttons: 'Apply hours to selected employees' (selected) and 'Apply hours to all employees for the task'. There are 'Cancel', 'Done', and 'Clear' buttons. A numeric keypad is visible on the right side of the dialog.

2.7.2.8 APPLY HOURS TO SELECTED EMPLOYEES


To save time, you can add hours to multiple employees at once. To do so, you would tap on the hours box for an employee and enter the number of hours you plan for them to work. You can then select **Apply hours to selected employees**.

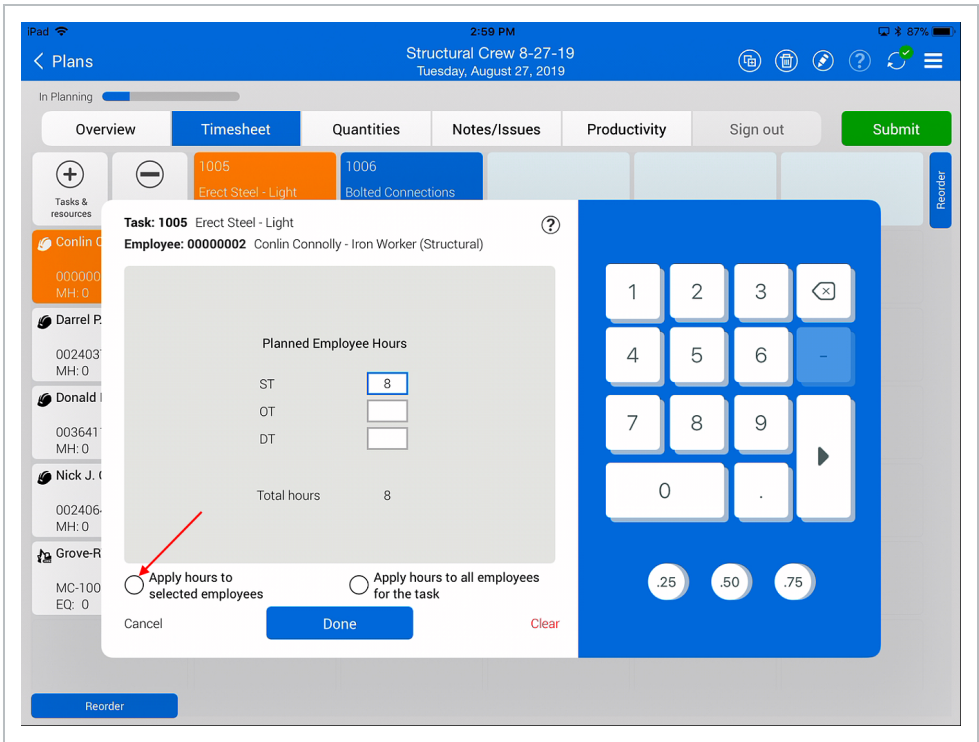

The Apply Hours dialogue box appears with further instructions. You can check the box to not show the message again, to avoid it in the future.

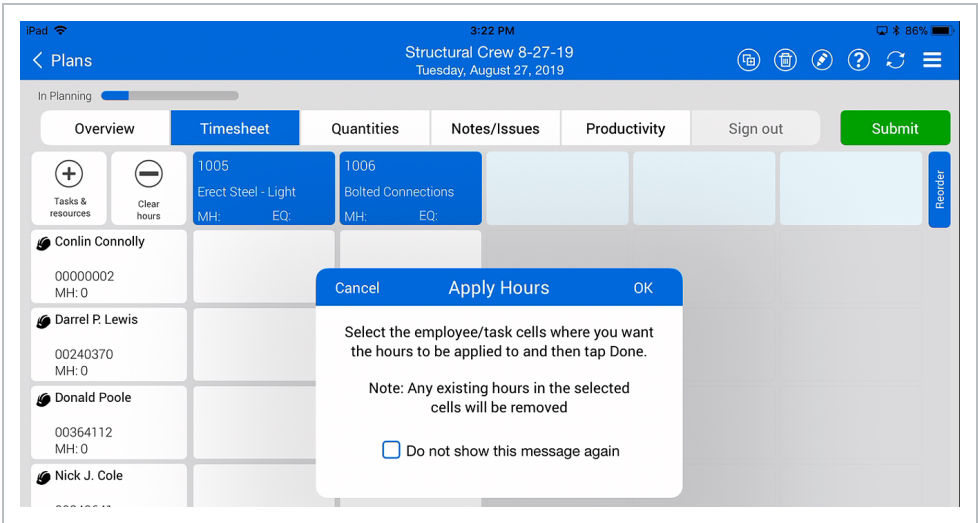


When you tap OK to close the dialogue, you can then select the hours boxes for all the employees you want to assign the same number of hours to, then tap Done.

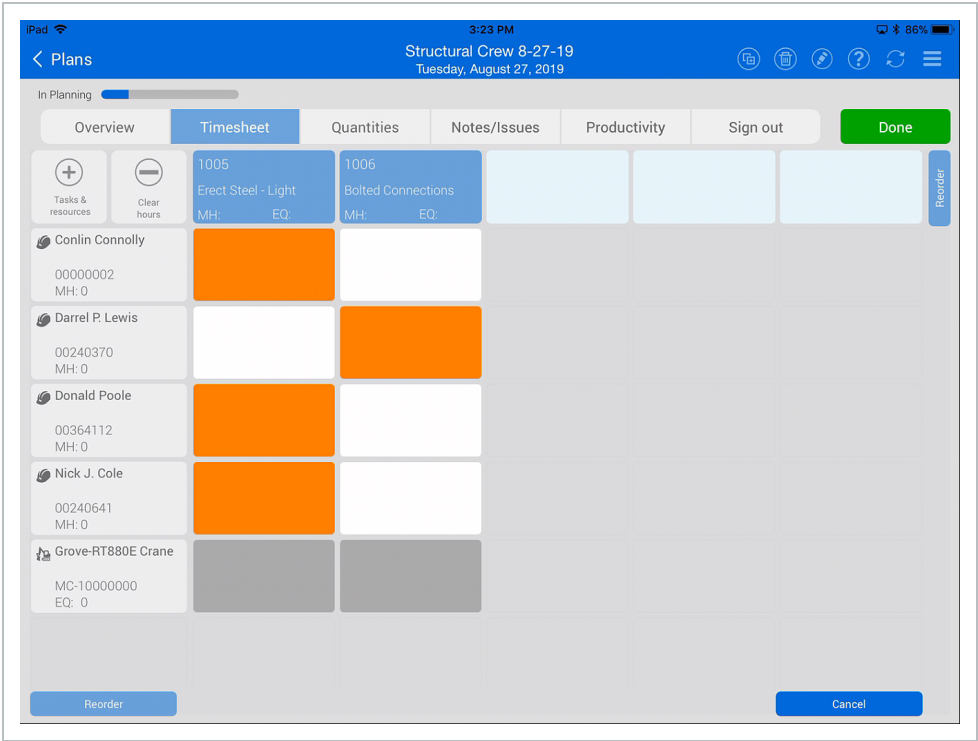

2.7.2.9 ADDITIONAL OPTIONS

By tapping on the individual employee box, you will have the following options:

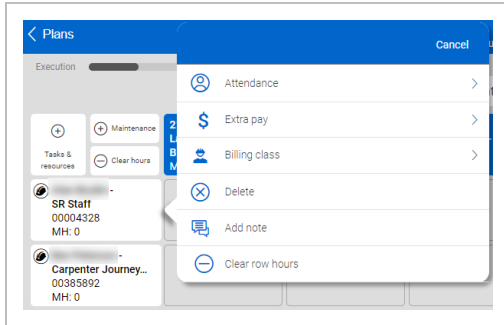

- When you select **Attendance**, you can mark an employee present, absent excused – unpaid, absent excused – paid, and absent unexcused – unpaid
- When you select **Extra pay**, you have the choice from none, premium, Foreman for the day, pay scale level change, and additional lump sum amount
- When you select **Billing class**, you can override the employee's default billing class with a different billing class.

NOTE

This change is only temporary. The employee's default billing class is not changed.

- Add a note
- Delete row
- Clear row hours

2.7.3 QUANTITIES TAB

Progress pulls in quantity components associated to cost items from InEight Plan to the Quantities tab, where you can select the planned quantities to be completed.

Plans Light Steel Install - Structure 1
Tuesday, September 25, 2018

In Planning

Overview Timesheet **Quantities** Notes/Issues Productivity Sign out **Submit**

Task **Add Components** 1005 - Erect Steel - Light

1005
Erect Steel - Light

Module 01 - C23: Cross Brace Assembly Module 1 - C23: Cross Brace Assembly

Priority	Complete	Step	Quantity	UoM	To-date quantity	Planned Quantity
🚩	☐	Shakeout/Tra...	0.25816	Ton	0	0
🚩	☐	Erect/Bolt Up	0.25816	Ton	0	0
🚩	☐	Final Torque	0.25816	Ton	0	0
🚩	☐	QC Verification	0.25816	Ton	0	0
Component Total			0.25816	Ton	0.000	0.000


Task Total **Ton** 0.000

2.7.3.10 COMPONENTS

Components are portions of a cost item created to divide cost item quantities into manageable and identifiable tasks, so they are easier to track out in the field. A component can be a beam, light pole, systems testing for a switchgear, a jet fan, etc. Within the components, you will see a breakdown of steps for completing the component.

On the Quantities tab, you can add tasks from your project list or add a temporary task.

- If you select a task from the project list, you will be able to see components loaded for that task, if they are associated with a Daily plan
- If no work plan was associated, you can go back to the Daily plans page and add a work plan
- If the Daily plan cannot be associated to any work plan, then within the Quantities tab, you can add a temporary component

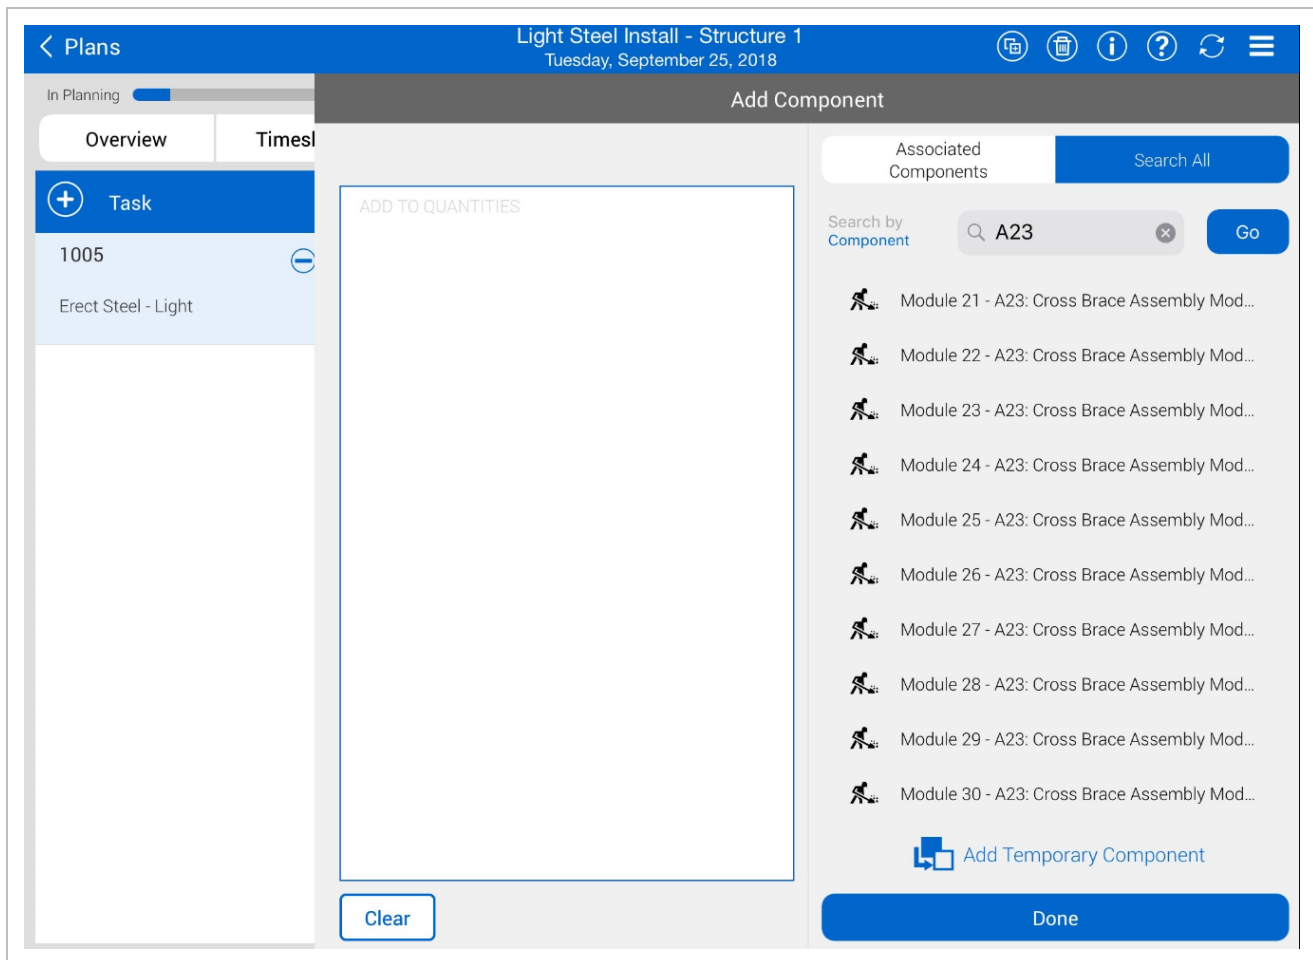

There are several types of components:

- Activity – Disciplines that show claiming schemes for physical work such as electrical
 - Denoted by 
- Material – Commodities that show claiming schemes for materials such as anchor bolts
 - Denoted by 
- Contract – Linked to Schedule of Value items in InEight Contract for billing validation.

2.7.3.11 PLANNED QUANTITY

The planned quantity gives you an idea of what to work towards as a goal. Meeting the planned quantity goal will keep you on schedule with completing the task and let you know how much quantity should be complete by the end of the day.

Plans

Light Steel Install - Structure 1

Tuesday, September 25, 2018

In Planning

Overview

Timesheet

Quantities

Notes/Issues

Productivity

Sign out

Submit

+

Task

1005

Erect Steel - Light

+

Add Components

1005 - Erect Steel - Light

Module 01 - C23: Cross Brace Assembly

Module 1 - C23: Cross Brace Assembly

Priority	Complete	Step	Quantity	UoM	To-date quantity	Planned Quantity
	☐	Shakeout/Tra...	0.25816	Ton	0	0
	☐	Erect/Bolt Up	0.25816	Ton	0	0
	☐	Final Torque	0.25816	Ton	0	0
	☐	QC Verification	0.25816	Ton	0	0
Component Total			0.25816	Ton	0.000	0.000

Task Total

Ton

0.000

2.7.3.12 CONTRACTS

Contracts can be added to a daily plan so that you can add associated contract components to track for billing validation.


NOTE

A contract must be associated with the same project and have schedule of value items to be available in a daily plan.

The following steps show you how to add a contract.

ADD A CONTRACT TO A DAILY PLAN

1. On the Quantities tab of a daily plan, click **Add task or contract** in the lower left of the page.

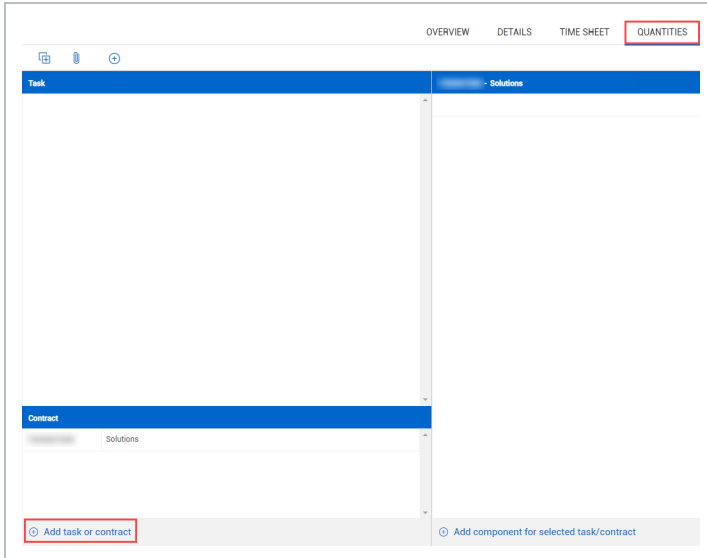

2. In the slide-out panel, open the **Contract** tab, and then select one or more contracts from the list. Selected contracts are moved to the Add to daily plan list.
3. Click **Done**.

After you add a contract, you can add any associated contract components in the Quantities tab.

2.7.3.13 CONTRACT COMPONENTS


Contract components are used to track quantities for billing validation.

NOTE A contract component is automatically created from Contract when a schedule of values item for a contract is not set to hide in Plan and Progress.

The following steps show you how to add a contract component to a daily plan. You must add a contract to the daily plan before adding a contract component.

ADD A CONTRACT COMPONENT TO A DAILY PLAN


- 1. Select a contract from the Contract list in the lower left of the Quantities tab.
- 2. Click **Add component for select task/contract.**

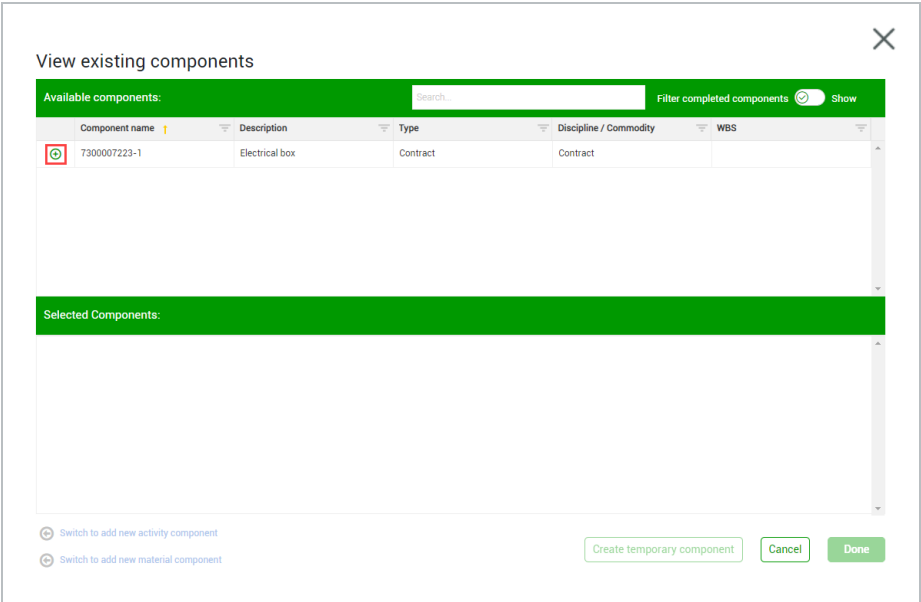

- 3. Select a contract component from the View existing components slide-out panel, and then click **Done.**

2.7.4 PLANNING SLIDE-OUT

You can access the Planning Slide-Out by tapping on this icon in the Tasks column.

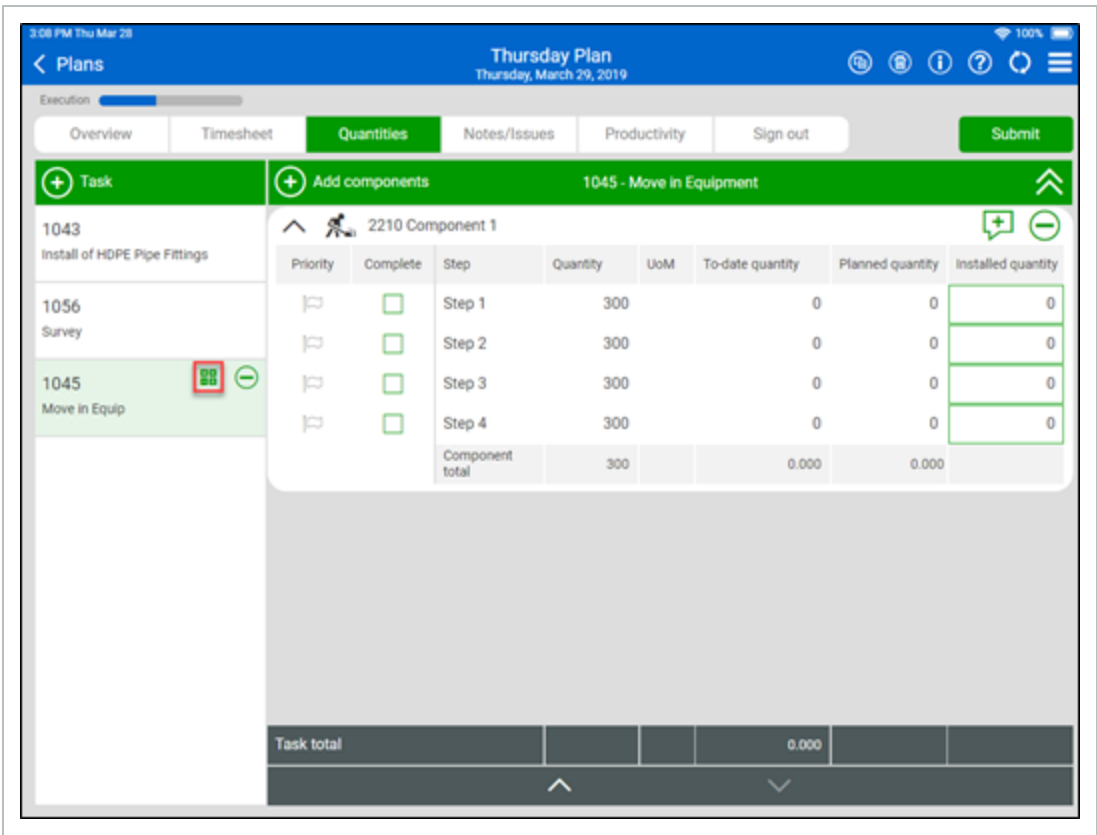

On this slide-out, you can view the quantity needed to break even for the selected task. Additionally, you can manually enter any quantity to see how it would affect the gain/loss for the selected task.

The screenshot shows the 'Calculate costs' dialog in the Progress User Guide app. The dialog has a blue header with 'Cancel' and 'Done' buttons. Below the header is a table with the following data:

Task	Cost	UoM
1043 Install Labor	\$ 3,600.00	
1056 Equipment	\$ 940.00	
Task total cost	\$ 4,540.00	


Below the table is a 'Break even' section with a blue information icon. It says 'Quantity needed to break even for this task.' and has a 'Qty' field with '454' and a 'UoM' field with 'LF'. Below this is a 'Calculate G/L' section with a blue information icon. It says 'Enter quantity to calculate Gain/Loss for this task, given the current Labor and Equipment hours.' and has a 'Qty' field with '454' and a 'UoM' field with 'LF'. There is a blue 'Calculate' button next to the 'Qty' field. At the bottom, there is a summary row: 'Earned' \$ - 'Cost' \$ 4,540.00 = 'G/L' \$.

A calculator overlay is visible on the right side of the dialog, showing a numeric keypad with buttons for digits 0-9, a decimal point, a minus sign, a 'Del' button, and a 'Next' button. There are also buttons for fractions: .25, .50, and .75.

2.7.5 NOTES/ISSUES TAB

The Notes/Issues tab is where you can note important information critical to your daily plan. Example notes might include:


- A permanent material needed as part of the installation work
- A Request for Information involving a change in the design that impacts the installation and daily plan
- An environmental concern
- Leave of Absence or extra pay for an employee

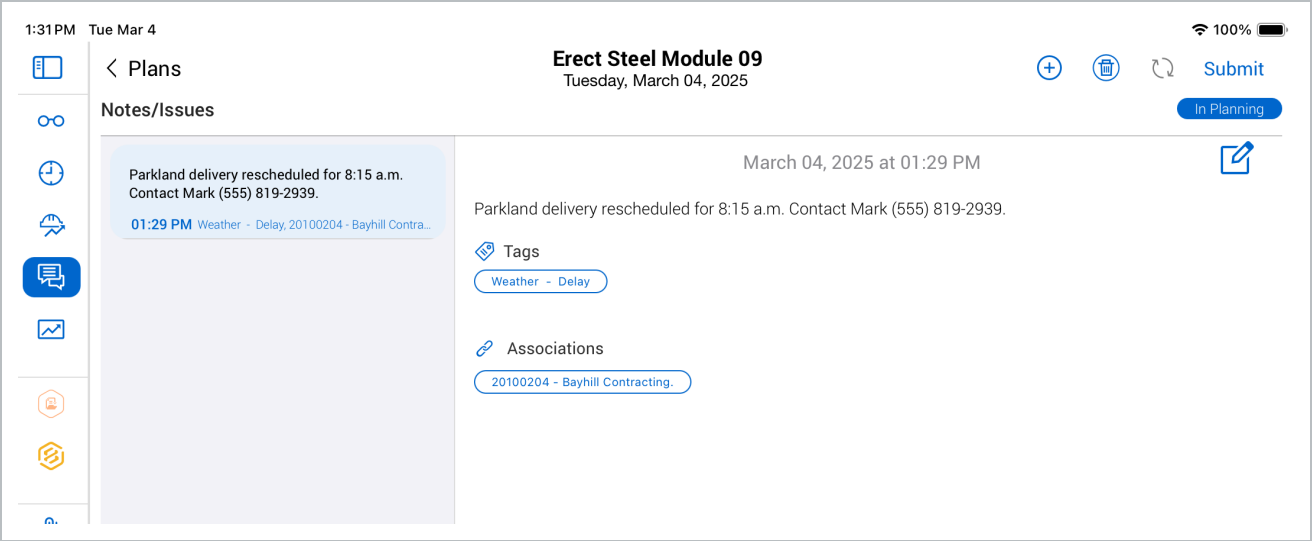

When you enter a note or issue, you can associate it with a tag, association, or picture.

2.7.5.14 TAGS AND ASSOCIATIONS


You can tag your notes or issues to group similar items for reporting purposes. Tags are configured in Organization Settings > Progress > Notes.

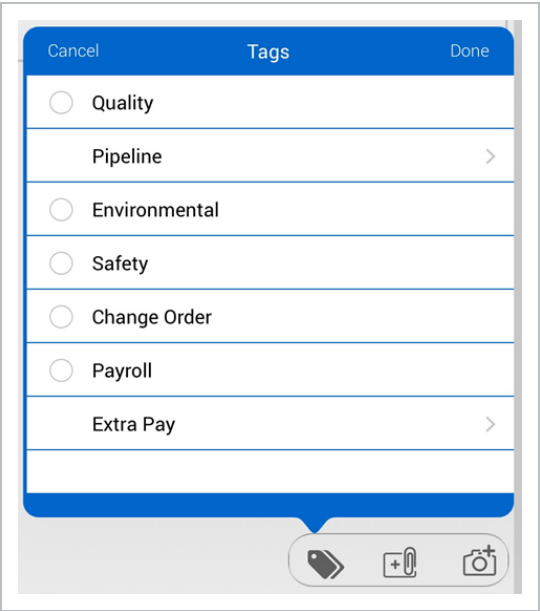

You can also associate notes and issues to any of the following categories:


- Task
- Employee
- Equipment
- Component
- Maintenance Task
- Vendor

After you tap a category name, you can select an association.

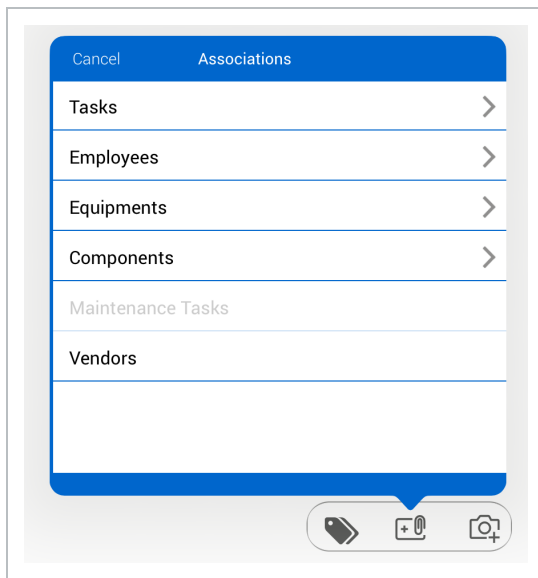


2.7.5.15 ADDING AND EDITING A PICTURE


You can add pictures to your notes or issues in the planning phase of your daily plan. You can add a picture from your Photo Library or take one directly from your device.

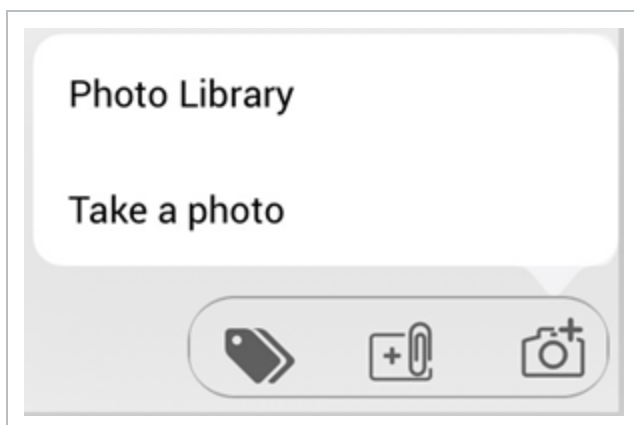

After you select a photo, you can move or resize the photo.

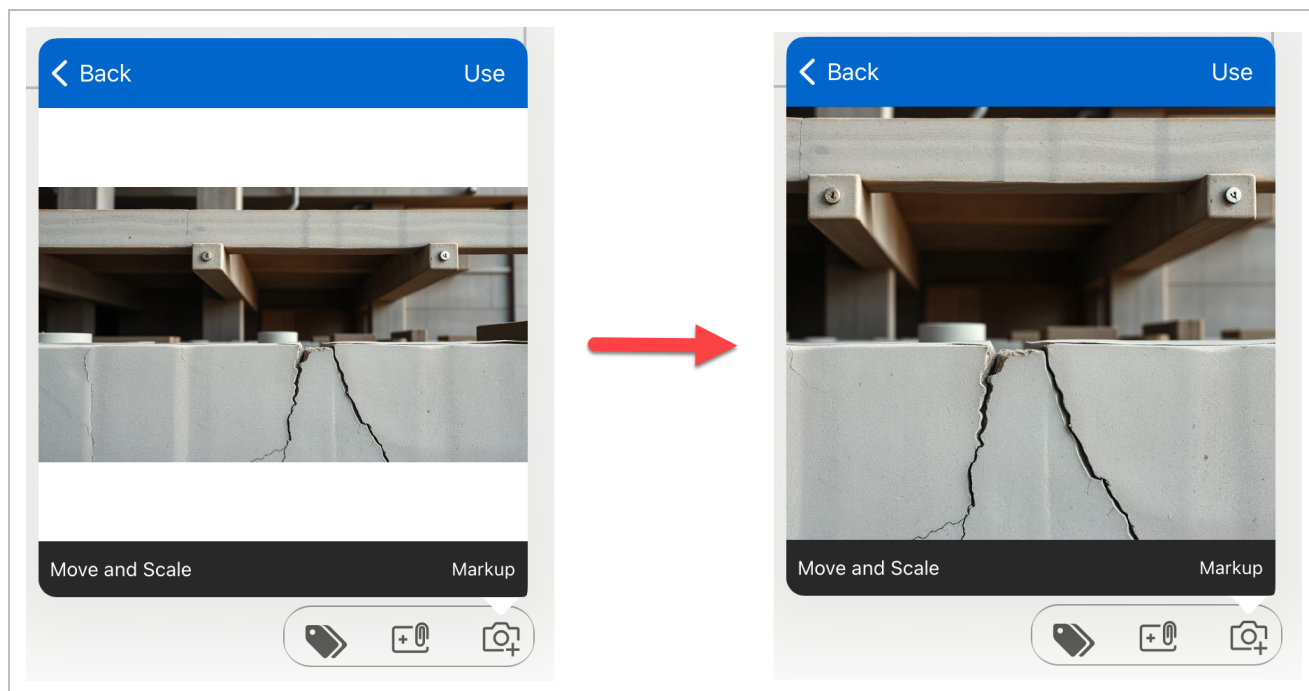

You can then add markups to your photos. To add markups, click the **Pen** icon at the bottom left to enable markup drawing. When you're finished, click **Done**.

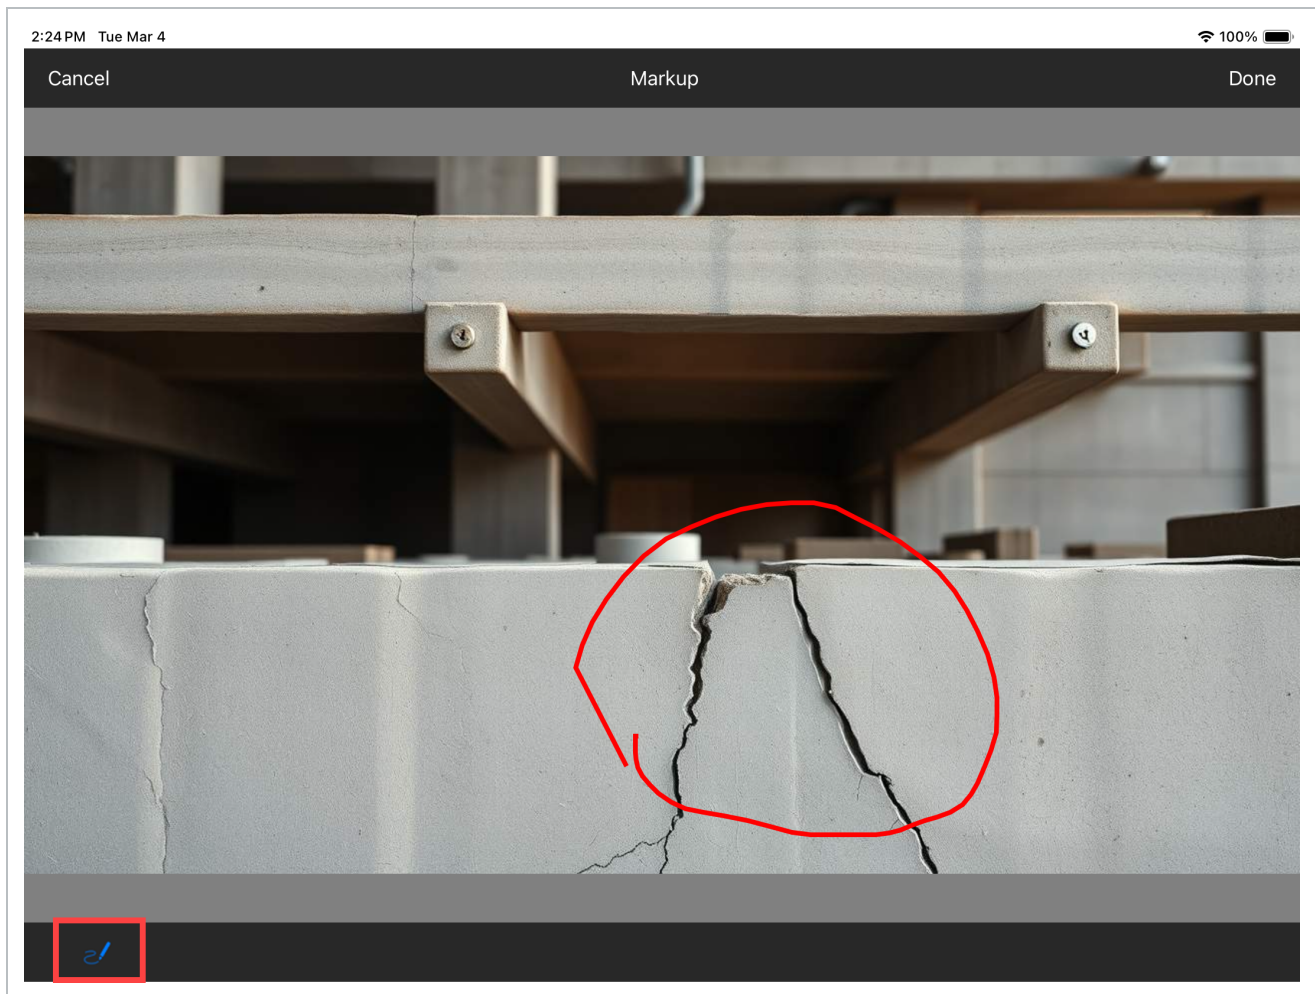

2.7.6 PRODUCTIVITY TAB

After planning your work within the Time sheet and Quantities tabs, you can view the quantities and man-hours within the Productivity tab.

On the Productivity tab, you can compare your planned quantities and man-hours against the budget. If there is an error for your planned quantities or man-hours, you can go back to the other tabs and revise.

< Plans

Light Steel Install - Structure 1
Tuesday, September 25, 2018

In Planning

Overview

Timesheet

Quantities

Notes/Issues

Productivity

Sign out

Submit

Task ID and Description		Planned			⇄ MHRs per Qty		Planned	
Task ID	Description	Quantity	UOM	MHRs	Planned	CB	Cost G/L	MHRs G/L
1005	Erect Steel - Light	0.155	Ton	32	206.590	20.000	155	-28.9
Totals				32			155	-28.9

2.7.7 SUBMIT AND SYNC BUTTON

Once you are complete with reviewing the Daily plan that you put together, you can now Submit and Sync the information, which updates the information to other applications and users in InEight. The engineer or superintendent that oversees your daily plans will then review and either approve or reject the Daily plan.

NOTE

Once you tap Submit, you can no longer edit the Daily plan in the planning phase. It will be moved into the Execution phase.

< Plans

Light Steel Install - Structure 1
Tuesday, September 25, 2018

In Planning

Overview

Timesheet

Quantities

Notes/Issues

Productivity

Sign out

Submit

Task ID and Description		Planned			⇄ MHRs per Qty		Planned	
Task ID	Description	Quantity	UOM	MHRs	Planned	CB	Cost G/L	MHRs G/L
1005	Erect Steel - Light	0.155	Ton	32	206.590	20.000	155	-28.9
Totals				32			155	-28.9

Submit plan to Execution

Are you sure you want to move this plan to Execution?

Cancel

Submit

2.7.8 CREATE A PLAN FROM SCRATCH WALK THROUGH

The following steps will walk you through creating a daily plan from scratch.

CREATE A DAILY PLAN FROM SCRATCH

1.

Log into the **InEight Progress** mobile application.
2.


Select a project from the Projects home page.
3.

Tap on the **Add**  button to create a plan from scratch.


The screenshot shows the 'Steel Structure Job' app interface. At the top, there's a blue header with a back arrow, the title 'Steel Structure Job', and icons for help, refresh, and menu. Below the header, there's a section for 'Daily Plans' with a green plus icon and a dropdown arrow. To the right, it says 'View by executor : My Plans' and a search icon. The main content area shows a list of existing plans with columns for date, description, status (Execution or In Planning), and action icons (edit, share, delete). A 'New daily plan' form is overlaid on the left side of the screen. The form has a 'Cancel' button at the top left and an 'Add' button at the top right. The fields in the form are: 'Date' (set to September 25, 2018), 'New Plan Name', 'Location (optional)', 'Shift' (set to Second Shift), 'Approver' (set to Jacob Rose - Account Administrator-...), 'Executor' (set to Jacob Rose - Kiewit Foreman), 'Work plan/ package' (set to Optional), and 'Skip planning' (a toggle switch).

4. Choose a date for the daily plan.
5. Give a description in the Enter Plan Description field.
6. Enter a location in the Enter Location field.
7. Select a **shift** from the Job Shift menu.
8. Select an **Approver**.
 - Maximum of 2 selections. Usually an engineer and superintendent
9. Select an **Executor**.
 - Only one selection. Usually a foreman
10. Select **Work Plan/Package**.
11. Select a work plan or package for the daily plan and tap **Back**.
12. Tap **Add** to create a plan.

13. Tap the **Add** button in the Safety section of Tool box talks to add project safety concerns and mitigation.
14. Tap the **Quality** tab and add a quality concern and mitigation.
15. Tap **Done** to add the Tool Box Talk items to the Overview screen.
16. Tap on the **Time sheet** tab.
17. Tap on the **Add** button.
18. If not already selected, tap the **Task** button at the top.
19. Select a task (i.e. 1005 – Erect Steel Light).
 - You can perform a search to find the task or scroll through the list

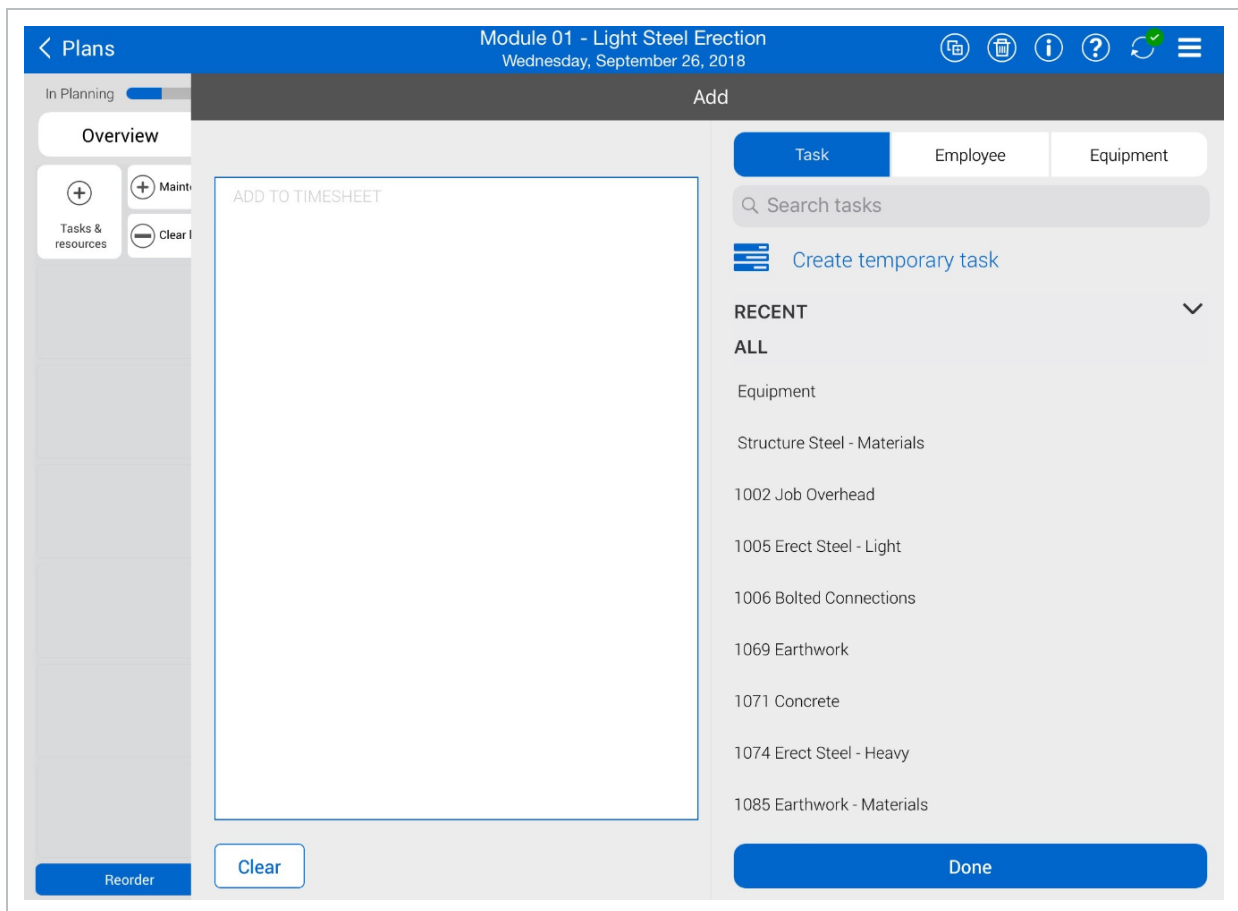

20. Tap on the **Employee** tab, then tap select the employees you want to add.
21. Tap on the **Equipment** tab, then select the equipment you want to add.

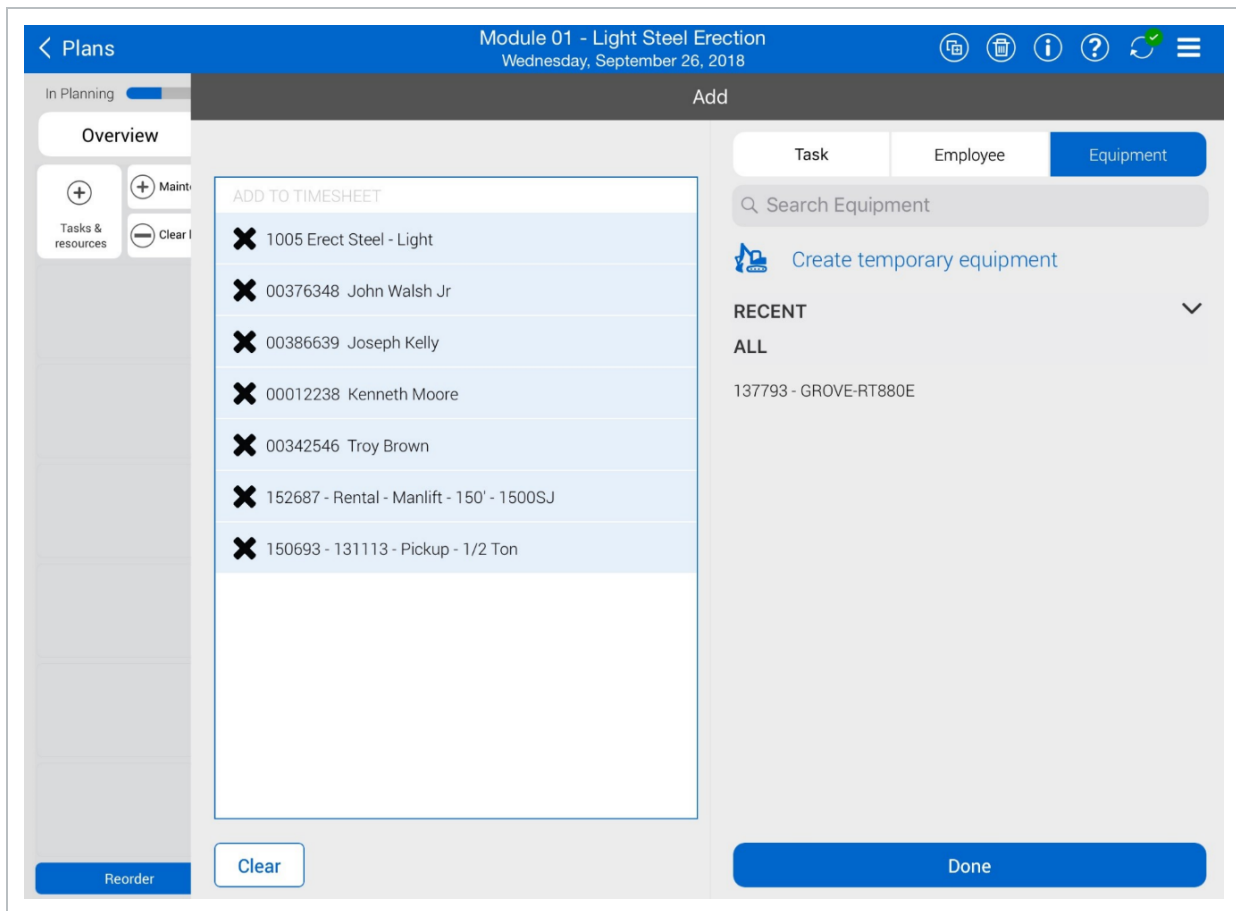

22. Tap **Done**.

- You will see the task, employee, and equipment appear on the Time sheet tab

23. Add employee time by tapping on the empty box next to an employee name.

TIP

Check the box for **“Apply hours to all employees for the task”** and then select **Done** to apply these hours to all of the employees selected for this daily plan.

NOTE

You can choose between straight time (ST), over time (OT), and double time (DT). Other premiums can be set within the project settings from the Progress web application.

24. Add equipment time by tapping on the empty box next to a piece of equipment.

TIP

Check the box for **“Apply hours to all equipment for the task”** and then select **Done** to apply these hours to all of the equipment chosen for your daily plan.

25. Tap on the **Quantities** tab.

- This opens the components section of each task
- You can also input the planned quantity

Plans Module 01 - Light Steel Erection
Wednesday, September 26, 2018

In Planning

Overview Timesheet **Quantities** Notes/Issues Productivity Sign out Submit

Task + Add Components 1005 - Erect Steel - Light

1005 -

Erect Steel - Light

Module 01 - A23: Cross Brace Assembly + -

Priority	Complete	Step	Quantity	UoM	To-date quantity	Planned Quantity
	☒	Shakeout/Tra...	0.15	Ton	0.15	0
	☐	Erect/Bolt Up	0.15	Ton	0	0
	☐	Final Torque	0.15	Ton	0	0
	☐	QC Verification	0.15	Ton	0	0
Component Total			0.15	Ton	0.023	0.000

Module 01 - A24: Cross Brace Assembly + -

Priority	Complete	Step	Quantity	UoM	To-date quantity	Planned Quantity
	☒	Shakeout/Tra...	0.24	Ton	0.24	0
	☐	Erect/Bolt Up	0.24	Ton	0	0
Task Total				Ton	0.303	

26. Select your task (i.e. 1005 – Erect Steel Light).

27. Tap the **Add Components** button.

28. Then, tap on the **Search All** tab.

29. In the search bar, type in a keyword and select your components.

30. Tap **Done** to add the component to the quantities.

31. Check the check boxes in the Complete column as needed for your components or their broken down steps.

- By checking these boxes you are communicating to your crew that you expect these steps or components to be completed in the daily plan

Plans

Module 01 - Light Steel Erection
Wednesday, September 26, 2018

In Planning

Overview

Timesheet

Quantities

Notes/Issues

Productivity

Sign out

Submit

+

Task

1005

Erect Steel - Light

+

Add Components

1005 - Erect Steel - Light

Module 01 - B23: Cross Brace Assembly

Module 1 - B23: Cross Brace Assembly

Module 01 - C23: Cross Brace Assembly

Module 1 - C23: Cross Brace Assembly

Priority	Complete	Step	Quantity	UoM	To-date quantity	Planned Quantity
	☒	Shakeout/Tra...	0.25816	Ton	0	0.25816
	☒	Erect/Bolt Up	0.25816	Ton	0	0.25816
	☐	Final Torque	0.25816	Ton	0	0
	☐	QC Verification	0.25816	Ton	0	0
Component Total			0.25816	Ton	0.000	0.155


Module 01 - E22: Horizontal Brace Assembly

Module 1 - E22: Horizontal Brace Assembly


Priority	Complete	Step	Quantity	UoM	To-date quantity	Planned Quantity
	☒	Shakeout/Tra...	0.1	Ton	0.1	0
Task Total				Ton	0.303	0.353

32. Tap on the **Notes/Issues** tab.
33. Tap on the **Add** button and select **Note** to add any project notes.

- Tap on the **textbox field** to bring up the keyboard on the iPad

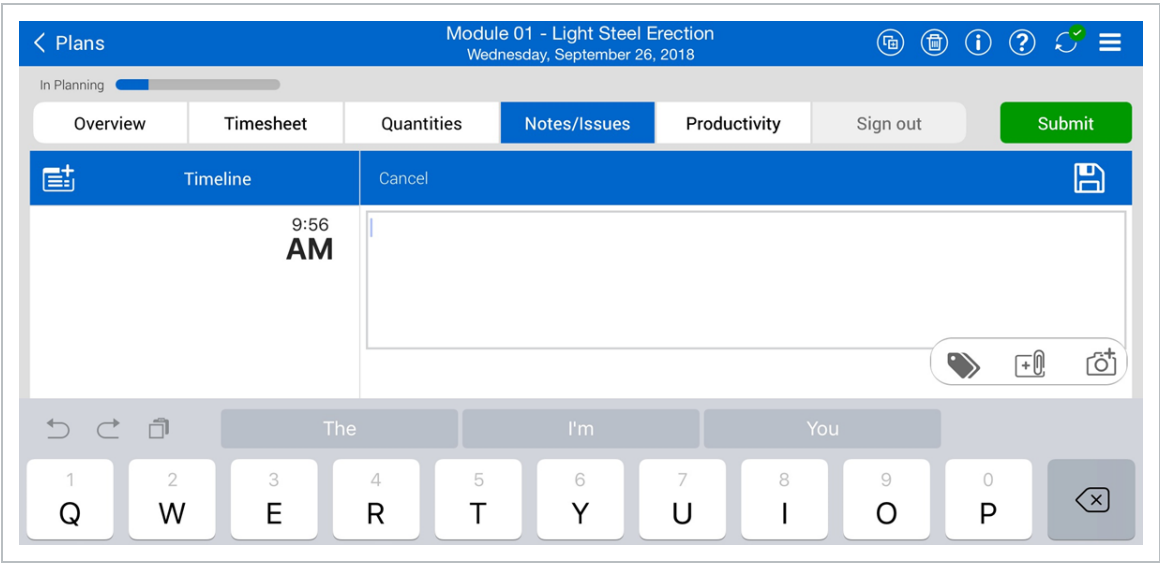

34. Tap on the **Tag**  icon to add any tags.

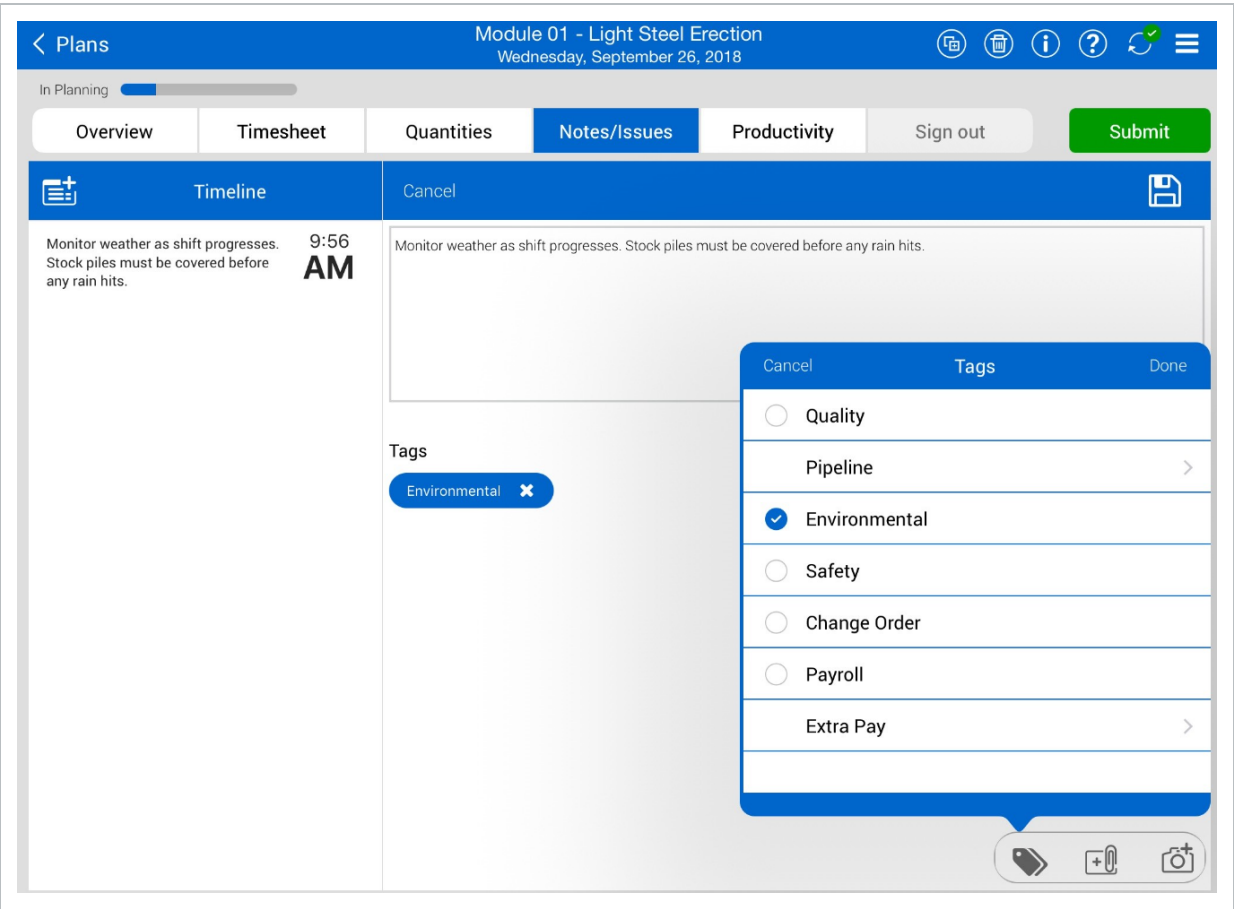

- 35. Tap on the **Camera**  icon to take a photo, make markups, or add text.
- 36. Select **Done**.
- 37. Tap on the **Productivity** tab and review your daily plan.

Module 01 - Light Steel Erection Wednesday, September 26, 2018								
In Planning								
Overview Timesheet Quantities Notes/Issues Productivity Sign out Submit								
Task ID and Description		Planned			⇄ MHRs per Qty		Planned	
Task ID	Description	Quantity	UOM	MHRs	Planned	CB	Cost G/L	MHRs G/L
1005	Erect Steel - Light	0.353	Ton	32	90.678	20.000	353	-24.9
Totals				32			353	-24.9

- 38. Review the **Planned Quantity**, **Planned MHRs**, and **Gain/Loss**.


- Tap the double arrows to flip between MHRs per Qty and Qty per MHRs

39. Tap on the **Submit** button.

- Once you tap Submit, a window appears asking if you are sure that you want to move the plan into execution

40. Tap **Submit** again.

- The application will automatically sync after submitting a plan to execution

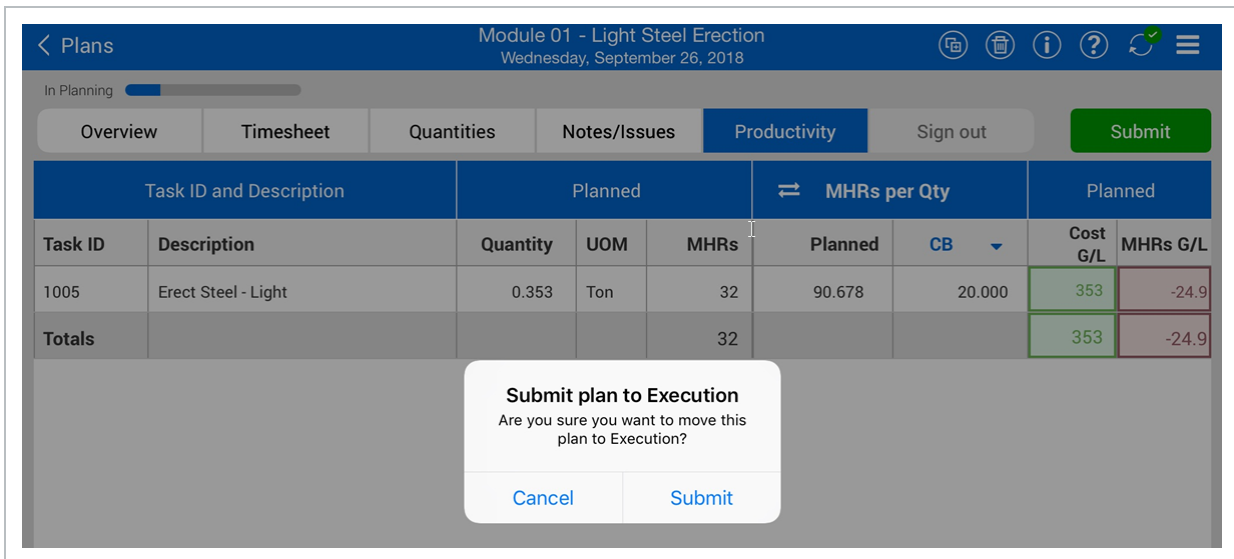

NOTE

Once you click submit, you will no longer be able to edit your plan. The only way to edit is to communicate with the engineer or superintendent to reject the plan or have them edit for you.

2.8 DAILY PLAN FROM COPY

Within Progress, you can create a daily plan by copying an existing plan. This will help you expedite the process in developing a plan if you have already performed similar work.


The copy of the Daily plan will be a mirror of the existing plan and you can edit the plan to tailor it to the new days objectives. For instance, if you have more crew members then when you last performed the work, you can add the new crew members to the Daily plan.

2.8.1 CREATE A PLAN FROM COPY

The following steps walk you through creating a daily plan from copy.


CREATE A DAILY PLAN FROM COPY

1. From the list of daily plans for your project, tap on the **Copy**  icon to make a copy of an existing plan. The Copy daily plan dialog box opens.

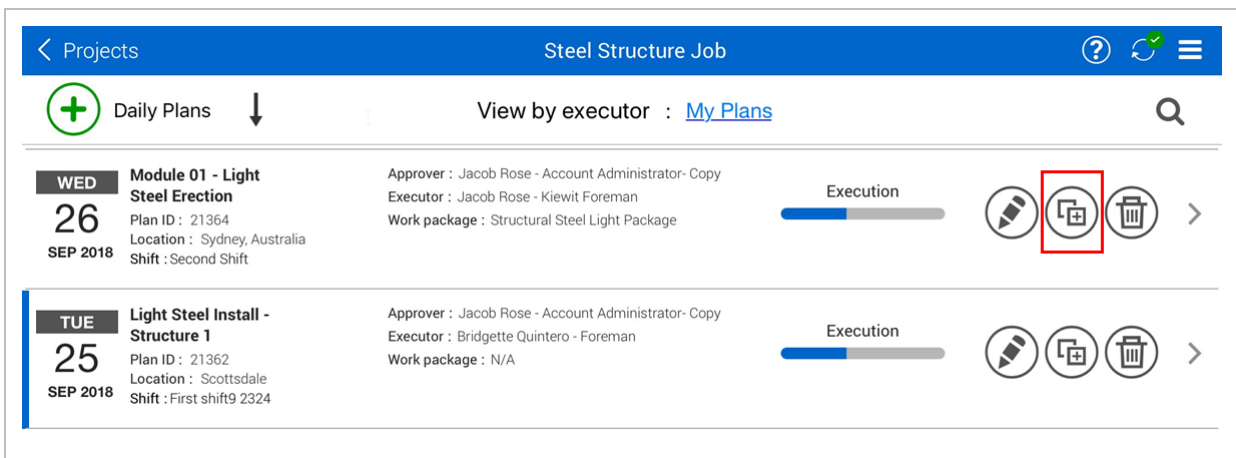

In the Copy daily plan dialog box, you can select items you want to copy to the new daily plan. All items are selected by default.

2. Deselect any items that you do not want to copy over to the new plan.

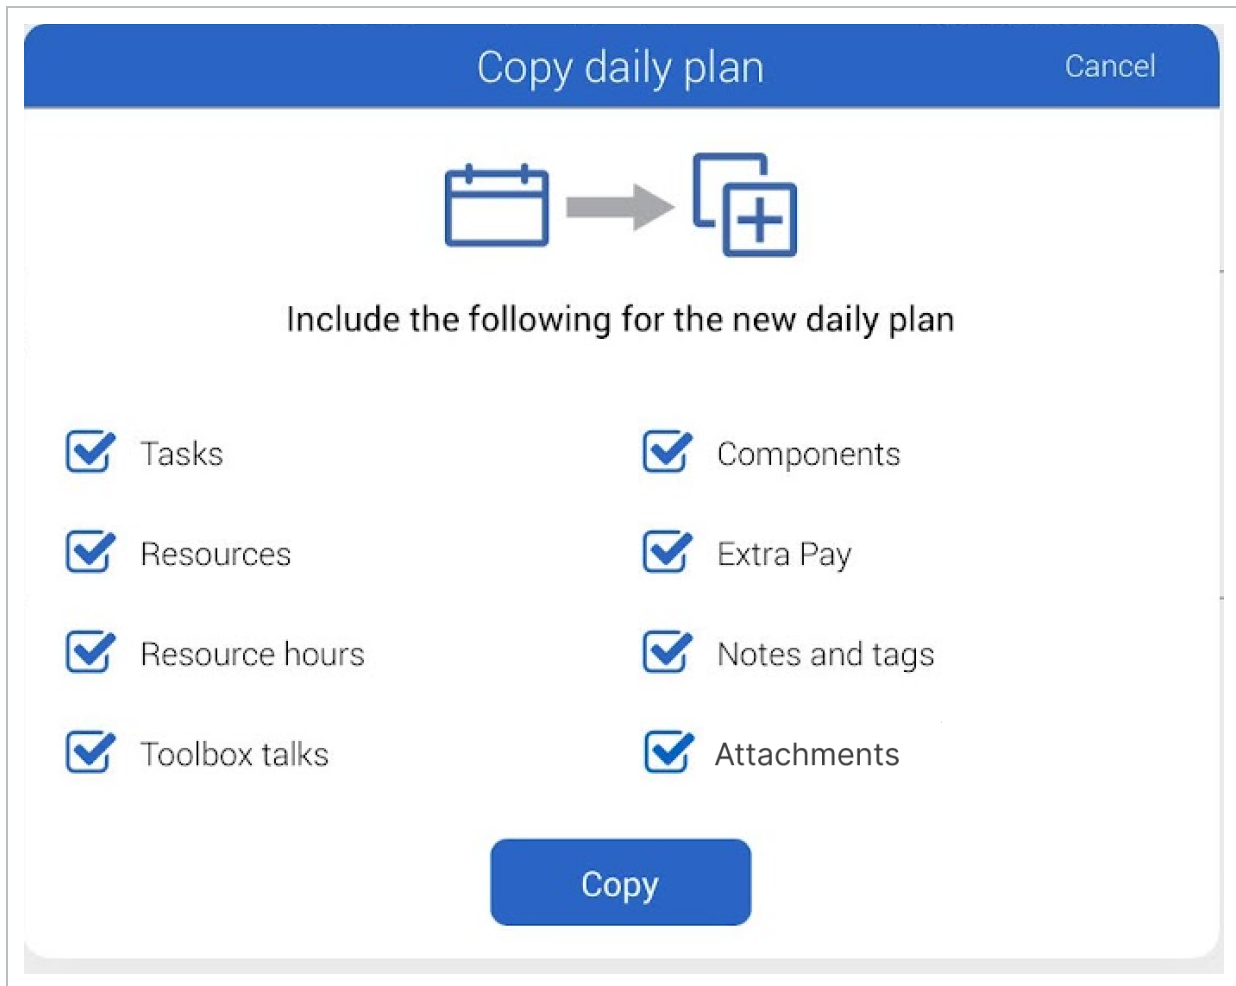


3. Tap **Copy**.
4. Edit the fields to reflect the new date.
5. Tap **Copy**.
6. Tap through each tab along the navigation bar and review that your content has been correctly copied over from the previous plan.

An exact copy of your existing daily plan has been created. All tasks, components, employees, equipment, notes, planned quantities, and tool box information has been copied.

2.9 PLAN REVIEW

Scenario


Your plan to install the horizontal and cross member assemblies (red columns) has been finalized and sent to the field for execution.

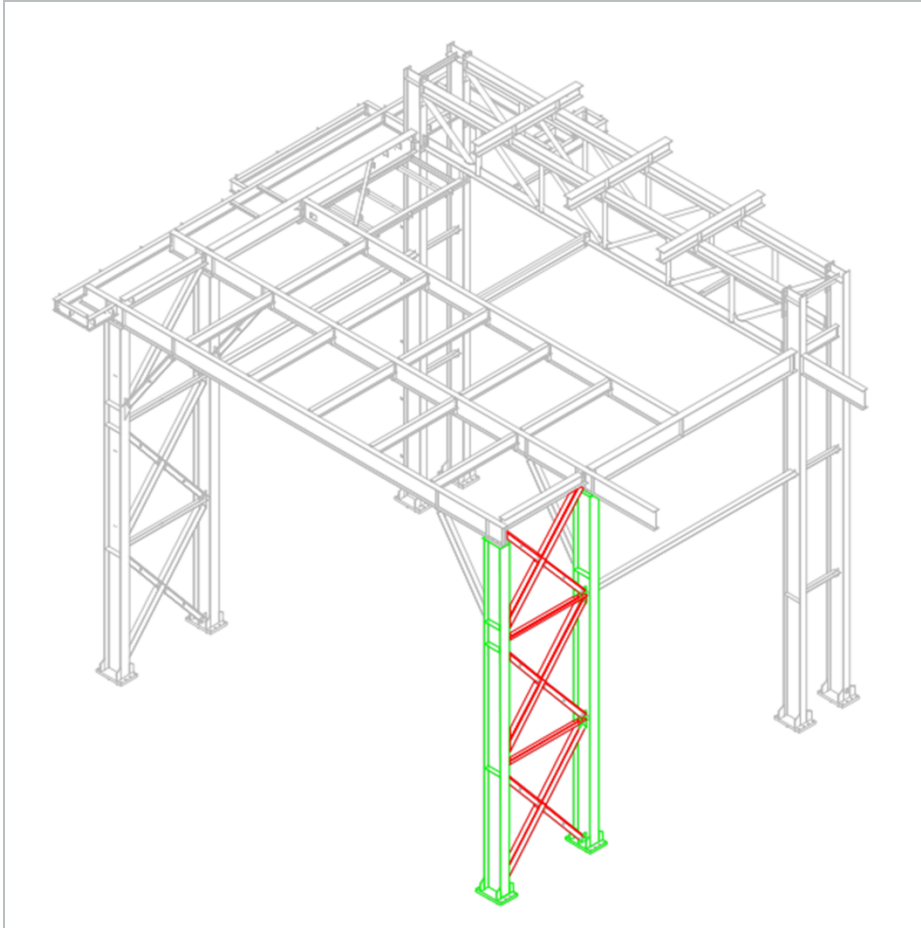

As a reminder, the steel members you will be installing are:

- A23
- A24
- B23
- B24
- C23

- C24
- D23
- E22
- E23
- E24
- F22

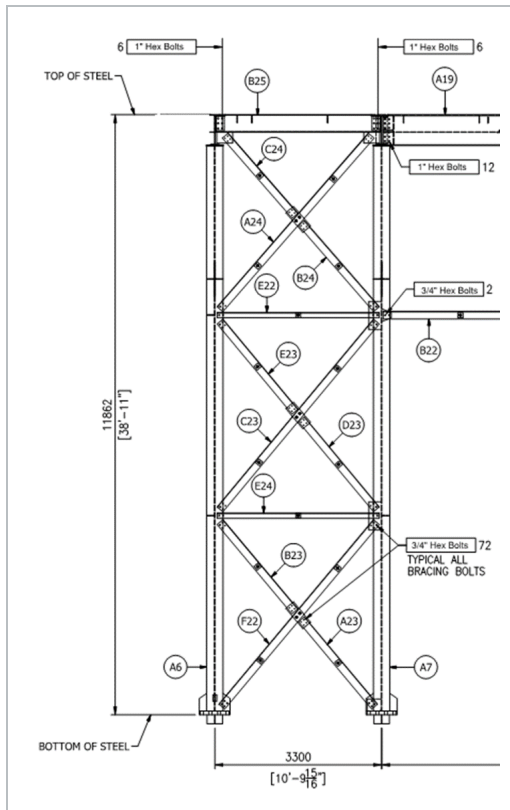

The plan will be to shakeout and transport the steel members by 1/2 ton pickup truck to the work area. You also plan to erect and bolt up members C23, D23, E23, and E24. You will use a JLG to help with erection.

After verifying the steel members with their respective drawings, it was noted that members E23 and E24 had dimensions that did not match the drawings. The foreman needs to create a note to communicate this discrepancy back to the approver. Instead of installing E23 and E24, the crew went ahead and installed B23, A23, and F22.

One of the crew did not show up for work today. He did not call in with a reason, therefore his absence will be unexcused and unpaid.

2.9.1 OVERVIEW

After the Daily Plan has been approved and synchronized, the plan is ready for execution in the field. During the morning meetings, the foreman can access the Daily Plan and review it with his crew before starting the operation.

When you access the Daily Plan for review, you first open to the Overview tab. You will notice that the plan color has now changed from blue to green. You can also tell what phase you are in by the bar in the upper left hand corner of your screen. Within the Overview tab, you can review the Tool Box Talks, Planner Notes, and Planned Tasks.

Moving to the Time sheet tab, you can note employees who are absent. You can also tell a crew member what their task is for the day, how many hours they must complete the task, and what equipment they have for their task.

You also want to tell your crew what the planned quantities are. The Quantities tab provides you with planned quantities for your crew to accomplish. There is also a breakdown of steps to complete each planned task.

You can also review any additional information related to your tasks in the Notes/Issues tab.

< Plans

Light Steel Install - Structure 1
Tuesday, September 25, 2018

Execution

Overview

Timesheet

Quantities

Notes/Issues

Productivity

Sign out


Submit

Planned tasks		Quantity		Time	Budget	Toolbox talks		
Task ID	Description	Planned	UOM	Planned	Plan G/L			
1005	Erect Steel - Light	0.155	Ton	32	-28.9			
Totals				32	-28.9			
Planner notes Verify steel member dimensions with updated drawings to ensure correct installation.						+ Safety		
						Safety concern		Mitigation
						Human - Equipment Interface		Use spotter at all times.
						+ Quality		
						Quality concern		Mitigation
						Material Quality		Cover stockpiles
						+ Environmental		
						Environmental concern		Mitigation
						Spills from JLG		Use drip trays under equipment when not in use.
						+ General discussion		
RFI-Metals-001 submitted to client. Allow 5 days for review and answer.								

TIP

In InEight Progress, from any screen, you can access the help screen by pressing the  button. This is located in the upper right hand side of the application.


Once selected, the help screen will look like the following:

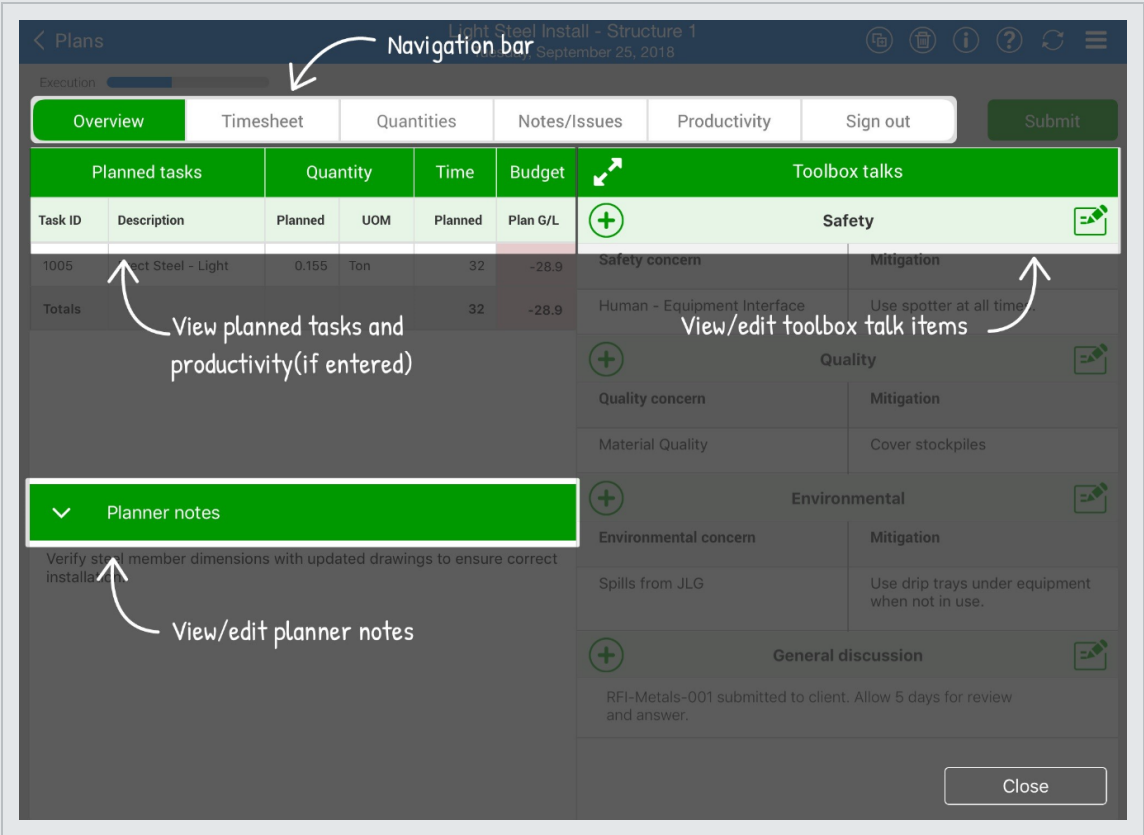

Simply select the close button at the bottom of your screen to close the help screen.


REVIEW DAILY PLAN OVERVIEW TAB

1. Launch the **InEight Progress** application through your mobile device.



2. Log into **Progress** using your credentials.

- This depends on your company and how they set up your log in information for you
- After you log in, you will open to the Projects page where you will see all the projects that you have access to



3. Select a project.
 - Depending on how many projects you have access to, you may have more than one project to select from
 - The Daily Plans page of the project opens, where you will see all the daily plans created for the project
4. Select a daily plan.

Projects

Steel Structure Job

?

↺

☰

+

Daily Plans

↓

View by executor : [My Plans](#)

Q

THU

27

SEP 2018

Good Luck

Plan ID : 21354

Location :

Shift : First shift9 2324

Approver : Jacob Rose - Account Administrator- Copy

Executor : Jacob Rose - Kiewit Foreman

Work package : N/A

Execution

>

WED

26

SEP 2018

Module 01 - Light Steel Erection

Plan ID : 21364

Location : Sydney, Australia

Shift : Second Shift

Approver : Jacob Rose - Account Administrator- Copy

Executor : Jacob Rose - Kiewit Foreman

Work package : Structural Steel Light Package

Execution

>

TUE

25

SEP 2018

Light Steel Install - Structure 1

Plan ID : 21362

Location : Scottsdale

Shift : First shift9 2324

Approver : Jacob Rose - Account Administrator- Copy

Executor : Bridgette Quintero - Foreman

Work package : N/A

Execution

>

- This opens the plan Overview tab where you can review the daily plan with your crew and the superintendent

Page 94 of 119

InEight Inc. | Release 25.7

Plans

Light Steel Install - Structure 1
Tuesday, September 25, 2018

Execution

Overview

Timesheet

Quantities

Notes/Issues

Productivity

Sign out

Submit

Planned tasks		Quantity		Time	Budget	Toolbox talks	
Task ID	Description	Planned	UOM	Planned	Plan G/L		
1005	Erect Steel - Light	0.155	Ton	32	-28.9		
Totals						32	-28.9

Planner notes

Verify steel member dimensions with updated drawings to ensure correct installation.

Safety

Safety concern

Mitigation

Human - Equipment Interface

Use spotter at all times.

Quality

Quality concern

Mitigation

Material Quality

Cover stockpiles

Environmental

Environmental concern

Mitigation

Spills from JLG

Use drip trays under equipment when not in use.

General discussion

RFI-Metals-001 submitted to client. Allow 5 days for review and answer.

2.10 INPUT ACTUALS

As the workday progresses, within Progress you can input the hours each crew member worked on a task, and the amount of quantity installed or completed. Inputting actuals for the Daily Plan takes place in the Time sheet and Quantities tabs.


2.10.1 TIME SHEET TAB

Within the Time sheet tab, you can enter the exact hours each crew member worked and the amount of hours the equipment was used.


You may need to track that a crew member has shown up late or missed a day of work. You can also add notes to an employee if there was an injury, tardiness, or extra work hours.

If you have crew members that must work overtime or double time to meet the schedule deadline, on the Time sheet tab you can enter straight time, overtime, and double time. In addition, to account for

fractions of an hour, there are buttons below the keypad (e.g., by 0.25, 0.50, or 0.75). If you enter overtime or double time, you will see the updated hours in the hour box.

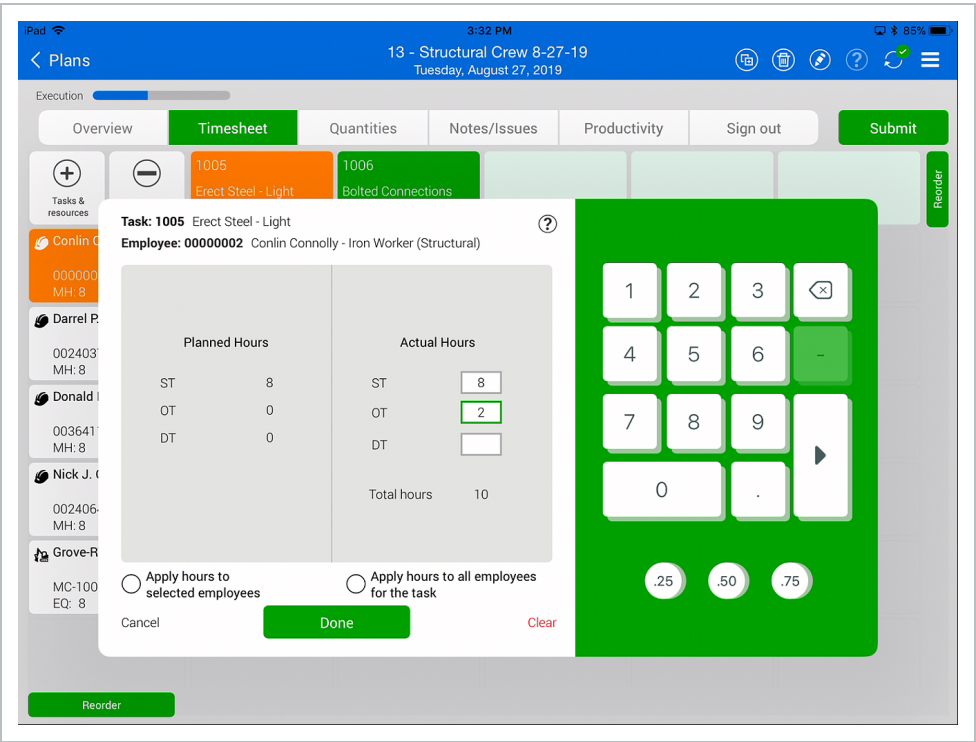


If everyone in your crew has worked the same hours, you can select the **Apply hours to all employees for the task** box. If you want to apply the same hours to some of the employees on the daily plan, you can select **Apply hours to selected employees** and select the hours boxes for all the employees you wish to allocate the hours to.

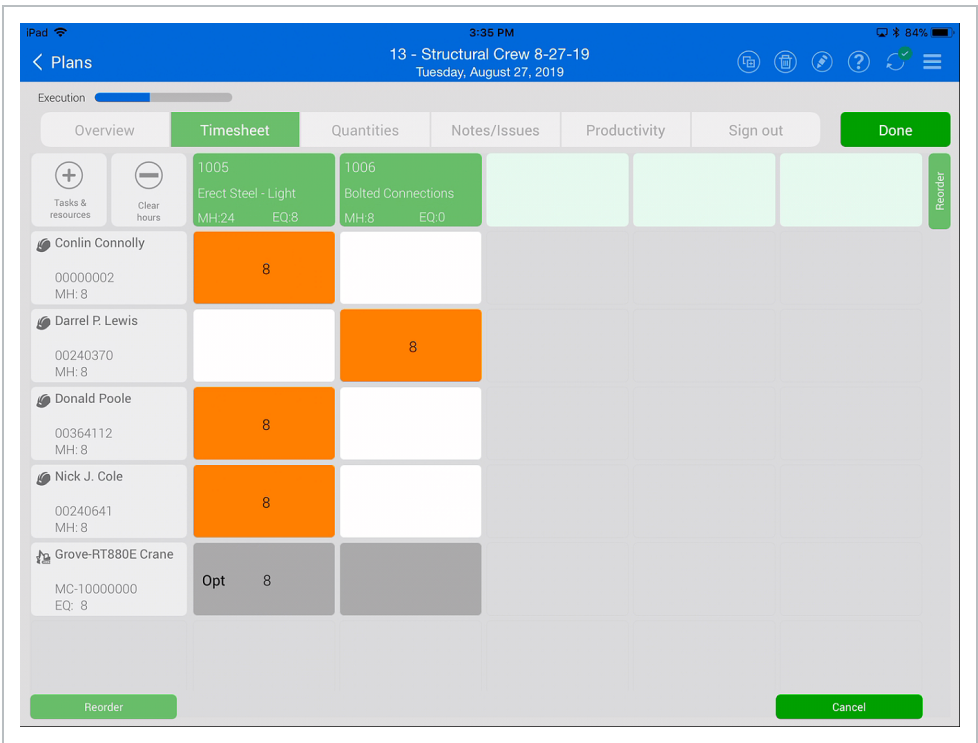

If you are adding hours to a vendor resource, there is an additional Number of employees field.

If your plan for the day has changed and you need to replace the task for the day, you can do so by tapping on the task box and selecting Swap task. This allows you to leave any hours you have already entered and not have to start from scratch.


You can also add a note or define any extra pay from this screen.

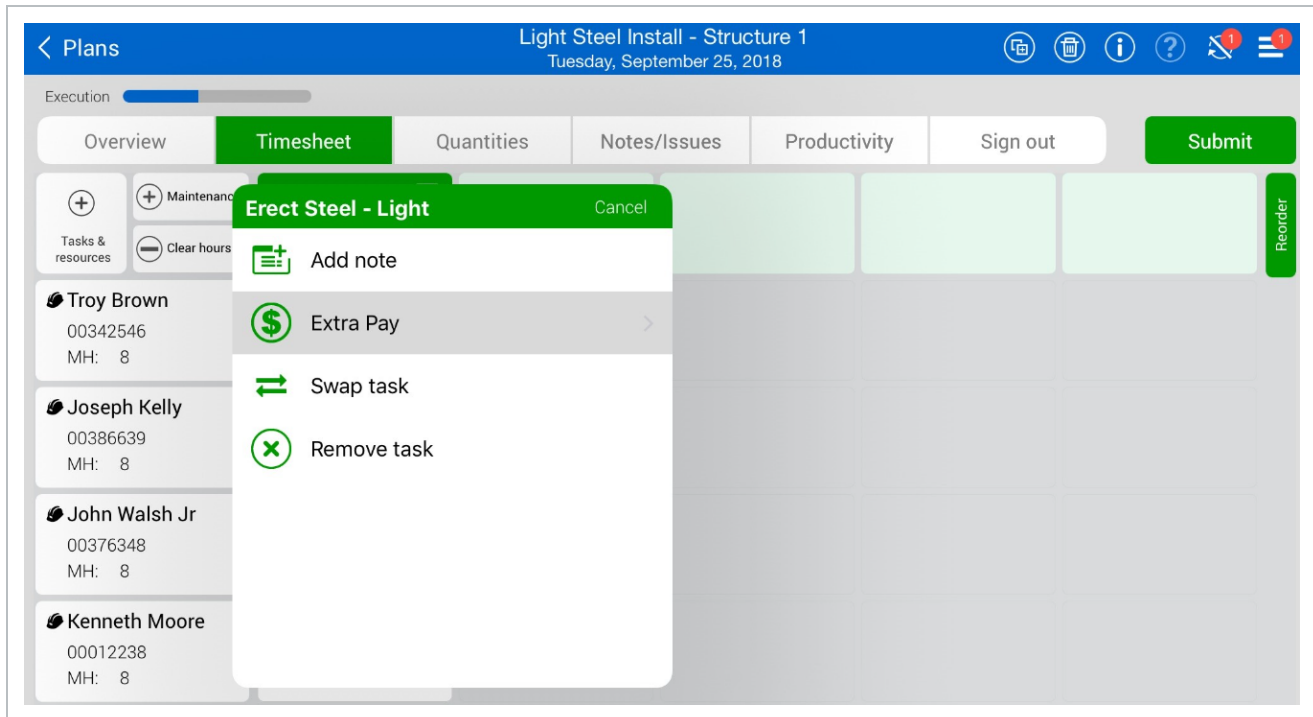

2.10.1.1 REMOVE UNUSED TASKS AND RESOURCES

You can remove all unused tasks or resources from a daily plan at the same time. At the top of the Time Sheet tab, click the **Remove unused tasks and resources** icon, and then select one of the following options:

- Remove unused resources: All employees with no daily plan data associated with them are removed from the daily plan.
- Remove unused tasks: All tasks with no daily plan data associated with them are removed from the daily plan.

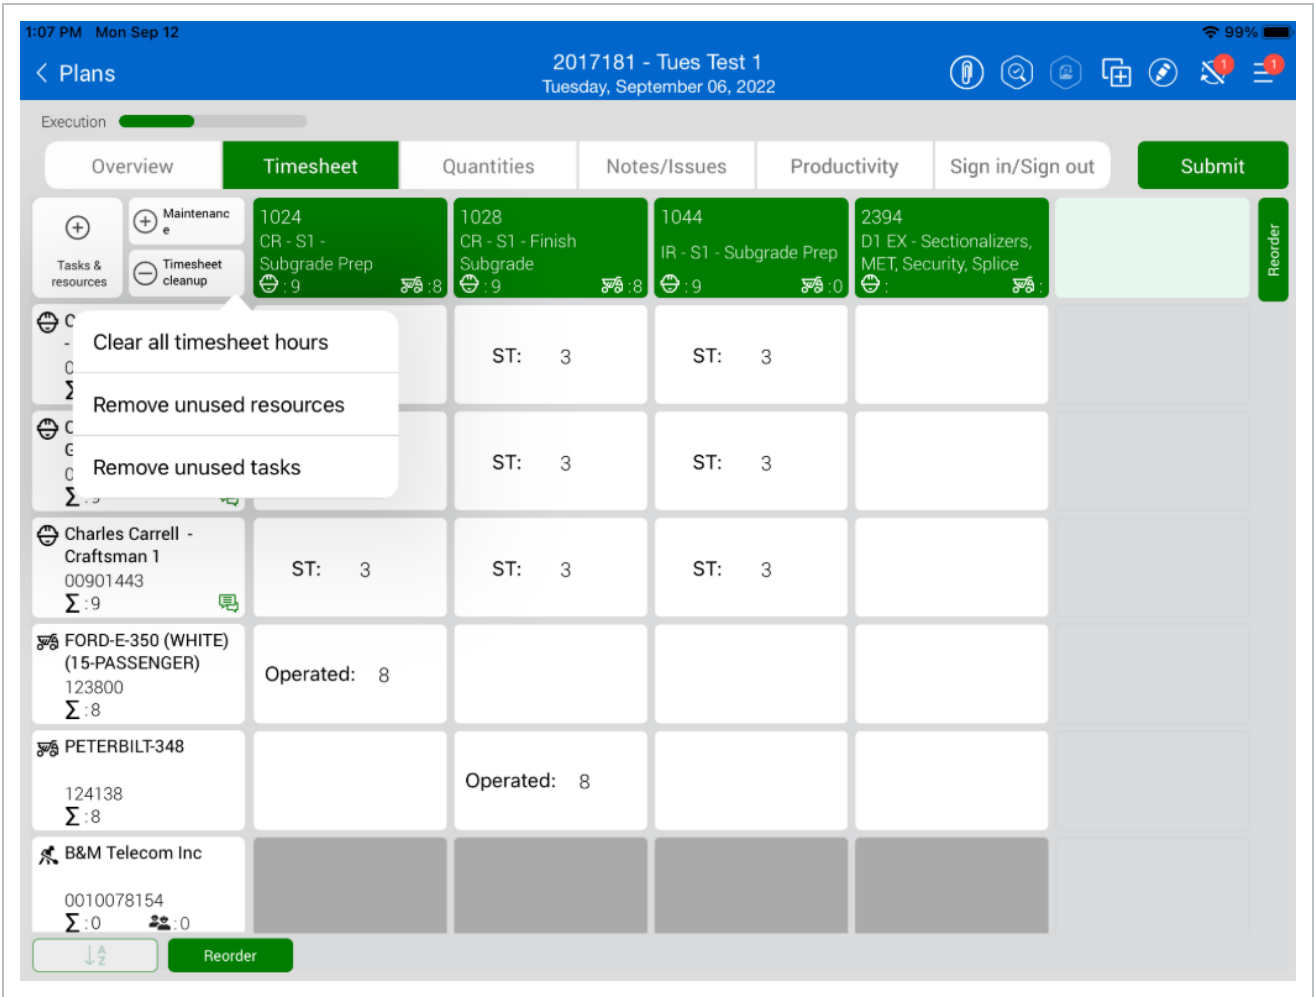

TIP

You can change the order of the employees and equipment in the Time sheet tab by selecting one of the two Reorder buttons. Each button is located at the end of the task row and resource column.

2.10.2 QUANTITIES TAB

On the Quantities tab, you can check off components and claiming steps as complete, or input the exact quantities completed for the day.

Plans

Light Steel Install - Structure 1
Tuesday, September 25, 2018

Execution

Overview

Timesheet

Quantities

Notes/Issues

Productivity

Sign out

Submit

+

Task

+

Add Components

1005 - Erect Steel - Light

1005

Erect Steel - Light

Module 01 - C23: Cross Brace Assembly Module 1 - C23: Cross Brace Assembly

Priority

Complete

Step

Quantity

UoM

To-date quantity

Planned Quantity

Installed Quantity

☒

Shakeout/Tra...

0.25816

Ton

0

0.25816

0.25816

☐

Erect/Bolt Up

0.25816

Ton

0

0.25816

0

☐

Final Torque

0.25816

Ton

0

0

0

☐

QC Verification

0.25816

Ton

0

0

0

Component Total

0.25816

Ton

0.000

0.155

0.039

Task Total

Ton

0.000

0.155

0.039

2.10.3 NOTES/ISSUES TAB

On the Notes/Issues tab, you can add new notes or issues or make updates to any notes or issues created during the planning phase.

< Plans

Notes/Issues

⚠ Cracked concrete slab

11:22 AM Crack in concert slab observed on Column B...

[➤ Send issue](#)

Parkland delivery rescheduled for 8:15 a.m.
Contact Mark (555) 819-2939.

01:37 PM Weather - Delay, 20100204 - Bayhill Contra...

March 05, 2025 at 11:22 AM

Issue name

Cracked concrete slab

Issue start date

March 04, 2025

TASK 1006 - Bolted Connections

Description

Crack in concert slab observed on Column B3. Crack appears to be deep/spreading.

Tags

Quality
Weather - Delay

Associations

Module 09 - A6 Connection to Foundation Module 9 - A6...


Photos (1 of 20 photos added to plan)

2.10.3.2 SEND ISSUE TO INEIGHT CHANGE

If your organization uses InEight Change, issues generated in Progress are sent to Change for review, and may be associated with change orders.

After an issue is created, the issue shows in the Timeline section of the Notes/Issues tab. The issue is sent to Change after the daily plan is approved.

When the issue requires immediate attention, click **Send issue** to immediately send the issue to InEight Change for review.

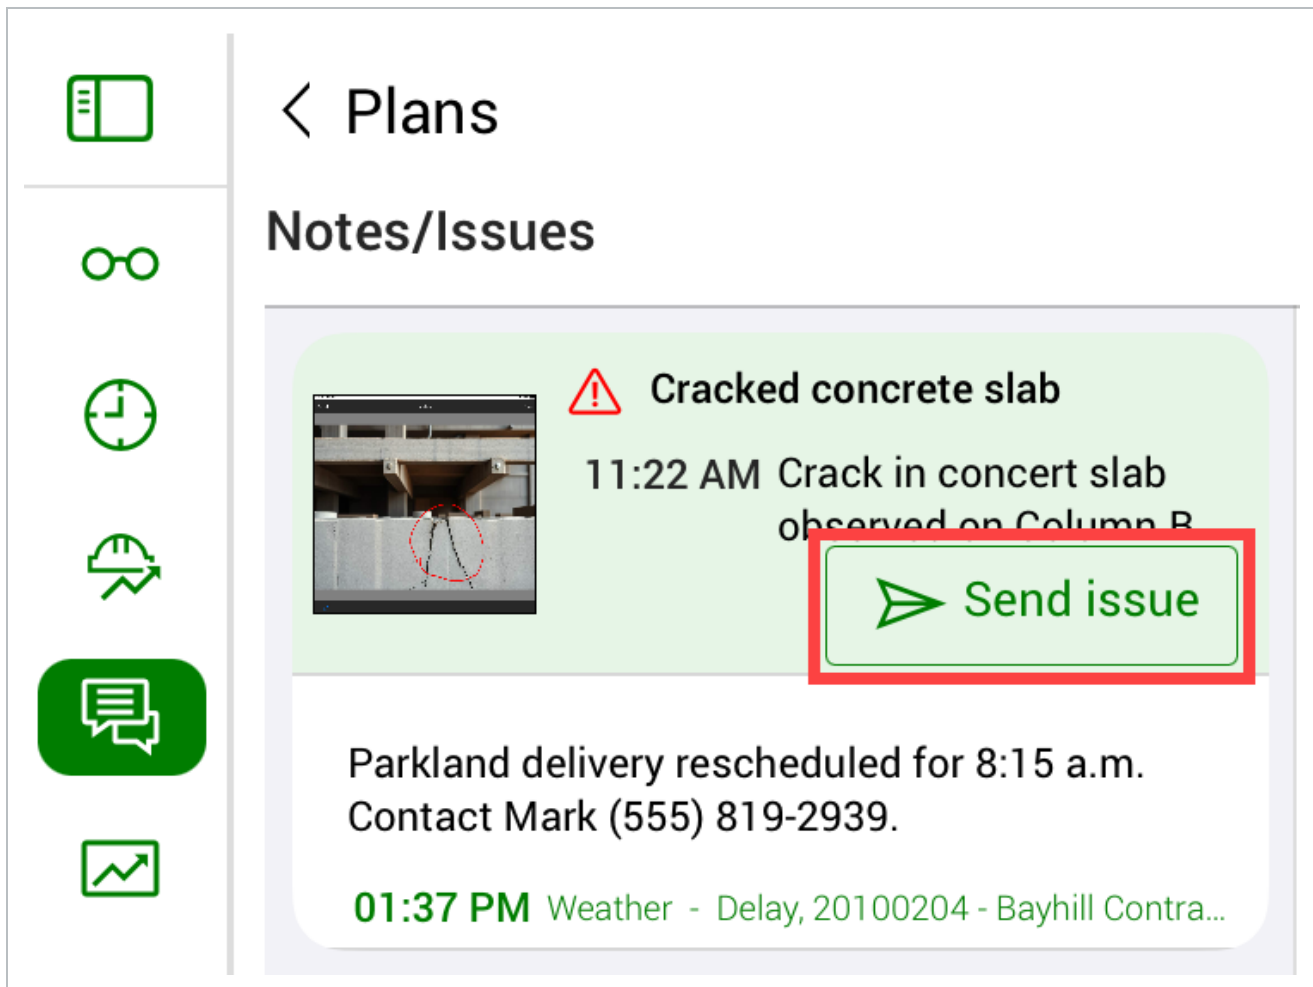

Plans

Notes/Issues

 **Cracked concrete slab**
11:22 AM Crack in concert slab observed on Column B
Send issue

Parkland delivery rescheduled for 8:15 a.m.
Contact Mark (555) 819-2939.

01:37 PM Weather - Delay, 20100204 - Bayhill Contra...

2.10.4 PRODUCTIVITY TAB

After adding notes, you can review your tasks, quantities and hours claimed for the task and compare the actuals to the planned quantity and hours within the Productivity tab.

MHR G/L and (\$) G/L are two productivity metrics used to determine performance against budget. By default, MHR G/L is always shown. (\$) G/L will be shown if the appropriate setting is selected in the project settings. The setting is called "Display cost in daily plan productivity during execution phase?" and is in the Daily Planning section of the project settings.

< Plans

Light Steel Install - Structure 1

Tuesday, September 25, 2018

Execution

Overview

Timesheet

Quantities

Notes/Issues

Productivity

Sign out

Submit

Task ID and Description		Actual			⇄ MHRs per Qty			Actual	
Task ID	Description	Quantity	UOM	MHRs	Planned	Actual	CB ▾	Cost G/L	MHRs G/L
1005	Erect Steel - Light	0.039	Ton	32	206.590	826.361	20.000	39	-31.2
Totals				32				39	-31.2

NOTE

The Actual G/L compares the actual cost and man-hours recorded on your executed daily plan to the budgeted, forecasted or current estimate costs and man-hours using the following equations:

Actual Cost G/L = (Sum of (Total actual quantity for the WBS * CE/CB/Forecast final unit cost) - (Actual total cost of labor + Actual total cost of equipment))

The drop down arrow next to CB under the MHRs per QTY header allows you to select which unit cost to compare against: CE, CB or Forecast

- Actual total cost of labor = Sum of Total number of hours worked by the employee * Hourly rate of the employee
- Actual total cost of equipment = Sum of (Total number of equipment hours operated * Hourly Unit rate of the equipment)

2.10.5 SIGN IN/SIGN OUT TAB

The Sign in/Sign out tab lets you sign in or out for the day, answer any questions associated with sign-in or sign-out, and enter any breaks you take.

NOTE

Sign in and Sign out are compatible with iPad and iPhone Face ID.

2.10.5.3 SIGN IN SUBTAB

The Sign In subtab lets you sign in for the day and answer questions at the beginning of your shift.

The screenshot shows the 'Plans' screen for project '45660 - Excavate' on Wednesday, February 24, 2021. The top navigation bar includes tabs for Overview, Timesheet, Quantities, Notes/Issues, and Productivity, along with 'Sign in/Sign out' and 'Submit' buttons. The left sidebar lists 'Employee' (John Doe), 'Sign out all eligible', and '* Client sign off'. The main content area for John Doe (00000000) features a 'Sign in' button, 'Breaks', and 'Sign out' subtabs. The 'Shift start' is set to 06:00 AM with an 'Edit shift time' link. A table shows shift hours: ST (0.00), OT (8.00), DT (0.00), and Total (8.00) hours. Below this is the 'Planned Tasks' section with a task 'Removal' (0.00 ST, 8.00 OT, 0.00 DT, 8.00 Total hours). The 'Sign in questions' section includes a statement 'I have listened to today's tooltalks and understand my tasks for today.' with 'Yes', 'No', and 'Clear' buttons. At the bottom, there is a 'Sign in' button and a 'Reject All' button.

SHIFT START TIME

You can enter shift start time. The Shift start field is synced with the Breaks and Sign Out subtabs. Changes made to the time in one subtab change the others.

NOTE

If you enter a Shift end value in the other subtabs, you cannot edit the Shift start field in the Sign In subtab.

EMPLOYEE SIGN-IN

To sign in as an employee, tap on your name. Each employee must enter a PIN (personal information number) to sign in, which can be your birth date or a number that the IT personnel has assigned. With

the proper project settings enabled, there is also an option to sign in with a signature.

SIGN-IN ON BEHALF OF EMPLOYEE

Depending on project settings you might also have the option to sign in on behalf of employees by using Touch ID or PIN. This project setting is recommended because crewmembers might forget to sign in when the crew iPad is not around, which prevents the daily plan from being submitted. As a field engineer, foreman, or other heavy user of the app, you can sign in for all employees at one time and use the electronic signature.


QUESTIONS

When you sign in, you or your crewmember might be asked a set of questions related to the work to be done that day. These questions are determined by management and set up for the job in the project settings by an administrator.

- For each question, you can answer yes or no
- If you give a non-compliant answer, a dialog box lets you put a note as to why you chose that answer
- You can tap **No Exceptions** if all answers are in compliance

NOTE

Employees who provide an answer that is out of compliance must provide a note, and a red Note indicator is shown with the employee on the sign in tab.



2.10.5.4 BREAKS SUBTAB

In the Breaks subtab, you can enter up to five breaks per daily plan and per person. To enter a break, you must enter its start time and length.

11:08 AM Tue Mar 9

45660 - Excavate
Wednesday, February 24, 2021

Plans

Execution

Overview Timesheet Quantities Notes/Issues Productivity Sign in/Sign out Submit

Employee John Doe (00000000)

John Doe
00000000 (Temporary e...)

Sign out all eligible

* Client sign off

Reject All

Sign in Breaks Sign out

Shift start	Shift end	ST	OT	DT	Total
06:00 AM	06:00 AM	0.00 hours	8.00 hours	0.00 hours	8.00 hours

Breaks

Break 1

Break 1 start time Break 1 length

Break 2


Break 2 start time Break 2 length

Break 3

Break 3 start time Break 3 length

2.10.6 CREW BREAK HOURS

If you click the **Crew hours** icon at the top of the Employee side panel, the Enter crew hours dialog box opens. In Crew break details, you can enter break start times and lengths for the entire crew.

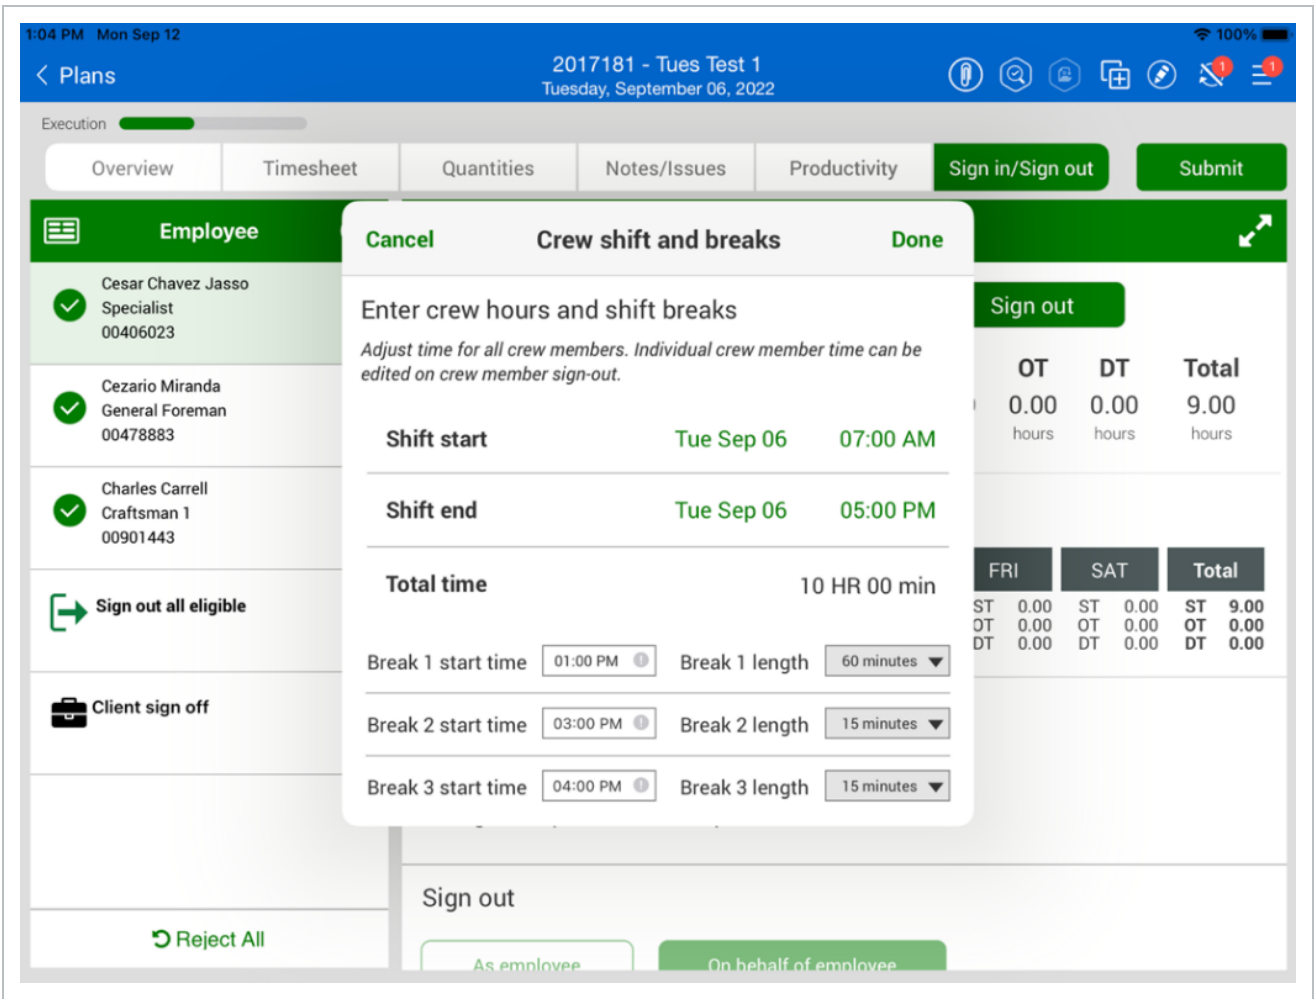

If you enter a break time for an individual employee, it overrides the crew break time for that employee.

At the top of the page, the total number of break hours is shown.

1:29 Mon, Sep 12

2017181 - Tues Test 1
Tuesday, September 6, 2022

Execution

OVERVIEW

TIME SHEET

QUANTITIES

NOTES/ISSUES

PRODUCTIVITY

SIGN IN/SIGN OUT

SUBMIT

Employee

Cesar Chavez Jasso (00406023)

Cesar Chavez Jasso
Specialist
00406023

Cezario Miranda
General Foreman
00478883

Charles Carrell
Craftsman 1
00901443

Sign out all eligible

Client sign off

Reject All

SIGN IN

Shift start

Shift end

Shift time

Break time

SIGN OUT

ST

OT

DT

Total

07:00 AM

05:00 PM

Edit shift time

10:00
(hr:min)

01:30
(hr:min)

9.00
hours

0.00
hours

0.00
hours

9.00
hours

This week's hours

SUN	MON	TUE	WED	THU	FRI	SAT	Total
ST 0.00	ST 0.00	ST 9.00	ST 0.00	ST 0.00	ST 0.00	ST 0.00	ST 9.00
OT 0.00	OT 0.00	OT 0.00	OT 0.00	OT 0.00	OT 0.00	OT 0.00	OT 0.00
DT 0.00	DT 0.00	DT 0.00	DT 0.00	DT 0.00	DT 0.00	DT 0.00	DT 0.00

Sign out questions

No sign-out questions are required

Sign out

AS EMPLOYEE

ON BEHALF OF EMPLOYEE

SHIFT START/END TIME

You can also change your shift start and shift end times on the Breaks subtab.

NOTE

If you change the shift start and end times, the Sign In and Sign Out subtabs change to match the new times.

2.10.6.5 SIGN OUT SUBTAB

The Sign Out subtab lets you sign out your hours and answer questions at the end of the day. Depending on settings and permissions, you can also sign out on behalf of eligible employees.

11:09 AM Tue Mar 9

45660 - Excavate
Wednesday, February 24, 2021

< Plans

Execution

Overview Timesheet Quantities Notes/Issues Productivity Sign in/Sign out Submit

Employee John Doe (00000000)

John Doe
00000000 (Temporary e...)

Sign out all eligible

* Client sign off

Reject All

Sign in Breaks Sign out

Shift start	Shift end	ST	OT	DT	Total
06:00 AM	06:00 AM	0.00	8.00	0.00	8.00
		hours	hours	hours	hours

Edit shift time

I have been authorized and permitted to take the time off for my rest periods in accordance with company policies and Wage Order 16

Yes No

I have not been hurt today.

Yes No

Clear No Exceptions

Sign out

Cancel Sign out

SHIFT START/END TIME

You can enter shift hours for an entire crew or for an individual (exception from crew) from the Sign out subtab. To enter the hours worked for an entire crew, select the clock icon at the top of the list of crew members on the left side of the page.

To enter hours worked on an individual level, select the crew member from the list, and then select **Edit shift time** on the right side to adjust the hours worked for that individual.

In the dialog box, you can adjust the Shift start and Shift end values to reflect the hours worked by the crew. You can either save these changes once you have finished or cancel the operation.

2.10.6.6 EMPLOYEE SIGN-OUT

To sign out as an employee, tap on your name. You can review the hours input by the foreman before signing the card and, at that point, you can agree or disagree with the hours and negotiate them before signing out. Each employee must enter a PIN (personal information number) to sign out, which can be your birthdate or a number that the IT personnel has assigned. With the proper project settings enabled, there is also an option to sign out with a signature.

2.10.6.7 SIGN-OUT ON BEHALF OF EMPLOYEE

Depending on project settings you might also have the option to sign out on behalf of employees by using Touch ID or PIN. This project setting is recommended because crewmembers might forget to sign out or leave early when the crew iPad is not around, which prevents the daily plan from being submitted. As a field engineer, foreman, or other heavy user of the app, you can sign out for all employees at one time and use the electronic signature on the sign-out subtab.

2.10.6.8 CLIENT SIGN-OUT

With the proper project settings enabled, you can include client sign-out on the Sign out subtab, either as an optional or required field, so the client can sign off for the work completed that day.

NOTE

The Client sign off is available until all employees are signed out.


2.10.6.9 QUESTIONS

When you sign out, you or your crewmember might be asked a set of questions related to the work done that day. These questions are determined by management and set up for the job in the project settings by an administrator.

- For each question, you can answer Yes or No
- If you give a non-compliant answer, a dialog box lets you put a note as to why you chose that answer
- You can tap **No Exceptions** if all answers are in compliance

NOTE

Employees who provide an answer that is out of compliance must provide a note, and a red Note indicator is shown with the employee on the sign out tab.

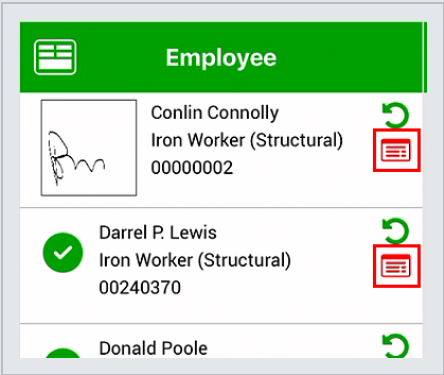

After all employees sign out, you must submit and synchronize the plan for the information from Progress mobile to upload to Progress web.

2.10.6.10 TIME SHEET SUMMARY

As a foreman, you can review the Extra pay (allowances) allocated to each employee by selecting the **Time sheet summary** icon. This opens a Time sheet summary page that lists each employee and which of the available allowances they have for their Time sheet.

Execution

Overview Timesheet Quantities Notes/Issues Productivity Sign out Submit

Cancel Timesheet summary Done


Employee name	Extra pay (Allowances)						Total hours
	New Crane Size Bump Edited1	789	98	565	dfgh	asdv	
Fred Farland	☐	☐	☐	☐	☐	☐	10.00
James Dowling	☐	☐	☐	☐	☐	☐	10.00
Jorje Zamarron	☐	☐	☐	☐	☐	☐	10.00
Michael Bench	☐	☐	☐	☐	☐	☐	10.00
Equipment name							Total hours
Employees: 4	0	0	0	0	0	0	40.00
Equipment: 0							0

From this page, you can view, add and edit allowance allocations for each employee. As you do so, these changes will update automatically for each employee on the Time sheet and Notes/Issues tabs of the daily plan.

The following steps walk you through entering actuals into your daily plan in Progress.

INPUT ACTUALS

1. Open a daily plan from one of your projects.

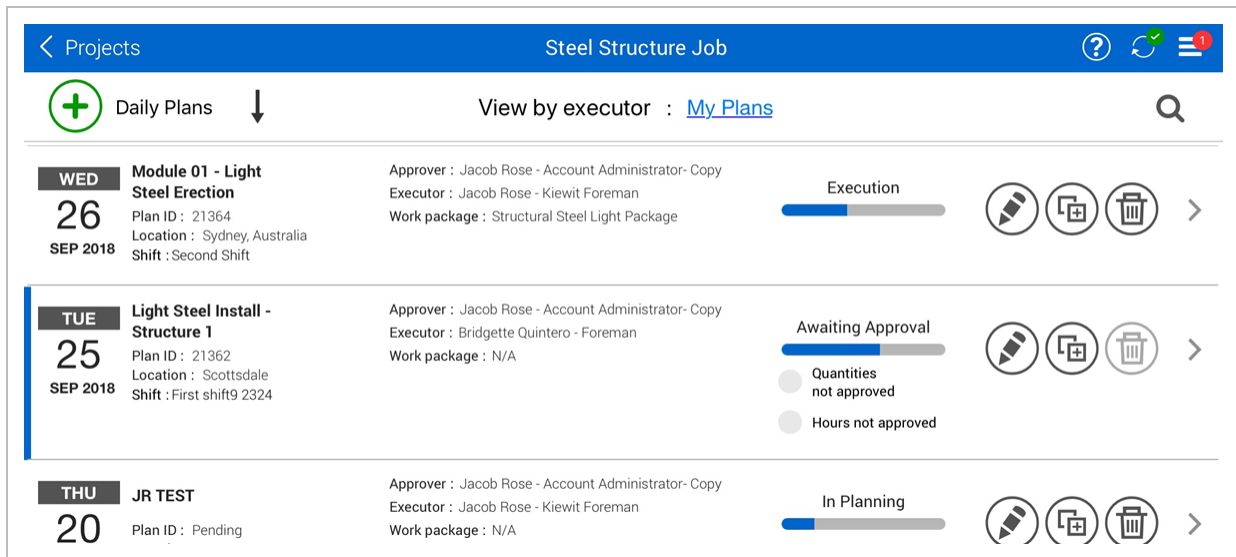

2. Tap on the **Time sheet** tab.
3. Input hours for all your employees and equipment.
4. Tap on the **Quantities** tab.
 - You will see the component assigned to the task from the planning phase
5. Check the check boxes in the "Complete" column wherever necessary for assigned components or their broken down steps.

Plans

Module 01 - Light Steel Erection
Wednesday, September 26, 2018

Execution

Overview

Timesheet

Quantities

Notes/Issues

Productivity

Sign out

Submit

Task

1005

Erect Steel - Light

Add Components

1005 - Erect Steel - Light

Module 01 - C23: Cross Brace Assembly

Module 1 - C23: Cross Brace Assembly

Priority	Complete	Step	Quantity	UoM	To-date quantity	Planned Quantity	Installed Quantity
	☒	Shakeout/Tra...	0.25816	Ton	0	0.25816	0.25816
	☐	Erect/Bolt Up	0.25816	Ton	0	0.25816	0
	☐	Final Torque	0.25816	Ton	0	0	0
	☐	QC Verification	0.25816	Ton	0	0	0
Component Total			0.25816	Ton	0.000	0.155	0.039

Module 01 - E22: Horizontal Brace Assembly

Module 1 - E22: Horizontal Brace Assembly

Priority	Complete	Step	Quantity	UoM	To-date quantity	Planned Quantity	Installed Quantity
	☒	Shakeout/Tra...	0.1	Ton	0.1	0	0
	☐	Erect/Bolt Up	0.1	Ton	0	0	0
Task Total				Ton	0.303	0.353	0.039

6. Tap the **Note**  icon to add a component note.
- Tap in the text entry field and your device keyboard will automatically appear

< Plans Module 01 - Light Steel Erection
Wednesday, September 26, 2018

Execution 0%

Overview Timesheet Quantities **Notes/Issues** Productivity Sign out Submit

Timeline Cancel

11:16 AM

Absent Unexcused - Unpaid 1a - 11:08 AM

Absent Unexcused - Unpaid, 00386639 - Jose... 11:08 AM

Monitor weather as shift progresses. 9:56

1 2 3 4 5 6 7 8 9 0 Q W E R T Y U I O P

7. Tap **Save** to return to the Quantities tab.
8. Tap on the **Notes/Issues** tab.
9. Tap on the **Note** icon to add a project note or concern.

< Plans Module 01 - Light Steel Erection
Wednesday, September 26, 2018

Execution 0%

Overview Timesheet Quantities **Notes/Issues** Productivity Sign out Submit

Timeline Cancel


Cross brace member E24 does not conform to issued engineering drawings. RFI may be required. 11:19 AM

Installed in place of planned steel members. 11:19 AM


Module 01 - E22: Horizontal Brace Assembly... 11:19 AM

11:19 AM

10. Tap the **Tag** icon and tag your note.
11. Select **Done**.

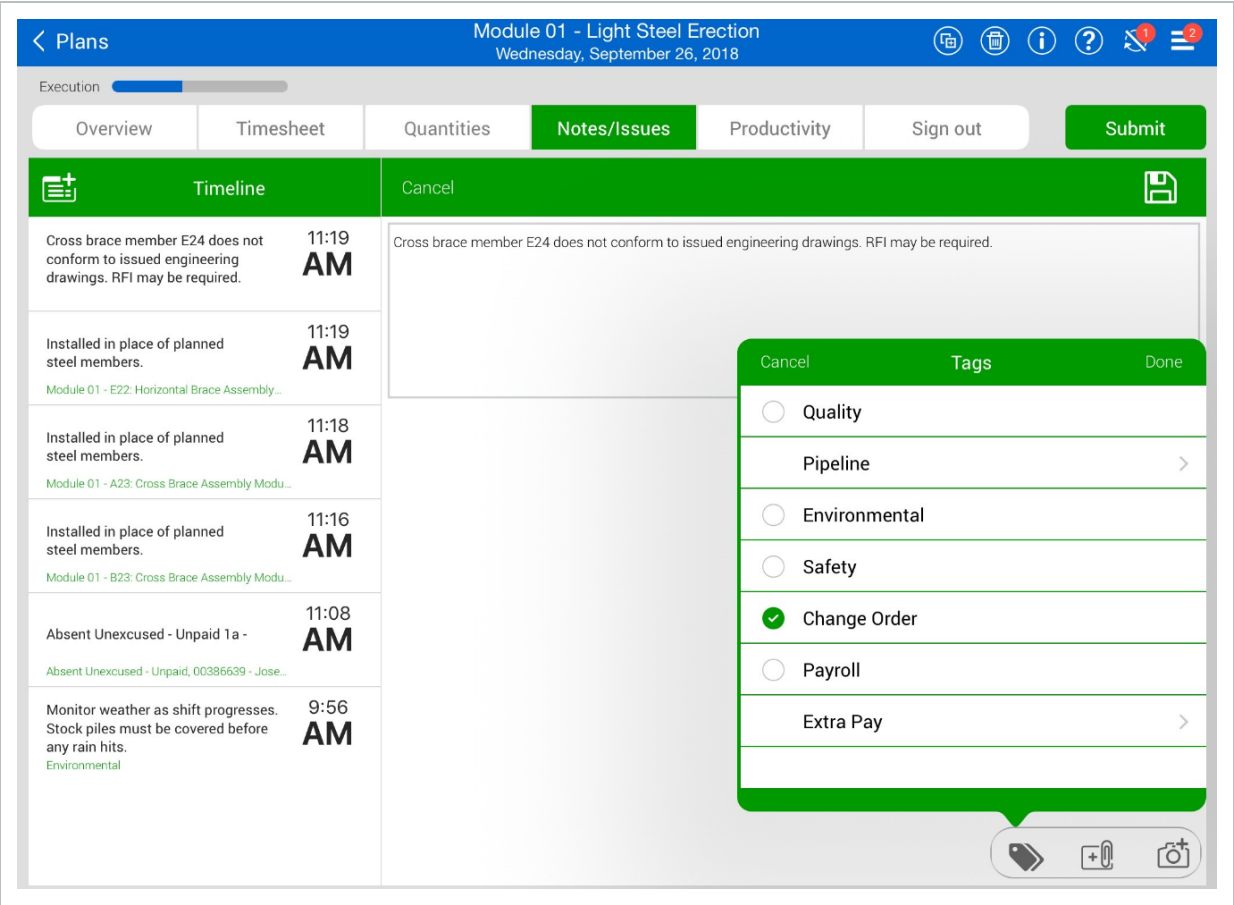

- 12. To associate the note with a component, tap the **Tag**  icon, then select **Components**.
- 13. Select a component.
- 14. Click **Done**.

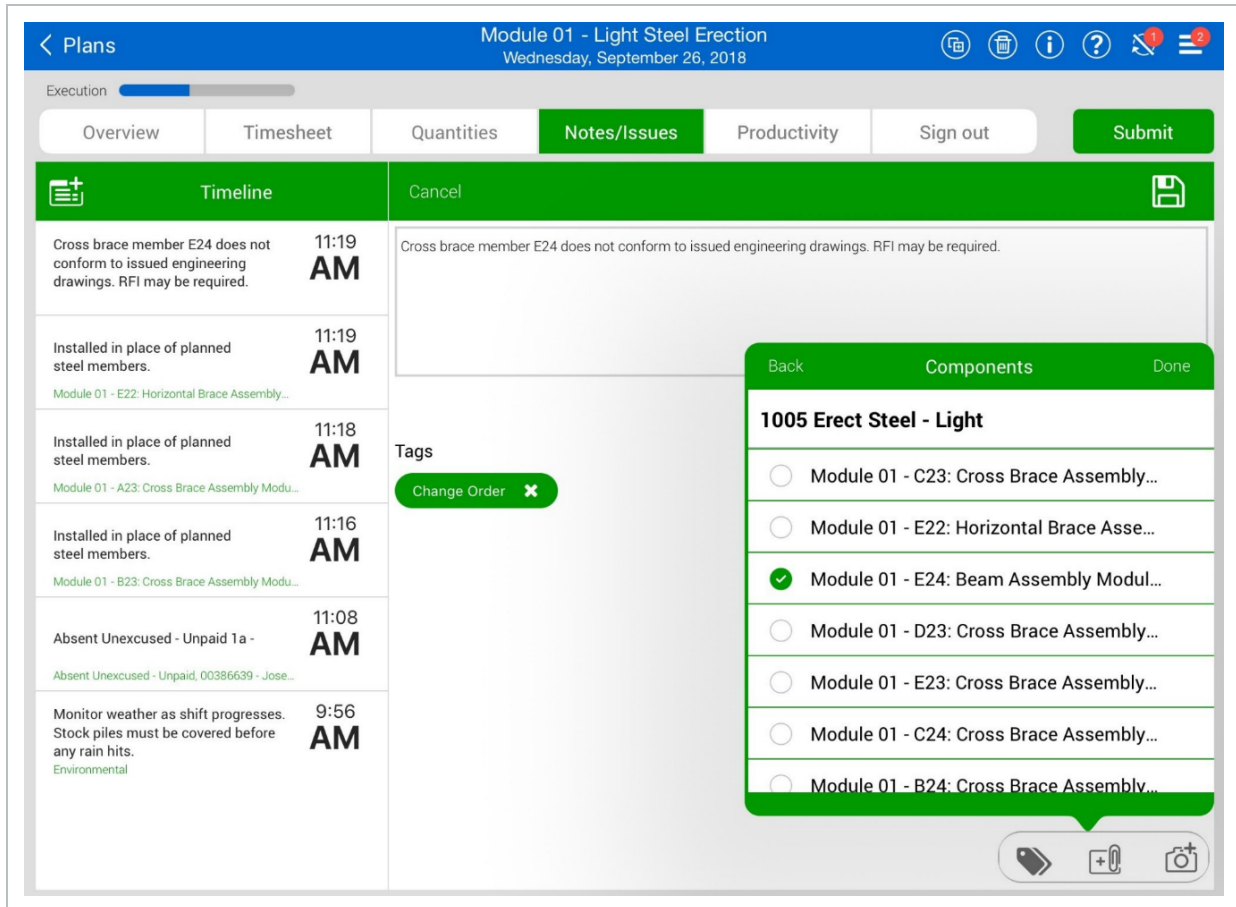

15. Tap the **Camera**  icon to add a photo to the note.
16. Tap **Use Camera** and take a picture using the iPad camera.
17. Make markups and add text.
18. Tap **Done** to add the picture to the note.
19. Review the **Productivity** tab.
 - Check to see if you are gaining or losing man hours and what your actuals are compared to the planned and budget columns

< Plans

Module 01 - Light Steel Erection
Wednesday, September 26, 2018

1

2

Execution

Overview

Timesheet

Quantities

Notes/Issues

Productivity

Sign out

Submit

Task ID and Description		Actual			⇄ MHRs per Qty			Actual	
Task ID	Description	Quantity	UOM	MHRs	Planned	Actual	CB ▾	Cost G/L	MHRs G/L
1005	Erect Steel - Light	0.353	Ton	24.00	90.678	68.009	20.000	353	-16.9
Totals				24.00				353	-16.9

20. Tap on the **Sign In/Sign Out** tab, and then tap the **Sign Out** subtab.
21. Sign out each employee by selecting **On Behalf of Employee**.
22. Tap on **Sign out with Touch ID or PIN**.
23. Enter the ID number for your iPad.
 - The first name in the employee list is automatically highlighted and the list of compliance questions is shown
 - These compliance questions are usually set by management. They are set up in the project settings
24. Answer employee sign out questions.
25. Tap **Done**.
26. Repeat the sign out steps for all employees.
27. Tap **Submit** to submit the plan to the approval phase.
 - Progress will automatically sync when the plan is submitted. This sync must be successful for it to show up in the InEight Progress web application

