

CONTROL USER GUIDE



Information in this document is subject to change without notice. Companies, names and data used in examples are fictitious.

Copyright ©2026 by InEight. All rights reserved. No part of this document may be reproduced or transmitted in any form or by any means, electronic or mechanical, for any purpose, without the express permission of InEight.

Microsoft Windows, Internet Explorer and Microsoft Excel are registered trademarks of Microsoft Corporation.

Although InEight Control has undergone extensive testing, InEight makes no warranty or representation, either express or implied, with respect to this software or documentation, its quality, performance, merchantability, or fitness for purpose. As a result, this software and documentation are licensed “as is”, and you, the licensee are assuming the entire risk as to its quality and performance. In no event will InEight be liable for direct, indirect, special, incidental or consequential damages arising out of the use or inability to use the software or documentation.

Release 26.7
Last Updated: 09 September 2026

CONTENTS

CHAPTER 1 – OVERVIEW	22
1.1 Overview	23
1.1.1 Account Code Management	23
1.1.2 Progress Measurement	23
1.1.3 Forecasting	24
1.1.4 Revenue Management	26
1.1.5 Change Management	26
1.1.6 InEight Control Workflow	28
CHAPTER 2 – GENERAL NAVIGATION	29
2.1 Page Navigation	30
2.1.1 Navigate the InEight Control Workspaces Page	32
2.1.2 Right Toolbar Overview	33
2.2 Workspaces	35
2.3 CBS register	35
2.4 ACS register	36
2.4.1 ACS Navigation	36
2.5 Pay Items register	37
2.5.1 Pay Items register columns	39
2.5.1.1 Revenue forecasting columns	39
2.5.1.2 Change management columns	39
2.5.2 Move Pay Items	40
Move pay items	41
2.6 Change Register	42
2.7 Audit Log register	43
2.8 Columns/Grouping/Sorting	44
2.8.1 Resize column width	44
2.8.2 Move Columns	46
2.8.3 Sort Columns	47
2.8.4 Filter Columns	50
2.8.4.1 Method 1: Filter from Column Header	50
2.8.4.2 Method 2: Filter by Query	51
2.8.4.3 Query Builder	51
2.8.5 Filter Indicator	53

2.8.6 Grouping	53
Group Data by Column Values	54
2.9 Data Blocks	56
2.9.1 Data Block Categories	57
2.9.1.1 Standard Data Block	57
2.9.1.2 Forecast Data Block	58
2.9.1.3 Cost Category Data Block	58
2.9.2 Manage Data Blocks	58
2.9.2.4 Thumbnail View	59
2.9.2.5 List View	60
2.9.3 Data Block Context Menu	62
Edit a Data Block	63
2.9.4 Custom Data Blocks	64
Create a Custom Data Block	64
2.10 Viewsets	69
Create and Save a Viewset	69
2.10.1 Sending Views and Data Blocks	70
Send a Viewset	70
2.11 Row Density	73
2.12 Audit Log	75
2.12.1 CBS	76
2.12.2 ACS	76
2.12.3 Pay Items	77
2.12.4 Integration	78
2.12.5 Import history	79
2.12.5.1 Pending status	81
Option 1	82
Option 2	85
2.12.5.2 Failed with errors status	85
2.13 Project Introduction	86
CHAPTER 3 – COST ITEM SETUP	89
3.1 Cost item setup workflow	90
3.2 Cost Item Overview	91
3.2.1 Cost Breakdown Structure	91
3.2.2 CBS Tree	94
3.2.3 Cost Item Menu	96
3.2.4 Cost Item Dashboard	97
3.3 Cost Items	99
3.3.1 Cost Item Creation	99

Create A New Cost Item	101
Create a New Subordinate Cost Item	103
3.3.1.1 Create Multiple Cost Items	105
3.3.2 Required Cost Items	106
3.3.3 Cost Item Arrangement	108
Move a Cost Item	108
3.3.4 Viewing the CBS Grouped by Column	110
CBS Group by Column	110
3.3.5 Cost Item Deletion	111
3.3.6 Copying Cost Items with Resources	113
Copy and paste cost items	113
3.3.7 Design total qty and Design total MHrs columns in the CBS	115
3.3.8 Create cost items in InEight Change	116
3.4 Hide in Plan, Progress, and Design	119
3.4.1 Hide feature in a cost item	120
3.4.2 Hide feature in the CBS Workspace	121
3.4.3 Considerations	121
3.5 Cost Item Excel Import	122
3.5.1 Forecast Excel Import	127
3.5.2 Spreadsheet Rules	128
3.5.3 Best Practices and Recommendations	130
3.5.4 CBS Hierarchy	130
3.5.4.1 CBS Predictive Hierarchy	131
Import CBS Data	133
3.5.5 Resolving Import Errors	139
3.5.6 Excel Import for committed cost	140
3.5.6.2 Generating the commitment cost Excel spreadsheet	141
3.5.6.3 Importing commitment data	142
Import Commitment Costs	143
CHAPTER 4 – COST ITEM MANAGEMENT	149
4.1 Cost item management workflow	150
4.2 Estimate Resources	150
4.2.1 Navigate to Estimate Resources	152
4.2.2 Manage estimate resources	154
4.2.3 Resource rates	155
4.2.4 Add estimate resources to a job	155
Add estimate resources	156
4.2.5 Data columns	157

4.3 Cost item details	159
4.4 Cost item details overview	159
4.5 Details tab	159
4.5.1 Pay item contribute quantity	162
4.6 Attributes tab	164
4.7 Cost categories tab	165
Enter Costs in Cost Categories	167
4.8 Current Estimate Resources tab	167
4.8.1 Cost Driver	169
4.8.2 Productivity and overall settings	173
4.8.2.1 Updates to resource quantities	175
4.9 Forecast Resources tab	177
4.9.1 Productivity and overall settings	179
4.9.2 Resource Details	180
4.9.2.1 Orphan Indicator	181
4.9.3 Cost Item Man-Hours	182
Define Cost Item Man-Hours	182
4.10 Issue tagging in the CBS	183
4.11 Lock Budget	186
4.11.1 Budgets vs Estimate	186
4.11.1.1 Original Budget	186
4.11.1.2 Current Budget	186
4.11.1.3 Current Estimate	187
4.11.2 Lock Budget and Price	188
4.11.3 Unlock Budget and Price	190
4.12 Assigned vendors	191
CHAPTER 5 – PROGRESS MEASUREMENT	195
5.1 Progress measurement workflow	196
5.2 Progress Measurement Overview	196
5.2.1 Budgets vs Estimate	197
5.2.1.1 Original Budget	197
5.2.1.2 Current Budget	197
5.2.1.3 Current Estimate	198
5.2.2 Earned value management terms	199
5.2.2.4 Planned Value (PV)	199
5.2.2.5 Earned Value (EV)	199
5.2.2.6 Schedule Performance Index	200
5.2.2.7 Actual Cost (AC)	200

5.2.2.8 Variance	201
5.2.2.9 Remaining	201
5.2.3 Productivity	202
5.2.3.10 Compensation Factor (CF)	203
5.2.3.11 Labor Efficiency Index (LEI)	203
5.2.4 Updating Forecast (T/O) Qty	203
5.2.4.12 Forecast (T/O) - CB qty delta column	204
5.2.5 Update Forecast (T/O) Qty with Plan components	205
5.3 Date Range Setup	208
Date Range Setup	208
5.4 Manage Actuals	211
5.5 Actuals by Sync	211
5.5.1 Sync Quantities	211
Performing a Get Quantities Sync	213
5.5.1.1 Types of Get Quantities Syncs	214
5.5.2 Sync Hours and Costs	217
5.5.3 Audit Log	221
5.6 Actuals by Import	221
Import Actuals	223
5.7 Actuals by Manual Entry	226
Claim Actuals by Manual Entry	227
5.7.1 Claim Quantities	228
5.7.1.1 Claim quantities for multiple cost items	230
Claim Quantities for Multiple Cost Items	230
5.7.2 Claim Man-hours	234
5.7.3 Claim Equipment Hours	235
5.7.4 Claim Cost	236
5.7.5 Add Additional Claiming entries	238
5.7.6 User-Defined Fields	238
5.8 Actuals by API	239
5.9 User-defined fields	239
5.10 Estimated Actuals	242
5.10.1 Claim Estimated Actuals in Control	244
Claim Estimated Actuals	244
5.10.2 Estimated Actuals from Progress	245
5.10.3 Reverse Estimated Actuals	247
Reverse Estimated ACTuals	248
5.11 Actuals History	249
5.12 Progress Control Settings	249

Progress Control Settings	250
5.13 Vendor Work Hours from Progress	251
5.13.1 Vendor MHrs from Progress	251
5.14 Track Open/Remaining and Total Committed Costs	254
Viewing Open/Remaining and Total Committed Costs	255
5.15 Committed cost from Contract	260
CHAPTER 6 – ACCOUNT CODES	263
6.1 Account codes workflow	263
6.2 Account Code Assignment	264
Assign Account Codes to Cost Items	264
6.3 Quantity Contribution	264
6.3.1 ACS Navigation	265
6.3.2 Account Code Quantity	266
Define Account Code Quantity	266
6.3.3 Quantity Contributors	267
6.3.3.1 Contribution Options - Cost Item to Account Code	267
6.3.3.2 Contribution Options - Child Account Code to Parent Account Code	268
6.3.4 ACS Unit of Measure Toggle	268
6.3.5 Account Code Quantity Conversions	269
6.3.6 Notes Column	271
Review	272
Summary	272
CHAPTER 7 – FORECASTING	273
7.1 Forecasting workflow	274
7.2 Forecasting overview	275
7.2.1 Private forecasts	275
7.2.2 Shared forecasts	275
7.2.3 Live forecast	276
7.3 Forecast management	276
7.3.1 Forecast data block	276
7.3.2 Push to shared forecast	280
Push to shared forecast	280
7.3.3 Compare forecasts	281
7.3.4 Live forecast data block	282
7.4 Fiscal Calendar	283
7.5 Forecast Methods	285
7.5.1 Forecast Method Assignment	286

7.5.1.1 Global Forecast Method	287
Set Global Forecast Method	287
7.5.1.2 Forecast Method for Selected Items	287
Set the Forecast Method for Selected Items	288
7.5.1.3 Forecast Method for Individual Items	289
Set the Forecast Method for Individual Items	289
7.5.1.4 Average Performance Forecast Method	290
7.5.1.5 Committed Cost Forecast Method	293
7.5.1.6 Contract Forecast Method	295
Unapproved Contract Line Items	296
7.5.1.7 Custom Forecast Method	297
7.6 Manual Forecasting	298
7.6.1 EAC vs. ETC	298
7.6.2 Manual EAC (Estimate at Complete) Forecast	299
Manually Adjust Forecast Final Cost	300
7.6.2.1 Proportional Adjustment	303
7.6.3 Manual ETC (Estimate to Completion) Forecast	305
7.6.3.2 Detailed ETC FC Method	305
7.7 Time Phased Forecasting	307
7.7.1 TPF Register	310
7.7.2 Auto Distribute	310
7.7.3 Manual Time Phased Forecast	311
7.7.3.1 Proportional Man Hours and Quantity	312
7.7.4 Static manual time phased forecasting (TPF)	315
7.7.5 Time Phased Forecast Settings	317
7.7.5.2 Enable Time Phased Forecasting	318
7.7.5.3 Cost Curves	318
7.7.6 Time Phased Forecast Prerequisites	320
7.7.7 Time Phased Forecast View	320
Time Phased Forecast Planning	320
7.7.8 Time Phased Forecast Microsoft Excel import	323
Time phased forecast Microsoft Excel import	325
7.7.9 Column Chooser	328
7.7.10 Audit Log	329
7.8 Push to Live Forecasts	329
Push Live Forecast by Selection in the CBS Tab	330
7.8.1 Time phased forecast push to live	330
Time phased forecast push to live forecast	331
7.9 Live Forecast Snapshot	333

7.9.1 Snapshot settings	334
7.9.2 Manage snapshots	334
CHAPTER 8 – CHANGE MANAGEMENT	337
8.1 Change management workflow	337
8.2 Change management overview	337
8.2.1 Managing changes using the InEight Suite	339
8.2.2 InEight Change integration with Control	340
8.3 Associated Budget Move	340
Perform an associated budget move	342
8.3.1 Associated Budget Move - Single Cost Item	348
Perform an associated budget move within a single cost item	349
8.4 Non-Associated Budget Move	352
Perform a non-associated budget move	355
8.4.1 Auto-Calculate budget move values	360
8.4.1.1 Update current budget (CB) adjustments from current estimate (CE)	360
Perform a budget move using Auto-calculate > Update CB from CE	360
8.4.1.2 Update Current Estimate from Adjusted Current Budget	361
8.4.1.3 Select cost items to update	363
8.4.1.4 Select automatic updates for multiple cost items	363
8.4.1.5 Set setting for default current estimate update	364
8.5 Budget move from InEight Change	365
8.5.1 Budget move in Change	365
8.5.2 Budget Move Integration Between Change and Control	366
8.6 Budget Quantity / Man-Hour Adjustment	366
Perform a Budget Quantity / Man-Hour Adjustment	367
8.7 Contract adjustment – Control	369
8.8 Contract adjustment in Control overview	370
8.8.1 Pay Item vs. Cost Item	370
8.8.2 Contract adjustment options	370
8.8.3 Contract adjustment header	371
8.9 Start with cost items contract adjustment	372
Contract adjustment starting with cost items	372
8.10 Start with pay items contract adjustment	381
Starting with pay items contract adjustment	382
8.11 Auto-calculate contract adjustment values	388
8.11.1 Update Current Budget (CB) Adjustments from Current Estimate (CE)	388

8.11.1.1 Auto-calculate current budget adjustments on the Start with Cost items workflow	388
8.11.1.2 Auto-Calculate Current Budget Adjustments on the Start with Pay Items Workflow	389
8.11.2 Update Current Estimate from Adjusted Current Budget	390
8.11.2.3 Select automatic updates for multiple cost items	392
8.11.2.4 Set setting for default current estimate update	393
8.12 Contract adjustment – InEight Change	393
8.13 Contract adjustment from InEight Change overview	394
8.14 Contract adjustment from InEight Change overview	394
8.15 Managing Changes in InEight Change	394
8.15.1 InEight Change Integration with InEight Control	395
8.15.2 Creating new cost items from Change executed change orders	395
8.15.3 Pay item associations from InEight Change executed change orders	397
8.15.4 Markup from InEight Change executed change orders	398
8.15.5 Revising a CCO-Draft contract adjustment	398
8.16 Contract adjustment header	399
8.17 Change Approval Process	401
8.17.1 Managing changes in the Change Register	404
8.17.1.1 Draft changes review	404
8.17.1.2 Pending changes review	405
8.17.2 Group By option	406
CHAPTER 9 – REVENUE MANAGEMENT	409
9.1 Revenue management workflow	409
9.2 Pay Items	410
9.3 Account code structure workflow	410
9.4 Pay Item details	410
9.4.1 Pay item details slide-out panel	411
9.4.2 Details Tab	412
9.4.3 Attributes Tab	413
9.4.4 Change Orders	415
9.4.5 Cost Items	416
9.4.6 Cost Categories	416
9.5 Creating and locking pay items	417
Upload pay items from a Microsoft Excel spreadsheet	417
9.5.0.1 Adding Pay Item details	418
9.5.0.2 Locking in your pricing	418

9.6 Billing methods	419
9.6.1 Fixed final price	420
9.6.2 Unit price	420
9.6.3 Cost Plus	420
9.7 Bulk Import Pay Items	425
9.7.1 Spreadsheet Rules	428
9.8 Markup percent	430
9.8.1 Markup % column	432
9.9 Earning Rules	433
Adjusting Pay Item Earning Rules	434
9.10 Billed Revenue	435
9.11 Billed Tab	436
9.11.1 Unit price proportional billing	437
9.11.1.1 Change Orders	438
Bill for revenue earned	438
9.12 Retention tab	439
9.13 Billed history tab	440
9.14 Billed revenue columns	441
9.15 Pay item revenue billing in bulk	442
Bill for multiple pay items	447
9.16 Sync billed revenue details	449
9.16.1 Sync billed revenue	449
9.17 Actualizing revenue	450
9.18 Change orders	453
9.19 Revenue Forecasting	455
9.19.1 Pay Item Position Code Column	455
9.19.2 Cost Item Revenue View	456
9.19.3 Cost item revenue calculation by allows as-built	457
9.20 Revenue forecasting columns	457
9.21 Revenue calculations	459
9.21.1 Cost Breakdown Structure (CBS) register revenue Calculations	459
9.21.2 Pay Items register calculations	465
9.22 Cost plus revenue forecast methods	466
9.23 Push forecast revenue	468
9.23.1 Revenue Snapshots	469
9.24 Revenue Forecast Probability	471
Approval Probability	471
9.25 Time-phased budget	474
9.25.1 Budget organization setting	474

9.25.2 Edit Past Time-Phased Budget Values	474
9.25.3 Switching off time-phasing budget	475
9.25.4 Switching on the time-phasing budget	476
9.25.4.1 Default all budget to current fiscal period	477
9.25.4.2 Default to project start and end dates	478
9.25.4.3 Populate missing dates manually	478
9.25.5 Time-phased budget in contract adjustment	478
9.25.6 Time-phased budget at the budget move	483
9.25.7 Time-phased budget grids	485
9.25.8 Changing Distribution type to cost item	486
9.25.9 Manual distribution of cost adjustment	487
9.25.10 Deltas in a adjusted cost columns	488
9.25.11 View cost columns	490
9.25.12 Date range filter	490
9.25.13 Approving budget warnings	491
9.26 Revenue calculations	491
9.26.1 Cost Breakdown Structure (CBS) register revenue calculations	492
9.26.2 Pay Items register revenue calculations	498
CHAPTER 10 – SCHEDULING	501
10.1 Scheduling overview	501
10.2 Schedule data block	501
Schedule Data Block	502
10.3 Schedule Excel import	505
Excel Import	505
10.4 Primavera Schedule integration	511
10.4.1 Primavera Schedule Integration Settings	511
10.4.1.1 Primavera XER Schedule Integration Prerequisites	513
Schedule Integration Import	515
Primavera Schedule Integration Export	519
10.4.2 Percent Complete column updates in CBS	520
CHAPTER 11 – ACCOUNT CODE STRUCTURE (ACS)	523
11.1 Account code structure workflow	523
11.2 What is an Account Code?	524
11.3 Account code setup	524
11.3.1 Staging vs. Published Account Codes	525
Create an Account Code	526
Edit Account Code Details	530

11.3.2 Account code permissions	531
11.3.2.1 Deleting account codes	531
Deleting account codes	532
11.3.2.2 Replacing deleted account codes	536
11.3.2.3 Renaming account codes	537
Renaming account codes	537
11.4 Measurement types	540
11.5 Cost category label customizations	541
CHAPTER 12 – INTERFACES	545
12.1 Push and Get actions	546
Sync Options	549
12.2 Scheduled syncs	551
12.2.1 Sync integrations	552
12.3 Audit log - Integration	556
Sync Audit Log	556
CHAPTER 13 – INEIGHT PLATFORM SETTINGS	557
13.1 Organizational breakdown structure	557
13.1.1 Unique budget code segments	558
Open Project Details	561
13.2 Project page	561
13.3 Manage users	563
13.3.1 User Management	563
13.3.2 Roles and permissions	563
13.3.3 Considerations	564
13.4 Organization general settings	565
13.5 Home page	565
13.6 Global options	566
13.6.1 Master data libraries	567
13.6.2 Role Assignment	567
13.6.3 Project display in primary navigation	567
13.6.4 Cost item integration behavior	568
13.6.5 Email preferences	569
13.6.6 Environment indicator	569
13.6.7 Session timeout	569
13.6.8 Landing page default view	570
13.6.9 Organization/Project images	570
13.6.10 Product integrations	571
13.7 Fiscal calendar	571

13.7.1 Fiscal calendar	571
13.8 Document types	572
13.8.1 Considerations	572
13.9 Custom lists	573
13.9.1 CBS URL columns	573
13.10 Attribute definitions	575
13.11 Menu options	576
CHAPTER 14 – CONTROL SETTINGS	577
14.0.1 Considerations	577
14.1 Project tracking	577
14.2 Tasks	578
14.2.1 Organizational and project level	578
14.2.1.1 Generate WBS phase code automatically	578
14.2.1.2 Enable Manual Snapshots	578
14.2.1.3 Default CE values to be updated from CB values	582
14.2.2 Project level	582
14.2.2.4 Maintain CBS Structure at a specific level	583
14.2.2.5 Allow syncs to replace manual snapshots	583
14.3 Actuals	584
14.4 Estimated actuals	590
14.5 Time-phasing	592
14.5.1 Budget	592
14.5.2 Enable time-phasing for budget	592
14.5.3 Edit previous time-phased budget values	594
14.5.4 Switching off time phasing budget	594
14.6 Forecast	596
14.7 Time-phasing	596
14.7.1 Forecasting	596
14.8 Forecast	597
14.8.1 Percent complete value at which delta from straight line calculation utilizes average performance	597
14.8.2 Mandatory notes for manual forecasts	598
14.9 Custom forecast method calculations	599
14.9.1 Enable Forecast methods based on Allow as-built selections	601
14.10 Estimate resources	603
14.11 Estimate resources	603
14.11.1 Wage rate composition	603
14.12 Schedule	604

14.13 Schedule	604
14.14 Define project schedule	605
14.15 Cost curves	606
14.15.1 Manage cost curve tables	607
Add a custom cost curve table	607
View a cost curve table	607
Delete a cost curve table	608
14.16 Plug day calculation	608
14.17 Schedule ID	608
14.18 Revenue	610
14.19 Revenue	610
14.20 Revenue and cost timing	610
14.20.1 InEight Change integration	612
14.21 Billing method default earnings rules	612
14.21.1 Fixed final price and Unit price	613
14.21.2 Cost plus	613
14.22 Pay item to Cost item Forecast (T/O) qty relationship	613
14.22.1 Enable pay item Forecast (T/O) quantity rollups	614
14.22.2 Enable pay item Forecast (T/O) quantity roll down	616
14.23 Markup	617
14.24 Sync integrations	621
14.25 Sync integrations	621
14.25.1 Organizational level	621
14.25.1.1 Actual cost and man-hour sync options	621
14.25.2 Project level	622
14.25.2.2 Sync integrations schedule	622
14.25.3 Considerations	623
14.26 Others	624
14.27 Others	624
14.27.1 Organizational level	624
14.27.1.1 Required cost items	624
14.27.1.2 Change order details	625
14.27.2 Project level	626
14.27.2.3 Required cost items	626
14.27.2.4 Decimal precision	626
14.28 Frequently Asked Questions	627
14.29 Frequently Asked Questions	631
14.30 Workflows	635
14.30.1 Product Workflows	635

14.30.1.1 InEight Control General Workflow	635
14.30.2 Business Process Workflows	636
14.30.2.2 Cost Budgeting and Forecasting: Budget Management	636
14.30.2.3 Cost Budgeting and Forecasting: Forecasting	636
14.30.2.4 Billing Management	637
14.30.2.5 Earned Value Management	638

STEP BY STEP PROCEDURES

Move pay items	41
Group Data by Column Values	54
Edit a Data Block	63
Create a Custom Data Block	64
Create and Save a Viewset	69
Send a Viewset	70
Create A New Cost Item	101
Create a New Subordinate Cost Item	103
Move a Cost Item	108
CBS Group by Column	110
Copy and paste cost items	113
Import CBS Data	133
Import Commitment Costs	143
Add estimate resources	156
Enter Costs in Cost Categories	167
Define Cost Item Man-Hours	182
Date Range Setup	208
Performing a Get Quantities Sync	213
Import Actuals	223
Claim Actuals by Manual Entry	227
Claim Quantities for Multiple Cost Items	230
Claim Estimated Actuals	244
Reverse Estimated Actuals	248
Progress Control Settings	250
Viewing Open/Remaining and Total Committed Costs	255
Assign Account Codes to Cost Items	264
Define Account Code Quantity	266
Push to shared forecast	280

Set Global Forecast Method	287
Set the Forecast Method for Selected Items	288
Set the Forecast Method for Individual Items	289
Manually Adjust Forecast Final Cost	300
Time Phased Forecast Planning	320
Time phased forecast Microsoft Excel import	325
Push Live Forecast by Selection in the CBS Tab	330
Time phased forecast push to live forecast	331
Perform an associated budget move	342
Perform an associated budget move within a single cost item	349
Perform a non-associated budget move	355
Perform a budget move using Auto-calculate > Update CB from CE	360
Perform a Budget Quantity / Man-Hour Adjustment	367
Contract adjustment starting with cost items	372
Starting with pay items contract adjustment	382
Upload pay items from a Microsoft Excel spreadsheet	417
Adjusting Pay Item Earning Rules	434
Bill for revenue earned	438
Bill for multiple pay items	447
Approval Probability	471
Schedule Data Block	502
Excel Import	505
Schedule Integration Import	515
Primavera Schedule Integration Export	519
Create an Account Code	526
Edit Account Code Details	530
Deleting account codes	532
Renaming account codes	537
Sync Options	549
Sync Audit Log	556

Open Project Details 561

Add a custom cost curve table 607

View a cost curve table 607

Delete a cost curve table 608

EXERCISES

CHAPTER 1 – OVERVIEW


1.1 OVERVIEW

As one of the applications within the InEight portfolio of products, InEight Control is a project management tool used for:

- Managing account codes
- Measuring progress
- Forecasting final man-hours and costs
- Managing revenue
- Managing budget/contract changes

1.1.1 Account Code Management

Within InEight Control, you can define and assign account codes to your cost items. This association can be synced to your ERP, and can also be used to benchmark data with other projects.

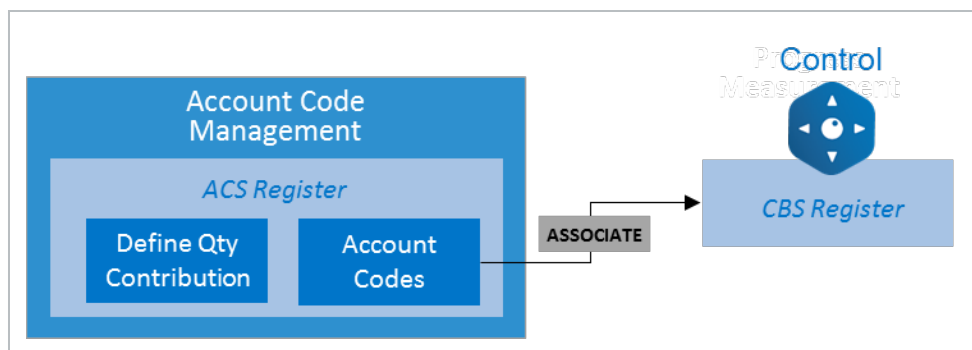


1.1.2 Progress Measurement

InEight Control is the application where your Cost Breakdown Structure and budget are established and where you can monitor project progress. You can:

- Import your conformed estimate and structure from InEight Estimate
- Create and manage cost items
- Import approved quantities from InEight Plan

- Import final hours and costs from your ERP system
- Track your actuals and compare them against your Current Budget and earned values

The following workflow illustrates how these functions relate and pass information between systems.

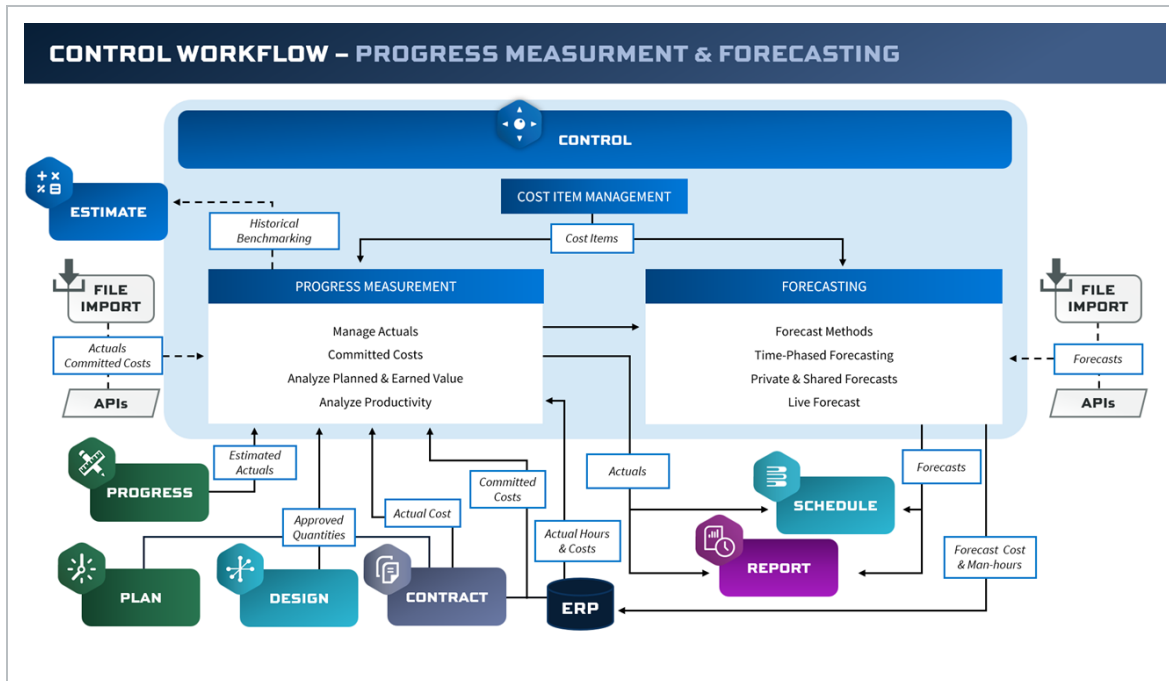

You can utilize this information to analyze trends, track productivity factors, and measure progress.

Tasks			Progress Overview				
	CBS Pos...	Description	% Complete	C B-Total C...	C B-Earned Total ...	Total Cost (To Date)	C B-Total Cost G/L (T...
	▼1	Infrastructure	0.01	\$14,193,548.20	\$80,054.65	\$3,000.00	\$77,051.61
	1.1	Mobilization	0.00	\$10,794.00	\$0.00	\$0.00	\$0.00
	▼1.2	West Screen Demolition	0.38	\$4,605.59	\$1,772.88	\$3,000.00	(\$1,227.13)
	1.2.1	West - Removal-Conduit	0.34	\$3,448.93	\$1,172.88	\$3,000.00	(\$1,827.12)

1.1.3 Forecasting

InEight Control provides options for forecasting final costs, man-hours, and productivity for your project.


Tasks		Task details			Forecast Created from Live forec...			
CBS position	Description	Resource	Forecast (T/O) quantity	UoM	Forecast final cost	Forecast final Mhrs	Forecast final man hours/Unit	Forecast final productivity factor
2	Earthwork	5	10,000.00	CY	\$ 400,000.00	8,000.00	0.80	1.00
3	Concrete	6	10,000.00	CY	\$ 1,500,000.00	30,000.00	3.00	1.00
4	Structural Steel		1,000.00	Ton	\$ 1,000,035.71	20,000.71	20.00	1.00
4.1	Erect Steel - Heavy	5	800.00	Ton	\$ 800,000.00	16,000.00	20.00	1.00
4.2	Erect Steel - Light	5	200.00	Ton	\$ 200,000.00	4,000.00	20.00	1.00
4.3	Bolted Connections	8	2,000.00	Ea	\$ 35.71	0.71	0.00	1.00

You can forecast your remaining work based on any of the following Forecast Methods:

- Current Budget
- Current Estimate
- Average performance
- Committed Cost
- Manual Entry


You can save private forecasts, share them with others, and push them to a “live” forecast which can be reviewed by all and used for official reporting. You can also compare the Live Forecast to other forecasts created, for example to compare to the previous month’s forecast.

The workflow diagram below illustrates how forecasting functions relate to the rest of InEight Control and other systems.

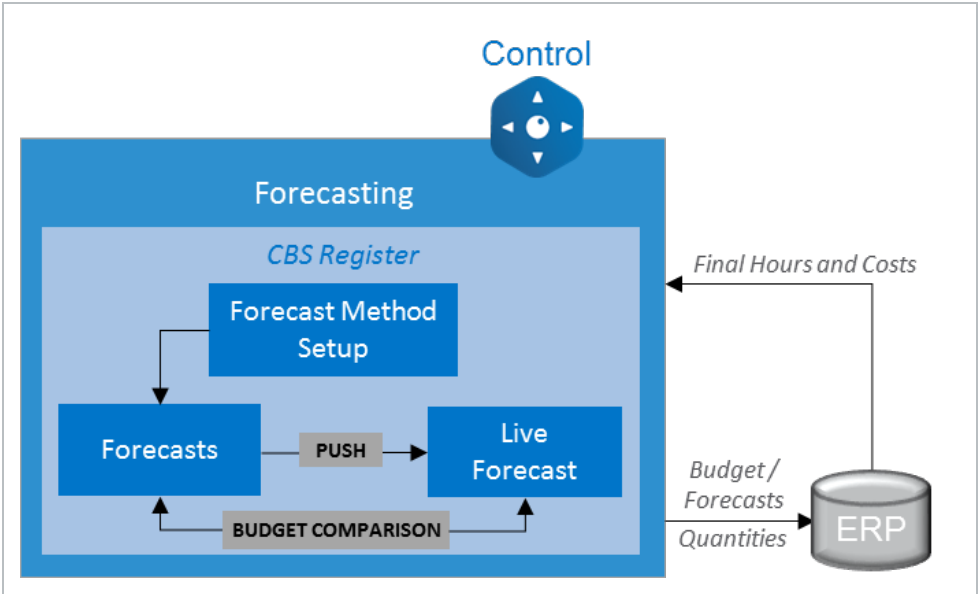

1.1.4 Revenue Management

Within InEight Control, you can create and manage pay items for tracking pay quantities, actual and forecasted revenue, and how much has been billed to the client.

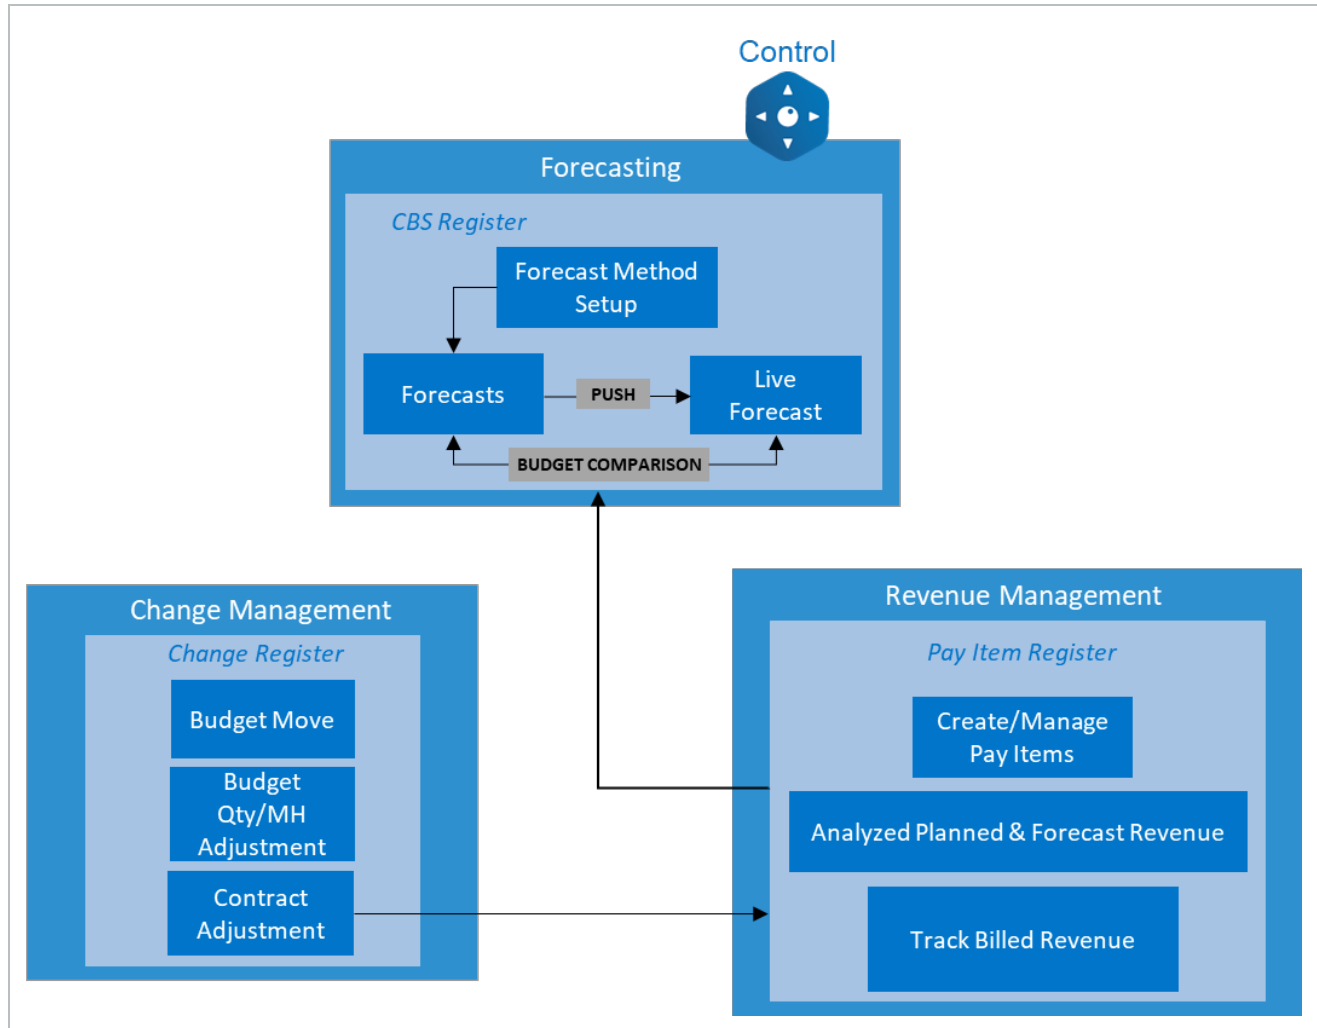


1.1.5 Change Management

InEight Control allows you to manage changes to quantities, man-hours, and costs in each cost item as needed during the execution of the project. You can make three different kinds of changes within the Change Management register:

- **Budget move** – Movement of costs between cost items where the total dollars moved must balance to zero. There is no revenue associated with this type of change
- **Budget quantity and man-hour adjustment** – change to quantities or man-hours within the project without changing costs
- **Contract adjustment** – both the budget and the revenue either increase or decrease and are not required to be a net zero transaction. You will associate pay items with the change order to reflect the revenue change

Approved changes update your Current Budget within the CBS register.

The below workflow shows the relationship of Change Management to the rest of InEight Control.

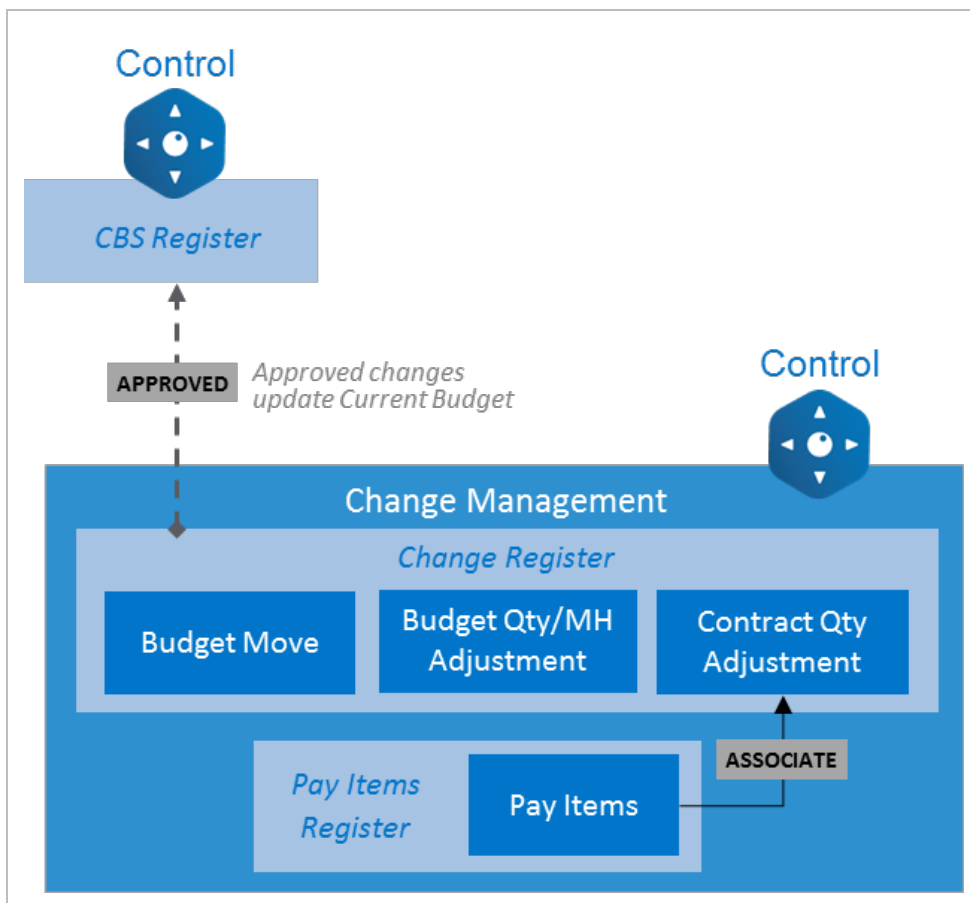


Below is an example of what the Change Register looks like in InEight Control.

Change Register						
ID	CCO	Issue #	Description	Type	Discipline	Total Budget \$ adjust
20.0	001	001	Increase budget in the code for Plan and Progress	Contract adjustment	1	\$4,800.00
21.0			Increase budget quantity for proper production factor	Budget Qty&MH adjustment	1	\$0.00

1.1.6 InEight Control Workflow

The following workflow illustrates how all the functions of InEight Control work together.

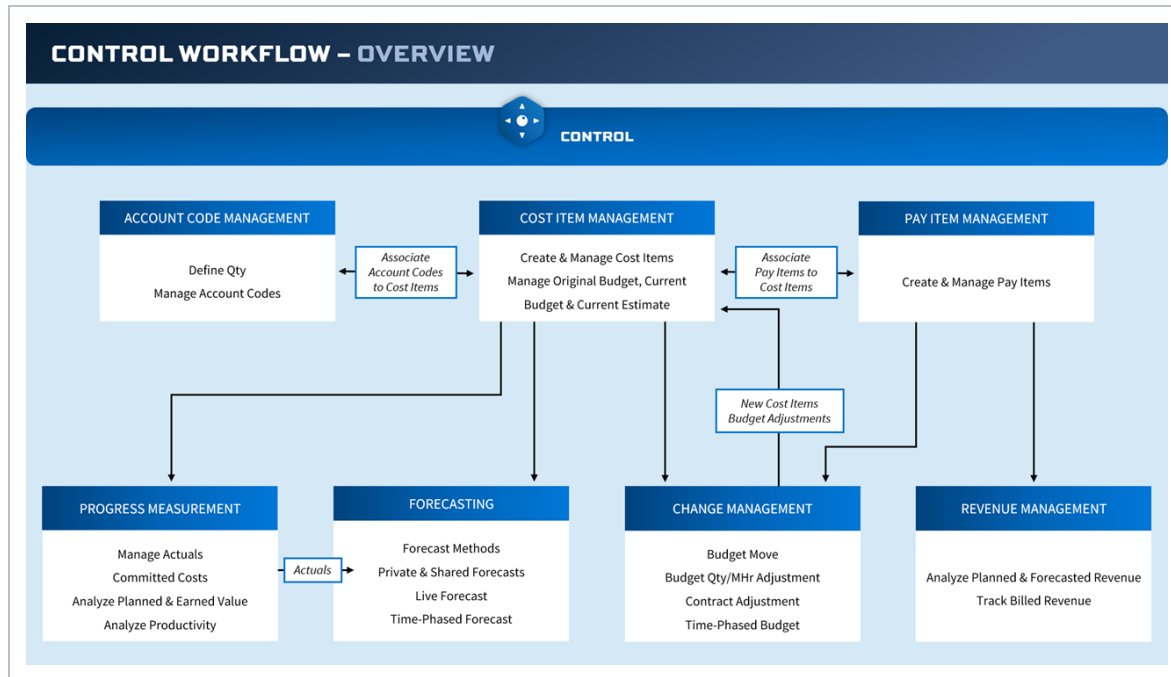


CHAPTER 2 – GENERAL NAVIGATION

2.1 Page Navigation	30
2.1.1 Navigate the InEight Control Workspaces Page	32
2.1.2 Right Toolbar Overview	33
2.2 Workspaces	35
2.3 CBS register	35
2.4 ACS register	36
2.4.1 ACS Navigation	36
2.5 Pay Items register	37
2.5.1 Pay Items register columns	39
2.5.2 Move Pay Items	40
2.6 Change Register	42
2.7 Audit Log register	43
2.8 Columns/Grouping/Sorting	44
2.8.1 Resize column width	44
2.8.2 Move Columns	46
2.8.3 Sort Columns	47
2.8.4 Filter Columns	50
2.8.5 Filter Indicator	53
2.8.6 Grouping	53
2.9 Data Blocks	56
2.9.1 Data Block Categories	57
2.9.2 Manage Data Blocks	58
2.9.3 Data Block Context Menu	62
2.9.4 Custom Data Blocks	64
2.10 Viewsets	69
2.10.1 Sending Views and Data Blocks	70
2.11 Row Density	73
2.12 Audit Log	75
2.12.1 CBS	76

2.12.2 ACS	76
2.12.3 Pay Items	77
2.12.4 Integration	78
2.12.5 Import history	79
2.13 Project Introduction	86

2.1 PAGE NAVIGATION

You can access Control within the InEight Cloud Suite using the link provided by your manager or facilitator. To access Control, you must open a project by selecting Main menu > **All projects & organizations**.

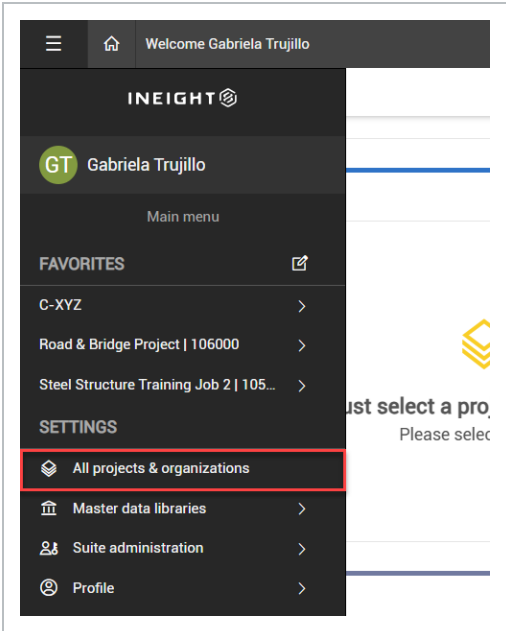

The All projects & organizations page opens to the Projects tab that shows all projects you are associated with.

All projects & organizations

PROJECTS

ORGANIZATIONS

ID	Name	Stat...	Organization	Created by	Created on	Forecast duration	Original contract ...	Contract nu
☐ 105091	Steel Structure Training Job	Active	C-XYZ	Jeremy cheek	08/31/2018 1:40:49 PM			
☐ 105092	Steel Structure Training Job 2	Active	C-XYZ	Jeremy cheek	08/31/2018 1:44:12 PM			
☐ 105093	Steel Structure Training Job 3	Active	C-XYZ	Jeremy cheek	08/31/2018 1:44:46 PM			
☐ 105094	Steel Structure Partner Job	Active	C-XYZ	Jeremy cheek	08/31/2018 1:45:25 PM			
☐ 183850	Wards Island WWTP	Active	C-XYZ	Jeremy cheek	11/07/2018 8:02:08 AM			
☐ BMS Test	BMS Test	New	C-XYZ	Brenda Steven	10/20/2020 1:55:15 PM			
☐ Heavy PM Estimate	Heavy PM Estimate	Active	C-XYZ	Jeremy cheek	01/08/2019 1:33:34 PM			
☐ Training Job	Training Job	Active	C-XYZ	Sterling yazzie	09/11/2018 10:28:37 ...			

You can search projects by clicking the Search icon at the top right of the page. This search function searches all columns in the page.

All projects & organizations

PROJECTS

ORGANIZATIONS

ID	Name	Stat...	Organization	Created by	Created on	Forecast duration	Original contract ...	Contract nu
☐ 105091	Steel Structure Training Job	Active	C-XYZ	Jeremy cheek	08/31/2018 1:40:49 PM			
☐ 105092	Steel Structure Training Job 2	Active	C-XYZ	Jeremy cheek	08/31/2018 1:44:12 PM			
☐ 105093	Steel Structure Training Job 3	Active	C-XYZ	Jeremy cheek	08/31/2018 1:44:46 PM			
☐ 105094	Steel Structure Partner Job	Active	C-XYZ	Jeremy cheek	08/31/2018 1:45:25 PM			
☐ 183850	Wards Island WWTP	Active	C-XYZ	Jeremy cheek	11/07/2018 8:02:08 AM			
☐ BMS Test	BMS Test	New	C-XYZ	Brenda Steven	10/20/2020 1:55:15 PM			
☐ Heavy PM Estimate	Heavy PM Estimate	Active	C-XYZ	Jeremy cheek	01/08/2019 1:33:34 PM			
☐ Training Job	Training Job	Active	C-XYZ	Sterling yazzie	09/11/2018 10:28:37 ...			

Search...

Click a project name to open it. The project opens to the **Project home** landing page. In the Project home landing page, you can access Control from the left menu.

Steel Structure Training Job 2 | 105092 / Project home

Add project image

Minimum of 540px x 360px

Steel Structure Training Job 2 | 105092

Model

Document

Schedule

Control

Workspaces

Project library

Plan

Quantity tracking

Links

Organization

Learn.InEight

InEight University



Project

InEight Inc. | Release 26.7

Page 31 of 639

2.1.1 Navigate the InEight Control Workspaces Page

In the Project home landing page, under Control, click Workspaces to open the **Workspaces** module.

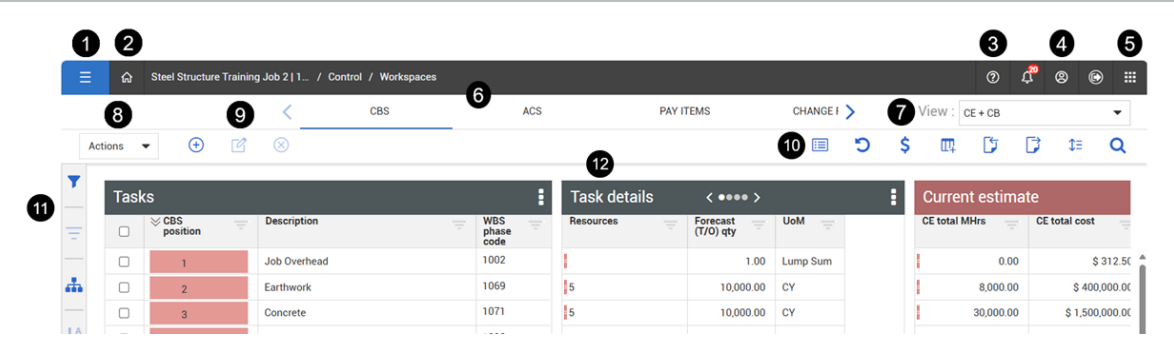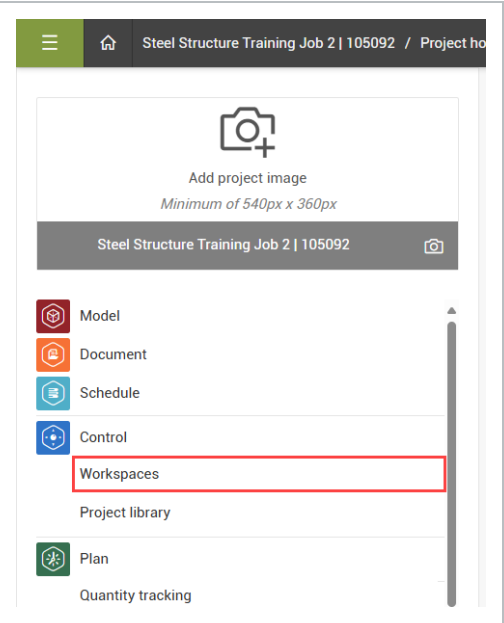

Overview - Control Workspaces Page


Title		Description
1	Left Navigation Menu	Opens a side panel where you can quickly access pages across the InEight Suite, such as settings, favorite projects, and other InEight applications.
2	Home Menu	Returns to the Organization or Project home landing page.
3	Help Menu	Opens a window where you can quickly access eLearning courses,

Overview - Control Workspaces Page (continued)

Title		Description
		Knowledge Library topics, and training videos.
4	User Profile	Access your User Profile and update preferences such as language and number formats.
5	Right Navigation Menu	Opens a side panel where you can quickly access project-specific pages and applications.
6	Tabs	Navigate to the CBS (Cost Breakdown Structure), ACS (Account Code Structure), Pay items, Change Register and Audit Log pages.
7	Viewset Menu	Display different preset views and manage custom viewsets.
8	Actions Menu	Select available actions for the current register tab you are viewing.
9	Left Toolbar	Contains commonly-used buttons to make changes in the register. In this case, Add is used to add cost items, Edit to edit cost items, and Delete to remove a cost item from the project.
10	Right Toolbar	Contains functions for the register page you are currently viewing. (Additional information shown below).
11	Side Toolbar	Contains options for filtering the register and indicators for filtering and sorting.
12	Register content	Displays page content in rows and columns, grouped together in customizable data blocks.

2.1.2 Right Toolbar Overview

The right toolbar allows you to use functions for the register page. The toolbar options change depending on which tab you select (CBS, ACS, Pay Items, Change Register, or Audit Log). The right toolbar is commonly used for the CBS register page. The following image and table show the right toolbar functions:

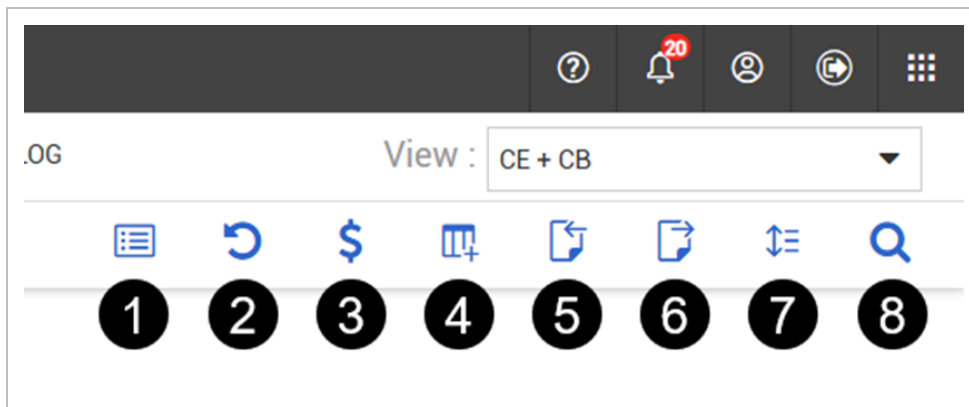

Overview - Workspaces Page CBS Tab - Right Toolbar

Icon		Function
1	Group Columns	Group rows of the cost breakdown structure by like information from selected columns.
2	Undo	Access a list of entries from the current day and select specific entries to undo.
3	Display Currency	Display currency in the CBS as entered or as the project default currency.
4	Add Data Block	Open a panel where you can manage data blocks and add data blocks to your view.
5	Import	Import cost item data from an Excel File.
6	Export	Export your register view to an Excel file. Only the data blocks currently displayed on the page will be exported to the file.
7	Row Density	Adjust the line height at which the register content is displayed. Choose between Relaxed, Narrow, or Tight.
8	Find	Find value in register content by selecting a data block column, selecting either the Begins with or Contains criteria, then entering the value to search for.

2.2 WORKSPACES

The Workspaces page is the main space where you do most of your project management tasks such as tracking progress, managing budget changes, and forecasting. The Workspaces page lets you access different areas of project tracking in the CBS, ACS, Pay Items, Change Register, and the Audit Log register tabs.

2.3 CBS REGISTER

When you open Workspaces, you land on the Cost Breakdown Structure (CBS) tab by default. The CBS is the main tab where you manage and track progress of your cost items that make up the cost breakdown structure of your project. You can manage items such as:

- **CBS structure** — Use the CBS position column to view the hierarchy of your superior and subordinate cost items. You can move cost items to adjust their position within the cost breakdown structure.
- **Color code hierarchy** — You have the option to differentiate your CBS structure by color. Click on the Tasks data block ellipsis to select Color-coded CBS position and Color-coded terminal items to help you identify the position level of the hierarchy where a specific cost item is located.
- **Add, edit, and delete cost items** — Easily add, edit, or delete superior and subordinate cost items.

CBS

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

View

Cost categories

Actions

For more information, see [Cost Item Overview](#).

2.4 ACS REGISTER

The Account Code Structure (ACS) is where you can view and manage account codes at the project level. You can view the account codes assigned to your cost items. The related parent account codes, account code details, and quantity contributors are also shown.

You can view other budget information that is automatically pulled into the ACS Details data block by clicking the right arrow on the ACS details data block to view the additional panels. You can select from multiple columns to view budget information such as:

- Total Cost
- Unit Cost
- Unit Rates
- Primary and Secondary Quantity Ratios
- Quantities Complete
- Account Code Tags

CBS

ACS

PAY ITEMSCHANGE REGISTERAUDIT LOGView : Unsaved (Quantity Managem...

Actions

ACS

Account code

Descr...

99

Change Order...

99.09

Back charges

99.09.02

Back charges ...

99.09.02.002

Back charges ...

99.09.04

Back charges ...

99.09.04.002

Back charges ...

99.09.06

Back charges ...

99.09.06.002

Back charges ...

ACS details

Primary Qty

Primary UoM

Auto-quantity (Primary)

Notes

Forecast total cost

Forecast total Mhrs

1.000000000000

PLS

☐

\$187,829,311.97999998927

3,535,755.04678499978

0.000000000000

PLS

☐

\$187,829,311.97999998927

3,535,755.04678499978

1.000000000000

PLS

☐

\$209,963,377.59999999404

3,535,755.04678499978

1.000000000000

PLS

☐

\$209,963,377.59999999404

3,535,755.04678499978

0.000000000000

PLS

☐

(\$22,134,065.62000000104)

0.000000000000

1.000000000000

PLS

☐

\$200.000000000000

0.000000000000

0.000000000000

PLS

☐

\$0.000000000000

0.000000000000

1.000000000000

PLS

☐

\$0.000000000000

0.000000000000

ACS qty contributors

Contribute Primary to Primary

Contribute Primary to Secondary

☐

☐

☐

☐

☐

☐

☐

☐

☐

☐

☐


☐

☐

☐

2.4.1 ACS Navigation

The ACS tree lets you easily navigate up and down your ACS structure and provides a way to filter down to a subset in the structure. Open the ACS tree slide-out panel by clicking on the ACS tree icon on the side toolbar.

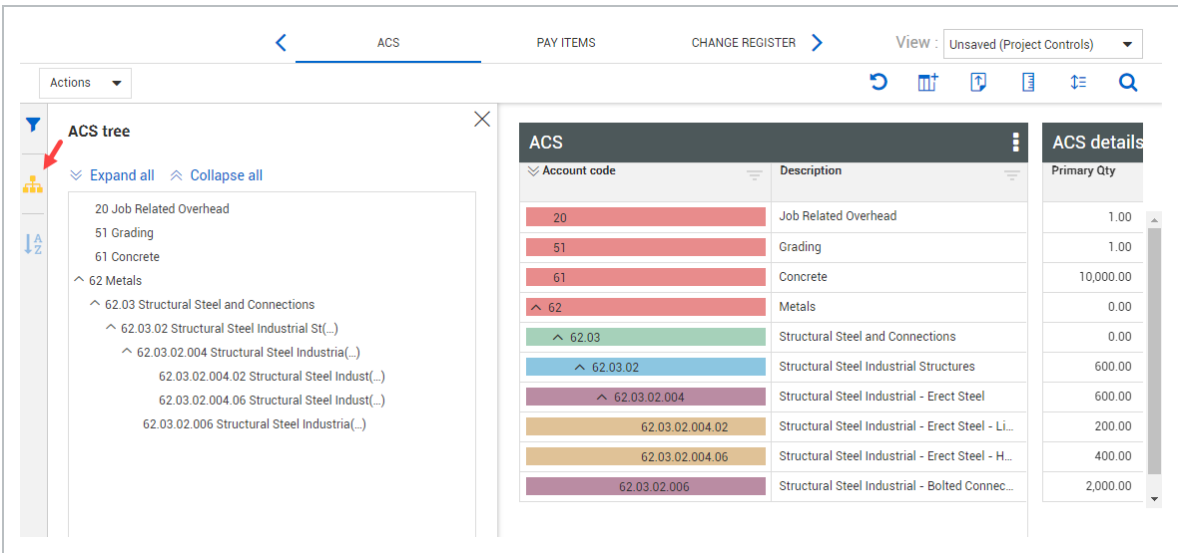


Like the CBS color-coded hierarchy, you have the option to differentiate your account codes by color. Click on the ACS data block ellipsis to select this option to help you identify at which level of the hierarchy a specific account code is located.

2.5 PAY ITEMS REGISTER

You can manage pay items in the Pay Items tab in Control. Pay items typically represent the owner-required deliverables a contractor must submit pricing for. In Control, pay items are used to distribute the cost calculated in the Cost Breakdown Structure and all markup, fees or contingencies calculated in the pay items. This allows the total estimate value to be distributed to a structure different from the CBS.

You can group pay items in a hierarchy by utilizing the Position Code column.

In the Pay Items tab, you can manage your project's pay items and their structure. The image and table below show the Pay Items tab functions:

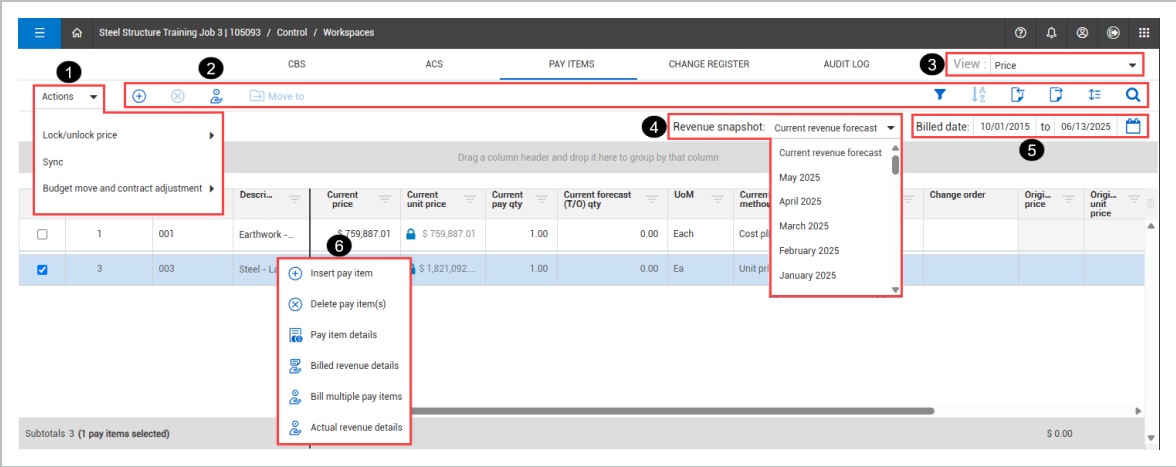

	Item	Description
1	Actions	In the Actions drop-down menu, you can: • Lock/unlock price - You can select to lock and unlock price and lock project budget and price. • Sync - You can select to sync pay items, billed revenue, and forecast revenue with other applications. • Budget move and contract adjustment - You can select to do a budget move, budget quantity and man hour adjustment, and contract adjustment.
2	Toolbar actions	Upper left toolbar actions: • Add and delete pay items • Claim revenue • Move to - Move pay items within the structure using another pay item position, number, or description. Upper right toolbar actions: • Filter - Create a query filter in the query builder. • Sorting - Sort in ascending or descending order. • Import and Export - Import and export sets of data. • Row density - Select from relaxed, narrow, or tight row density on the register. • Find - Search scope items.
3	View	You can select from the default Revenue and Price views. You can create new views, save updated views, and rename and delete custom views.
4	Revenue	You can view snapshot data for past periods. When the <i>Enable manual</i>

	Item	Description
	snapshot	<i>snapshots</i> option is turned on in the project's Project Tracking settings, you can also create a manual snapshot using the <i>Take revenue snapshot</i> option from the drop-down list and the <i>Take snapshots</i> options in the Actions drop-down menu.
5	Billed date filter	Filter the revenue data based on a selected time frame of billed dates to apply to columns based on the billed date. To reset the filter, click the Calendar icon, and then select To date . When you use the Billed date filter, the To date option includes all bills and all cost item actuals. Selecting a date range filters to bills and actuals only within that date range.
6	Right-click menu options	Right-click a pay item to do the following: • Insert pay item • Delete pay item(s) • View pay item details • View billed revenue details • Bill multiple pay items • View actual revenue details

2.5.1 Pay Items register columns

There are multiple columns available in the Pay Items register where you can easily view and manage cost item data. You can use the pre-defined Revenue and Price views to load revenue or price-relevant columns. You can also use the Column Chooser feature to manage columns and then save your custom defined view.

Key columns shown in the register relate to your budget and revenue.

2.5.1.1 Revenue forecasting columns

Data in these columns help you understand the projected revenue and health of your project. For more information, see [Revenue forecasting columns](#).

2.5.1.2 Change management columns

When integrated with InEight Change, you can view project changes such as budget moves that involve items like quantity, man-hour, and contract adjustments. Data in these columns let you view the

number of change orders and amounts, providing greater visibility to track the progress of the project and better manage costs.

CBS

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

View : Unsaved (Revenue)

Actions

+

✕

👤

📁 Move to

\$

🔍

📄

📄

⌕

🔍

Revenue snapshot:

Current revenue forecast

Billed date:

05/14/2025

to

11/24/2025

📅

Drag a column header and drop it here to group by that column

☐	✓ Pay item position	Pay item number	Description	Current price	Revenue forecast method	Current billing method	Is billed	Change order	Billed revenue	Billed change order amount	Total change order amount	Billed qty	
☐	1	Fixed final pri...		\$ 75,060.00	Default	Fixed final price	☐	⋮ (2)	\$ 0.00	\$ 0.00	\$ 60.00	0.00	
☐	1	1	1st Mobilization Paym...	\$ 10,200,000.00	Default	Unit price	☐		\$ 0.00	\$ 0.00	\$ 0.00	0.00	
☐	1	1	1st Mobilization Paym...	\$ 10,200,000.00	Default	Unit price	☐		\$ 0.00	\$ 0.00	\$ 0.00	0.00	
☐	2	Unit price - F...	Unclassified Excavation	\$ 500,060.00	Default	Unit price	☐	⋮ (1)	\$ 0.00	\$ 0.00	\$ 60.00	0.00	
☐	2	2	2nd Mobilization Paym...	\$ 11,700,000.00	Default	Unit price	☐		\$ 0.00	\$ 0.00	\$ 0.00	0.00	
☐	2	2	2nd Mobilization Paym...	\$ 11,700,000.00	Default	Unit price	☐		\$ 0.00	\$ 0.00	\$ 0.00	0.00	
☐	3	3	Punchlist Completion	\$ 2,000,000.00	Default	Unit price	☐		\$ 0.00	\$ 0.00	\$ 0.00	0.00	
☐	^ 3	3	Punchlist Completion	\$ 150,060.00	Rollup		☐		\$ 8,100.00	\$ 0.00	\$ 60.00		:
☐	3.1	Fixed final pri...		\$ 150,060.00	Default	Fixed final price	☒	⋮ (1)	\$ 8,100.00	\$ 0.00	\$ 60.00	20.00	:
☐	^ 4	4	Final Acceptance Miles...	\$ 3,250.00	Rollup		☐		\$ 750.00	\$ 0.00	\$ 16,000.00		
Subtotals 1068 (1 pay items selected)				\$ 1,030,927,345.96					\$ 8,850.00	\$ 0.00	\$ 44,760.00	\$	

The following are key Change columns in the Pay Items register:

- **Change orders** — View the change order number, which helps you in associating the change order or contract adjustment.
- **Billed change order amount** — Amount billed to a customer from an actual change order.
- **Total change order amount** — Shows how much of a pay item's price is from change orders.

2.5.2 Move Pay Items

You can reorder pay items on the Pay Items tab. Use the **Move to** button to rearrange pay items into superior, equal, or subordinate positions.

Move pay items

1. Select the pay item(s) to be moved, and then click **Move to**.

CBSACS

Actions

Move to

Drag a column header

☐	Pay item position	Pay item number	Description	Curr... price	Curr... unit price	C p q
☐	23	23	Install Double Yellow Line	\$ 1,584.00	\$ 3.00	
☐	24	24	Grind and Install Double Yell...	\$ 282.50	\$ 0.50	
☒	25	25	Install Yellow Dashed and S...	\$ 162.00	\$ 0.30	
☐	26	26	Grind and Install 12-inch So...	\$ 665.00	\$ 19.00	
☐	27	27	Grind and Install Directional...	\$ 5,800.00	\$ 725.00	
☒	28	28	Install 4-inch Solid White Li...	\$ 274.50	\$ 0.30	
☐	29	29	Grid and Install 4-inch Solid...	\$ 518.75	\$ 1.25	
☒	30	30	Install 8-inch Solid White Li...	\$ 60.00	\$ 0.60	
☐	31	31	Grind and Install 8-inch Soli...	\$ 1,185.00	\$ 3.00	

2. Enter the pay item position, pay item number, or the description. Select the correct pay item from the drop-down options. This is the position that the selected pay item will be moved to.

Actions

23

23 - 23 - Install Double Yellow Line

3. Click the **Move to** icon.

23 - 23 - Install Double Yellow Line

Move to

4. To move the selected pay item(s) to an equal position, select **Sibling**. To move the pay item(s) into a subordinate position, select **Child**.

Move to 23 as:

Child

Sibling

To move a pay item into a child position, the parent pay item must have a value of 0 for billed revenue, billed quantity, and current price, and no cost items can be assigned to it.

5. The selected pay item(s) will now show in the new position.

CBS

ACS

Actions

+

×

Move to

Drag a column

☐	Pay item position	Pay item number	Description	Curr... price	Curr... unit price
☐	23	23	Install Double Yellow Line	\$ 1,584.00	\$ 3.00
☒	24	25	Install Yellow Dashed and S...	\$ 162.00	\$ 0.30
☒	25	28	Install 4-inch Solid White Li...	\$ 274.50	\$ 0.30
☒	26	30	Install 8-inch Solid White Li...	\$ 60.00	\$ 0.60
☐	27	24	Grind and Install Double Yell...	\$ 282.50	\$ 0.50

2.6 CHANGE REGISTER

In the Change Register tab, you can review the details of contract adjustments and budget moves, and either revise, reject, or approve the changes (with the applicable permissions).

CBS			ACS			PAY ITEMS			CHANGE REGISTER		AUDIT LOG													
Actions																								
ID	Description	CCO	Creation date	Issue #	Last changed by	Last changed on	Notes	Status	Total budget cost	Total budget M1	Total contract price	Type	Approval probability											
43.1			03/31/2023		Nathaniel Tures	03/04/2025		Approved	\$ 66,741,2000...	0.00000000	\$ 0.00000000	Contract adjust...	100.00000000%											
43.0			03/31/2023		Nathaniel Tures	03/04/2025		Revised	\$ 1,618,831.06...	0.00000000	\$ 0.00000000	Contract adjust...	0.00000000%											
42.0			03/31/2023		Nathaniel Tures	03/04/2025		Approved	\$ 136,648,920...	0.00000000	\$ 0.00000000	Contract adjust...	100.00000000%											
41.0	EW to ESDC		03/28/2023		Nathaniel Tures	03/04/2025		Approved	(\$ 0.00000100)	155.49125146	\$ 0.00000000	Budget move												
40.0	T&M Offset March 23		03/21/2023		Nathaniel Tures	03/04/2025		Approved	(\$ 2,813,426.8...	0.00000000	\$ 0.00000000	Contract adjust...	100.00000000%											
39.0			03/15/2023		Nathaniel Tures	03/04/2025		Approved	\$ 0.00000000	65.00000000	\$ 0.00000000	Budget move												
38.0	Sheladia Budget Mo...		03/15/2023		Nathaniel Tures	03/04/2025		Approved	(\$ 3,764,5000...	73.90993849	\$ 0.00000000	Contract adjust...	100.00000000%											
37.0	CSIE to Contingency		03/15/2023		Nathaniel Tures	03/04/2025		Approved	(\$ 24,944,710...	-1,912.000000...	\$ 0.00000000	Contract adjust...	100.00000000%											
36.1			03/21/2023		Nathaniel Tures	03/04/2025		Rejected	\$ 42,731.3600...	0.00000000	\$ 0.00000000	Contract adjust...	0.00000000%											
36.0			03/03/2023		Nathaniel Tures	03/04/2025		Revised	\$ 42,731.3600...	0.00000000	\$ 0.00000000	Contract adjust...	0.00000000%											
35.0			03/03/2023		Nathaniel Tures	03/04/2025		Approved	\$ 343,000.000...	0.00000000	\$ 0.00000000	Contract adjust...	100.00000000%											
34.0			03/03/2023		Nathaniel Tures	03/04/2025		Approved	\$ 1,385,635.99...	9,861.87317457	\$ 0.00000000	Contract adjust...	100.00000000%											
33.1			03/21/2023		Nathaniel Tures	03/04/2025		Rejected	(\$ 367,35658...	0.00000000	\$ 0.00000000	Contract adjust...	0.00000000%											
33.0			02/05/2023		Nathaniel Tures	03/04/2025		Revised	(\$ 367,35658...	0.00000000	\$ 0.00000000	Contract adjust...	0.00000000%											
32.1			03/21/2023		Nathaniel Tures	03/04/2025		Rejected	(\$ 48,113.550...	0.00000000	\$ 0.00000000	Contract adjust...	0.00000000%											
32.0			02/05/2023		Nathaniel Tures	03/04/2025		Revised	(\$ 48,113.550...	0.00000000	\$ 0.00000000	Contract adjust...	0.00000000%											
31.1			03/21/2023		Nathaniel Tures	03/04/2025		Rejected	\$ 100,854.887	0.00000000	\$ 0.00000000	Contract adjust...	0.00000000%											
Subtotals									\$ 2,065,968.9...	-6,434.94563...	\$ 0.00000000													

For more information, see [Change Approval Process](#) in Change Management.

2.7 AUDIT LOG REGISTER

The Audit Log register tab captures changes that were made within InEight Control and is broken down into five sub-tabs located on a left sidebar menu.

- CBS
- ACS
- Pay items
- Integration

- Import history

AUDIT LOG										
CBS ACS PAY ITEMS CHANGE REGISTER AUDIT LOG										
Actions	Audit ID	Data type	Item type	Description	WBS	Attribute	Changed by	Changed date	Value before	Value after
CBS ACS Pay items Integration Import history	121534606	Actuals	Cost Item	KIE Engineering Sc...	4447	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	10,634.00000000	10,648.00000000
	121534605	Actuals	Cost Item	Intercompany Auto...	2082	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	10,634.00000000	10,648.00000000
	121534604	Actuals	Cost Item	G&A	2083	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	10,634.00000000	10,648.00000000
	121534603	Actuals	Cost Item	Miscellaneous Rev...	2086	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	10,986.00000000	11,000.00000000
	121534602	Actuals	Cost Item	JOR Line Item	2000	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	11,626.00000000	11,640.00000000
	121534601	Actuals	Cost Item	Miscellaneous Rev...	2088	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	11,626.00000000	11,640.00000000
	121534600	Actuals	Cost Item	iDesign Review	1144	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	11,659.00000000	11,673.00000000
	121534599	Actuals	Cost Item	AB - New Carrollto...	1151	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	12,583.00000000	12,597.00000000
	121534598	Actuals	Cost Item	KIE FHV Protection ...	1174	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	12,538.00000000	12,552.00000000
	121534597	Actuals	Cost Item	Sheladia ESDC DSUB	1612	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	12,118.00000000	12,132.00000000
	121534596	Actuals	Cost Item	Sheladia ESDC FES	1616	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	12,118.00000000	12,132.00000000
	121534595	Actuals	Cost Item	JAC Fire Protection...	1028	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	12,652.00000000	12,666.00000000
	121534594	Actuals	Cost Item	Kim ASD - Cheverly	1080	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	12,735.00000000	12,749.00000000
	121534593	Actuals	Cost Item	NOT IN USE	1907	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	12,959.00000000	12,973.00000000
	121534592	Actuals	Cost Item	NOT IN USE	1908	Claimed Equipment...	InEight Service Acc...	06/22/2025 11:05...	13,599.00000000	13,613.00000000


For more information, see [Audit Log](#) in General Navigation.

2.8 COLUMNS/GROUPING/SORTING

You can customize the columns on your pages according to your preferences. Changes made to columns and filtering will be retained across projects each time you access Control.

2.8.1 Resize column width

You can resize the width of a column to let you view the data more clearly. To resize a column, select the column border on the right, and then drag it to a new position.

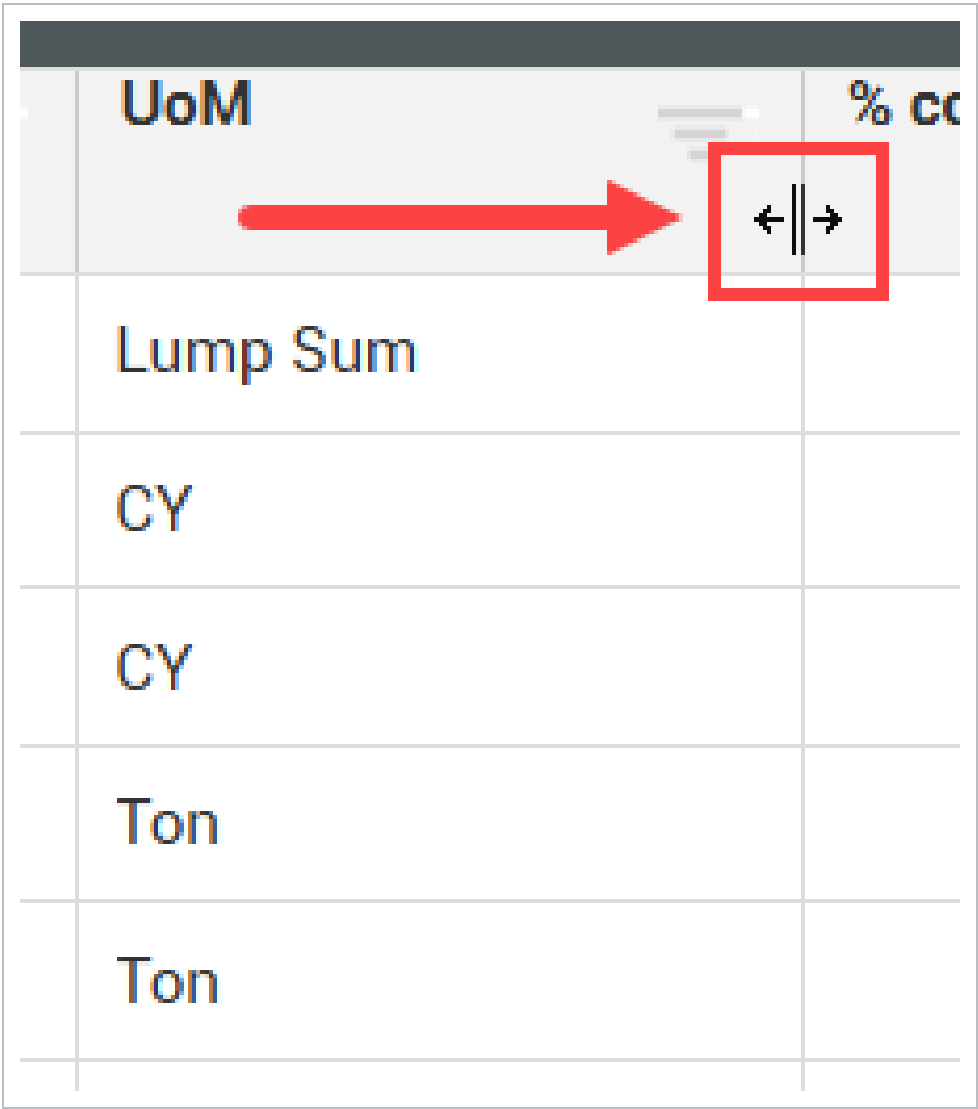

The image shows a table with a header row and several data rows. The header row has a grey background and contains the text 'UoM' and '% CC'. The first data row contains 'Lump Sum'. The second and third data rows contain 'CY'. The fourth and fifth data rows contain 'Ton'. A red arrow points from the left towards the border between the first and second columns. A red square highlights a double-click icon (two vertical lines with arrows pointing outwards) on this border.

UoM	% CC
Lump Sum	
CY	
CY	
Ton	
Ton	


To auto-fit the column to its contents, double-click the column border.

	UoM	%
00	Lump Sum	
00	CY	
00	CY	
00	Ton	

2.8.2 Move Columns

You can move a column from one place to another to customize your view using drag and drop.

To move a column, select the column header, and then drag and drop the column into a new position.

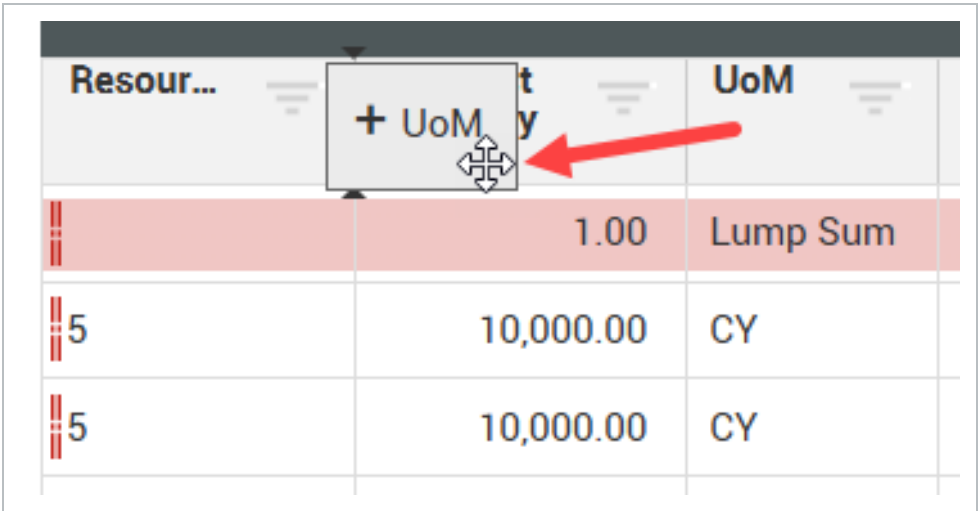

Resour...	+ UoM y	UoM
	1.00	Lump Sum
5	10,000.00	CY
5	10,000.00	CY

Notice that two black arrows indicate the new position of the column.

irr... it ice	Curr... pay qy	+ UoM	Curr... ore... T/O)	UoM	
\$ 759,8...		1.00	0.00	Each	
2,919,02...		1.00	0.00	Each	
1,821,09...		1.00	0.00	Each	

2.8.3 Sort Columns

You can sort columns by clicking the column header. Click once to sort the column in ascending order.

Description	
000 - Specifications	
31510-151-DRG-CC-013	
Bolted Connections	
Concrete	
Concrete - Materials	
Earthwork	
Earthwork - Materials	
Erect Steel - Heavy	
Erect Steel - Light	
Job Overhead	

Click the column header a second time to sort the column in descending order.

Description
Structure Steel - Materials
Structural Steel
Materials
Job Overhead
Erect Steel - Light
Erect Steel - Heavy
Earthwork - Materials
Earthwork
Concrete - Materials
Concrete


To clear the sorting, click the column header a third time.

2.8.4 Filter Columns

You can filter your column data to only show specific information you want to view. There are two ways to set a filter:

2.8.4.1 Method 1: Filter from Column Header

You can set a filter for a column by clicking the **Filter** icon on any column header. This opens a drop-down list of items you can filter by to apply to that specific column.

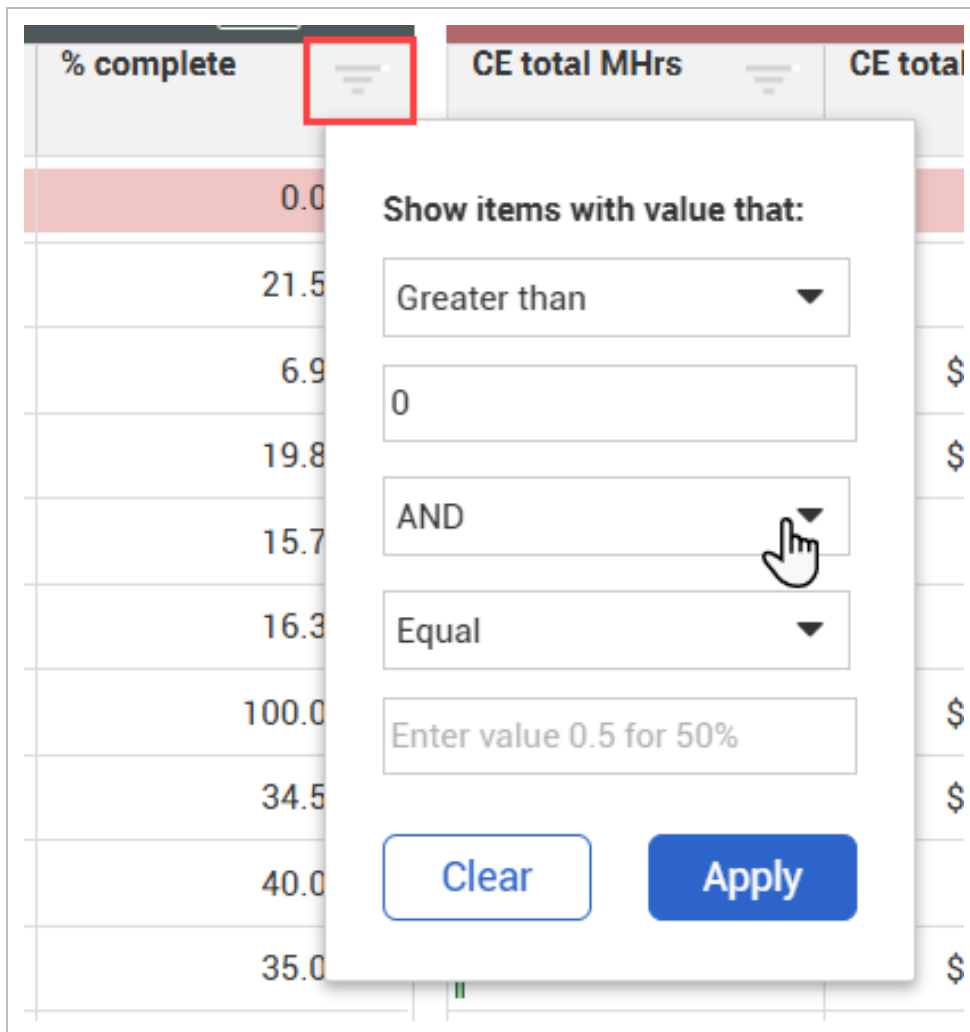


If you want to remove a single filter, locate the column you filtered, click the **Filter** icon, and then click the **Clear** button.

Selecting the Filter icon will remove all the filters applied to the columns.

2.8.4.2 Method 2: Filter by Query

You can also set a filter by clicking the **Filter** icon and selecting **Query**.

On the CBS and ACS tabs, the Filter icon shows on the side toolbar. On the Pay Items tab, Change Register, and Audit Log, the Filter icon shows on the top right toolbar.

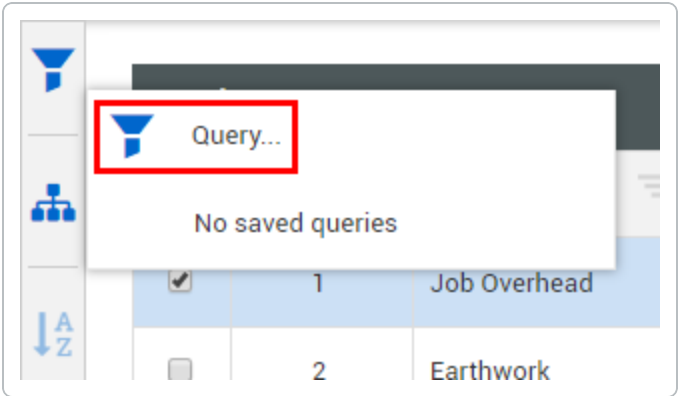


The filter by Query option is helpful when you:

- Need to search for the column you need to filter
- Need to apply filters to more than one column

Selecting Query opens the Query builder slide-out panel, where you can set the filter criteria.

2.8.4.3 Query Builder

You can build a query using multiple criteria. Each criterion includes a column, an operator, and a value. Use the AND/OR options to combine criteria and define how they relate to each other. The following image and table show the Query builder functions:

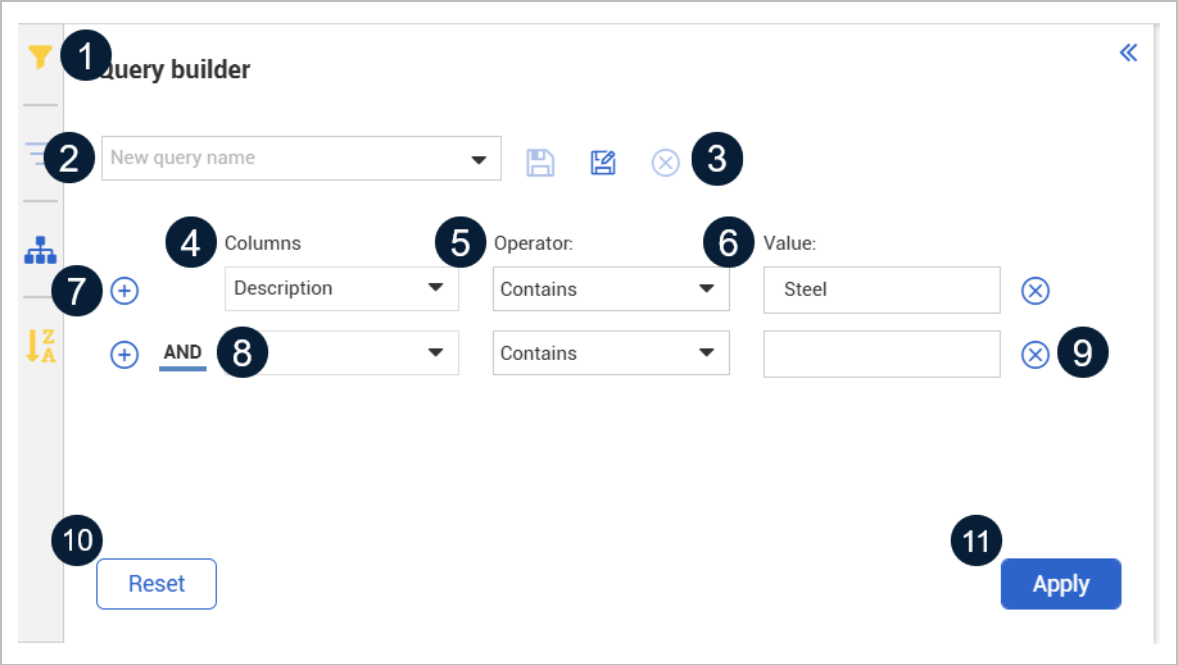


	Title	Description
1	Filter icon	Opens the Query builder slide-out panel.
2	Query name	Click the Save as icon to the right to input a name for the query. Open the query name drop-down menu to select a saved query.
3	Save Query icons	Click the Save as icon to enter a name for a new query, and then click the Save icon to save the query. Click the Delete icon to delete the saved query.
4	Columns	Open the Columns drop-down menu to select the column that the filter criterion will apply to.
5	Operator	Open the Operator drop-down menu to select the condition to be applied to the selected column.
6	Value	Enter the value you want to search for.
7	Add icon	Click the Add icon to add another criterion to the query.
8	AND/OR options	Click AND/OR to define how the query criteria relate to one another. When you click here, the options toggle between “And” and “Or”.
9	Delete icon	Click the Delete icon to remove the criterion from the query.

	Title	Description
10	Reset	Click the Reset button to remove the filter criteria from the CBS and close the Query builder.
11	Apply	Click the Apply button to apply the filter criteria to the CBS.

2.8.5 Filter Indicator

On the CBS tab, in addition to the two filtering methods, there is also a Filter indicator on the side toolbar. When a filter is applied, the Filter indicator turns yellow. Hover over the icon to view details of the applied filters.

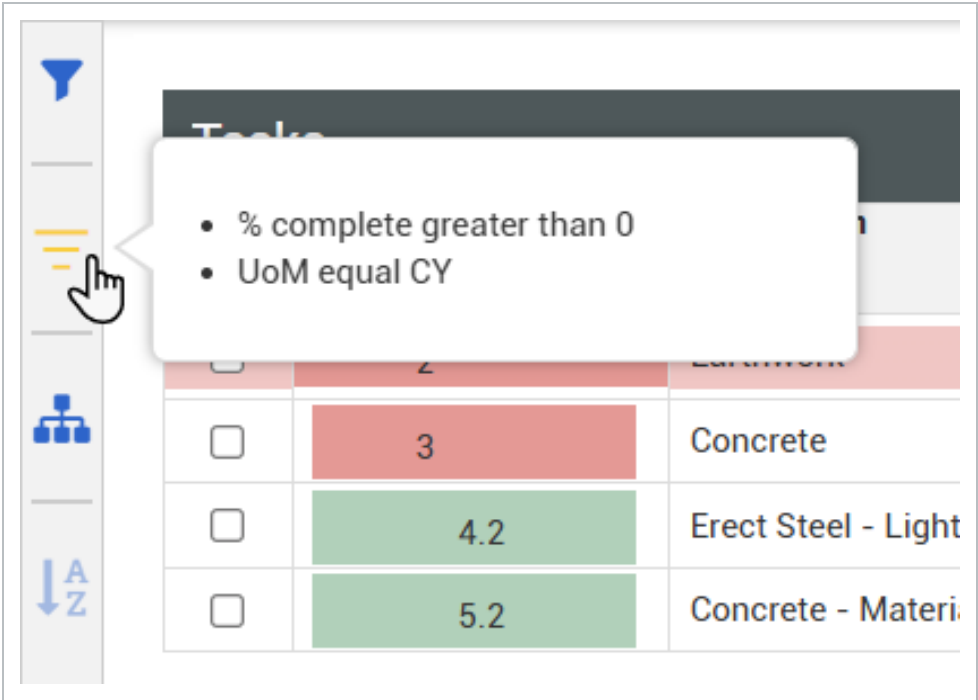

Clicking the filter icon will remove all of the applied filters.


2.8.6 Grouping

Several tabs in Workspaces let you organize your data into groups based on column. This is useful when you want to view related records together, or if you want to see subtotal values by group.

Note that only columns with a discrete or predefined set of values such as categories, statuses, or units of measure can be used for grouping.


Group Data by Column Values

1. From the right toolbar, click the **Group columns** icon. This opens the grouping area at the top of the page.

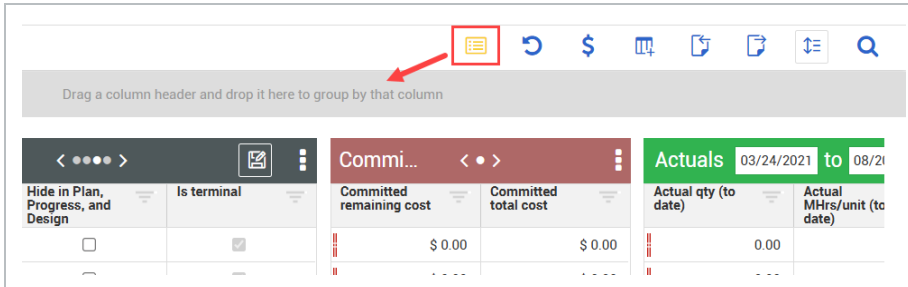

On the Pay Items tab, the grouping area is always open.

2. Select a column header, and then drag and drop it into the grouping area. Your data is now grouped based on the values in that column.

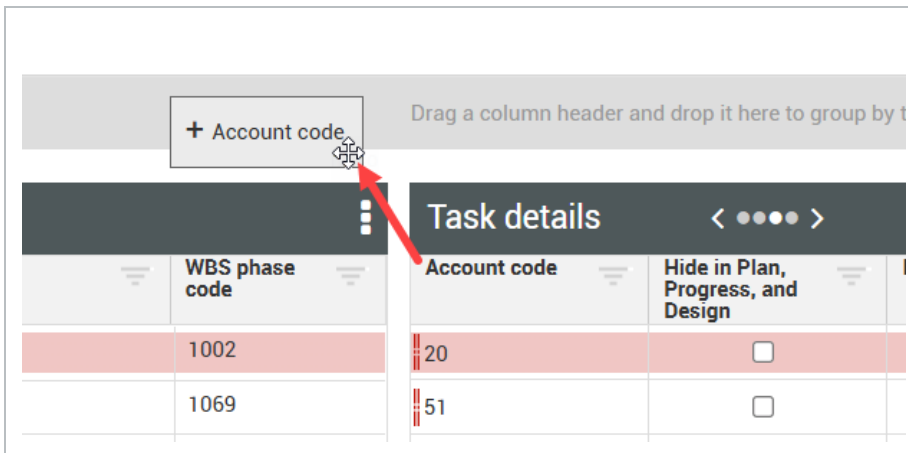

3. To create a subgroup, select another column header, and then drag and drop it into the grouping area.

Actions + ✎ ✕

Account code ✕

UoM ✕

Tasks

	☐	CBS position	Description	WBS phase code
Account code: (Count:13)				
UoM: CY (Count:4)				
	☐	2	Earthwork	1069
	☐	3	Concrete	1071
	☐	5.1	Earthwork - Materials	1085
	☐	5.2	Concrete - Materials	1086
		Count:4		
UoM: Ea (Count:1)				
	☐	4.3	Bolted Connections	1006
		Count:1		

Current estimate

CE total Mhrs	CE total cost
8,000.00	\$ 400,000.00
30,000.00	\$ 1,500,000.00
0.00	\$ 250,000.00
0.00	\$ 1,000,000.00
38,000.00	\$ 3,150,000.00
1,246.00	\$ 62,300.00
1,246.00	\$ 62,300.00

4. To reverse the sorting of the groups, click the column header inside the grouping area.


Account code ✕

UoM ✕

Tasks

	☐	CBS position	Description
	☐	4.3	Bolted Connector
		Count:1	
UoM: Each (Count:1)			

To rearrange the subgrouping, drag and drop a column header inside the grouping area into a new position.

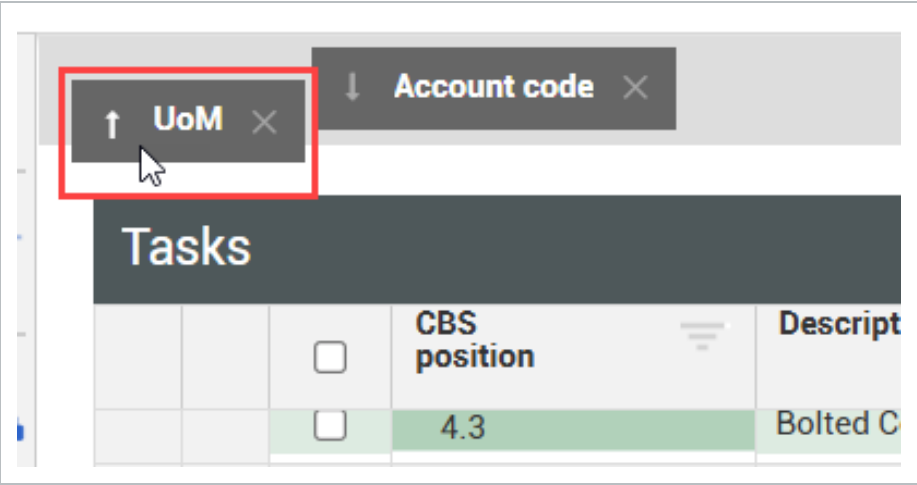

Click the **Close** icon on the column header to remove it from the grouping.

- 5. To remove the grouping on the page, click the Group columns icon again.

2.9 DATA BLOCKS

Each data block is a set of columns grouped together based on categories of information. Using data blocks helps you organize and manage all the columns on a page.

Data blocks are customizable, and you can view them side by side and move them within the register. The information in each data block shows in a grid-like format, maintaining a spreadsheet look and feel.

CBS

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

View : Forecasts

Actions

Tasks

CBS position

Description

WBS phase code

1

Job Overhead

1002

2

Earthwork

1069

3

Concrete

1071

4

Structural Steel

1073

4.1

Erect Steel - Heavy

1074

4.2

Erect Steel - Light

1005

4.3

Bolted Connections

1006

5

Materials

1084

5.1

Earthwork - Materials

1085

5.2

Concrete - Materials

1086

5.3

Structure Steel - Mat...

1087

5.4

Iron Trailer

1088

Subtotals 13

Task details

Resource

Forecast (T/O) quantity

UoM

16

1.00 Lump Sum

5

10,000.00

CY

6

10,000.00

CY

1,000.00

Ton

5

800.00

Ton

5

200.00

Ton

8

2,000.00

Ea

1.00

Each

1

10,000.00

CY

1

10,000.00

CY

1,000.00

Ton

1.00

PLS

Forecast

Created from Live forec...

Forecast final cost

Forecast final M/Hrs

Forecast final man hours/Unit

Forecast final productivity factor

Forecast final unit cost

\$ 695.00

11.00

11.00

0.00

\$ 400,000.00

8,000.00

0.80

1.00

\$ 1,500,000.00

30,000.00

3.00

1.00

\$ 1,000,035.71

20,000.71

20.00

1.05

\$

\$ 800,000.00

16,000.00

20.00

1.00

\$

\$ 200,000.00

4,000.00

20.00

1.00

\$

\$ 35.71

0.71

0.00

1,400.00

\$ 1,750,000.00

0.00

0.00

0.00

\$ 1.75

\$ 250,000.00

0.00

0.00

0.00

\$ 1,000,000.00

0.00

0.00

0.00

\$ 500,000.00

0.00

0.00

0.00

\$ 0.00

0.00

0.00

0.00

\$ 4,650,730.71

58,011.71

Each type of data block has its own unique default settings such as date range selectors and date preset options (for financial periods). You can choose the total number of columns and panels for each data block.

2.9.1 Data Block Categories

There are three categories of data blocks: Standard, Cost Category and Custom.

2.9.1.1 Standard Data Block


Standard data blocks include the following:

- Task Details
- Actuals
- Current Budget & Estimate
- Forecast
- Forecast Delta
- Live Forecast
- Schedule

You can customize the columns grouped within each of these data blocks.

2.9.1.2 Forecast Data Block

When you add a forecast data block to your view, you are prompted to select the specific forecast to show in this data block. You can create a new private or shared forecast or select an existing forecast.

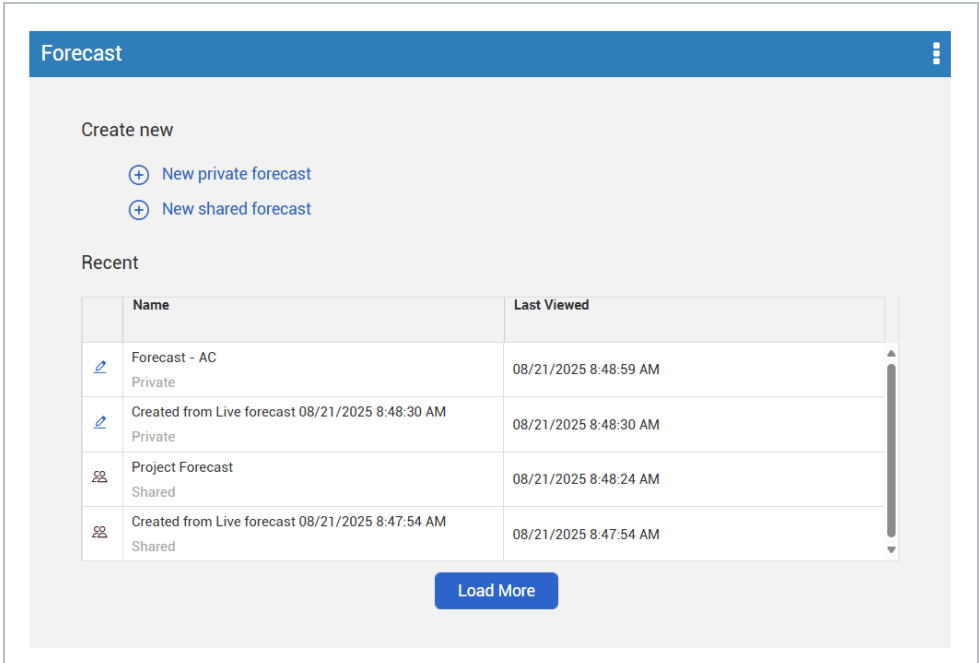

See [Forecast Management](#) for more details on forecast data blocks.

2.9.1.3 Cost Category Data Block


The Cost category data blocks organize key project progress information by cost category, and include the following:

- Cost categories: Actuals
- Cost categories: Current Budget
- Cost categories: Current Estimate
- Cost categories: Forecast

You can change the columns in Cost Category data blocks.

2.9.2 Manage Data Blocks

You can manage your data blocks by opening the Add data block slide-out panel. To open the Add data block slide-out panel, click the **Add data block** icon.




In the Add data block slide-out panel, you can switch between Thumbnail view or List view.


2.9.2.4 Thumbnail View

Thumbnail view is the default view of the Add data block slide-out panel. In this view, data blocks are shown as thumbnails.

To add a data block to your view, drag and drop it onto the page from the slide-out panel.

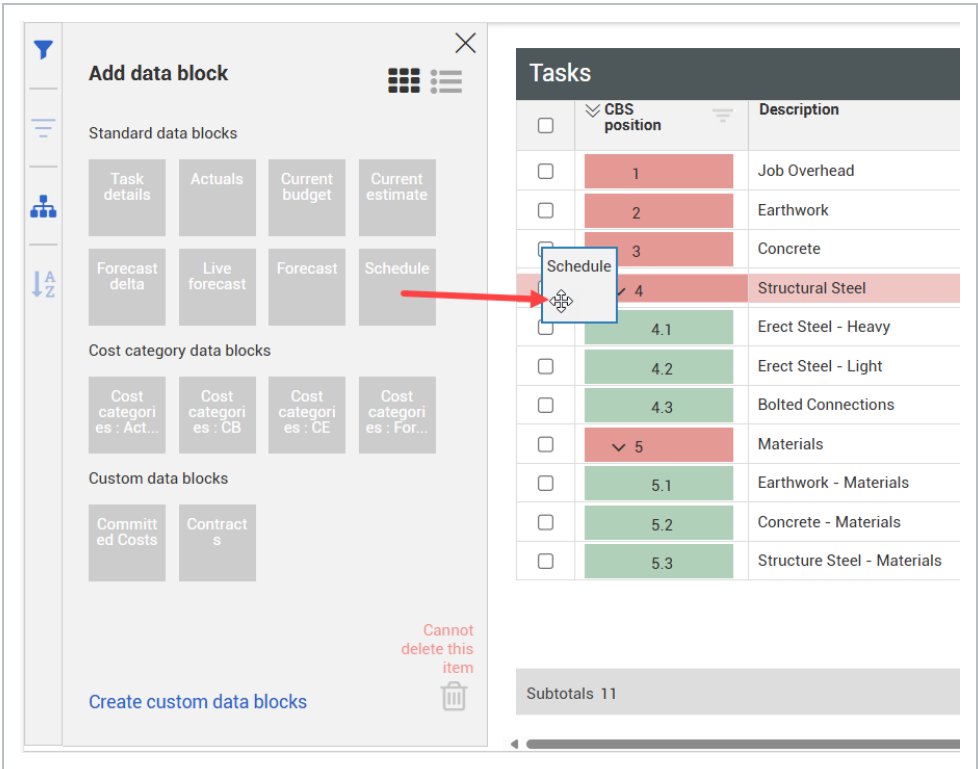


To delete a custom data block, drag and drop it onto the **Delete** icon.

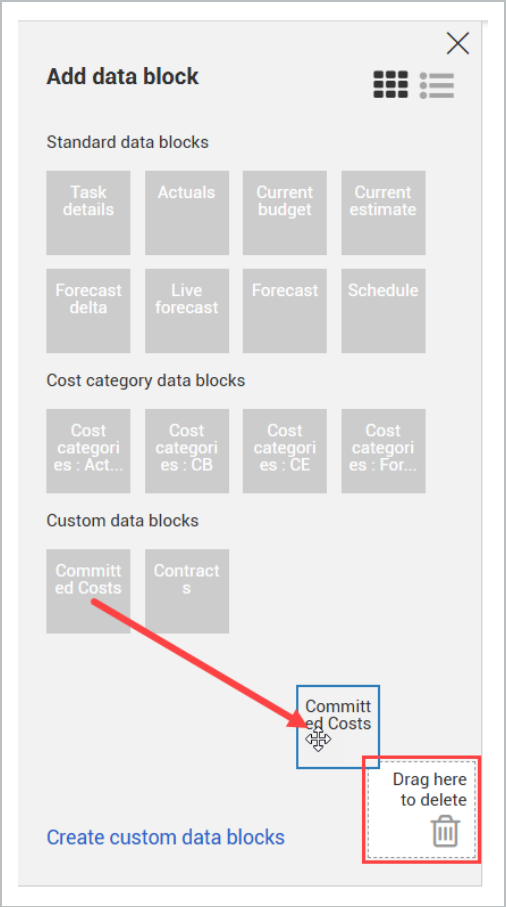


Note: You cannot delete preset data blocks.

2.9.2.5 List View

Click the **List View** icon to switch to List view.

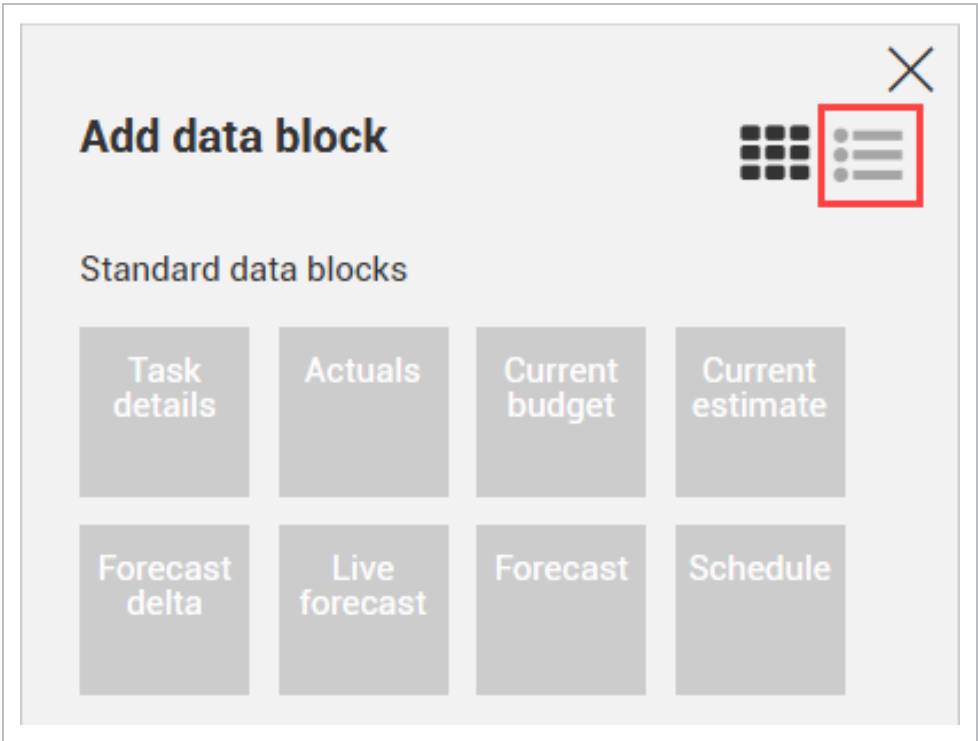


In this view, data blocks are shown in a list. You can search for a specific data block from the search bar. You can also add a data block to your view by double-clicking it from the list.

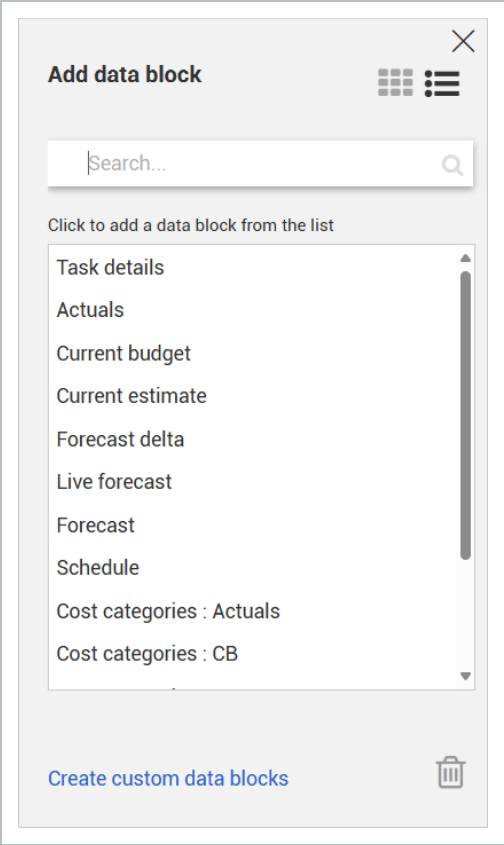

2.9.3 Data Block Context Menu

The data block Context Menu allows you to perform different operations specific to the data block you select.

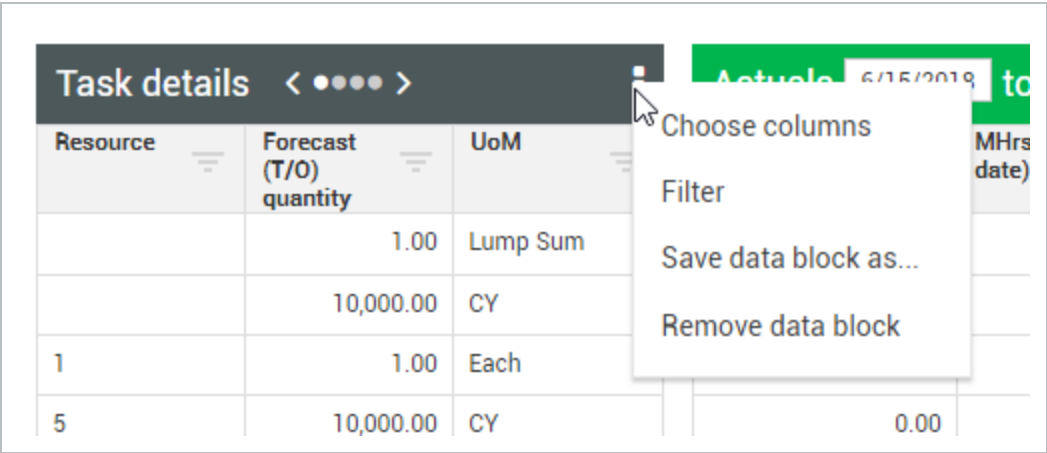


The following table provides an overview of Context Menu options:

Data Block Context Menu	
Title	Description
Choose columns	Open the column chooser menu and move, add, and remove columns from the data block.
Filter	Filter data within a data block.
Save data block as	Create a copy of the existing data block and save it.
Remove data block	Remove the data block from the current view.
Color coded terminal items (Tasks data block only)	Add colors to terminal items of your current data block.
Color-coded CBS position (Tasks data block only)	Adds colors to all CBS lines.
Show/Hide WBS Phase Code (Tasks data block only)	Display or remove the WBS Phase Code column within the Tasks data block.

In the following step by step, you will learn how to modify a custom or an existing data block using the Context Menu.

Edit a Data Block

1. In the CBS register, select the **Context Menu** icon of the custom data block you created.
2. Select **Choose columns** from the context menu.
3. Add a new column to your custom data block.
4. Remove a column from your custom data block by selecting the header and clicking the left-facing arrow to return it to the left column.

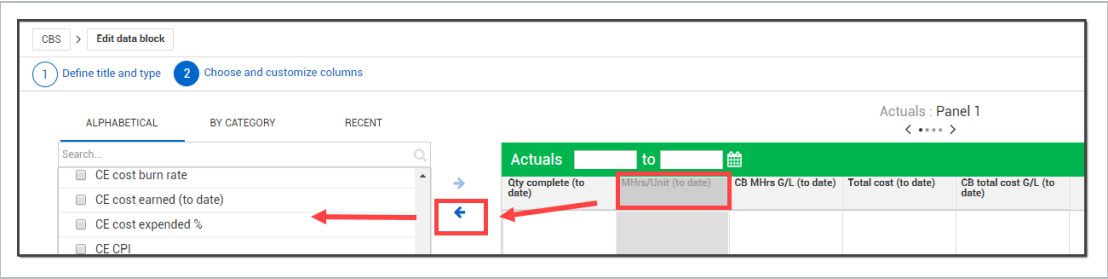


5. To close the slide out panel, click the **APPLY** button on the bottom right of the slide out.

2.9.4 Custom Data Blocks

You can create a custom data block based on your needs. Custom data blocks can be organized by color-coded type, and you can apply the same header functionality used in preset data blocks. Custom data blocks can be added to your view or saved for future use.

Create a Custom Data Block

1. From the right toolbar, click the **Add data block** icon.



2. From the Add data block slide-out panel, click **Create custom data blocks**.

Actions

Add data block

Standard data blocks

Task details

Actuals

Current budget

Current estimate

Forecast delta

Live forecast

Forecast

Schedule

Cost category data blocks

Cost categories : Act...

Cost categories : CB

Cost categories : CE

Cost categories : For...

Custom data blocks

Committ ed Costs

Create custom data blocks

Tasks

	CBS position
☐	
☐	1
☐	2
☐	3
☐	4
☐	4.1
☐	4.2
☐	4.3
☐	5
☐	5.1
☐	5.2
☐	5.3

Subtotals 11

3. In the data block title field, enter a name for your data block.

InEight Inc. | Release 26.7

Page 65 of 639

CBS > Create new data block

1 Define title and type 2 Choose and customize columns

• Data block title
Contracts

• Data block type
☒ General
☐ Forecast
☐ Live forecast
☐ Forecast delta
☐ Actuals
☐ Schedule
☐ Revenue
☐ Cost category
☐ Tasks

Preview

Contracts


General

Cancel Next

4. Under Data block type, select the type that best fits your data block.

The forecast, live forecast, forecast delta, and actuals data block types have unique header features.

5. Click **Next**.
6. Add columns to your data block. You can add a column by double-clicking the column from the left panel, or by dragging and dropping the column from the left panel to the data block preview on the right.

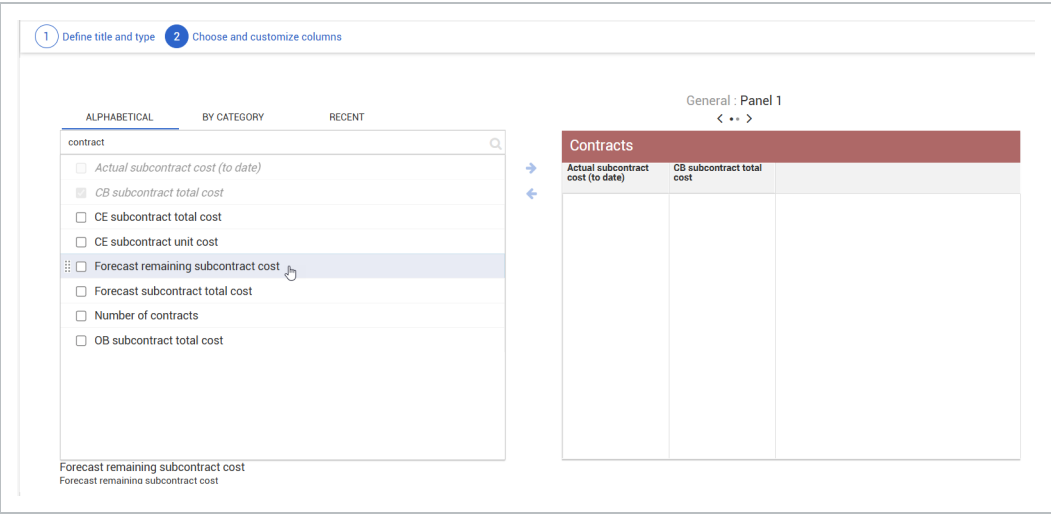

You can also add or remove columns by selecting the column(s) and using the left and right arrows.

The diagram illustrates the process of adding or removing columns. It shows a search bar with the text 'NT' and a list of columns. To the right of the list are two arrows: a blue right arrow and a blue left arrow, both enclosed in a red box. To the right of the arrows is a preview table titled 'Contracts' with the following columns:
- Actual subcontract cost (to date)
- CB subcontract total cost
The table is currently empty.

- 7. You can reorder the columns from the data block preview by dragging and dropping columns into a new position.

General : Panel 1
< . . >

Contracts				
Actual subcontract cost (to date)	CB subcontract total cost	Forecast remaining subcontract cost	Forecast subcontract total cost	
+ Number of contracts				

8. When finished, click **Save**.

Custom data blocks can be managed from the Add data block slide-out panel.

Actions

+

✎

✕

+

✎

✕

+

✎

✕

×

☰

☰

☰

☰

☰

Standard data blocks

Task details

Actuals

Current budget

Current estimate

Forecast delta

Live forecast

Forecast

Schedule

Cost category data blocks

Cost categories : Act...

Cost categories : CB

Cost categories : CE

Cost categories : For...

Custom data blocks

Committed Costs

Contracts

Create custom data blocks


🗑

2.10 VIEWSETS


Once you have all desired data blocks organized to your liking, you can create a saved view of your page so that you can always revert to it. This saved view is called a Viewset. The viewset can also be shared with other users.

Create and Save a Viewset


1. From the CBS register page, click on the **View** drop-down arrow.

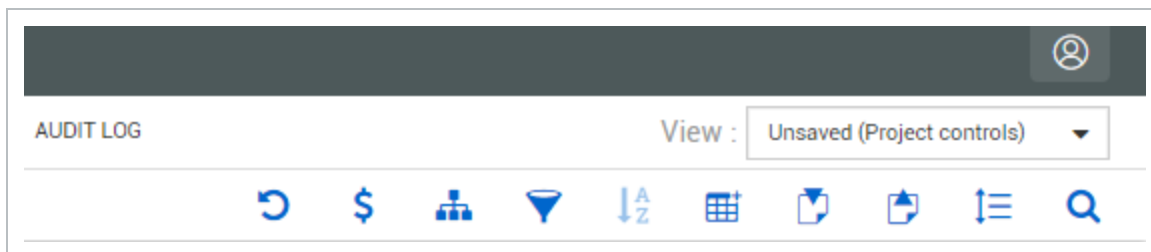

2. From the Viewset drop-down list, select **Save view as**.

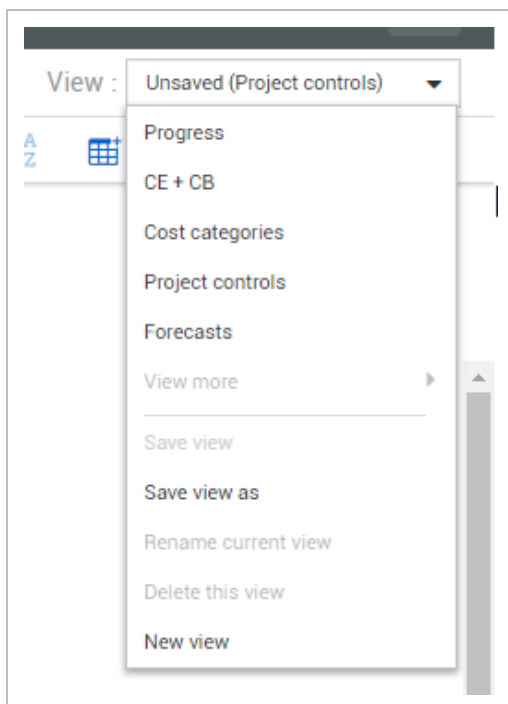

3. Name your view **[your initials] – Saved view**.

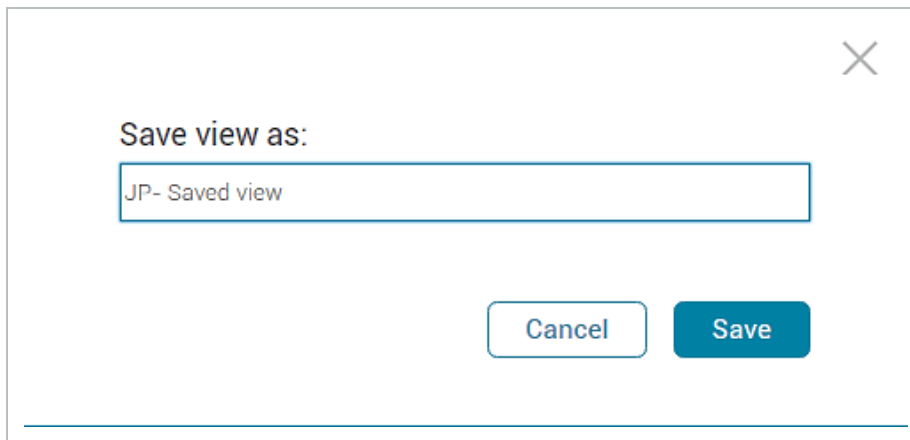A dialog box titled "Save view as:" with a close button (X) in the top right corner. Below the title is a text input field containing "JP- Saved view". At the bottom of the dialog are two buttons: "Cancel" and "Save".

Save view as:

JP- Saved view

Cancel Save

4. Click **Save**.

2.10.1 Sending Views and Data Blocks

Certain permissions are needed to send views and data blocks to roles.

You can send views to all users that have a certain role. You can also send it to specific projects or full organizations. To send to a project, you have to be a user on that project or in that organization.

Send a Viewset

1. With the Viewset selected and shown, from the Viewset drop-down list, select **Send view**.
2. In the **Search for a User** field, type an employee's name and select their name from the list.

×

Send view (test danielle) to

Users

Search for a user...

Send to

Users

No users selected

⊖

Roles

No roles selected

⊖

Projects

No projects selected

⊖

Organizations

No organizations selected

⊖

⊖ Remove all


Cancel

Send


- To send to a project, you have to be a user on that project or organization. Then select the Send View to drop down list and select the option you want.

InEight Inc. | Release 26.7

Page 71 of 639

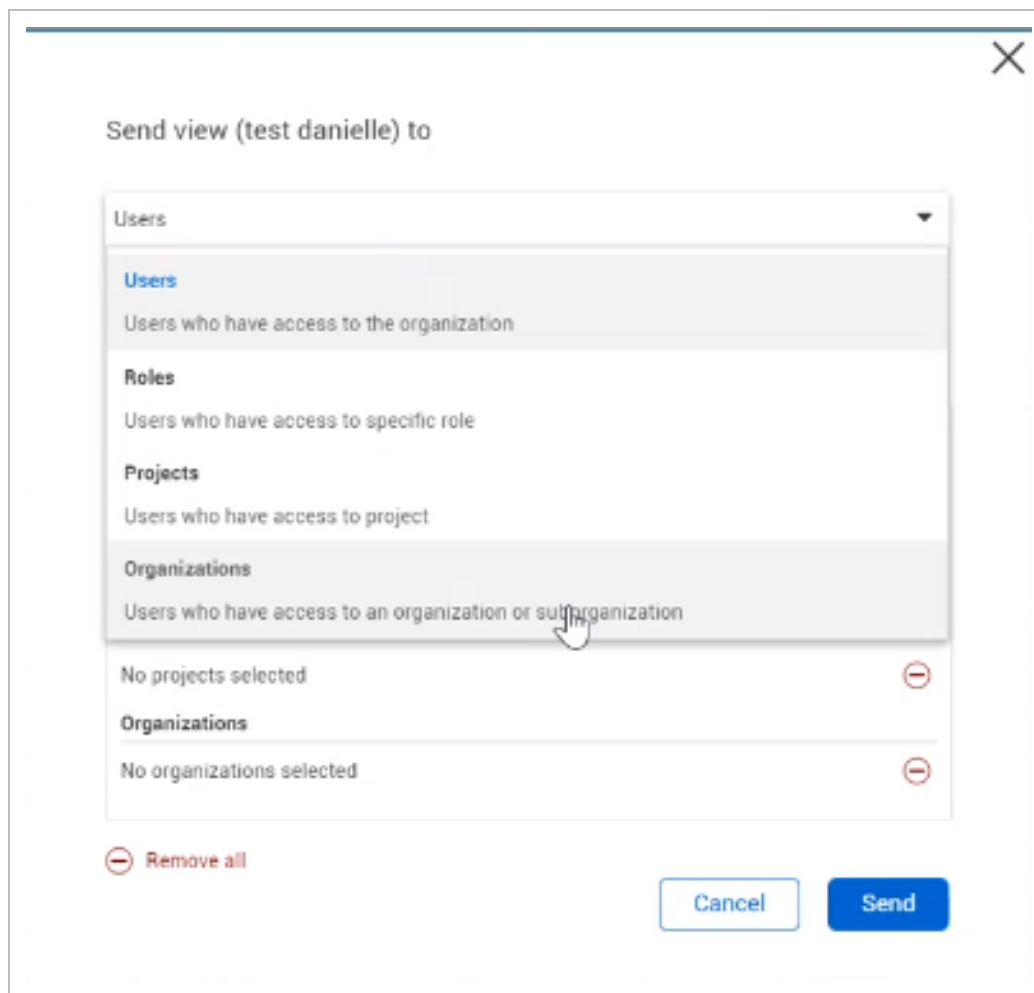

3. Click **Send**.
4. The selected Viewset will send a notification to the selected employee, and will be available in their drop-down list with sender's name and when the Viewset was sent.

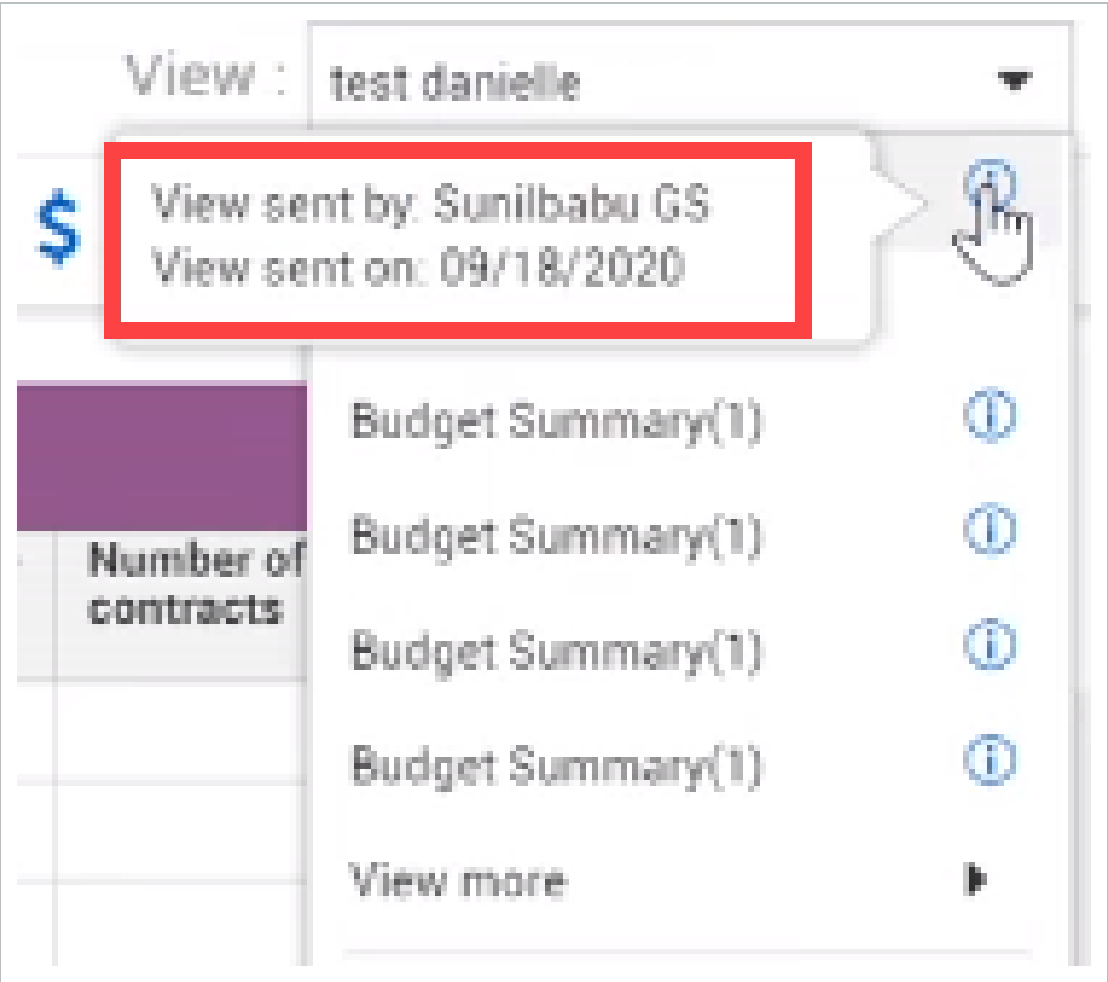

If the user does not have the proper permissions to view all the columns in the view that was sent to them, then the employee will only be able to view the columns for which they have permissions.

2.11 ROW DENSITY

The row density feature allows you to change the spacing between rows within the various pages and slide out panels in Control, allowing you to view your data with the amount of spacing you prefer.

There are three options available:

- Relaxed

Tasks			Task details < ● ● ● ● >		
☐	CBS position	Description	Resource	Forecast (T/O) quantity	UoM
☐	1	Job Overhead		1.00	Lump Sum
☐	^ 2	Earthwork		10,000.00	CY
☐	2.1	Earthwork Review	1	1.00	Each
☐	2.2	Earthwork	5	10,000.00	CY

- Narrow

Tasks			Task details < ● ● ● ● >		
☐	CBS position	Description	Resource	Forecast (T/O) quantity	UoM
☐	1	Job Overhead		1.00	Lump Sum
☐	^ 2	Earthwork		10,000.00	CY
☐	2.1	Earthwork Review	1	1.00	Each
☐	2.2	Earthwork	5	10,000.00	CY
☐	3	Concrete	5	10,000.00	CY


- Tight

Tasks			Task details < ● ● ● ● >		
☐	CBS position	Description	Resource	Forecast (T/O) quantity	UoM
☐	1	Job Overhead		1.00	Lump Sum
☐	^ 2	Earthwork		10,000.00	CY
☐	2.1	Earthwork Review	1	1.00	Each
☐	2.2	Earthwork	5	10,000.00	CY
☐	3	Concrete	5	10,000.00	CY
☐	^ 4	Structural Steel		1,000.00	Ton

The Row density icon is available on the CBS, ACS, Pay Items, Change Register, and Audit Log tabs.



When you select the Row density icon, a drop-down menu appears, where you can select the row density (space between rows) you prefer.



The row density you select applies to all registers within Control, including all tabs and slide out panels on the Workspaces and Project Library pages.

Row density is user-specific, so different users can apply different row densities within Control, and the row density option you select will remain the next time you log in.

Row density is independent from the Viewsets you create. The row density you select is therefore not saved as part of your viewsets.

2.12 AUDIT LOG

The **Audit Log** tab within the CBS register is used to capture changes that were made within InEight Control and is broken down into five sub-tabs located on a left sidebar menu. Each log is designed to capture the changes that happened within each of the different registers and during synchronization.

All five audit logs can be accessed by selecting the Audit log tab on the menu bar, then selecting each individual audit log on the far left.

CBS ACS PAY ITEMS CHANGE REGISTER AUDIT LOG													
Actions ▾													
CBS	Audit ID	Data type	Item type	Desc	WBS	Attrit	Chan by	Chan date	Value befor	Value after	Actu comp	Forec total co...	Forec total co...
ACS	4871359	CBS	Cost Item	Concrete	1071	Schedule ...	Michael M...	07/23/20...	False	True			
Pay items	4871358	CBS	Cost Item	Earthwork	1069	Schedule ...	Michael M...	07/23/20...	False	True			
Integration	4871357	CBS	Cost Item	Job Overh...	1002	Schedule ...	Michael M...	07/23/20...	False	True			
Import history	4871356	CBS	Cost Item	Structural...	1073	Scheduled	Michael M...	07/23/20...	False	True			

2.12.1 CBS

You can access the CBS audit log by selecting CBS from the left side menu.

The **CBS audit Log** captures changes in the CBS register and utilizes an attribute field to identify what type of change was made. Other columns include:

- Changed By (who made the change)
- Change Date (the date and time the change was made)
- The attribute value before and after
- Forecast cost before and after
- Forecast man-hours before and after
- Posting date before and after

CBS	Audit ID	Data type	Item type	Desc	WBS	Attrit	Chan by	Chan date	Value befor	Value after
ACS	4871359	CBS	Cost Item	Concrete	1071	Schedule ...	Michael M...	07/23/20...	False	True
Pay items	4871358	CBS	Cost Item	Earthwork	1069	Schedule ...	Michael M...	07/23/20...	False	True
Integration	4871357	CBS	Cost Item	Job Overh...	1002	Schedule ...	Michael M...	07/23/20...	False	True
Import history	4871356	CBS	Cost Item	Structural...	1073	Scheduled	Michael M...	07/23/20...	False	True

2.12.2 ACS

You can access the ACS Audit Log by selecting **ACS** from the left side menu.

The **ACS Audit Log** functions similarly to the CBS Audit Log, but contains the changes that were made within the ACS (Account Code Structure) tab. The fields utilized to capture what changes were made are:

- Change attribute
- Changed By (who made the change)
- Changed Date (the date and time the change was made)
- Attribute value before and after

CBS	Audit ID	Data type	Item type	Description	AC No.	Attribute	Changed by	Changed date	Value before	Value after
ACS	177	ACS	Account Code	Structural Steel industrial...	62.03.02.004.02	Primary Auto Quantity	Paul Serrison	11/19/2018 12:28 PM	False	True
Pay items	176	ACS	Account Code	Structural Steel industrial...	62.03.02.004.02	Primary Auto Quantity	Paul Serrison	11/19/2018 12:04 PM	True	False
Integration	175	ACS	Account Code	Structural Steel industrial...	62.03.02.004.06	Primary Quantity	Paul Serrison	11/19/2018 12:21 PM	806.00	406.00
Import history	174	ACS	Account Code	Structural Steel industrial...	62.03.02.004.06	Primary Auto Quantity	Paul Serrison	11/19/2018 12:21 PM	True	False
	170	ACS	Account Code	Structural Steel industrial...	62.03.02.004	Contribute Primary To Pri...	Paul Serrison	11/19/2018 11:39 AM	False	True

2.12.3 Pay Items

You can access the Pay Item Audit Log by selecting **Pay Items** from the left side menu.

CBS	Audit ID	Data type	Item type	Description	Pay item No.	Attribute	Changed by	Changed date	Value before	Value after
ACS	4873330	Pay Item	Pay Item	Pay Item 1	001	Billing Method	Renee Japp	07/26/2019 01:...	Cost Plus	Fixed Final Price
Pay items	4872029	Pay Item	Pay Item		1	Pay item tag 8	Renee Japp	07/24/2019 02:...		PY 8
Integration	4872028	Pay Item	Pay Item		1	Pay item tag 6	Renee Japp	07/24/2019 02:...		PY 6
Import history	4872027	Pay Item	Pay Item		1	Pay item tag 4	Renee Japp	07/24/2019 02:...		PY 4

The **Pay Item Log** again functions similarly but contains changes that were made to the pay items. The fields utilized to capture what changes were made are:

- Attribute
- Changed By (who made the change)
- Changed Date (the date and time the change was made)
- Value before and Value after
- Total price before and after

Audit ID	Description	Attribute	Changed by	Changed date	Value before	Value after	Total price before
1333638	Testing 07/31	Description	paul trippi	07/31/2019 08:...	Test	Testing 07/31	\$1040.00000000...
1333637	Testing 07/31	Sales Order	paul trippi	07/31/2019 08:...		S1	\$40.0000000000...

2.12.4 Integration

You can access the Integration/Sync Audit Log by selecting **Integration** from the left side menu.

	Audit ID	Interface	Status	Processing details	Start	Finish	User name	Log Handle
CBS								
ACS	65639	ActualQty	Succeeded	4 of 4	07/29/2019 03:23 PM	07/29/2019 03:24 PM	pavithra baskaran1	4a2a98f6-eaa6-431b-81f-
Pay items	65638	LiveForecast	Succeeded	4 of 4	07/29/2019 03:23 PM	07/29/2019 03:24 PM	pavithra baskaran1	ce90c8df-f916-4a50-847-
Integration	65637	Budget	Succeeded	4 of 4	07/29/2019 03:23 PM	07/29/2019 03:24 PM	pavithra baskaran1	43b8dc1c-6825-413a-9c-
Import history	65636	CBS	Succeeded	4 of 4	07/29/2019 03:23 PM	07/29/2019 03:24 PM	pavithra baskaran1	0985605a-745c-4f27-88-

The **Sync Audit Log** is different from the other three. This log is used to capture:

- Whether the synchronization process between InEight Control and the ERP system was completed successfully
- How long the sync process took to complete and who requested the sync

It keeps track of the functions performed under the Actions > Sync menu.

The syncing process will be discussed further in the [12.3 Audit log - Integration on page 556](#).

To help troubleshoot sync issues, you can click the link under the Processing details column to get more information on which steps succeeded, are suspended, or failed.


Last updated: 08/29/2018 01:03 PM
Use shortcut key F5 to refresh status


Completed details - - Plan quantities pull: 31570

Step	Status
Step 1: Recieving data	Complete
Step 2: Populating data	Complete

Close

© 2018 InEight Inc. [Privacy and Terms](#) | v 18.3
INEIGHT

If a sync error should occur, you can click on the Log Handle link to obtain troubleshooting information.



This brings you into the InEight **Suite App Logs screen**, where you can see information relating to the error including Level, Time, Domain, Area, Exception Message, Exception Type and Correlation Id, which can help you determine the cause of the sync error.

2.12.5 Import history

You can access the Import history audit log by selecting **Import history** from the left side menu.

The Import history log contains status information for all imports coming into all InEight products. For example, cost item and actuals import processes can both be viewed in the Import history log for status, then you can eventually make corrections and reprocess.

	File name	Status	Processi Details	Total line items	Errors	Total imported	Added estimate resource	Added pay items	Created by	Created date	Last edited by	Last edited date
CBS												
ACS	Market_St_9_8_17_GMP_Baseline.xer (Mark...	Failed	Step 3	1842	0	0	0	0	Renee Japp	07/24/2019 1...	Renee Japp	07/24/2019 1...
Pay Items	Market_St_9_8_17_GMP_Baseline.xer (Mark...	Failed	Step 3	1842	0	0	0	0	Renee Japp	07/23/2019 1...	Renee Japp	07/23/2019 1...
Integration	Book1.xlsx	Processing		2	2	0	0	0	Renee Japp	07/12/2019 0...	paul trippi	07/30/2019 0...
Import history	Market_St_9_8_17_GMP_Baseline.xer (Mark...	Cancelled	Step 5	0	0	0	0	0	Renee Japp	07/10/2019 0...	Renee Japp	07/23/2019 1...

The Import history audit log allows you to take action on import and sync failures, based on error messages. Error messages are contained within the error file for those imports that have failed import.

You can view progress in sync longs, view error messages, and then resolve issues in effort to continue with your import.

Control – Audit Log

Section		Description
1	File name	The name of the actual import file being used to import data.
2	Status	The current status of the import file. There are six import status that can define the current state of an import process.
3	Processing Details	This column describes the processing state in which the file is being processed. This column is not applicable for all statuses.
4	Total line items	This is the total line items that are included within the Excel import file.

Control – Audit Log (continued)



Section		Description
5	Errors	This is a count of the number of errors during import.
6	Total import	This is the total amount of records that were successfully imported from the Excel import file.
7	Added estimate resources	This is the total amount of added estimate resources that were added in the CBS.
8	Added pay items	This is the total amount of pay items successfully imported from the Excel import file.
9	Created by	This is user responsible for importing the Excel upload file.
10	Created date	This is the actual date the Excel upload file was imported.
11	Last edited by	This is the last user to edit the Excel upload file.
12	Last edited date	This is the last date the Excel upload file was edited.



File name	Status	Processing Details	Total line items	Errors	Total imported	Added estimate resources	Added pay items	Created by	Created date	Last edited by	Last edited date
NEWPROJ.xer (D...	 Pending	Step 5	18	0	0	0	0	paul trippi	08/02/2019 12:1...	paul trippi	08/02/2019 12:1...
NEWPROJ.xer (D...	 Cancelled	Step 5	0	0	0	0	0	paul trippi	08/02/2019 12:1...	paul trippi	08/02/2019 12:1...
NEWPROJ.xer (D...	 Cancelled	Step 5	0	0	0	0	0	paul trippi	08/02/2019 12:0...	paul trippi	08/02/2019 12:1...
NEWPROJ.xer (D...	 Cancelled	Step 5	0	0	0	0	0	paul trippi	08/02/2019 12:0...	paul trippi	08/02/2019 12:0...

If you hover over one of these Status symbols below, it provides you with a brief explanation of the selected status.



Here are some examples:






There are six possible import statuses listed below.

Import history Statuses

Status	Status Icon	Definition
Failed		Import failed due to a duplicate row within the Excel file.
Failed with errors		Import failed with an attachment to download with further information.
Pending		The Excel import file is pending, further action is needed. The double blue arrows will open a new window where you can correct and re-process the Excel import file. The blue circle with the line through it will cancel the import completely.
Cancelled		The Excel import file has been cancelled.
Processing		The Excel import is still processing. Once this is complete, the status will move into one of the other five statuses.
Complete		Processing of the Excel import files is complete.

2.12.5.1 Pending status

When an import is in a **Pending** status, this means that further action is needed to complete the Excel file import.



There are two options:

Option 1

1. By selecting the double blue errors, you will be taken to another window to continue processing the faulty records.

File name	Status
CBS Import.csv	Pending

As an example, in the below screenshot, there are 3 existing errors. If you hover over one of the errors, it will tell you what needs to be corrected.

In this case, there is an issue with the account code assignment, as the pop-up hover suggests.

Audit log > Import history > CBS Import.csv

Find previous error

3 errors remain

Find next error

Cancel

Import

Status Details (WBS phase code)		Import Columns				
Import status	CBS match status	Import method	CBS position	Description	WBS phase code	Account code
Pending	✓ to 1002 [1] [Job Overhead]	Update existing items o...	1	Job Overhead	1002	20
Pending	✓ to 1069 [2] [Earthwork]	Update existing items o...	2	Earthwork	1069	51
Pending	✓ to 1071 [3] [Concrete]	Update existing items o...	3	Concrete	1071	61
Pending	✓ to 1073 [4] [Structural Steel]	Update existing items o...	4	Structural Steel	1073	
Pending	✓ to 1074 [4.1] [Erect Steel - H...]	Update existing items o...	4.1	Erect Steel - Heavy	1074	62.03.02.004.06
Pending	✓ to 1005 [4.2] [Erect Steel - L...]	Update existing items o...	4.2	Erect Steel - Light	1005	62.03.02.004.02
Pending	✓ to 1006 [4.3] [Bolted Connec...]	Update existing items o...	4.3	Bolted Connections	1006	62.03.02.006
Pending	✓ to 1084 [5] [Materials]	Update existing items o...	5	Materials	1084	1112233
Error	✓ to 1085 [5.1] [Earthwork - M...]	Update existing items o...	5.1	Earthwork - Materials	1085	1112234
Error	✓ to 1086 [5.2] [Concrete - Mat...]	Update existing items o...	5.2	Concrete - Materials	1086	1112235
Error	✓ to 1087 [4.4] [Module 01 - Er...]	Update existing items o...	4.4	Module 01 - Erect Steel ...	1087	1112236

2. When you double click into one of the 3 errors, it will take you directly into an account code assignment screen where you can make the correction.

From here you can select an account code and click on Assign.

Assign account code

Search...

Select	Account code	Description	UoM
☐	00	Overhead.6233 EDIT	PLS
☐	00.03	OH - Get Work	MWk
☐	00.03.02	OH - Estimating	MWk
☒	00.03.02.002	OH - Estimating - Engineering (Pr...	MWk
☐	00.03.02.006	OH - Estimating - Research & Qu...	MWk
☐	00.03.02.008	OH - Estimating - Prepare Estima...	MWk
☐	00.03.02.010	OH - Estimating - Review (Pre-Bid)	MWk
☐	00.03.02.014	OH - Estimating - Post Bid	MWk
☐	00.03.02.016	OH - Estimating - Management	MWk
☐	00.03.02.018	OH - Estimating - 2nd Estimates	MWk

Cancel

Assign

3. After all corrections have been made to the existing errors, you can select the Import button on the top right on the screen.


Find next error

Cancel


Import

Description	WBS phase code	Account code
Job Overhead	1002	20
Earthwork	1069	51
Concrete	1071	61
Structural Steel	1073	

4. A warning message appears stating that changes will be made, and this project will be disabled until completion.

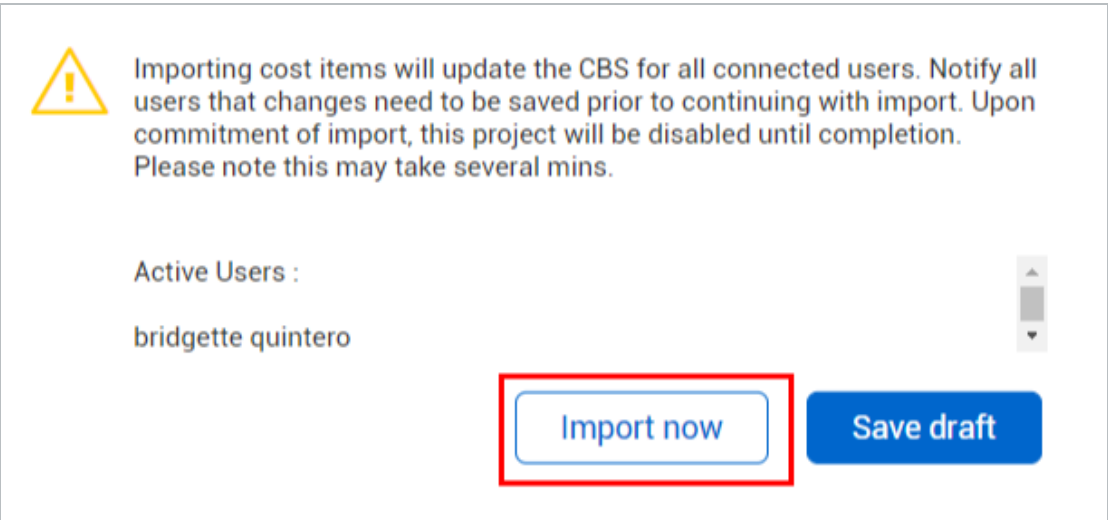

5. Once processing has finished, you will receive an Import complete message.



6. The Import history page now shows that the imported file is now successfully imported and updates the Last edited date.

File name	Status	Total line items	Errors	Total imported	Added estimate resources	Added pay items	Created by	Created date	Last edited by	Last edited date
CBS Import.csv	Complete	11	0	0	0	0	Keith Anderson	06/19/2019 06:30 ...	paul trippi	07/31/2019 10:32 ...


Option 2

- 1. Selecting cancel, the blue circle with the line through it, will cancel the import completely.

File name	Status
CBS Import.csv	 Pending  

2.12.5.2 Failed with errors status

When an import is in a **Failed with errors** status, the system will generate a Word error report. The document displays detected errors while attempting to import the Excel file values. Errors will need to be reviewed within the Word document



An example of the Failed with errors Word **error file** provides direction on how to proceed with correcting the Excel import errors, and a course of action to run the import again


```
Import actuals CBS data: CBS import.xls
File Import attempted on: 7/31/2019 3:45:03 PM

The following errors were detected while attempting to import actual
values into control.
Review the errors below, once all the errors have been resolved,
reattempt the import to Control.

Error 1: Posting date in external system must be valid (this error
affects 10 WBS/CBS items out of 10 total attempted imported WBS/CBS items
and 10 rows out of 10 total attempted imported rows)

WBS: 2904
CBS: 10
Row: 7

WBS: 2905
CBS: 11
Row: 8

WBS: 2906
CBS: 12
Row: 9


WBS: 2907
CBS: 13
Row: 10
```


The only option with a Failed with errors status is to review the errors, resolve them within the initial Excel file import, and then re-import the file.

2.13 PROJECT INTRODUCTION

You will be using the project titled “**Steel Structure Training Job**” for the InEight Control training. Within this Control training, you will create cost items and other data that will be utilized in trainings covering the other InEight products (Plan, Progress, etc.)

The project consists of the construction of multiple steel support platforms in a greenfield site. The project scope ranges from site preparations, concrete foundation and footing pours, steel erection, and bolted connections.

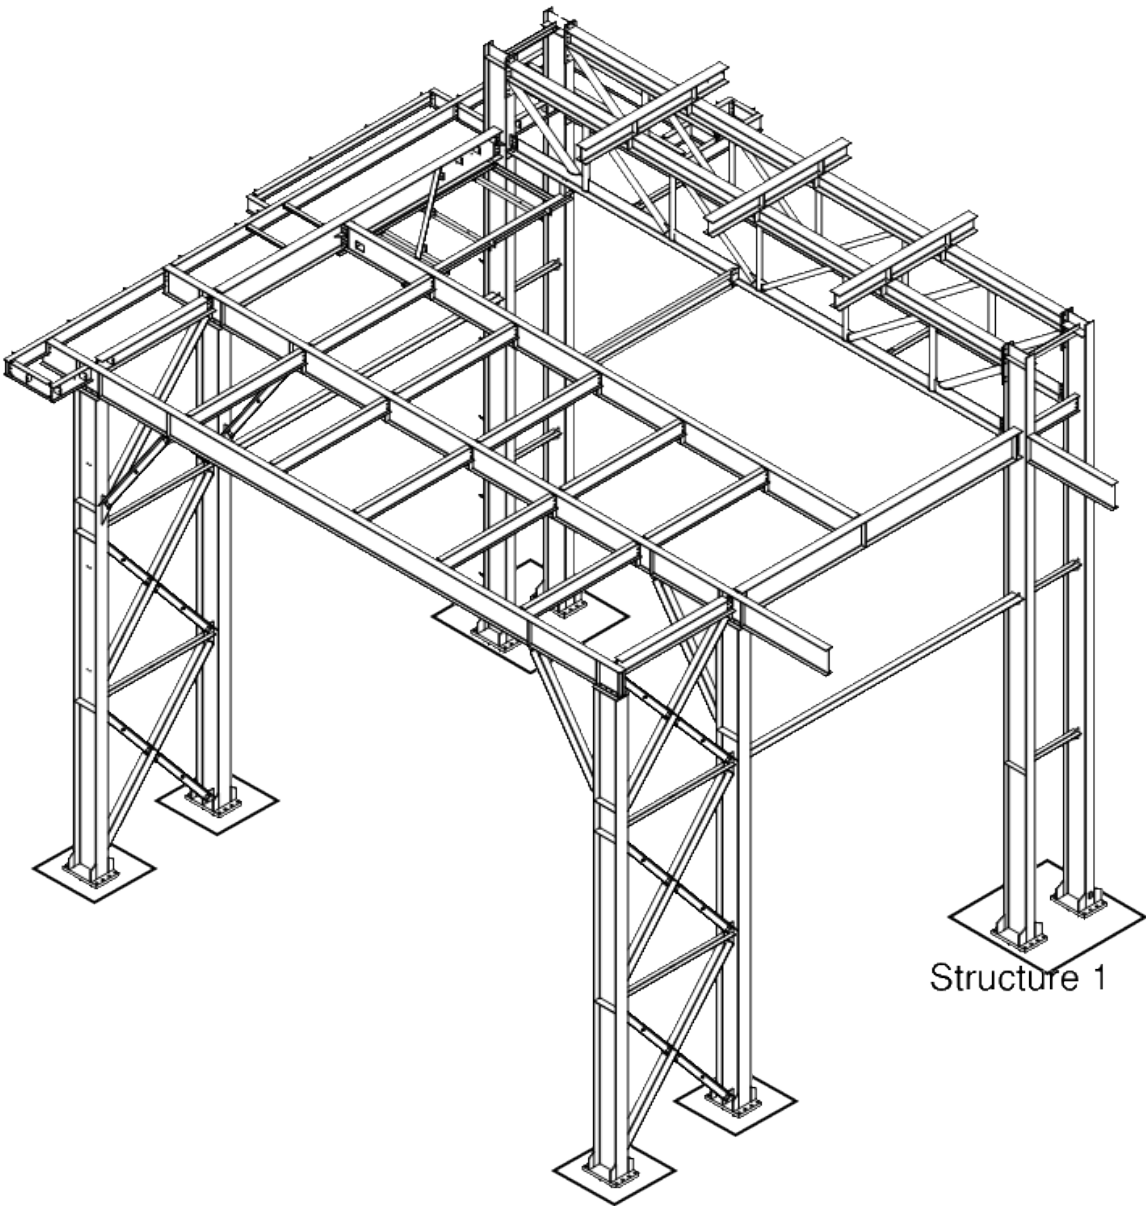


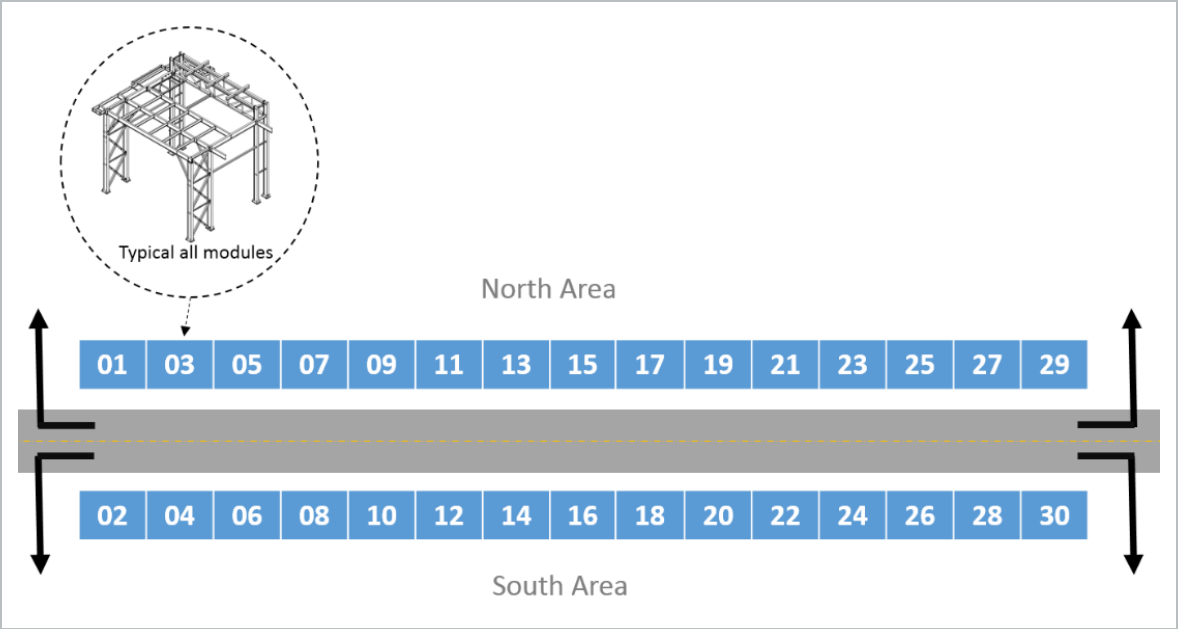


CHAPTER 3 – COST ITEM SETUP

3.1 Cost item setup workflow	90
3.2 Cost Item Overview	91
3.2.1 Cost Breakdown Structure	91
3.2.2 CBS Tree	94
3.2.3 Cost Item Menu	96
3.2.4 Cost Item Dashboard	97
3.3 Cost Items	99
3.3.1 Cost Item Creation	99
3.3.2 Required Cost Items	106
3.3.3 Cost Item Arrangement	108
3.3.4 Viewing the CBS Grouped by Column	110
3.3.5 Cost Item Deletion	111
3.3.6 Copying Cost Items with Resources	113
3.3.7 Design total qty and Design total MHrs columns in the CBS	115
3.3.8 Create cost items in InEight Change	116
3.4 Hide in Plan, Progress, and Design	119
3.4.1 Hide feature in a cost item	120
3.4.2 Hide feature in the CBS Workspace	121
3.4.3 Considerations	121
3.5 Cost Item Excel Import	122
3.5.1 Forecast Excel Import	127
3.5.2 Spreadsheet Rules	128
3.5.3 Best Practices and Recommendations	130
3.5.4 CBS Hierarchy	130
3.5.5 Resolving Import Errors	139
3.5.6 Excel Import for committed cost	140

3.1 COST ITEM SETUP WORKFLOW

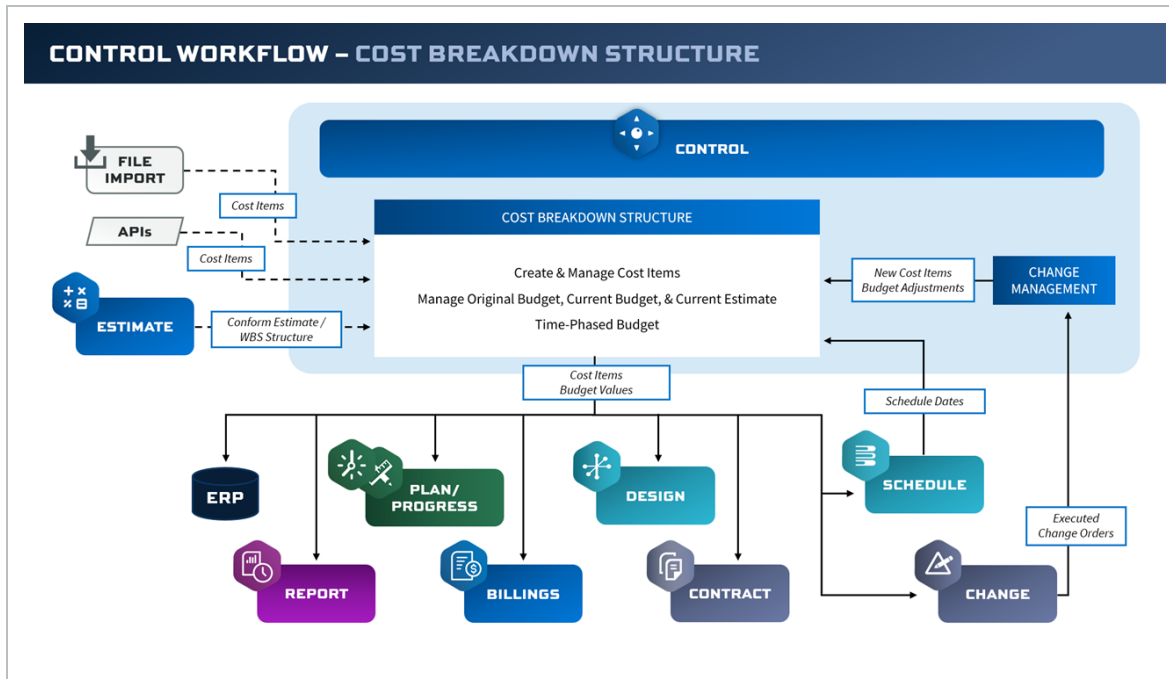

InEight Control is the application used to create and manage cost items. The cost breakdown structure developed and maintained in Control is utilized by other InEight applications which inherently share the same data set to eliminate duplicate data entry.

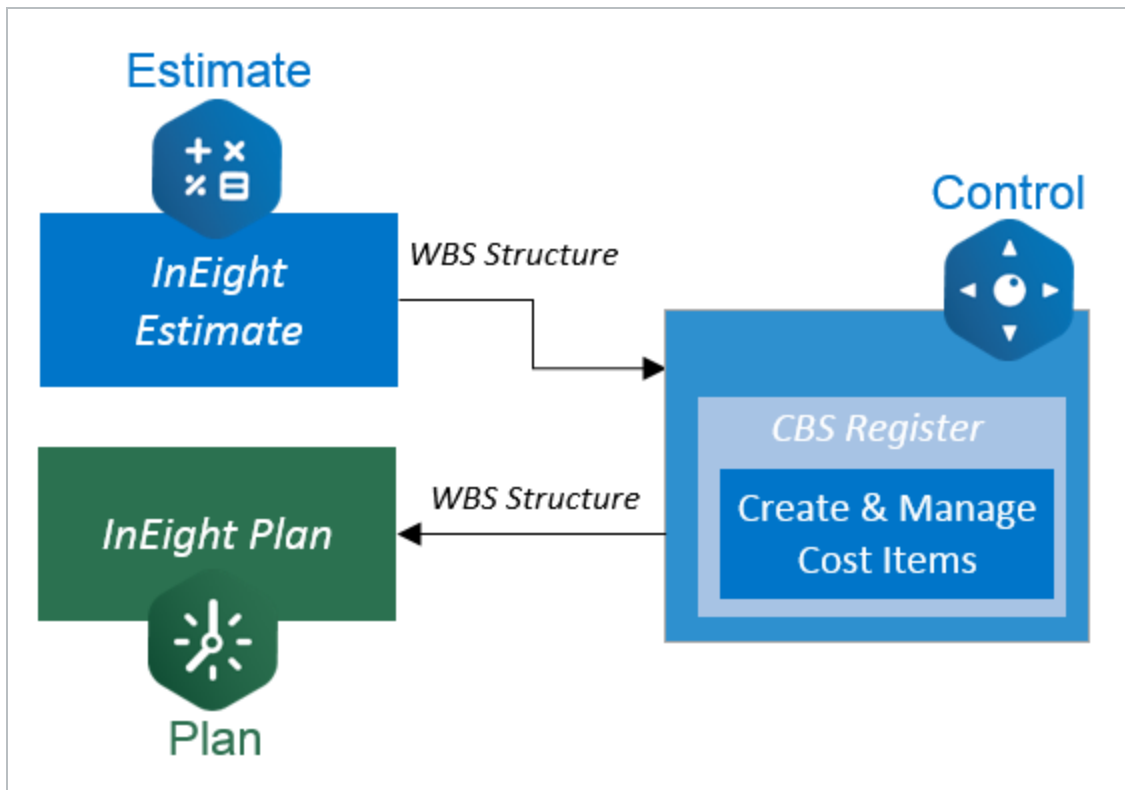

3.2 COST ITEM OVERVIEW

3.2.1 Cost Breakdown Structure

The CBS (Cost Breakdown Structure) is the main tab of the Workspaces page in Control and is the tab where you typically spend most of your time. Each row in the CBS represents a work activity and is called a cost item.

Steel Structure Training Job 2 | 1... / Control / Workspaces

CBS ACS PAY ITEMS CHANGE REGISTER AUDIT LOG View: CE + CB

Actions

Tasks				Task details			Current estimate			
	CBS position	Description	WBS phase code	R.	Forecast (T/O) qty	UoM	CE total Mhrs	CE total cost	CE Mhrs/unit	CE units/Mhr
☐	1	Job Overhead	1002			1.00		\$ 250,000.00	0.00	0.00
☐	2	Earthwork	1069	5	10,000.00	CY	8,000.00	\$ 400,000.00	0.80	1.25
☐	3	Concrete	1071	5	10,000.00	CY	30,000.00	\$ 1,500,000.00	3.00	0.33
☐	4	Structural Steel	1073		1,000.00	Ton	23,000.00	\$ 1,150,000.00	23.00	0.04
☐	4.1	Erect Steel - Heavy	1074	5	900.00	Ton	18,000.00	\$ 900,000.00	20.00	0.05
☐	4.2	Erect Steel - Light	1005	5	200.00	Ton	4,000.00	\$ 200,000.00	20.00	0.05
☐	4.3	Bolted Connections	1006	5	2,000.00	Ea	1,000.00	\$ 50,000.00	0.50	2.00
☐	5	Materials	1084		1.00	Each	0.00	\$ 1,750,000.00	0.00	0.00
☐	5.1	Earthwork - Materials	1085	1	10,000.00	Ton	0.00	\$ 250,000.00	0.00	0.00
☐	5.2	Concrete - Materials	1086	1	10,000.00	CY	0.00	\$ 1,000,000.00	0.00	0.00
☐	5.3	Structure Steel - Materials	1087		1,000.00	Ton	0.00	\$ 500,000.00	0.00	0.00
☐	6	Merrill Iron & Steel - Steel Material	1088		100.00	Ton	0.00	\$ 50,000.00	0.00	0.00

The CBS is organized in a hierarchy of superior and subordinate cost items. A cost item is superior and/or subordinate based on its relationship to other cost items. This is similar to a parent and a child relationship where an individual can be both a parent and a child at the same time. The CBS is color coded to identify which level of the hierarchy a specific cost item is located.

Tasks			
	CBS position	Description	WBS phase code
☐	1	Job Overhead	1002
☐	2	Earthwork	1069
☐	3	Concrete	1071
☐	4	Structural Steel	1073
☐	4.1	Erect Steel - Heavy	1074
☐	4.2	Erect Steel - Light	1005
☐	4.3	Bolted Connections	1006
☐	5	Materials	1084
☐	5.1	Earthwork - Materials	1085
☐	5.2	Concrete - Materials	1086
☐	5.3	Structure Steel - Materials	1087

Superior

Tasks			
☐	CBS position	Description	WBS phase code
☐	1	Job Overhead	1002
☐	2	Earthwork	1069
☐	3	Concrete	1071
☐	4	Structural Steel	1073
☐	4.1	Erect Steel - Heavy	1074
☐	4.2	Erect Steel - Light	1005
☐	4.3	Bolted Connections	1006
☐	5	Materials	1084
☐	5.1	Earthwork - Materials	1085
☐	5.2	Concrete - Materials	1086
☐	5.3	Structure Steel - Materials	1087

Subordinate

If a cost item has no subordinates it is considered a terminal cost item. Terminal cost items are where cost is tracked. All superior items are a roll up of the budget, manhours, and cost of the cost items below. Terminal items are identified with a special symbol located at the first column of each data block.

Tasks				Task details	
☐	CBS position	Description	WBS phase code	Resources	
☐	1	Job Overhead	1002	☐	
☐	2	Earthwork	1069	☐	
☐	3	Concrete	1071	☐	
☐	4	Structural Steel	1073	☐	
☐	4.1	Erect Steel - Heavy	1074	☐	
☐	4.2	Erect Steel - Light	1005	☐	
☐	4.3	Bolted Connections	1006	☐	
☐	5	Materials	1084	☐	

Terminal

This terminology and associated graphics provide a way to communicate and understand the hierarchy of the Cost Breakdown Structure. The following table provides definitions for each of these terms.


Term	Definition
Superior	Cost item that has subordinate subcost items that roll up under it.
Subordinate	Cost item that is a child to a superior cost item.
Terminal	Cost item that has no subordinate beneath it. Costs and hours are defined at the terminal level.

As accurate as estimators try to build the estimate, changes occur during the project’s execution that affect the CBS register in Control. To learn how to maintain, improve, and use the CBS register properly, this topic focuses on the fundamentals of the Cost Breakdown Structure.


3.2.2 CBS Tree

The CBS tree provides a way to navigate up and down your Cost Breakdown Structure and a way to filter down to a subset of the structure.


You open the CBS tree slide out panel by clicking on the CBS Tree icon on the Side Toolbar.

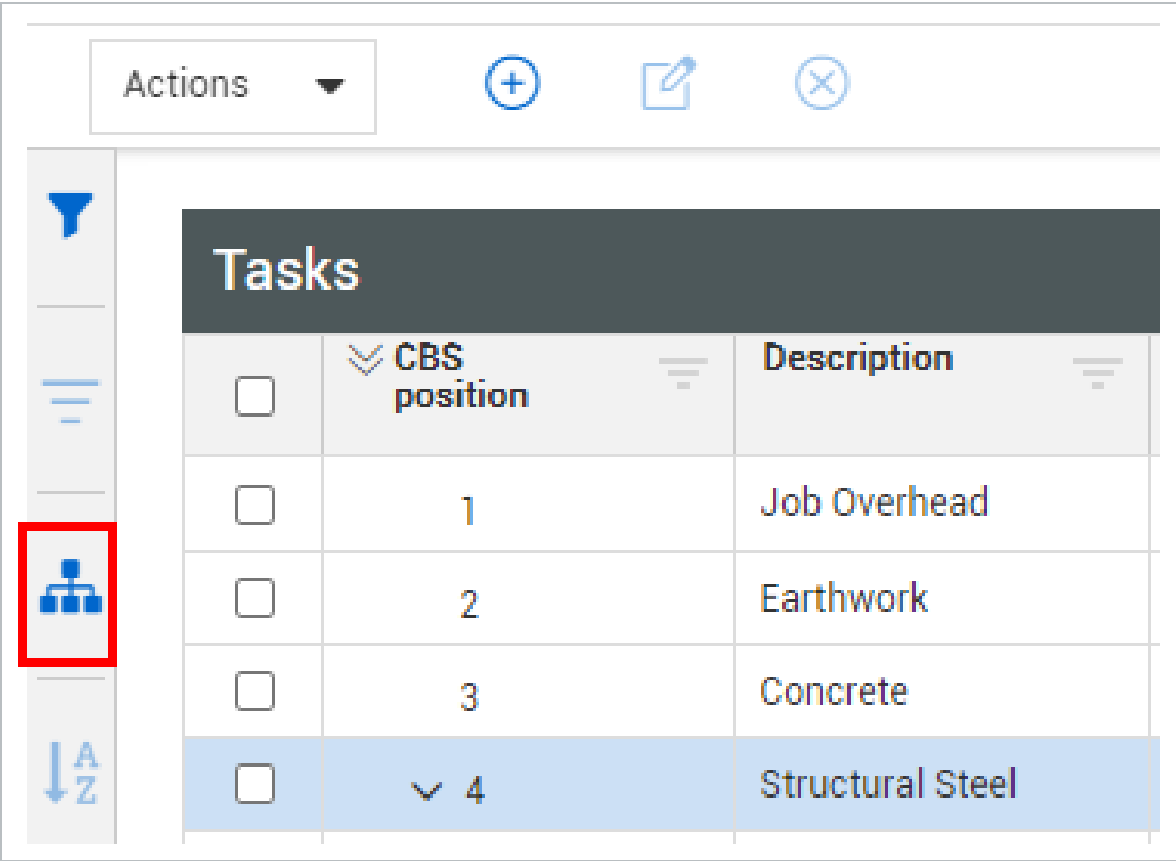

When selected, the CBS tree icon turns yellow and the slide out panel appears.

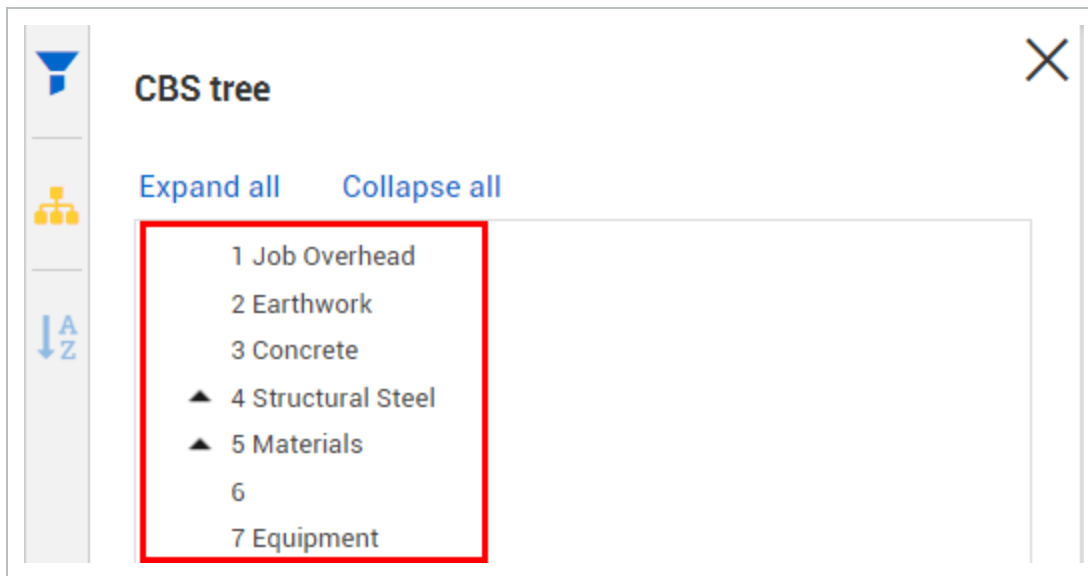


- Select Expand all to expand the entire Cost Breakdown Structure
- Select Collapse all to collapse the entire Cost Breakdown Structure
- Click on the arrow icons to expand a cost item to view its subordinates
- Select a cost item and then click **Apply** to filter your view to that cost item and its subordinates
- To clear the CBS filter, click the CBS tree icon and then click Disable

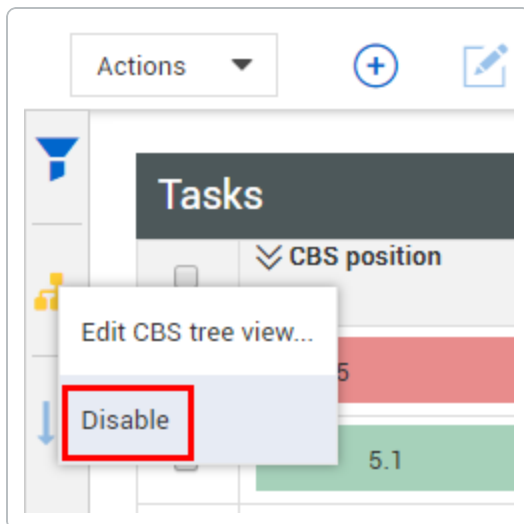

You can select more than one cost item on the tree to create a customized view.

3.2.3 Cost Item Menu

You can access a variety of cost item details and actions from the Cost Item menu.

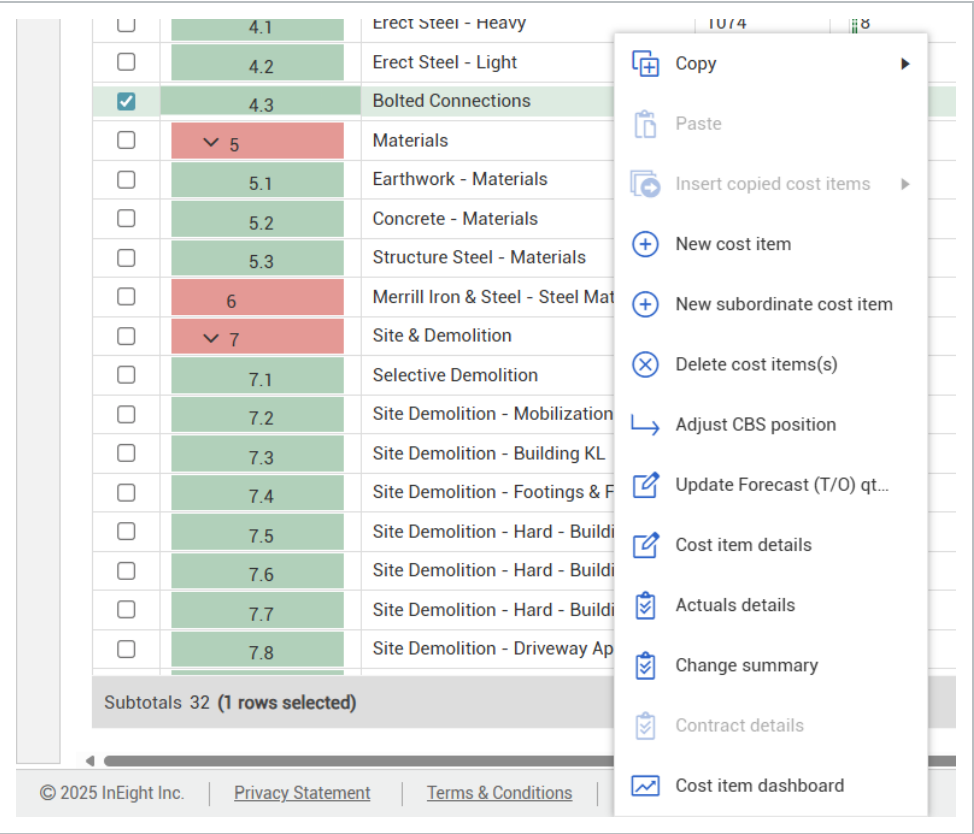

You can open the Cost Item menu in one of two ways:

- Right-click the cost item
- Click the three vertical dots in the Description column

☐	4.2	Erect Steel - Light	1005
☐	4.3	Bolted Connections	1006
☐	5	Materials	1084

The following table provides details for the options in the Cost Item menu.

Option	Details
Copy cost item	Copy the selected cost item with its associated resources.

Option	Details
Copy selection	Copy the value from a specific cell.
Paste	Paste the copied content.
Insert copied cost items	Insert the copied cost item in a CBS position that is above, below, or subordinate to the selected cost item.
New cost item	Create a new cost item.
New subordinate cost item	Create a new cost item that is subordinate to the selected cost item.
Delete cost item(s)	Delete the selected cost item.
Adjust CBS position	Move the selected cost item to a new position in the CBS.
Update Forecast (T/O) qty with Plan component total qty	Copy the total quantity of the associated component in InEight Plan to the Forecast (T/O) quantity of the selected cost item.
Cost item details	Open the Cost Item Details slide-out panel, where you can manage the cost item.
Actuals details	Open the Actuals Details slide-out panel, where you can input claimed quantities and view actuals history and commitments.
Change summary	Open the Change Order Details slide-out panel, where you can view associated change orders, the budget change summary, and the change order summary.
Contract details	Open the Contract Details slide-out panel, where you can view associated contract details from InEight Contract.
Cost item dashboard	Open the Cost Item Dashboard slide-out panel.


3.2.4 Cost Item Dashboard

The Cost Item Dashboard slide-out panel shows multiple cost item affiliated graphs. These graphs let you further analyze cost item past and current performance trends related to time-phased distribution, current budget changes, value over time, completion progress indicators, and a CBS audit history log.


1074

Erect Steel - Heavy


Time phased distribution

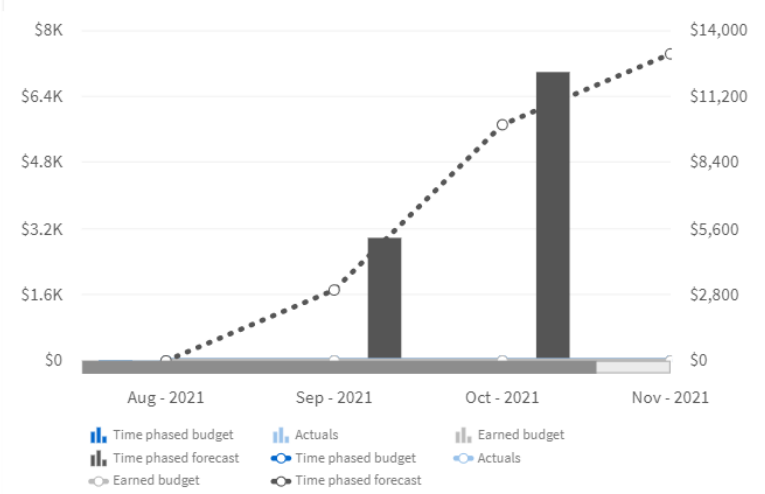


Current budget changes

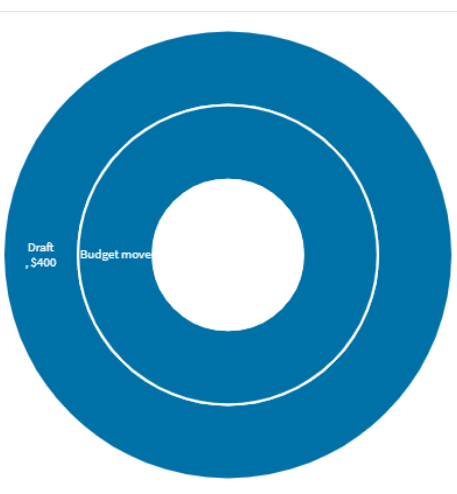


Value change over time

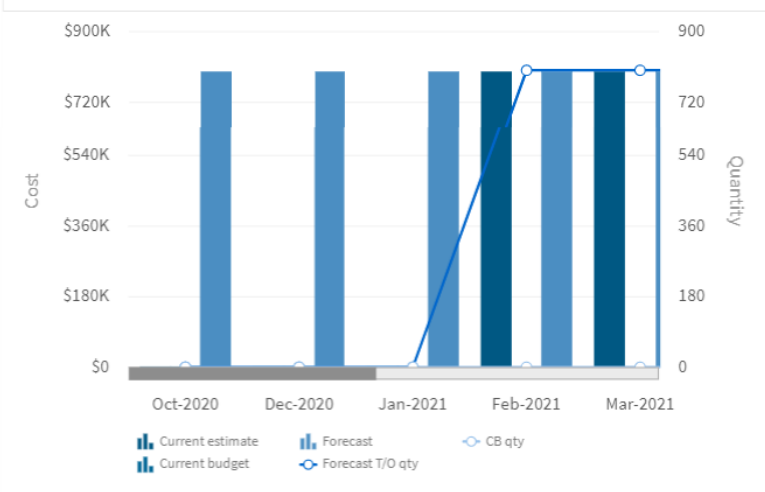

CBS audit log history

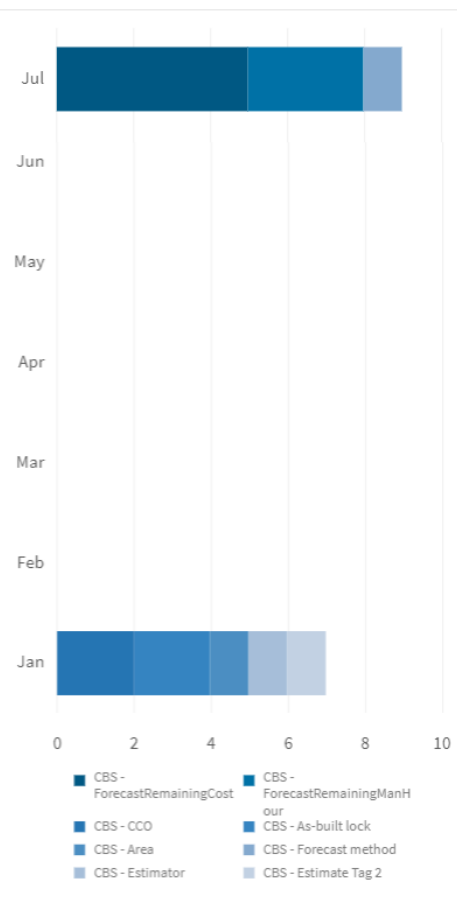

Completion progress

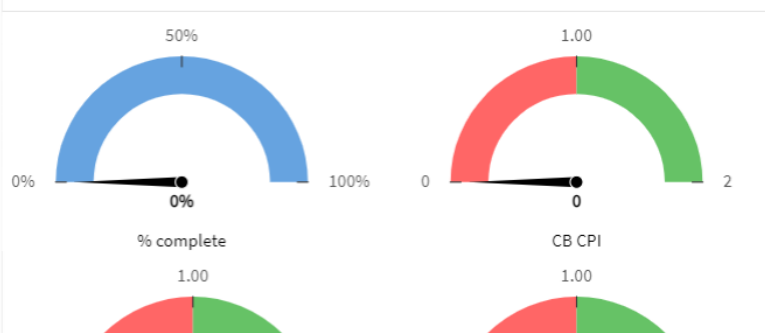

3.3 COST ITEMS

While most of your project structure typically imports from your estimating system, you may need to adjust the Cost Breakdown Structure (CBS) to better reflect how the work will be executed in the field. Additionally, contract changes or newly added scope may require updates. To accommodate these needs, you can add, edit, and rearrange cost items as necessary.

If you need to build additional structure from the ground up, you can create new cost items manually. This flexibility allows you to construct an entirely new project structure within Control – even starting from a blank project if needed.

3.3.1 Cost Item Creation

In Control, you can create a new cost item in two ways:

- **New Cost Item:** Creates a new cost item at the same hierarchy level as the selected item, using the next available number. For example, if you select 1.6, the new item will be 1.7 (if available).
- **New Subordinate Cost Item:** Creates a new cost item one level below the selected item, using the next available number at that level. For example, if you select 1.6, the new item will be 1.6.x, where x is the next available number.

When creating a new cost item, there are multiple fields available for populating the cost item details. Not all fields are required; you can edit these details after the cost item has been created. The following table provides more information on the available options.


Field	Required	Details
Description	Optional	Text field for the name or description of the cost item.
Forecast T/O qty	Required	The Forecast Takeoff Quantity is the amount of work or materials expected to be completed for the cost item. This value can be updated as project details progress.
UoM	Required	The Unit of Measure is the standard measurement used to quantify the Forecast T/O qty, such as linear feet, cubic yards, or labor hours.

Field	Required	Details
Cost source	Required	Indicates how the cost item's value is derived - either as a Plug (a lump-sum amount) or as Detail (built from associated quantities, rates, or resources).
Current Estimate fields	Optional	If available, input costs, unit rates, man-hours, and/or equipment hours. Many of these values are linked, and changes to these values will update related values as well as the Current Estimate total cost. Fields include CE total cost , CE total MHrs , CE total equipment Hrs , CE unit cost , CE MHR/Unit , CE Units/MHrs , and CE labor cost/MHrs .
Cost segment	Required	Categorizes whether the cost item is a direct or indirect cost. • Direct Cost - Costs that directly pertain to the deliverables (pay items) of the job • Job Overhead - Overhead costs associated with running and managing the job (e.g., management, jobsite facilities) • Business Overhead - Overhead costs associated with running the business (not directly related to running the job) • Subcontract - Subcontract associated costs
Pay item assignment	Optional	Select an existing pay item to associate to this cost item.
Account code	Optional	Select an organizational account code for this cost item.
Live forecast method	Optional	Select how the live forecast is calculated for this cost item. Forecast Method applies to individual cost items and can be changed at any time.


Field	Required	Details
Allow as-built	Required	Determines whether you can enter actual costs and quantities for a cost item. • None - Cost item does not accept cost or quantities. This is typically seen in Superior cost items • All - Allows a cost item to accept both direct costs and quantities • Quantities - Cost item only accepts quantities • Cost - Cost item only accepts costs, man hours, and equipment hours
Quantity driver	Required	Defines how a cost item's Forecast T/O qty is controlled. • Superior CI - Automatically updates the quantity based on changes to a parent cost item using a proportional multiplier • Fixed - Keeps the quantity constant regardless of changes to related cost items
Currency	Required	Select a currency unit for this cost item.
As-built lock	Optional	Select the checkbox to lock the ERP status for this cost item. Once you lock the ERP status, your ERP does not allow the cost item to be progressed.
Hide in Plan, Progress, and Design	Optional	Select the check box to make this cost item unavailable for claiming in InEight Plan, Progress, and Design. For more information, see Hide in Plan, Progress, and Design .
CBS contribute qty	Optional	Select the check box to add the Forecast (T/O) qty of this cost item with any other selected siblings to the superior (parent) cost item. Note that the UoM must be the same for all cost items.

Create A New Cost Item

1. From the CBS tab of Control > Workspaces, click the **Add Cost Item** icon on the top left toolbar.

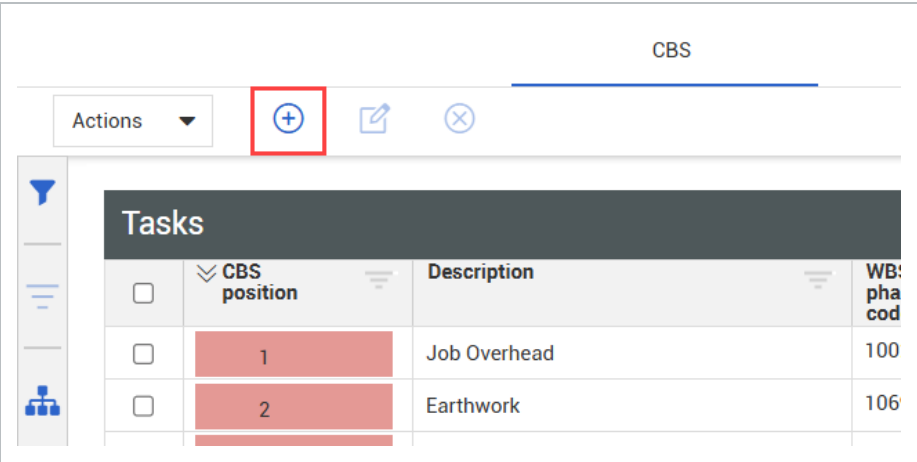

2. Select **Create a new blank cost item**, and then click **Yes**.

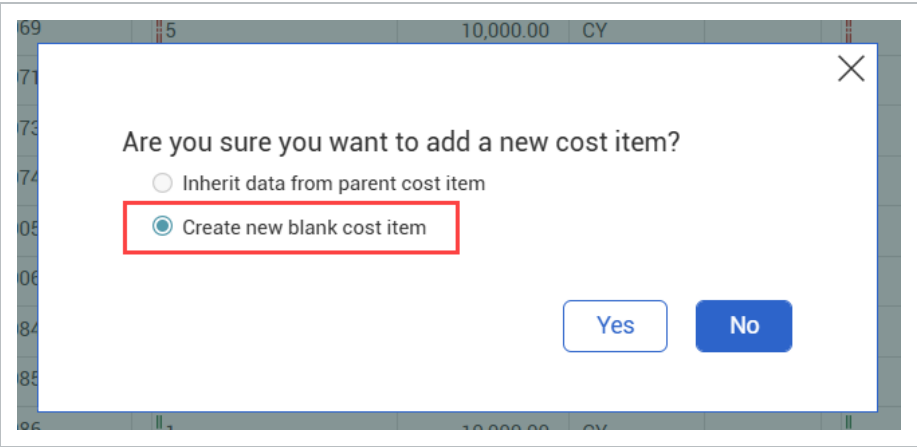

- To specify the CBS position of the new cost item, first select an existing cost item from the CBS, and then click Add Cost Item > **New cost item**.
3. The New cost item dialog box opens to the Details tab. Enter the cost item details as needed.

New cost item

New cost item

⊕

Add new cost item

DETAILS

ATTRIBUTES

Forecast T/O qty

UoM

CE unit cost

CE total cost

1.00

PLS

\$0.00

\$0.00

Description

• Forecast T/O qty

• UoM

WBS phase code

1.00

PLS

Generated on Save

• Cost source

CE total cost

CE total MHrs

CE total equipment Hrs

Plug

\$0.00

0.00

0.00

CE unit cost

CE MHr/Unit

CE Units/MHrs

CE labor cost/MHrs

\$0.00

0.00

0.00

\$0.00

Cancel

Save

4. When finished, click **Save**.

Create a New Subordinate Cost Item

1. From the CBS tab of Control > Workspaces, select the superior cost item.

CBS

ACS

Actions

⊕


✎

⊗


Tasks

	CBS position	Description	WBS phase code
☐	1	Job Overhead	1002
☐	2	Earthwork	1069
☐	3	Concrete	1071
☒	4	Structural Steel	1073
☐	4.1	Erect Steel - Heavy	1074
☐	4.2	Erect Steel - Light	1005

2. On the top left toolbar, click **Add cost item > New subordinate cost item**.

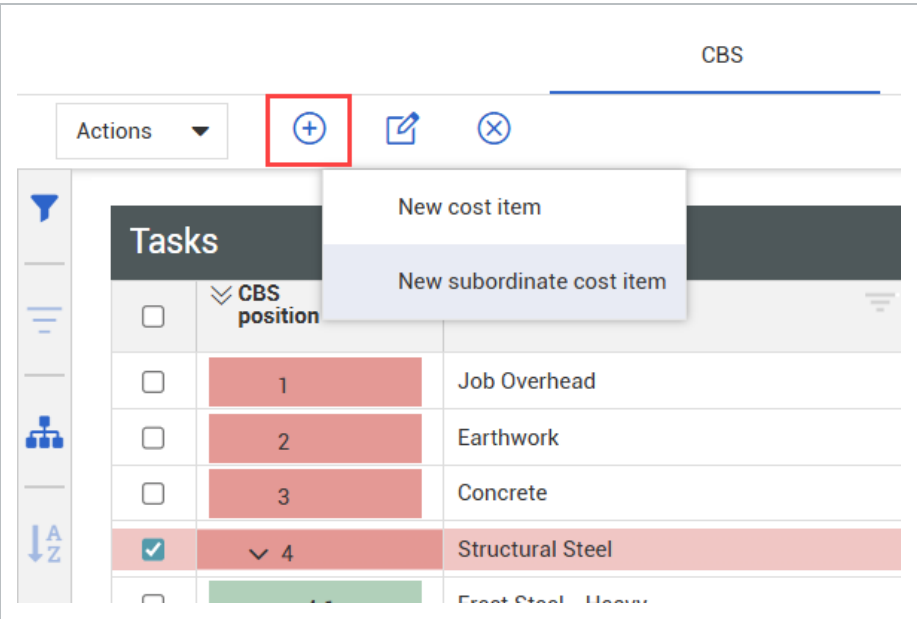

3. Select **Inherit data from parent cost item**, and then click **Yes**.

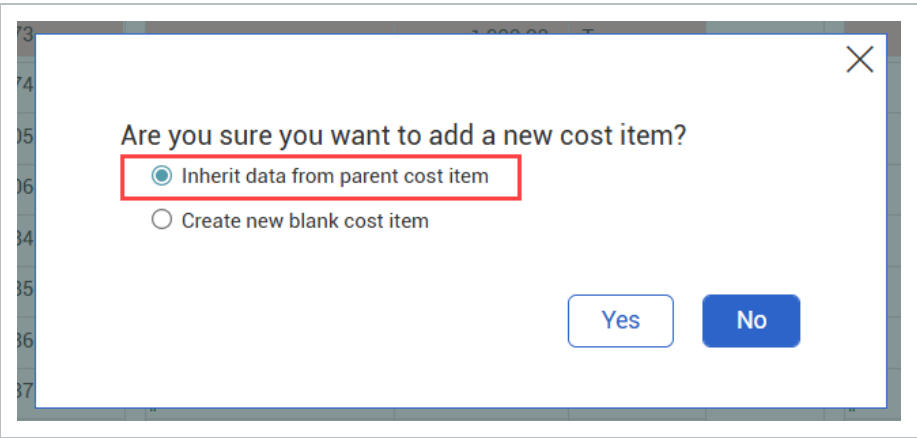

- Note that the fields in the New cost item window are populated with the existing data from the selected cost item.
4. Modify the cost item details as needed.

Structural Steel

Structural Steel

+

 Add new cost item

DETAILS

ATTRIBUTES

Forecast T/O qty

UoM

CE unit cost

CE total cost

1,000.00

Ton

\$0.00

\$0.00

Description

• Forecast T/O qty

• UoM

WBS phase code

Structural Steel

1,000.00

Ton

Generated on Save

• Cost source

CE total cost

CE total M/Hrs

CE total equipment Hrs

Plug

\$0.00

0.00

0.00

CE unit cost

CE M/Hr/Unit

CE Units/M/Hrs

CE labor cost/M/Hrs

\$0.00

0.00

0.00

\$0.00

• Cost segment

Pay item assignment

Account code

★ Live forecast method

Job Overhead

None

Cancel

Save

5. When finished, click **Save**.

3.3.1.1 Create Multiple Cost Items

When you need to create multiple cost items, you can save time by including additional cost items in the New cost item window. From the left panel, click **Add new cost item** to add another cost item record.

Precast Concrete

New cost item

+

 Add new cost item

DETAILS


Forecast T/O qty

UoM

1.00

PLS

To copy the details of a new cost item record, click the **Copy cost item** icon.

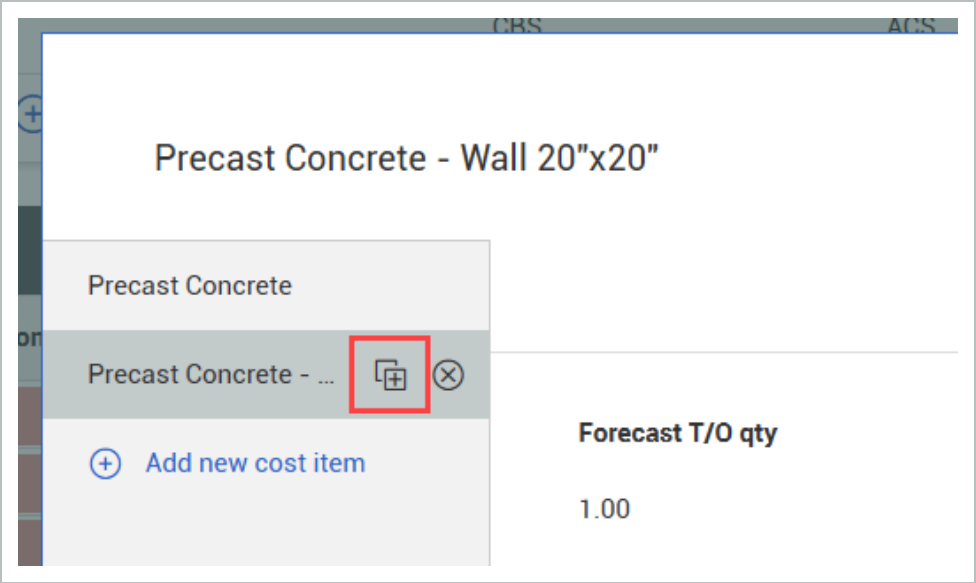


When you're finished, click **Save**. The new cost items will appear in sequence in the CBS.

☒	4.4	Precast Concrete Wall - 8"	1089	69.00	Ea
☒	4.5	Precast Concrete Wall - 9"	1090	71.00	Ea
☒	4.6	Precast Concrete Wall - 20"	1091	1.00	Ea
☒	4.7	Precast Concrete Wall - 20"X20"	1092	29.00	Ea


3.3.2 Required Cost Items

The Required cost items feature lets you create standardized or commonly used cost items at the organization level, and then add them at the project CBS level. Changing any of the required cost items at the organization level, such as the account code or UOM, also updates the cost items at the project level.

When required cost items are added in Settings > Control > Others > **Required cost items**, the feature provides standardization across all projects for those cost items that are commonly used.

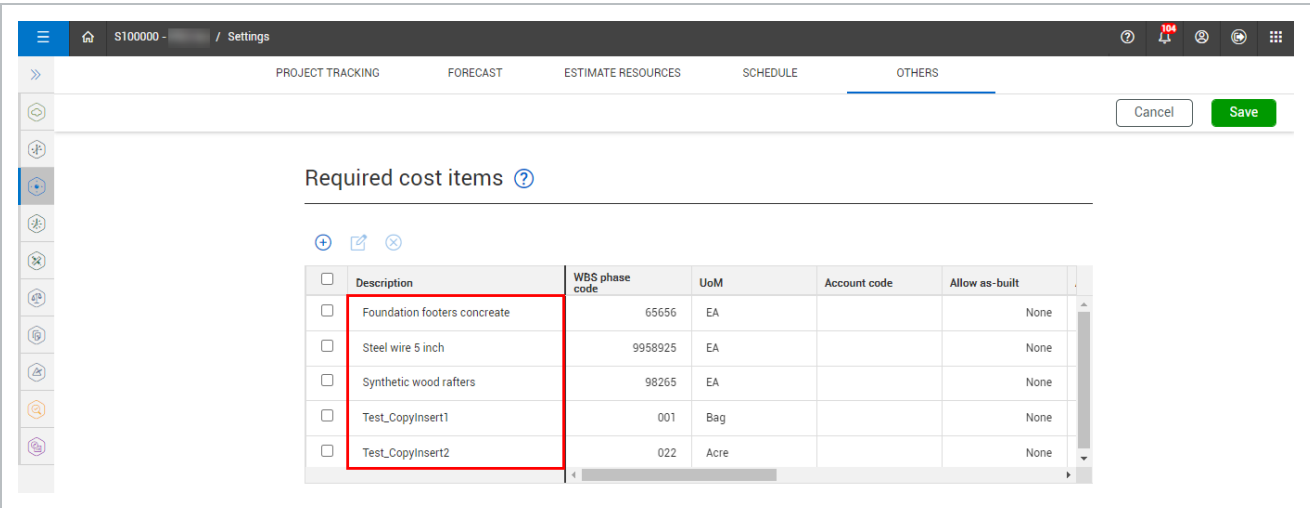

This feature can be a substitute for copying and pasting cost items from one project into another and ensures the same WBS phase code is being used regardless of the project a team member is working on.

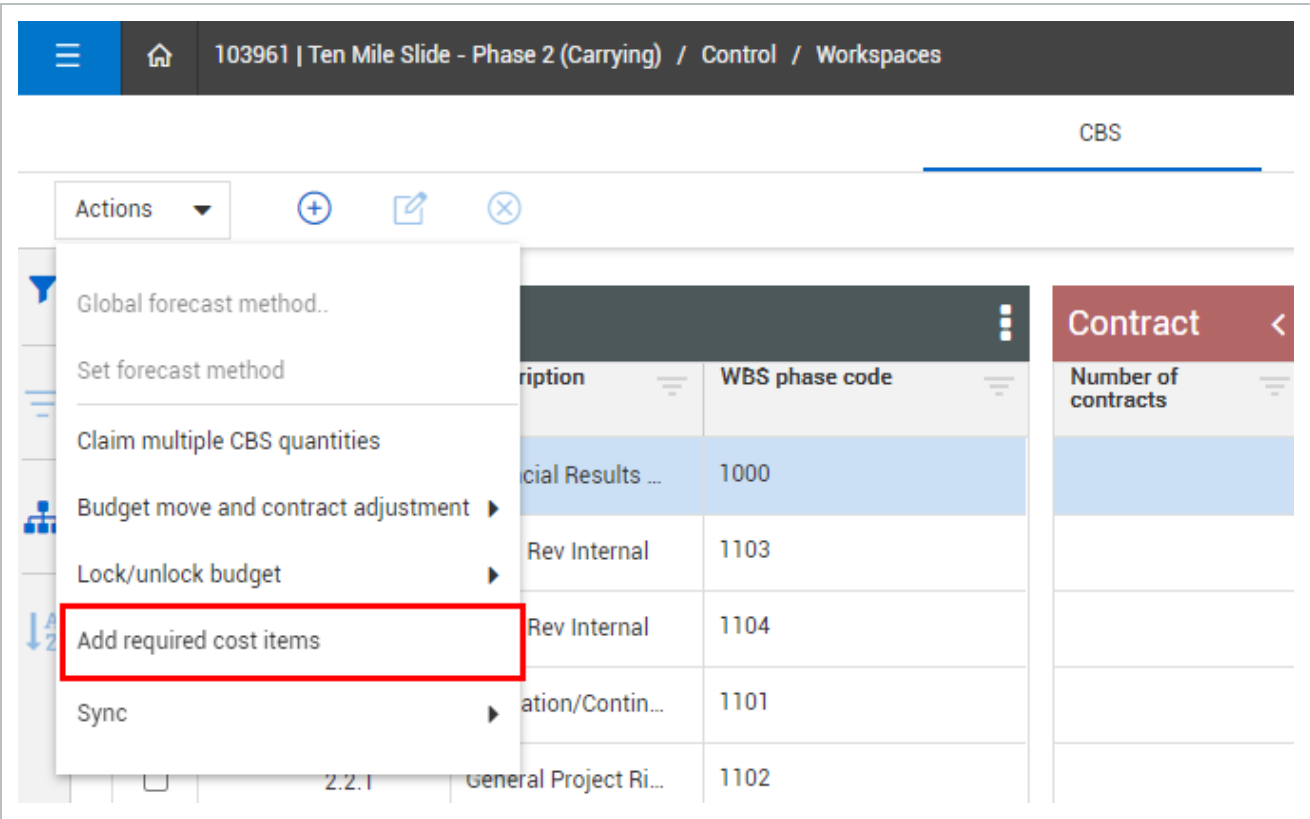


3.3.3 Cost Item Arrangement

As the project progresses, you may need to rearrange cost items in the CBS to accommodate project changes.

Move a Cost Item

- 1. Select the cost item(s) that you want to move.
- 2. Right-click the cost item(s) to open the cost item menu, and then select **Adjust CBS position**.

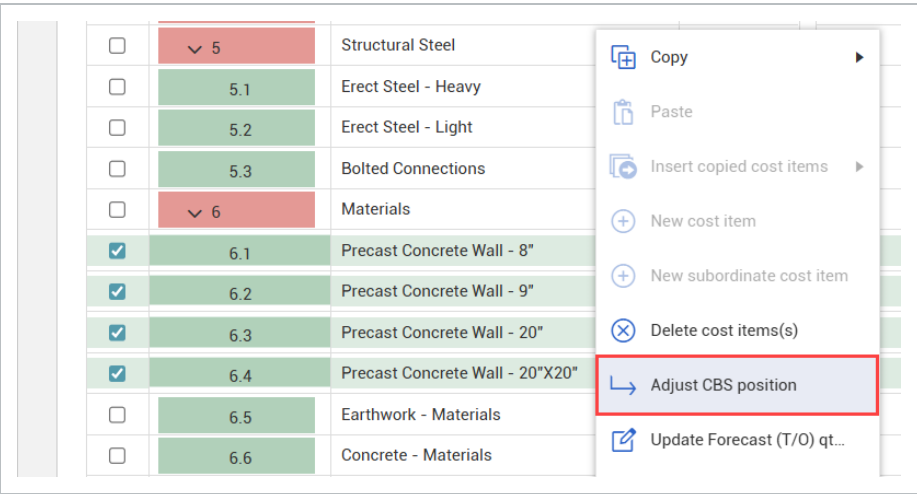

- 3. In the Adjust CBS Position window, drag and drop the selected cost item(s) into a new position in the CBS.

- This icon indicates that the cost item is moved into a subordinate position.

CBS > Adjust CBS Position

Move to

	CBS position	Description	WBS phase code
☐	1	Job Overhead	1002
☐	2	Earthwork	1069
☐	3	Concrete	1071
☐	4	Precast Concrete	1093
☐	5	Structural Steel	1073
☐	5.1	Erect Steel - Heavy	1074
☐	5.2	Erect Steel - Light	1005
☐	5.3	Bolted Connections	1006
☐	6	Materials	1084
☒	6.1	Precast Concrete Wall - 8"	1089
☒	6.2	Precast Concrete Wall - 9"	1090
☒	6.3	Precast Concrete Wall - 20"	1091
☒	6.4	Precast Concrete Wall - 20"X20"	1092

- This icon indicates that the cost item is moved into an equal position.

☐	4	Precast Concrete	1093
☐	5	Structural Steel	1073
☐	5.1	Erect Steel - Heavy	1074
☐	5.2	Erect Steel - Light	1005
☐	5.3	Bolted Connections	1006
☐	6	Materials	1084
☒	6.1	Precast Concrete Wall - 8"	1089
☒	6.2	Precast Concrete Wall - 9"	1090
☒	6.3	Precast Concrete Wall - 20"	1091
☒	6.4	Precast Concrete Wall - 20"X20"	1092

- If you prefer not to use drag and drop, click the **Move to** icon. Input the applicable CBS position, and then click **Move to** again. Select Child to move the cost item(s) into a subordinate position, or Sibling to move the cost item(s) to an equal position.

CBS > Adjust CBS Position

Move to

4 [1093] Precast Concrete

CBS > Adjust CBS Position

	CBS position	Description
☐	1	Job Overhead


4. Confirm the new position in the Adjust CBS Position window. When finished with the changes, click **Save**.

3.3.4 Viewing the CBS Grouped by Column


Navigating the CBS can be challenging when searching for specific information, as data is often distributed across multiple levels. Projects may contain large volumes of diverse data, making it difficult to locate and view relevant details- especially in a flat list format. The CBS Group By feature helps simplify this by allowing users to organize the CBS into logical groupings based on shared attributes. You can drag and drop column headers to group cost items by the criteria most relevant to your workflow.


CBS Group by Column

1. On the CBS register tab, select the **Group Columns** icon on the right toolbar.



2. Drag the **column header** of a column and drop it into the grey grouping area.
 - Note that this feature can only be used with columns with a predefined set of discrete values, such as UoM or Allow as-built.

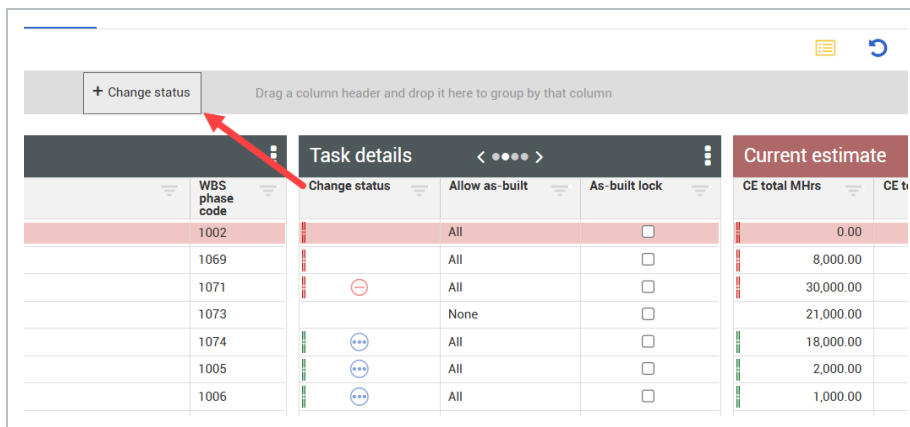

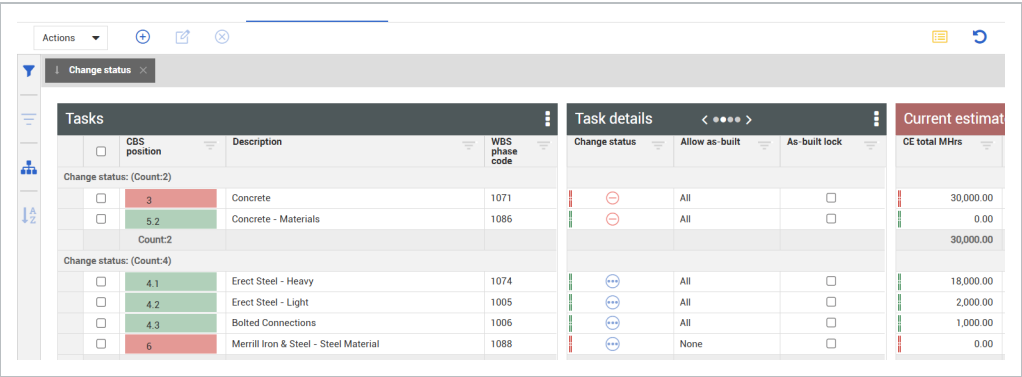


Tasks	CBS position	Description	WBS phase code
Change status: (Count:2)			
☐	3	Concrete	1071
☐	5.2	Concrete - Materials	1086
Count:2			
Change status: (Count:4)			
☐	4.1	Erect Steel - Heavy	1074
☐	4.2	Erect Steel - Light	1005
☐	4.3	Bolted Connections	1006
☐	6	Merrill Iron & Steel - Steel Material	1088

Task details	Change status	Allow as-built	As-built lock
1071	⊖	All	☐
1086	⊖	All	☐
1074	⊕	All	☐
1005	⊕	All	☐
1006	⊕	All	☐
1088	⊕	None	☐

Current estimate	CE total Mhrs
1071	30,000.00
1086	0.00
Count:2	30,000.00
1074	18,000.00
1005	2,000.00
1006	1,000.00
1088	0.00

3. To add subgroupings, drag and drop additional column headers into the grouping area. You can rearrange these headers in the grouping area to modify the subgroupings.

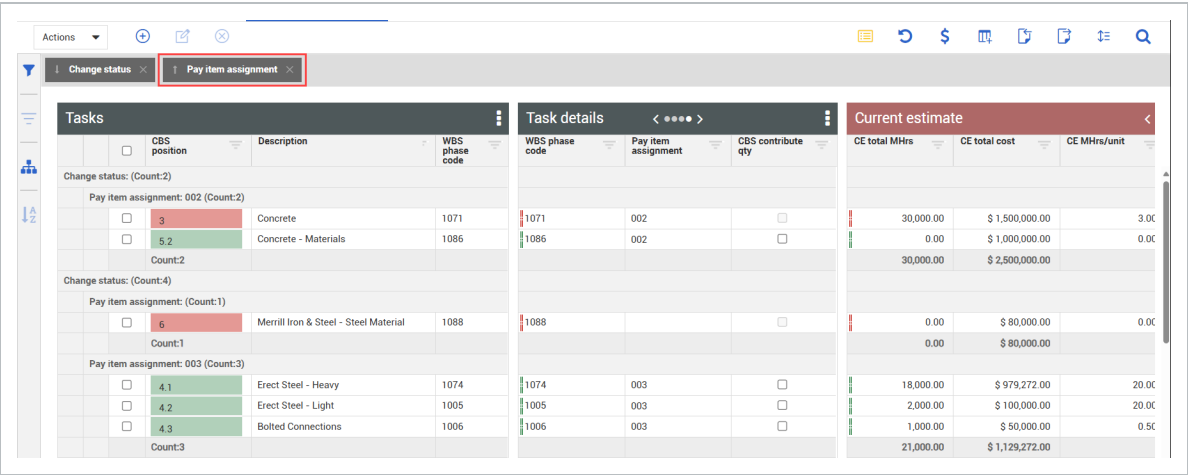

Tasks	CBS position	Description	WBS phase code
Change status: (Count:2)			
☐	3	Concrete	1071
☐	5.2	Concrete - Materials	1086
Count:2			
Change status: (Count:4)			
☐	6	Merrill Iron & Steel - Steel Material	1088
Count:1			
Pay item assignment: 002 (Count:2)			
☐	4.1	Erect Steel - Heavy	1074
☐	4.2	Erect Steel - Light	1005
☐	4.3	Bolted Connections	1006
Count:3			

Task details	WBS phase code	Pay item assignment	CBS contribute qty
1071	002		☐
1086	002		☐
1088			☐
1074	003		☐
1005	003		☐
1006	003		☐

Current estimate	CE total Mhrs	CE total cost	CE Mhrs/unit
1071	30,000.00	\$ 1,500,000.00	3.00
1086	0.00	\$ 1,000,000.00	0.00
Count:2	30,000.00	\$ 2,500,000.00	
1088	0.00	\$ 80,000.00	0.00
Count:1	0.00	\$ 80,000.00	
1074	18,000.00	\$ 979,272.00	20.00
1005	2,000.00	\$ 100,000.00	20.00
1006	1,000.00	\$ 50,000.00	0.50
Count:3	21,000.00	\$ 1,129,272.00	

4. To return to the standard CBS, click the **Group columns** icon again.

3.3.5 Cost Item Deletion

You can delete one cost item or multiple cost items by selecting the cost items, right clicking, and then selecting **Delete Cost Item**.

When deleting cost items from the CBS, deleting the forecast, clearing out the account code, or changing attributes to delete a cost item is not necessary.

☒	2	Earthwork	1069
☐	3	Concrete	
☐	▼ 4	Structural	
☐	4.1	Erect Ste	
☐	4.2	Erect Ste	
☐	4.3	Bolted C	
☐	▼ 5	Materials	
☐	5.1	Earthwor	
☐	5.2	Concrete	
☐	5.3	Structur	
☐	5.4	Materials	
☐	5.5	Materials	
☐	6		

Subtotals 14 (1 rows selected)

Copy

Paste

Insert copied cost items

New cost item

New subordinate cost item

Delete cost items(s)

Adjust CBS position

Cost item details

Actuals details

Change summary

Contract details

Cost item dashboard

You can also select a cost item and click the **Delete** icon on the left toolbar.

Actions

+

Tasks

CBS position	Description

A cost item must meet the following conditions to be deleted:

- Total Cost (To Date) = 0, MH (To Date) = 0, Eqp Hours (To Date) = 0, Qty Complete (To Date)=0
- C B-Total Cost = 0, C B-Total MH = 0, CB-Total Quantity = 0, C B-Qty Remaining = 0
- If the cost item is a parent item, all the subordinate cost items will also need to be checked to see if they can be deleted

If you are deleting multiple cost items and do not meet the following conditions for deletion, a downloadable file appears that lists all of the validations and why they failed.

3.3.6 Copying Cost Items with Resources

You can copy and paste entire cost items with resources from the CBS tab to any cost item you select.

When you copy a cost item, you cannot copy the current budget because the current budget must be approved in a contract adjustment or budget move.

Follow the step by step to copy a cost item.

Copy and paste cost items

1. From the CBS tab, select one or more cost items that you want to copy that contain a resource.

This can be checked in the Resources column. If the cost item has a 1 or higher, then a resource is attached to that cost item.

2. Right-click your selected cost items.
3. Hover over the Copy selection and select **Copy cost item**.

☒	3.1	Excavation
☒	3.2	Embankment
☒	▼ 4	Aggregate
☐	4.1	Furnish &
☐	4.2	Finegrade
☐	▼ 4.3	Install Agg
☐	4.3.1	Place Agg
☐	4.3.2	Blue Top A
☐	▼ 5	Asphalt Co
☐	5.1	Furnish &
☐	5.2	Install Hot
☐	▼ 6	36 Inch RC
☐	6.1	Furnish RC
☐	6.2	Excavate F
☐	6.3	Install RC
Subtotals 96 (3 rows selected)		

Copy

Copy cost item

Paste

Copy selection

Insert copied cost items

New cost item

New subordinate cost item

Delete cost item(s)

Adjust CBS position

Cost item details

Actuals details

Change summary

Contract details

Cost item dashboard

InEight Inc. | [Privacy Statement](#) | [Terms](#)
WZGsy

4. Right-click on another cost item in the CBS tab.
5. Hover over the option **Insert copied cost items**. You have three options as to where to place the copied cost items:
 - Insert above
 - Insert below

- Insert as a subordinate

Tasks

☐	CBS position	Description
☐	1	Financial Results Analysis
☐	2	Misc. Rev Internal
☐	2.1	Misc. Rev Internal
☐	2.2	Escalation/Contingency
☐	2.2.1	General Project Risk
☒	2.3	Directs
☐	2.3.1	Direct Labour
☐	2.3.1...	Grading Work
☐	2.3...	Resurface Existing Acces
☐	2.3...	Maintain Access Road
☐	2.3...	Clear & Grub Bench B & V

Task details

Resources	Forecast (T/O) qty	UoM
	1.00	PLS
	1.00	PLS
	1.00	PLS
	1.00	Each
	52.45	K\$
	1.00	PLS
	1.00	PLS
		LS
		2
		/k
	0.50	HA

Copy

Paste

Insert copied cost items

New cost item

New subordinate cost item

Delete cost items(s)

↑ Insert above

↓ Insert below

→ Insert as subordinate

You can also view the pasted cost items in the Resources tab of the Cost item details slide-out panel.

3.3.7 Design total qty and Design total MHrs columns in the CBS

Control displays the sum of the Forecast T/O quantity from the associated InEight Design items against the attributed cost items. You can compare the Design total quantity and Design total man-hours to the Forecast (T/O) quantity and Forecast hours columns, to make sure the values match up with what is in Design.

Design total qty Forecast T/O qty as determined and pulled from the Design application (Quantity item - Forecast TO qty)		Design total MHrs Current estimate man hours as determined and pulled from the Design application (Quantity item - CE MHrs)	
 Forecast remaining cost	Design total qty	Design total MHrs	 Forecast method
\$ 52,598,900.46	53,898.000	0.993	Rollup
\$ 5,760,886.07	370.000	0.651	Rollup

3.3.8 Create cost items in InEight Change

You can also create cost items with resources in Change, and then have them created in Control upon the approval of a contract adjustment. This reduces the amount of extra steps needed for creating cost items in multiple areas.

Creating cost items in Change is performed by first creating an issue with your newly created cost items, then executing your change order.

683 | Art Museum - Addition / Change

Executed Change order sent to Control

Change management > CCO-Demo 22.2-New scope

Executed ... Cost Billing mark... Markup Margin Deductions Net va... CCO status Pricing status Proposal status

\$6,116.00 \$5,560.00 \$0.00 \$556.00 10.00% \$0.00 \$6,116...

Executed None None

Actions

DETAILS PRICING SUPPORTING DOCUMENTS WORKFLOW ASSIGNMENTS

Cancel Save

Pricing summary ROM Estimate Proposal Agreed

Direct cost total

Labor

Type labor name

Issue 75 - New scope

Labor cost item pricing

Labor subtotal

Materials

Type material name

Issue 75 - New scope

Materials cost item pricing

pu

In Control, go into the Change Register and click on the change order to review the new cost items that originated from Change.

CBS ACS PAY ITEMS CHANGE REGISTER AUDIT LOG

Actions

Ch...	ID	Description	CCO	Crea... date	Issue #
16...	28.0	New scope	Demo 22.2	02/28/2022	75
16...	27.0	Budget Move: IWO/...		11/29/2021	
16...	26.0	Budget Allowance M...		11/29/2021	
16...	25.0	Buyout Gain: PVS; M...		11/23/2021	
16...	24.0	Budget Move: Temp ...		11/04/2021	
16...	23.0	Budget Move: Temp ...		11/04/2021	
16...	22.1	Budget Move: Morol...		11/04/2021	
16...	22.0	Budget Move: Morol...		11/02/2021	
16...	21.0	Budget Move: Adjust...		11/01/2021	
16...	20.0	Budget Move: BTA m...		11/01/2021	
16...	19.0	Budget Move: Distrib...		10/29/2021	
16...	18.0	Temp Entrance: Lab...		09/30/2021	02
16...	17.2	Buyout Adjustment: ...		09/23/2021	
16...	17.1	Buyout Adjustment: ...		09/23/2021	

28.0

New scope

Type Contract adjustment (Cost ite...

Status CCO-Approved

Originated on 02/28/2022

Originated by Morgan Smith

Last changed on 02/28/2022

Last changed by Morgan Smith

Approved on 02/28/2022

Approved by Morgan Smith

Approval probability 100.00 %

Pay item details

Pay item number	Description	Current billing method	Adjusted current price	Adjusted current unit price	Adjusted current pay qty	Locked date
2	Amendment #2	Fixed final price	\$ 6,116.00	\$ 0.00	6,116.00	
			\$ 6,116.00	\$ 0.00		

Cost item details

CBS position	Description	WBS phase code	Adjusted CB total cost	Adjusted CB total Mfrs	Adjusted CB total Qty	Locked date
4.36	New scope - Plug values	1353	\$ 5,150.00	50.00	1.00	02/28/2022
4.37	New scope - Resources	1354	\$ 410.00	0.00	1.00	02/28/2022

Review

Revise

InEight Inc. | Release 26.7

Page 117 of 639

Revise the change order to make any further adjustments, such as associating pay items to your cost items. Notice how the cost category assignments have all come over to Control that originated from the change document.

Change register > 28.0 - Contract adj...

CCO total budget
\$ 5,560.00

CCO unassigned budget
\$ 0.00

Net budget change
\$ 5,560.00

Net quantity change
Yes

Net man hour change
50.00

Markup
\$ 0.00

Fee
\$ 0.00

Net contract change
\$ 0.00

CCO agreed price
\$ 6,116.00

CCO unassigned price
\$ 6,116.00

Approval probability
100.00% - Executed Change Order

1 Details

2 Cost items

3 Pay items

4 Summary

Assign cost to

CBS position	Description	WBS phase code	CB total cost	Adjusted CB total cost	Markup	Marku
Unassigned cost items						
☒	New scope - Plug values		\$ 0.00	\$ 5,150.00		
☐	New scope - Resources		\$ 0.00	\$ 410.00		

New scope - Plug values

CB total cost
\$ 0.00

Pending budget cost
\$ 0.00

CB total Mtrrs
0.00

CB total quantity
0.00

Cost category	CB total cost	Pending
^ Total	\$ 0.00	\$ 5,150.00
✓ Labor	\$ 0.00	\$ 50.00
✓ Construction Equipment	\$ 0.00	\$ 0.00
✓ FOM Rented Equipment	\$ 0.00	\$ 0.00
✓ Supplies	\$ 0.00	\$ 0.00
✓ Materials	\$ 0.00	\$ 5,100.00
✓ Subcontract	\$ 0.00	\$ 0.00
✓ Fees	\$ 0.00	\$ 0.00
✓ Allowance	\$ 0.00	\$ 0.00
G & A	\$ 0.00	\$ 0.00
Undefined	\$ 0.00	\$ 0.00
Totals	\$ 0.00	\$ 5,150.00

Subtotals 2

\$ 0.00

\$ 5,560.00

Cancel

Draft

Back

Next

Approving the change order creates the new cost items with the resources specified in Change, and places them within the hierarchy specified in the contract adjustment, and if none is specified, then they are placed at the bottom of the CBS.

		CBS	ACS	PAY ITEMS		CHANGE REGISTER			
Actions									
ID	Description	Created date	Last changed by	Last change on	Notes	Status	Change number tag 1	Change number tag 2	Change number tag 3
28.0	New scope	02/28/2022		02/28/2022		CCO-Pending			
27.0	Budget Move: IWO/...	11/29/2021	Details	11/29/2021		Approved			
26.0	Budget Allowance M...	11/29/2021	Revise	11/29/2021		Approved			
25.0	Buyout Gain: PVS; M...	11/23/2021	Approve	11/23/2021		Approved			
24.0	Budget Move: Temp ...	11/04/2021	Review	11/04/2021		Approved			
23.0	Budget Move: Temp ...	11/04/2021		11/04/2021		Approved			
22.1	Budget Move: Morol...	11/04/2021		11/04/2021		Draft			

Tasks			
☐	CBS position	Description	WBS phase code
☐	4.13	Visqueen Material - Available	1229
☐	4.14	LICENSES, PERMITS, & BONDS	1039
☐	4.15	Security Personnel IWO - Available	1320
☐	4.16	Available	1169
☐	4.17	Available	1171
☐	4.18	Available	1172
☐	4.19	Available	1183
☐	4.20	Available	1158
☐	4.21	Available	1349
☐	4.22	Available	1143
☐	4.23	Available	1147
☐	4.24	Available	1150
☐	4.25	Available	1126
☐	4.26	Available	1127
☐	4.27	Available	1131
☐	4.28	Available	1132
☐	4.29	Available	1136
☐	4.30	Available	1107
☐	4.31	Available	1110
☐	4.32	Available	1339
☐	4.33	Construction Equipment	1070
☐	4.34	FINISH CARPENTRY	1188
☐	4.35	SHEAR CORE WALLS	1121
☐	4.36	New scope - Plug values	1353
☐	4.37	New scope - Resources	1354

Subtotals 41

3.4 HIDE IN PLAN, PROGRESS, AND DESIGN

When you create a cost item, there are multiple fields and options available for populating the cost item details. The Hide in Plan, Progress, and Design option is available for you to select to make the cost item unavailable for claiming in the InEight Plan, Progress, or Design applications. This feature is typically used to make sure items such as indirect or overhead items do not get claimed against.

By selecting the Hide in Plan, Progress, and Design check box, you can hide items, so they do not show in those applications. This makes it easier for the supervisor or foreman in the field to see only their work-related tasks.

The hide feature drives whether the cost item shows in Plan, Progress and Design. When the hide feature is not selected, the cost item shows in Plan, Progress, and Design. Those applications use the *Allow as-built* and the *As-built lock* to determine which type of actuals can be claimed (cost, quantity, man hours, equipment hours) or whether the cost item should not have actuals.

In Control, you can use the hide feature in combination with the *Allow as-built* and *As-built lock* feature to do the following:

- Determine if you can claim quantities in Control when the hide feature is selected.
- Allow other applications to sync claimed quantities when the hide feature is not selected and *Allow as-build* is selected for quantities.

3.4.1 Hide feature in a cost item

On the CBS tab, when you add or edit a cost item , you have the option to select the **Hide in Plan, Progress, and Design** check box in the details for the cost item.

New cost item

DETAILS

ATTRIBUTES

• Cost source
Plug

CE total cost
\$0.00

CE total MHrs
0.00

CE total equipment Hrs
0.00

CE unit cost
\$0.00

CE MHR/Unit
0.00

CE Units/MHrs
0.00

CE labor cost/MHrs
\$0.00

• Cost segment
Direct Cost

Pay item assignment

Account code

★ Live forecast method
None

• Allow as-built
None

• Quantity driver
Superior CI

• Currency
USD \$

☐ As-built lock

☐ Hide in Plan, Progress, and Design

☐ CBS contribute qty

Cancel Save


3.4.2 Hide feature in the CBS Workspace

On the CBS tab in the CBS Task details block, you can select the check box for the cost item to hide it in the Plan, Progress, and Design applications.

Tasks		Task details
CBS position	Description	Account code
1.1	Road - Ramp and ...	Hide in Plan, Progress, and Design: ☒ Is terminal: ☐
1.1.1	Structural South ...	Hide in Plan, Progress, and Design: ☐ Is terminal: ☒
1.1.2	Walls - SB Ramp/...	Hide in Plan, Progress, and Design: ☐ Is terminal: ☒
1.1.3	Structural - SB Ra...	Hide in Plan, Progress, and Design: ☐ Is terminal: ☒
1.1.4	Traffic Model - De...	Hide in Plan, Progress, and Design: ☐ Is terminal: ☒
1.1.5	Roadway - Civil D...	Hide in Plan, Progress, and Design: ☐ Is terminal: ☒
1.1.6	Drainage - System	Hide in Plan, Progress, and Design: ☐ Is terminal: ☒
1.1.7	Landscape - SB R...	Hide in Plan, Progress, and Design: ☐ Is terminal: ☒
1.1.8	D16 408 Permit	Hide in Plan, Progress, and Design: ☐ Is terminal: ☒
1.1.9	Geo Report	Hide in Plan, Progress, and Design: ☐ Is terminal: ☒
2	Construction	Hide in Plan, Progress, and Design: ☒ Is terminal: ☐
2.1	Bridge Work	Hide in Plan, Progress, and Design: ☐ Is terminal: ☐
2.1.1	Erect Structural St...	Hide in Plan, Progress, and Design: ☐ Is terminal: ☒
Subtotals 14		

3.4.3 Considerations

- You must select to hide the cost item before any claiming is done in Plan, Progress, or Design. After claiming is received for the cost item, the hide option is then unavailable.
- When the job-to-date quantities, costs, or man-hours are not zero, and you elect to hide the cost item, a message shows indicating that you cannot edit the setting, as shown in the following example.

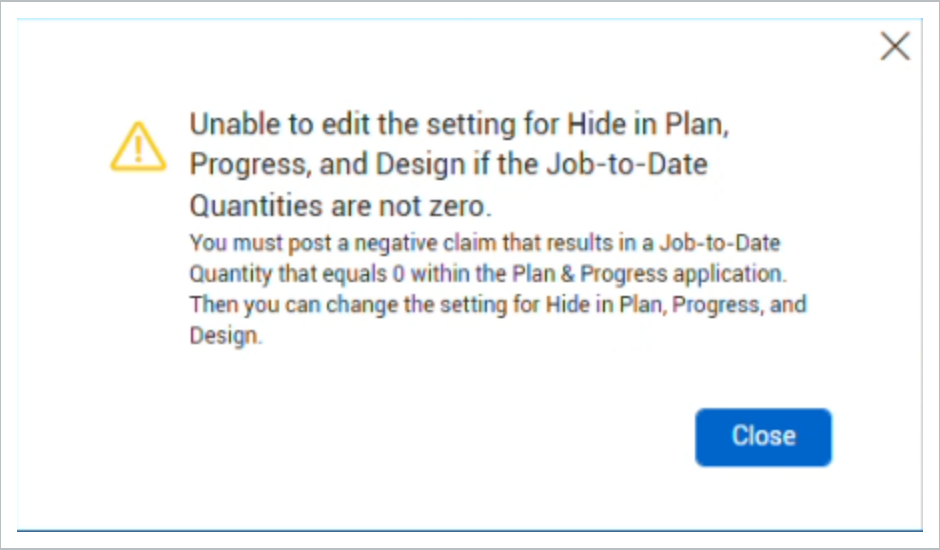


To select the setting, you must post a negative claim that will result in the quantities, costs, or man-hours to equal zero.

- You must have applicable Control permissions for Actuals in InEight Platform. For more information, see [Manage users](#).

3.5 COST ITEM EXCEL IMPORT

When you need to add multiple cost items to your project, adding them manually can be tedious and time consuming. To save time, if you can export your cost items to Microsoft Excel (e.g., export to Excel from your estimating software), you can import them into Control, allowing you to update your estimate in bulk, without needing to manually enter data into individual cells.

Click the **Import** icon on the right toolbar of the Control > **Workspaces** page to go access the Excel import feature.




The table below indicates the data you can import into Control from Excel.

Data Type	CBS Columns
Tasks	CBS position, Description, UoM, code-related fields, user-defined fields, other

Data Type	CBS Columns
	settings found in the Task details data block in Control.
Schedule	Schedule ID, schedule dates, Scheduled, Schedule plug days, Plug days, Cost curve, Roll up schedule
Current Estimate	CE final MHrs, final costs, total equipment hours, MHr/Unit, units/MHr, equipment hour/unit, labor cost/MHr, equipment cost/MHr, Secondary Qty, Scales 1, 2, and 3.
Cost Categories	Total and unit costs.

When you click on the **Import** icon on the CBS tab of the Workspaces page, you have three import type options. You can import cost items, actuals, or a schedule.

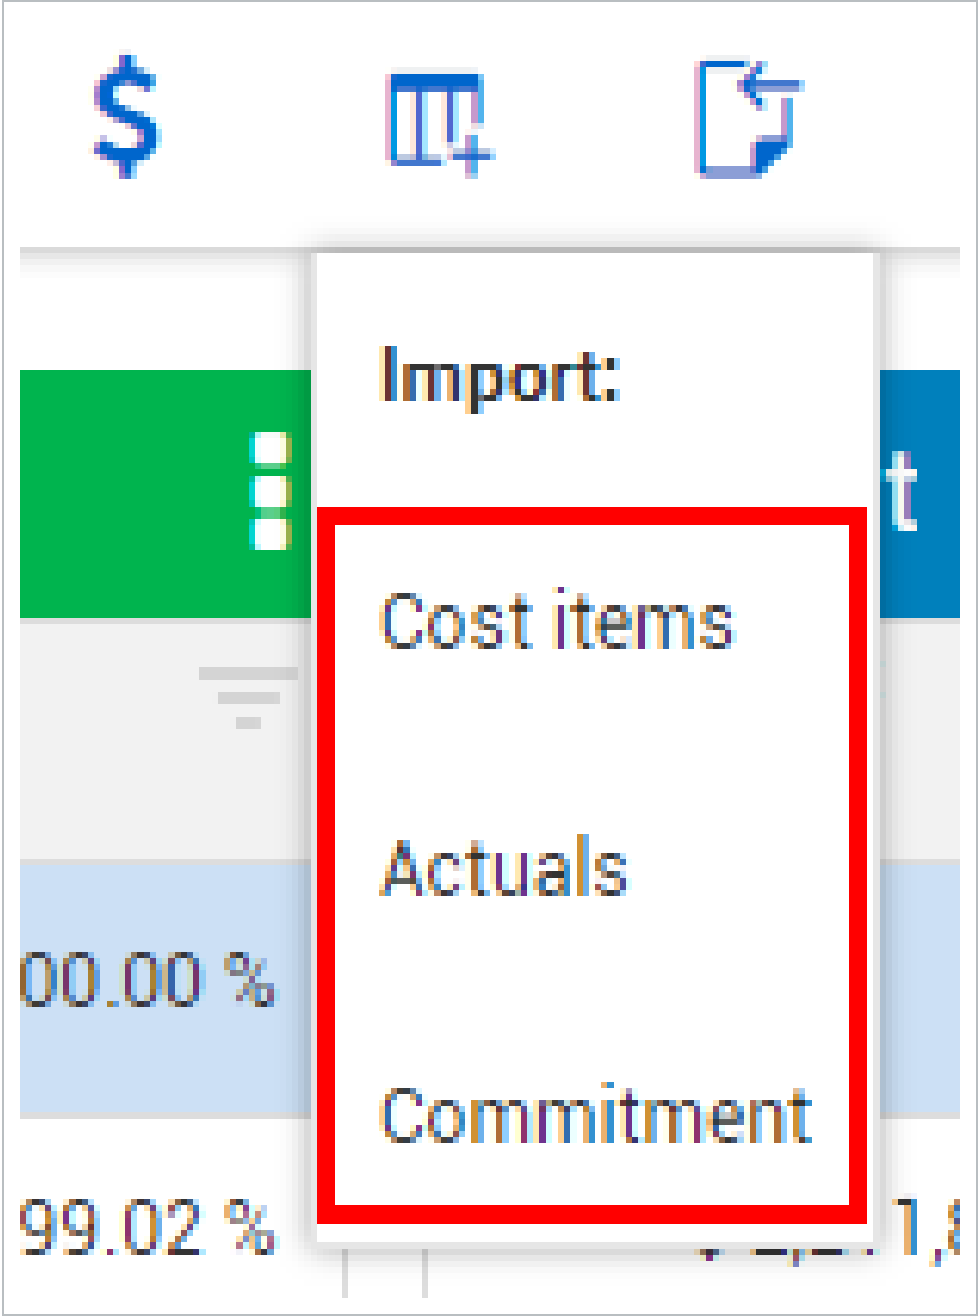

After you make a selection, the Import CBS data window opens.

Overview - Import CBS Dialog box

Title		Description
1	Import from Excel	You can either drag and drop or browse to the file to import. Microsoft Excel files (.xlsx,, .xls) and Comma Separated Value (.csv) files can be

Overview - Import CBS Dialog box (continued)

Title		Description
		imported.
2	Options	You can add new cost items and update cost items that already exist in the project, choose to only update existing cost items, or only add new.
3	Cost item matching criteria	When adding and updating cost items, the structure in the spreadsheet you are importing from may be in a different order than the structure in Control. By specifying a code for matching your cost items, the import routine will know which cost items in the spreadsheet are new when adding new items, and which cost items to update with data from the spreadsheet when updating cost items.
4	Information message	This information provides a description of available functionality and instructions for proceeding to the next step.

Import CBS data

1

Import from Excel (.xlsx, .xls) or Comma separated value (.csv)

Drag and drop the file here

or browse

Browse

Options

2

* Import type

Cost items and cost item attributes

☒ Update existing and new items

Cost item matching criteria

WBS phase code

3

☐ Update existing items

☐ New items

4

i

Once the import file is read, Cost item match options and field mapping can be specified. Mapping uses row 1 headers from the source document. New cost items are inserted to the bottom of the CBS.

Clicking Next opens the Map columns dialog box, where you can map your Excel columns to the appropriate column in Control.

Overview - Map Columns Window

Title		Description
1	Template	After you map the import file columns to the CBS columns in Control, you can save your settings as a template for future use. This is helpful when you need to make scope changes or updates on a regular basis.
2	Control field	The names of the column headers in Control that you can map your data to.
3	Mapped	A green checkmark indicates the column in your import file is mapped

Overview - Map Columns Window (continued)

Title		Description
		correctly to the CBS column. The Green key indicates the matching code you specified is locked.
4	File columns	The names of the column headers in your import file that you can map to the CBS columns in Control.

1

Template

Unsaved template

Control field	2	Mapped	3	File columns	4
Cost segment				Blank-do not import	
Description			✓	Description	
Optional code				Blank-do not import	
WBS phase code				Blank-do not import	
Allow as-built				Blank-do not import	
CBS position			✓	CBS Position	
UoM				Blank-do not import	

* Required fields

Reset

Cancel

Back

Next

3.5.1 Forecast Excel Import

When manually importing cost items by either updating existing cost items or importing new cost items, you can also import forecast values via Excel. How the fields are mapped in Excel determines which CBS forecast columns are populated.

Examples of some forecast columns that can be mapped via the Excel CBS import cost item process include, Forecast total cost, Forecast total MHrs, and Forecast total unit cost. Cost categories can also be selected for importing into Control.

Import CBS data - ALL PERMISSION LC_12102021054633.xlsx

Map columns

Template

Unsaved template

Control field	Mapped	File columns
Live Forecast		
Forecast method		Blank-do not import
Forecast total Cost		Blank-do not import
Forecast total Mhrs		Blank-do not import
Forecast total Mhr/Unit		Blank-do not import
Forecast total productivity		Blank-do not import
Forecast total unit cost		Blank-do not import
Forecast remaining cost		Blank-do not import
Forecast remaining Mhrs		Blank-do not import

* Required fields

Reset

Cancel

Back

Next

3.5.2 Spreadsheet Rules

For the import process to work correctly, the items in your Excel spreadsheet must be formatted in a certain way so that Control can recognize the items. The following table indicates important spreadsheet rules to follow to make sure your data imports successfully.

Attribute	Rules
Import function	Reads the first worksheet within the referenced workbook.
First row of data	Considered to be the header row of the data. This imports as titles which are referenced during the mapping process. The import stops reading headers if it encounters a blank header cell.
Numbers	Needs to be the actual number, and not the summation of cells. Values cannot contain the \$ symbol or other currency symbols.
Second row of data	Considered the first row of data to be imported.

If you make changes in the spreadsheet, you must save the spreadsheet before importing (only saved data will be imported).

Below is a list of items to be aware of during the population of the import template.

1. The Excel file should not be open while simultaneously using the import wizard.
 - a. If there are any edits made to the spreadsheet, it must be saved and closed prior to importing.
2. CBS positions cannot be duplicates. They must be unique to each cost item.
 - a. The system will show an error if there are any duplicates.
3. The WBS phase codes are not required during the import but must also be unique per cost item.
4. Cost categories are spelling and case sensitive, and must match directly to the cost categories spelling.
 - a. The cost categories list can be exported from the import wizard.
5. The Excel sheet cannot contain any blank cells during the import. Blank cells show an error and cause the import to stall.
6. Make sure any blank columns from an export file are removed before importing again.
7. Date formats must match spreadsheet date formats. The Import Wizard will prompt you to chose a date format used in the spreadsheet.
 - a. The Import wizard will prompt you to chose a date format prior to initiating the import.

3.5.3 Best Practices and Recommendations

1. Use WBS phase code as the matching criteria for updating existing items.
 - a. WBS phase code are tied 1:1 for each cost item. The CBS position can be changed, but the WBS phase code remains the same regardless of CBS position.
2. Set up the views for exporting of data to match the import template created. Views are customizable for flexibility in what is being imported/exported.
3. Import template mapping is unique to each individual user. Master mapping cannot be set at a global level. It is recommended to provide users with a step-by-step import mapping document to set up data mapping initially during the on-boarding of InEight.
4. When exporting data in Control, current system drops trailing zeros on CBS positions. Example: 1.10 exports as 1.1.
 - a. One way to get around this is opening data as a CSV file in Excel.
5. Once you have downloaded the export file, proceed to the following steps.
 - Open blank Excel sheet
 - Navigate to **Data** tab
 - Click **Get Data > From File > From Text/CSV**
 - Choose downloaded export file
 - Click **Import**
 - Click **Load**

Your data will now be imported into the sheet where updates are made. Once you have completed your updates, you may save and re-import the same file.

3.5.4 CBS Hierarchy

If you select CBS position as the matching criteria for the import, the import routine recognizes the hierarchy of your structure by the numbering of the codes.

A2				1.1.1.5
	A	B	C	
1	CBS position	Description	Forecast T/O qty	
2	1.1.1.5	Parent		1
3	1.1.1.5.1	Child 1		10
4	1.1.1.5.2	Child 2		1
5	1.1.1.5.2.1	Child 2.1		15
6	1.1.1.5.2.2	Child 2.2		20
7	1.1.1.5.3	Child 3		1

After the import is complete, if the CBS position for the new cost items match existing cost items in the CBS, your new CBS cost items will import as you have defined them. The existing CBS cost items will shift down and be relabeled to match the next corresponding number.

When adding new cost items to an existing CBS position, a warning message displays informing you the CBS positions you have picked already exist. The message then asks you to confirm if you would like to continue with this import.

3.5.4.1 CBS Predictive Hierarchy

New cost items created via the import process automatically adjust the CBS structure hierarchy to match your import as needed and predict the movements in the current hierarchy, and the hierarchy that is being added via the Excel import.

Tasks			
☐	CBS position	Description	WBS phase code
☐	1	A - Road materials	1000
☐	1.1	B - Rock	1001
☐	1.1.1	C - Mix	1002

For example, you have three cost items that you want to import, as shown below. Positions 1 and 1.1 already exist in the CBS, and position 2.1.2 is new.

	A	B
1	CBS position	Description
2	1	D - Maintenance
3	1.1	E - Equipment
4	2.1.2	F - Subcontracts

The import process imports Excel CBS positions 1 and 1.1, and places 2.1.2 at the bottom of the hierarchy.

Tasks			
☐	CBS position	Description	WBS phase code
☐	1	D - Maintenance	1003
☐	1.1	E - Equipment	1004
☐	2	A - Road materials	1000
☐	2.1	B - Rock	1001
☐	2.1.1	C - Mix	1002
☐	2.1.2	F - Subcontracts	1005

The following steps walk you through the import process.

The following steps are only applicable when importing new cost items.

Options


* Import type

Cost items and cost item attributes

- ☐ Update existing and new items
- ☐ Update existing items
- ☒ New items

Import CBS Data


1. From the Control > Workspaces page, on the CBS tab, click on the **Import** icon on the right toolbar.




2. Select **Cost Items** when the Import CBS data window appears.
3. Click on the **Browse** button to select a file to import.



4. Browse to the Excel file you wish to import.
 - The file and its location should be indicated by your instructor if you're in a classroom setting, otherwise you can select one of your own
5. Select the import file and click **Open**.

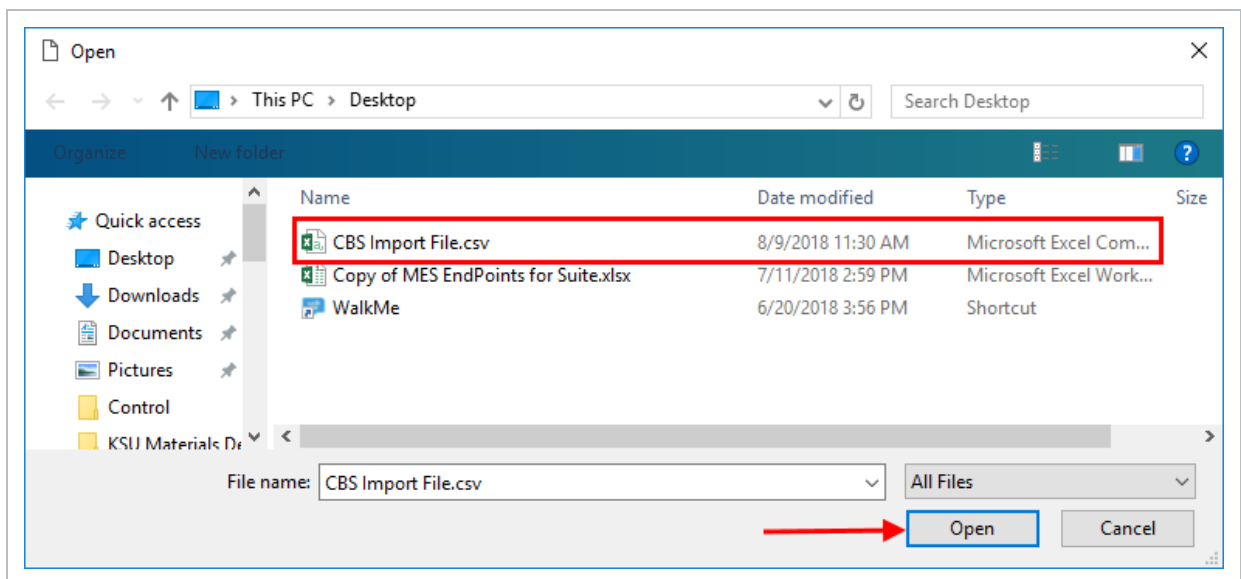

- The import file is now selected

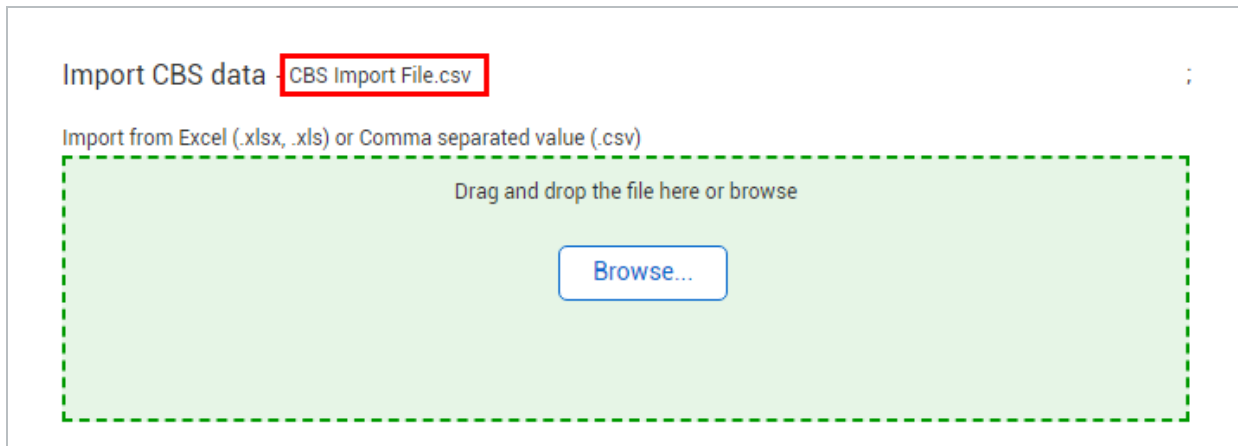


Import CBS data **CBS Import File.csv** ;

Import from Excel (.xlsx, .xls) or Comma separated value (.csv)

Drag and drop the file here or browse

Browse...

6. Under Options, select **New Items** (if not already selected).
7. For the Cost item matching criteria, select **Cost items and cost item attributes** from the drop-down list.

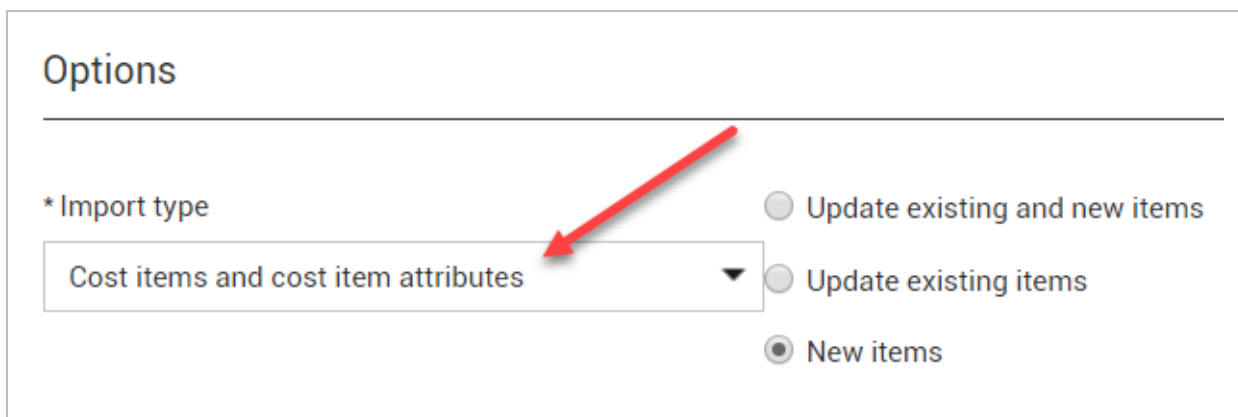

Options

* Import type

Cost items and cost item attributes ▼

☐ Update existing and new items

☐ Update existing items

☒ New items

8. Click **Next**.
 - This takes you to the **Map columns** window
 - Note that the File columns fields are set to **Blank-do not import by default**
9. Under File columns, click in the field on the same row as the UoM CBS column, then click again to expand the drop-down list for that field.

Map columns

Template

Unsaved template

Control field	Mapped	File columns
WBS phase code		Blank-do not import
Allow as-built		Blank-do not import
CBS position		Blank-do not import
UoM		Blank-do not import Blank-do not import CBS Position Description CE materials total cost CE subcontract total cost UOM

| Account code | | |
| Pay item assignment | | |

* Required fields

Reset

Cancel

10. Select UOM from the drop-down list to map the UOM column in the Excel file to the UoM CBS column.
11. Repeat the selection process to select the appropriate File columns to map to the following CBS columns:
- CBS position

• Description

• WBS Phase Code

• Forecast (T/O) quantity

• CE Final MHrs

• CE final cost

- A green check mark indicates successful mapping of your file columns

Import CBS data - cost item import.xlsx

Map columns

Template

Unsaved template

Control field ↑	Mapped	File columns
CE equipment cost/Hr		Blank-do not import
CE equipment-Hrs/Unit		Blank-do not import
CE final cost		Blank-do not import
CE final MHrs	✓	CE Final MHrs
CE final unit cost	✓	CE final cost
CE labor cost/MHr		Blank-do not import
CE MHrs/Unit		Blank-do not import

* Required fields

Reset

Cancel

Back

Next

12. To save these settings for future use, click in the Template field and type **Steel Structure Template**.

Map columns

Steel Structure Template

Order	Data type	CBS columns	Mapped	File columns
-------	-----------	-------------	--------	--------------


13. Click the **Save** icon to save the template.

Steel Structure Template


Order	Data type	CBS columns	Mapped	File columns
-------	-----------	-------------	--------	--------------

14. Click **Next**.

- A progress bar appears informing you the import is in progress




- A prompt appears, indicating the project will be disabled from use during the importing process

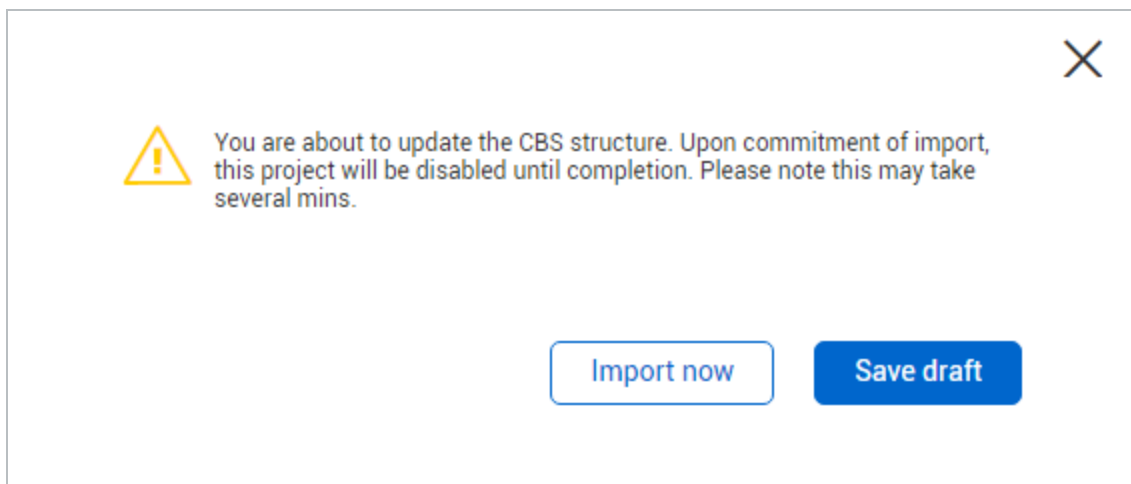


15. Click **Import now**.

- A prompt appears informing you that the project is currently locked for the importing process




- Once completed, you will receive the following prompt, informing you the data imported successfully

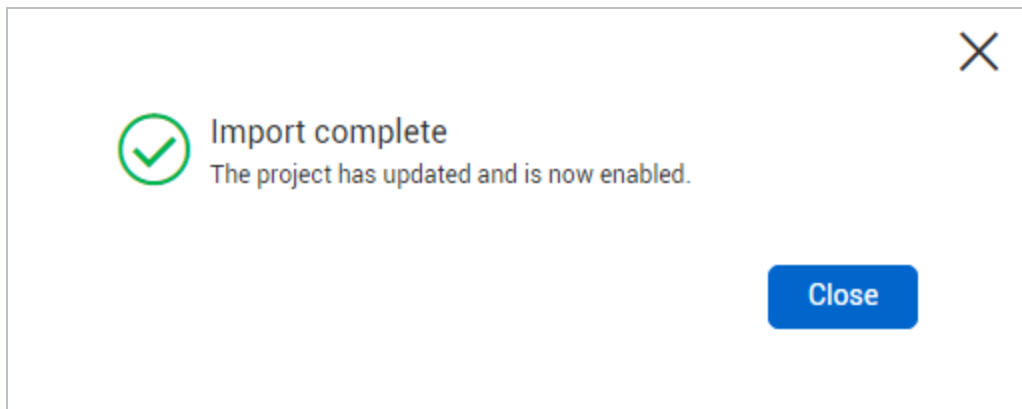

3.5.5 Resolving Import Errors

When conducting the import, you may run into errors. This will be indicated when you attend to run the import routine by the following prompt:

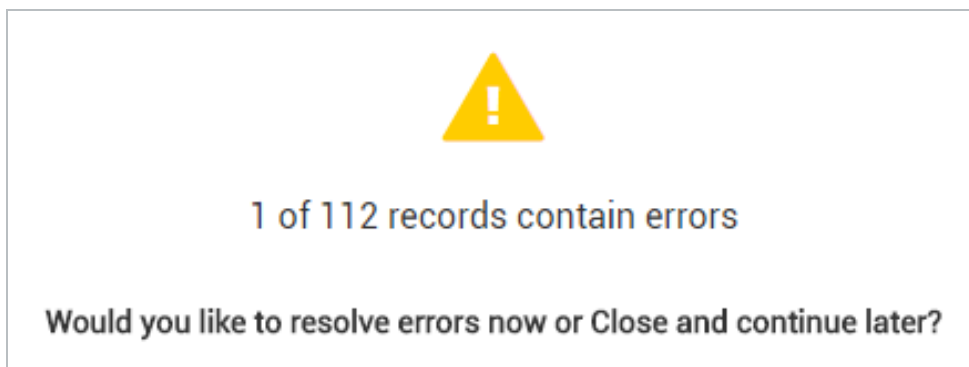

The prompt window includes a Review errors and items for import link, which you can click on to resolve any issues prior to final import. An error resolution page opens where you can identify and resolve your errors.

Audit log > Import history > CBS Import File.xlsx		Find previous error 1 errors remaini... Find next error		Cancel import	Import
Status Details (🔍 CBS position)		Import Columns ⚠️			
Import status	CBS match status	Import method	CBS position	Description	CE final Mhrs
Pending	No match found, new item	Add new items and upd...		Bolted Connections	1000
Pending	No match found, new item	Add new items and upd...		Module 01 - Erect Steel...	16000
Pending	No match found, new item	Add new items and upd...		Structural Steel	0
Pending	No match found, new item	Add new items and upd...		Structural Steel	0
Pending	No match found, new item	Add new items and upd...		Module 001 - Erect Ste...	0
Error	No match found, new item	Add new items and upd...		Structural Steel	0
Pending	No match found, new item	Add new items and upd...		Materials	0
Pending	No match found, new item	Add new items and upd...		Environment	0

There can be situations where the cost item Excel import process will successfully process some cost items, but fail to import other cost items. In this situation the process will show as failed. For example, you imported 100 cost items, and 90 of the cost items import successfully. There are 10 cost items that did not import successfully. In this scenario you would need to resolve the import errors.

3.5.6 Excel Import for committed cost

Importing committed cost mainly helps to keep track of subcontract cost items where you would have a purchase order that would drive all of your cost.


You can import two types of committed cost:

- Open/Remaining Committed Cost
- Total committed cost

Open/Remaining Committed Cost is the cost you still have left to pay on the purchase order. Total committed cost is the total purchase order amount for the purchase order.

Committed cost were previously located in different areas of Control. You can have Open and Total committed cost columns in your CBS. The same columns are also in the Commitments tab of the Actual Details Slideout where you can make manual edits to the committed costs. Columns in CBS for Open and Total committed costs only reflects the manual edits you made in the Actual Details Slideout. Open and Total committed costs are also shown in cost item details slideout cost categories tab.

You can import committed costs using the import icon on the CBS and selecting **Commitment**.

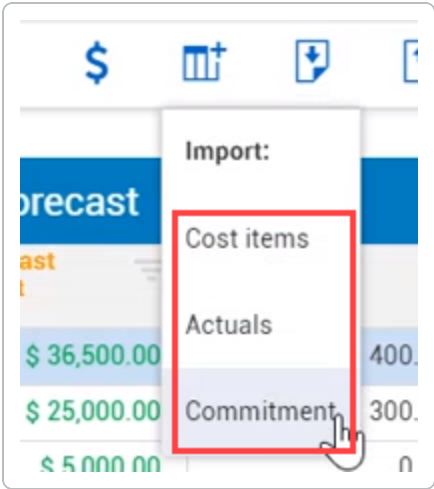

3.5.6.2 Generating the commitment cost Excel spreadsheet

To bring in committed cost from the excel import, you first need an existing value in your CBS that matches the Excel Spreadsheet value. This can be one of two options:

- WBS phase code
- CBS position

You will also need the **Type** of committed cost you want to import, either Open/Remaining Committed Cost or Total commitment.

Type					
	A	B	C	D	E
1	WBS phase code		Cost	Category	Type
2	1003		100	Undefined	Open commitment
3	1003		100	Undefined	Total commitment
4	1004		450	Undefined labor	Open commitment
5	1004		750	Undefined labor	Total commitment

Open/Remaining Committed Cost and Total commitment types need to be spelled exactly word for word as it is written in the screenshot. If you shorten any of the wording in the Type column, the system will not accept the import and you will receive an error.

Each Type of committed cost has to be its own line item on the Excel spreadsheet. You can do multiple transactions for one cost item, but only one commitment type per line item. If they are different types, you need to separate them out into different line items.

	A	B	C	D	E	F
1	WBS phase code		Cost	Category	Type	
2	1003		100	Undefined	Open commitment	
3	1003		100	Undefined	Total commitment	
4	1003		100	Undefined labor	Total commitment	
5	1004		450	Undefined labor	Open commitment	
6	1004		750	Undefined labor	Total commitment	

Each column needs to be created and defined if you are to do a Commitment Excel Import. You must include a Cost column and a Category column as shown in the above image.


Open/Remaining Committed Cost should never be greater than your total. Open/Remaining Committed Cost cost should either be equal or less than the Total commitment cost.

3.5.6.3 Importing commitment data


Follow the step by step to Import commitment data.

Import Commitment Costs


1. From Control's CBS tab, select the import icon. Then select **Commitment**.

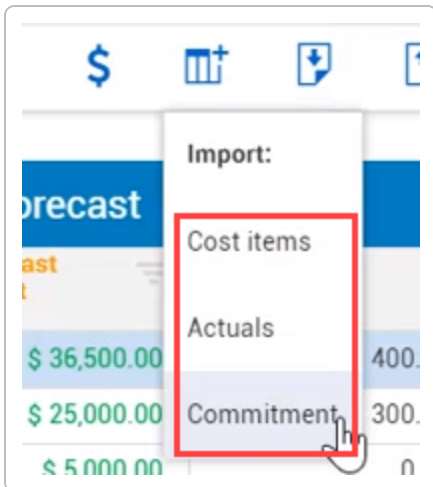


2. After you have created your Excel spreadsheet with your commitment costs, select **Browse** from the Import from Excel window. Then select the Excel file name you saved.
3. After you return to the Import commitment data window, under the Options section, select the **Import type** drop down arrow. If it is not already selected, select the **Commitment values** option.

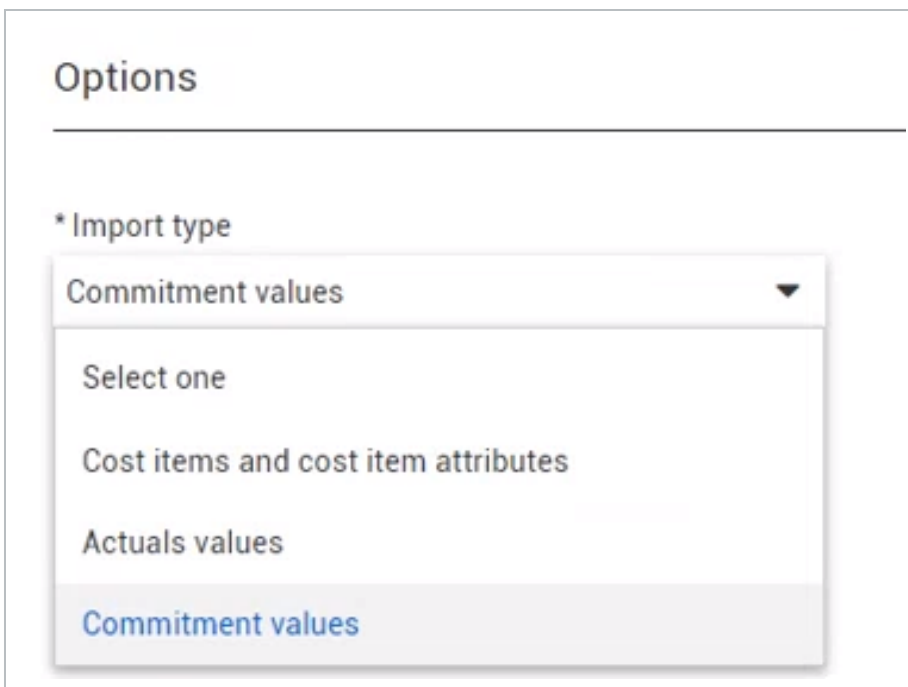

- 4. Select the Cost item matching criteria drop down and choose either WBS phase code or CBS position.

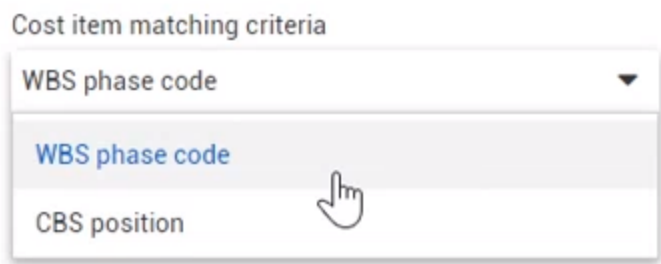

- 5. After selecting the drop down options, select **Next** in the bottom right corner.
- 6. From the Map columns screen, select the columns you are importing from your Excel spreadsheet.

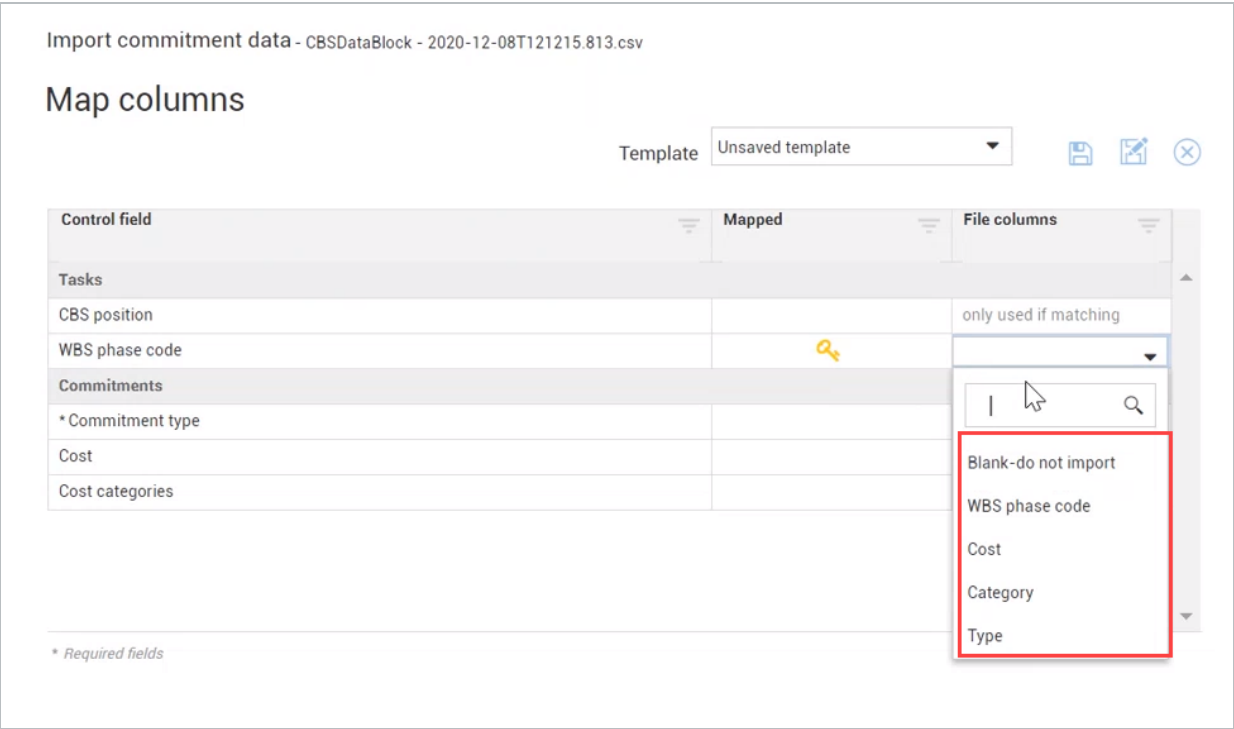

- 7. The Control field should match the File columns. For example, Commitment type in Control field should match Type in File columns as shown below. Once done, select **Next**.

Map columns

Template

Unsaved template

Control field	Mapped	File columns
Tasks		
CBS position		only used if matching
WBS phase code	🔑	WBS phase code
Commitments		
* Commitment type	✓	Type
Cost	✓	Cost
Cost categories	✓	Category

* Required fields

8. If there are no errors in the mapping stage, you should see a green check mark on the next screen, indicating everything is ready to be imported.

Document contains no errors

5 record(s) ready for import

Select next to continue with import steps.

If you receive any errors in the mapping stage, you will receive an error with a download option to download a word document that shows you all the errors.

Import commitments CBS data: CBSDataBlock - 2020-12-08T121215.813.csv
File Import attempted on: 12/8/2020 9:04:55 PM

The following errors were detected while attempting to import commitment values into control.
Review the errors below, once all the errors have been resolved, reattempt the import to Control.

Error 1: Invalid commitment type. (this error affects 2 WBS/CBS items out of 2 total attempted imported WBS/CBS items and 4 rows out of 4 total attempted imported rows)

WBS: 1003
CBS: 1.3
Row: 1, 2

WBS: 1004
CBS: 1.4
Row: 3, 4

9. Click **Next** and then select **Import now**. This will create a line item in the Import history section of the Audit Log tab.
10. From Control, go to the Audit Log tab. Then select **Import history**. Hover over the yellow triangle to view the information on the pending import item.

Actions

CBS

ACS

Pay items

Integration

Import history

Pending

0 of 5 line items contain errors

Continue Import

Cancel

		Status
		Pe...
		Pe...
		Failed ...
	CBSDataBloc...	Commitment
	CBSDataBloc...	Commitment
	CBSDataBloc...	Commitment
		Complete

After the pending import is Complete, the committed costs populate in the Cost Categories Details tab, as well as the CBS. If the costs also appear in the Commitments tab from the Actuals Details Slideout and populates into the new Open and Total cost committed columns.


If the imported commitment costs fail to import, the Audit Log Import history would show that the import failed completely.

This page intentionally left blank.

CHAPTER 4 – COST ITEM MANAGEMENT

4.1 Cost item management workflow	150
4.2 Estimate Resources	150
4.2.1 Navigate to Estimate Resources	152
4.2.2 Manage estimate resources	154
4.2.3 Resource rates	155
4.2.4 Add estimate resources to a job	155
4.2.5 Data columns	157
4.3 Cost item details	159
4.4 Cost item details overview	159
4.5 Details tab	159
4.5.1 Pay item contribute quantity	162
4.6 Attributes tab	164
4.7 Cost categories tab	165
4.8 Current Estimate Resources tab	167
4.8.1 Cost Driver	169
4.8.2 Productivity and overall settings	173
4.9 Forecast Resources tab	177
4.9.1 Productivity and overall settings	179
4.9.2 Resource Details	180
4.9.3 Cost Item Man-Hours	182
4.10 Issue tagging in the CBS	183
4.11 Lock Budget	186
4.11.1 Budgets vs Estimate	186
4.11.2 Lock Budget and Price	188
4.11.3 Unlock Budget and Price	190
4.12 Assigned vendors	191

4.1 COST ITEM MANAGEMENT WORKFLOW

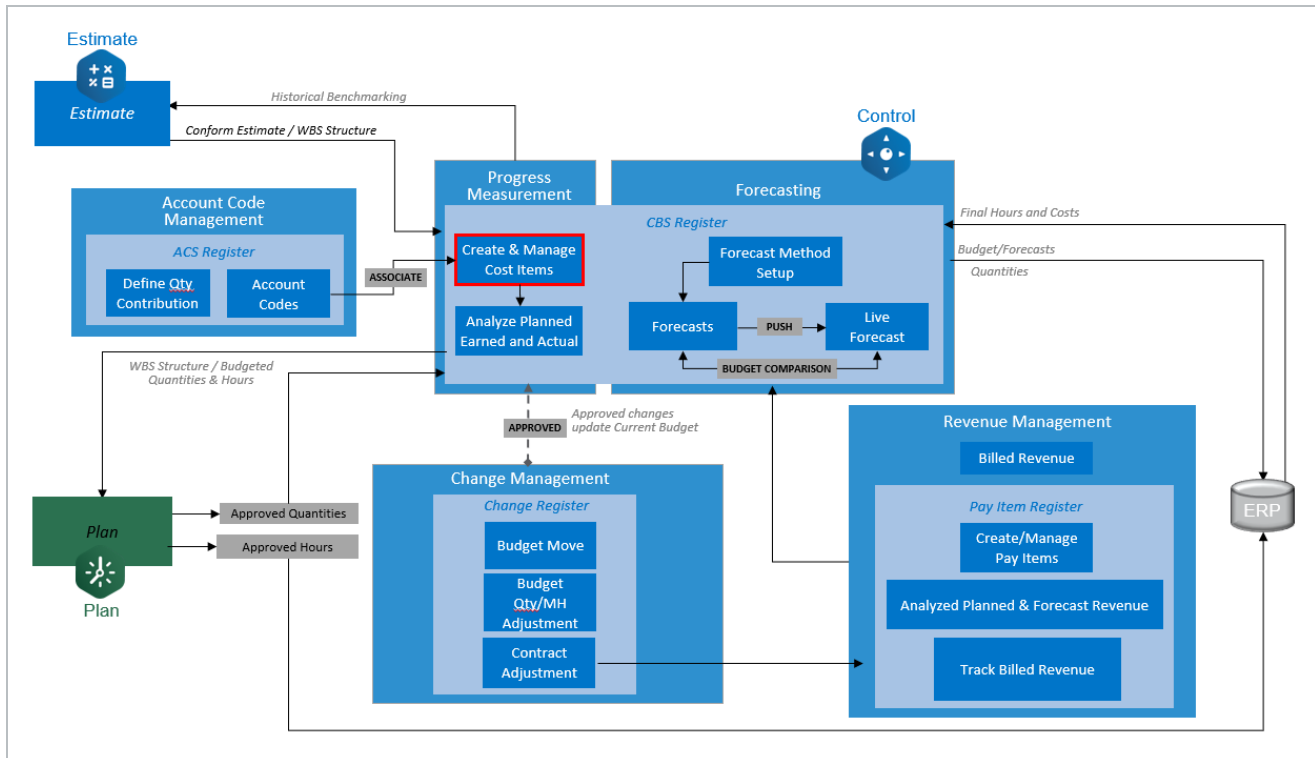

4.2 ESTIMATE RESOURCES

InEight Control refers to labor, equipment, materials, installed equipment, and supplies as resources. These resources are used as the basic building blocks for detailing the estimated costs which create your budget.

The Project library includes all resources used to estimate costs for the cost items in the cost breakdown structure (CBS).

Steel Structure Training Job 2... / Control / Project library

ESTIMATE RESOURCES

Labor		Resource code	Description
Construction equipment	☐	1.C.01.1.05	Laborer
Rented construction equipment	☐	1.C.01.1.06	Crane Operator
Installed material	☐	1.C.01.1.07	Civil Operator
Installed equipment	☐	1.C.04.1.02	Concrete Foreman
Supplies	☐	1.C.04.1.03	Concrete Journeyman
Unique	☐	1.C.04.1.04	Concrete Apprentice
	☐	1.C.05.1.02	Ironworker Foreman
	☐	1.C.05.1.03	Ironworker Journeyman
	☐	1.C.05.1.04	Ironworker Apprentice
	☐	1.C.05.1.08	Civil Foreman
	☐	1.C.05.1.09	Civil Journeyman
	☐	1.C.05.1.23	Civil Apprentice
	☐	L001	General Labor
	☐	LWLBJ	Welder Journeyman

Most of the CBS cost detail is imported directly from InEight Estimate, but you might need to create additional cost item detail for conforming your budget and creating change orders.

Estimate resources in the Project library are organized into seven resource types:


Resource	Description
Labor	Human resources that perform the work, classified by trade (e.g., pipefitters,

Resource	Description
	electricians, iron workers).
Construction Equipment	Owned construction equipment.
Rented Construction Equipment	Construction equipment rented from a third party.
Installed Material	Materials that remains installed on site after the project is completed, (e.g., concrete, piping, aggregate).
Installed Equipment	Equipment that remains installed on site after the project is completed, (e.g., boilers, heat exchangers, vessels, cooling towers).
Supplies	Expendable items that are not permanently installed (e.g., small tools, consumables).
Unique	Resources of a unique nature which cannot be associated with other resource types (e.g., dump fees, hauling charges and equipment rented by the month, and subcontracted work).


Estimate resources are the equivalent of the Resource Rate Register in InEight Estimate.

4.2.1 Navigate to Estimate Resources

To access the Estimate resources page, go to the project home page, and then click **Project library**. The Project library page opens and shows the **Estimate Resources** tab.

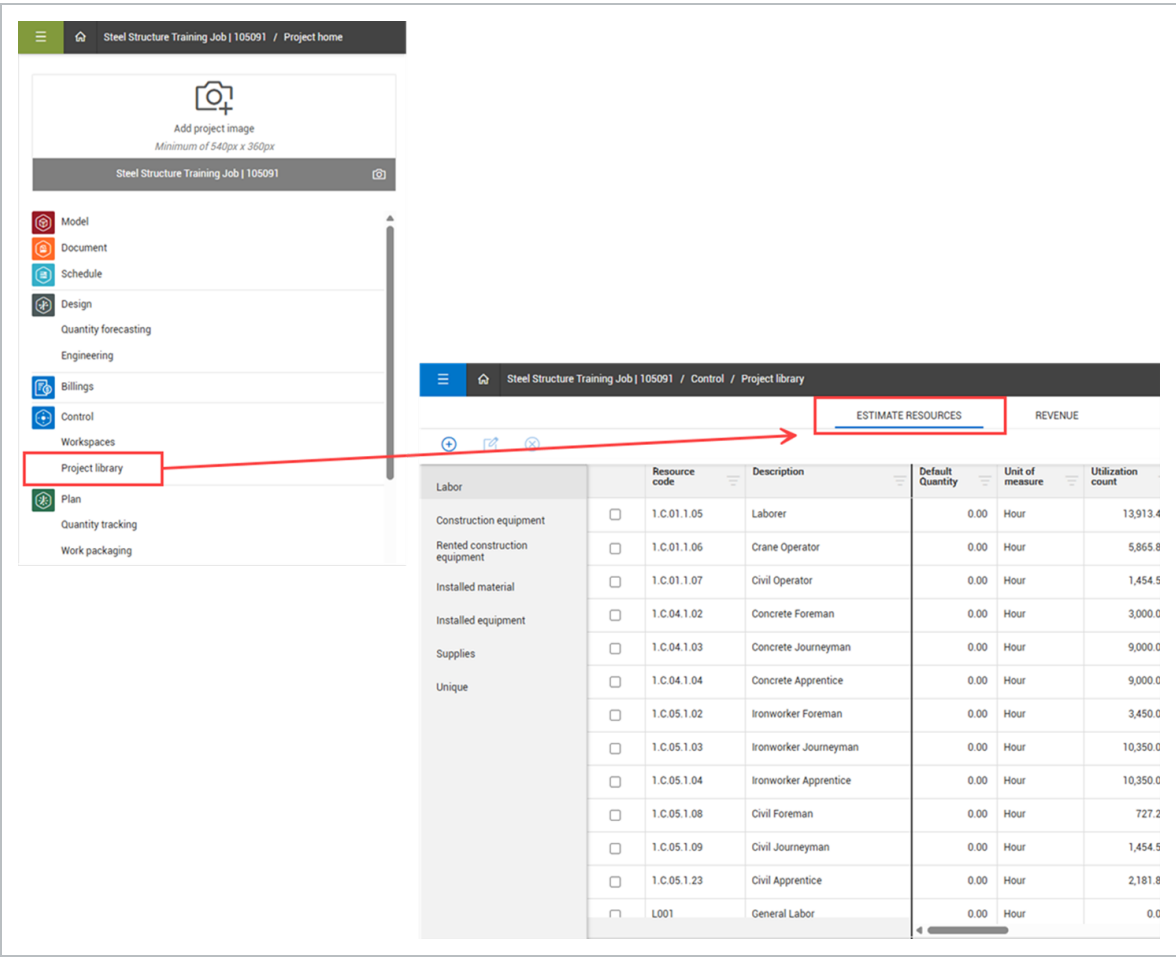


You can also access Estimate Resources from the CBS page. In the CBS page, select a line item and then hover over the resource number in the Resources column of the Task details data block. In the Resource Summary dialog box, click **Resource library** to open the Project library.

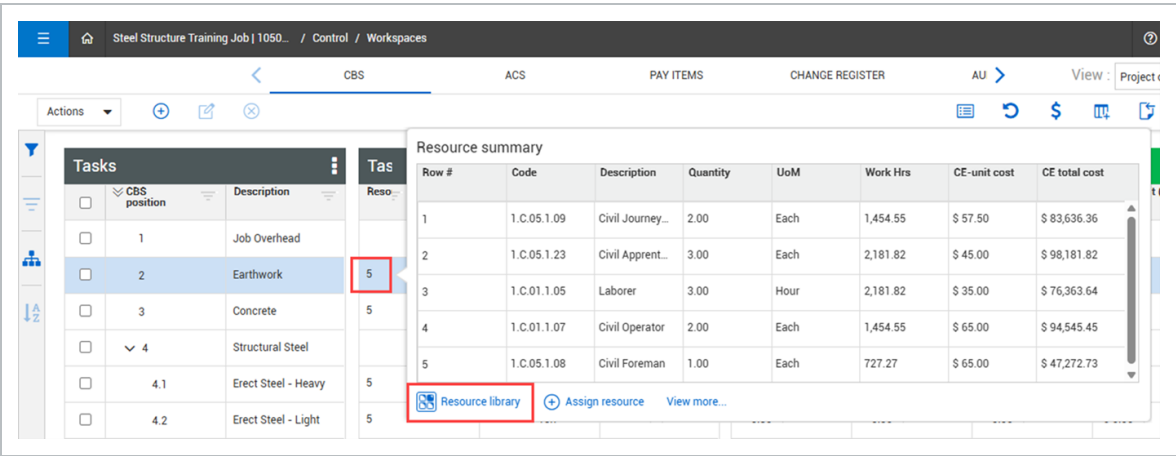


4.2.2 Manage estimate resources

You can manage estimate resources by adding, deleting, or editing estimate resources.

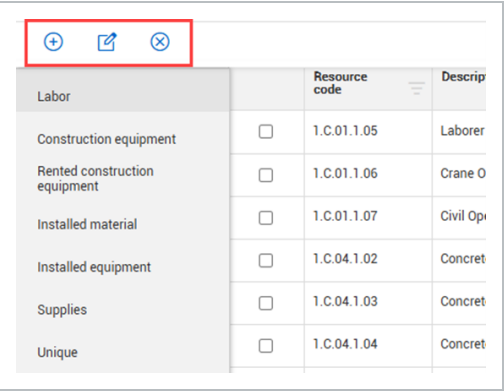

To add an estimate resource to the Estimate Resources library, you must first choose the resource type in the left-side section (Labor, Construction equipment, etc.), and then click the **Add estimate resource** icon. In the Add estimate resource dialog box, enter the applicable required and optional resource data, and then click **Add** to add the estimate resource.

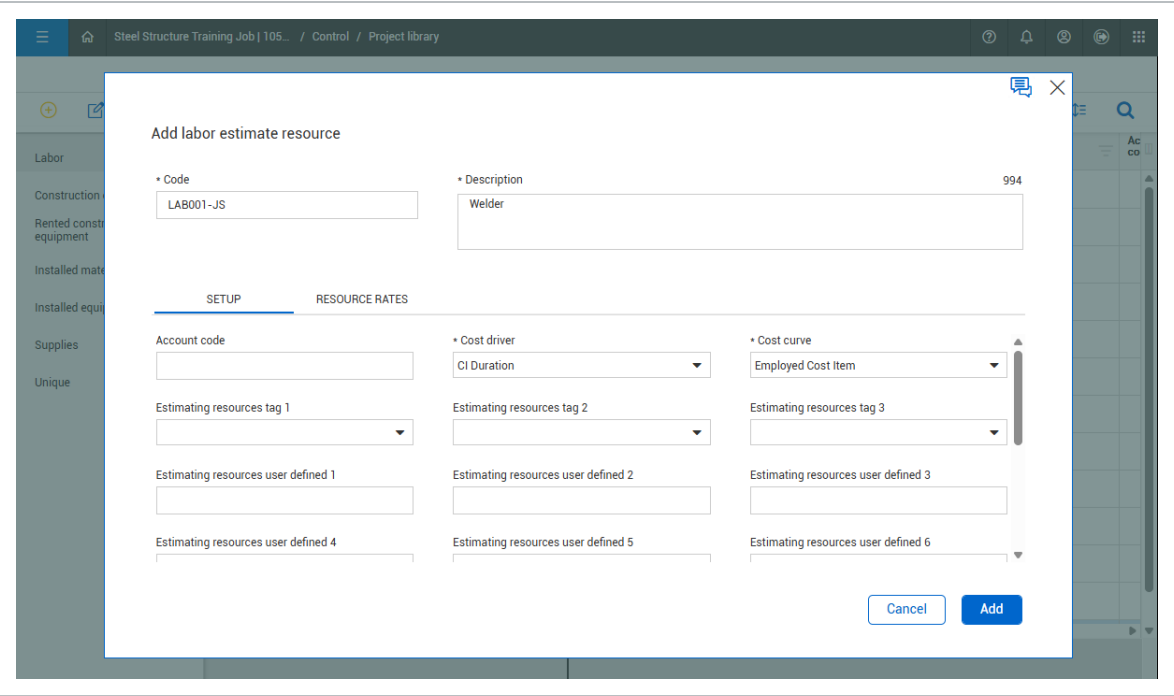

You can add your own notes to review later and to communicate with other users information about the estimate resource. Click the **Show notes** icon at the top right to open the Conversation notes and add additional notes.

To edit or delete an estimate resource, select the estimate resource, and then click the **Edit estimate resource** or **Delete estimate resource** icon. If an estimate resource has been assigned to a project, it cannot be deleted.

4.2.3 Resource rates

In the Resource Rates tab, you can import, modify, and add billable rates to estimate resources. This is particularly helpful for time and material or cost plus contracts to drive accurate invoicing.

Resource billing rates are also used for Forecast final revenue, as it will rely on the billing rates of the resources on the cost items that are assigned to pay items. These values generate revenue forecast for cost items that are associated to a cost plus or time and material (billing method) pay item.

Add labor estimate resource

* Code

LAB001-JS

* Description

Welder

994

SETUP

RESOURCE RATES

Billing rate	\$ 50.00	\$ 0.00	\$ 0.00
Billing rate markup	\$ 50.00	\$ 0.00	\$ 0.00
Billing rate markup %	0.00 %	0.00 %	0.00 %
Charge rate	\$ 50.00	\$ 0.00	\$ 0.00

Cancel


Add

4.2.4 Add estimate resources to a job

After resources are created, you can add them to a job.

Add estimate resources

- 1. Go to Workspaces > **CBS** register.
- 2. Right-click a cost item, and then in the context menu, select **Cost item details**.
- 3. On the Cost item details slide-out, select the **Current Estimate Resources** tab.
- 4. Expand the Current estimate resources section, and then click the **Add resource** button.

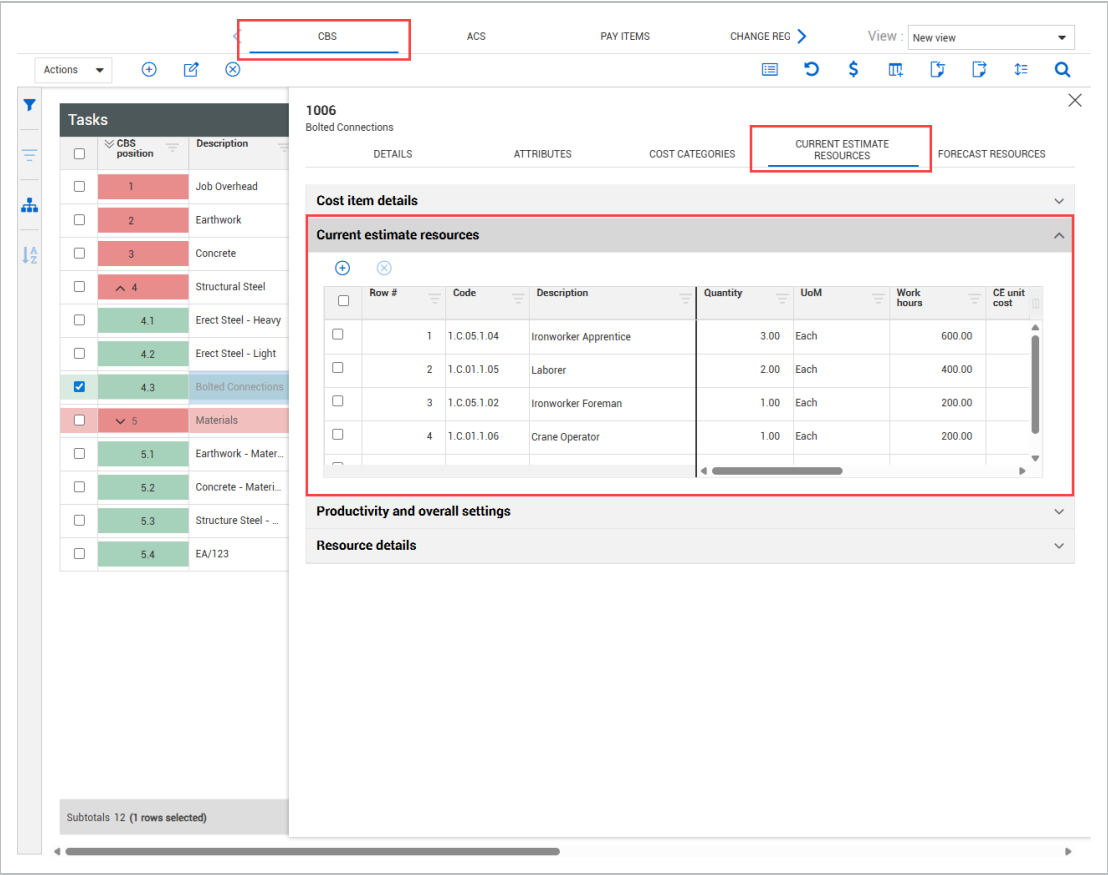

- 5. In the Add a resource dialog box, select the resources to add to the cost item, and then click **Add**.

Add a resource

LABOR

CONSTRUCTION EQUIPMENT

RENTED CONSTRUCTION EQ...

INSTALLED MATERIAL

INSTALLED EQUIPMENT

SUPPLIES

UNIQUE

Search...

☐	Resource code	Description	Default Quantity	Unit of measure	Utilization count	C E-unit cost (Scale 1)	Cost driver
☐	1.C.01.1.07	Civil Operator	0.00	Hour	1,454.55	\$ 65.00	Cl Duration
☐	1.C.04.1.02	Concrete Foreman	0.00	Hour	3,000.00	\$ 65.00	Cl Duration
☐	1.C.04.1.03	Concrete Journey...	0.00	Hour	9,000.00	\$ 55.00	Cl Duration
☐	1.C.04.1.04	Concrete Apprentice	0.00	Hour	9,000.00	\$ 45.00	Cl Duration
☒	1.C.05.1.02	Ironworker Foreman	0.00	Hour	600.00	\$ 65.00	Cl Duration
☒	1.C.05.1.03	Ironworker Journe...	0.00	Hour	1,800.00	\$ 55.00	Cl Duration
☐	1.C.05.1.04	Ironworker Appren...	0.00	Hour	1,800.00	\$ 45.00	Cl Duration
☐	1.C.05.1.08	Civil Foreman	0.00	Hour	727.27	\$ 65.00	Cl Duration
☐	1.C.05.1.09	Civil Journeyman	0.00	Hour	1,454.55	\$ 57.50	Cl Duration
☐	1.C.05.1.23	Civil Apprentice	0.00	Hour	2,181.82	\$ 45.00	Cl Duration
☒	L001	General Labor	0.00	Hour	0.00	\$ 50.00	Cl Duration

3 items selected

Cancel

Add

4.2.5 Data columns

You can view, add, and remove columns on the Estimate Resources page. To view all available columns, click the **Column chooser** icon at the right of the column headers. In the Column chooser, you can select and deselect columns from your view.

The following image and table show key columns available in the Resource library.

Steel Structure Training Job | 105... / Control / Project library

ESTIMATE RESOURCESREVENUE

Labor		Resource code	Description	Default Quantity	Unit of measure	Utilization count	C E-unit cost (Scale 1)	Cost driver	Account code
Construction equipment	☐	1.C.01.1.05	Laborer	0.00	Hour	13,913.42	135.00	Cl Duration	
Rented construction equipment	☐	1.C.01.1.06	Crane Operator	0.00	Hour	5,865.80	210.00	Cl Duration	
Installed material	☐	1.C.01.1.07	Civil Operator	0.00	Hour	1,454.55	210.00	Cl Duration	
Installed equipment	☐	1.C.04.1.02	Concrete Foreman	0.00	Hour	3,000.00	210.00	Cl Duration	
Supplies	☐	1.C.04.1.03	Concrete Journeyman	0.00	Hour	9,000.00	180.00	Cl Duration	
Unique	☐	1.C.04.1.04	Concrete Apprentice	0.00	Hour	9,000.00	150.00	Cl Duration	
	☐	1.C.05.1.02	Ironworker Foreman	0.00	Hour	3,450.00	210.00	Cl Duration	
	☐	1.C.05.1.03	Ironworker Journeyman	0.00	Hour	10,350.00	180.00	Cl Duration	
	☐	1.C.05.1.04	Ironworker Apprentice	0.00	Hour	10,350.00	150.00	Cl Duration	
	☐	1.C.05.1.08	Civil Foreman	0.00	Hour	727.27	210.00	Cl Duration	
	☐	1.C.05.1.09	Civil Journeyman	0.00	Hour	1,454.55	188.00	Cl Duration	
	☐	1.C.05.1.23	Civil Apprentice	0.00	Hour	2,181.82	150.00	Cl Duration	


Column	Description
Resource code	Alphanumeric label to quickly identify resources.
Description	Additional label to provide more resource detail.
Default Quantity	The quantity the resource will have by default when it is assigned to a cost item.
Unit of measure	The unit the resource is measured by.
Utilization count	The number of units of that resource being used in the project.
C E -Unit cost (Scale 1)	The resource's rate per unit.
Cost driver	Shows what drives the cost for that resource when it is assigned to a cost item (cost, quantity, or fixed).
Account code	Code assigned to resources for accounting and benchmarking purposes.

4.3 COST ITEM DETAILS

4.4 COST ITEM DETAILS OVERVIEW

The cost item detail slide out panel contains many different fields to edit and enter cost item-related information. To access the cost item slide-out panel, select the cost item, and then right-click the selected cost item. In the context menu, select **Cost item details**. In the Cost item details slide-out, there are four tabs to select from:

- Details tab
- Attributes tab
- Cost Categories tab
- Current Estimate Resources
- Forecast Resources tab



All editable cells in the cost item detail slide-out panel are single click.

4.5 DETAILS TAB

The Details tab contains the values and settings related to the cost detail of the item.

1069
Earthwork

DETAILS

ATTRIBUTES

COST CATEGORIES

CURRENT ESTIMATE
RESOURCES

FORECAST RESOURCES

Forecast T/O qty

UoM

CE unit cost

CE total cost

CBS position

10,000.00

CY

\$ 40.00

\$ 400,000.00

2

Last changed on

Last changed by

07/02/2025 06:51 AM

InEight Service Account

Description

Earthwork

Account code

51

* Cost source

Detail

* Forecast T/O qty

10,000.00

* UoM

CY

⊕ Live forecast method

Current estimate

CE total cost

\$ 400,000.00

CE unit cost

\$ 40.00

Average performance settings

CE total MHrs

8,000.00

CE total equipment Hrs

0.00

CE labor cost/MHrs

\$ 50.00

CE MHR/Unit

0.80

CE Units/MHrs

1.25

* Cost segment

Direct Cost

* Allow as-built

All

Pay item assignment

001

* Currency

USD \$

☐ As-built lock

* Quantity driver

☐ CBS contribute qty

☐ Hide in Plan, Progress, and Design

☐ Pay item contribute qty

Below is an explanation of some of the key settings on the Details tab.


Term	Function
Cost source	Indicates how costs are entered on the cost item. • Detail - Resources and duration defined to determine costs • Plug - Unit and total costs entered at the cost category level
Live Forecast method	Determines the Forecast Method for the cost item. For more information, see Forecasting overview .
Cost segment	Categorizes whether the cost item is a direct or indirect cost. • Direct Cost - costs that directly pertain to the deliverables (pay items) of

Term	Function
	the job • Job Overhead - Overhead costs associated with running and managing the job (e.g., management, jobsite facilities) • Business Overhead - Overhead costs associated with running the business (not directly related to running the job) • Subcontract - subcontract associated costs
Allow as-built	Determines whether you can enter actual costs and quantities for a cost item. • None - Cost item does not accept cost or quantities. This is typically seen in Superior cost items • All - Allows a cost item to accept both direct costs and quantities • Quantities - Cost item only accepts quantities • Cost - Cost item only accepts costs, man hours, and equipment hours.
Quantity driver	Superior cost item will have the Forecast T/O qty update when the superior cost item (parent cost item) receives an update. The change to the qty will be the original value multiplied by the same multiplier that was applied to the superior cost item. For example: if the superior cost item qty doubles, the item with Superior CI will double as well. Cost items with Fixed as the selection will not be affected by changes to the parent cost item.
Cost item contribute quantity	Checked cost items will have the Forecast T/O qty roll-up to the parent cost item if the UoM on both of the items are the same.
Hide in Plan, Progress, and Design	Select this feature to make the cost item unavailable for claiming in InEight Plan, Progress, and Design. For more information, see Hide in Plan, Progress, and Design.
Pay item contribute quantity	Checking this box lets you choose which cost items contribute to the Pay item's forecast (T/O) quantity and can affect earnings rules for the associated pay item. This field is only visible if you have the Enable Pay item Forecast (T/O) quantity rollups setting turned on in Settings > Control > Revenue.

4.5.1 Pay item contribute quantity

The Pay item contribute qty function works only when the Pay item Forecast (T/O) qty rollups toggle is set to *On* in Settings > Control > **Revenue**. If you have a unit price pay item, its forecast (T/O) quantity is the sum of all the contributing cost items forecast (T/O) quantities.

This function lets you define which cost items roll up their quantities to a pay item.

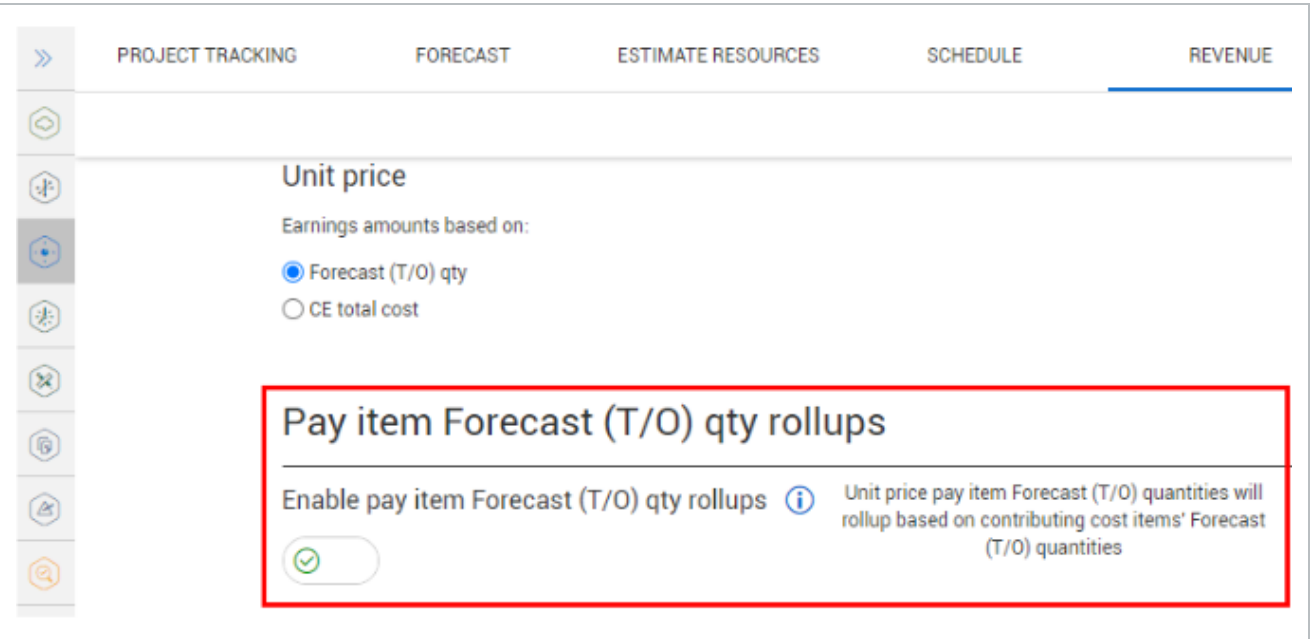

In the CBS, you can quickly modify the pay item contribute quantity either in bulk or by selecting a single cost item.

Tasks

☐	☒ CBS position	De...
☒	3	Misc. i
☒	3.1	Misc. i
☒	3.1.6	B/C 88
☐	3.1.6.1	8888 C
☐	3.1.6.2	8888 C
☐	3.1.6.3	8888 C
☐	3.1.6.4	Bower
☐	3.1.6.5	

Multiple cost items selected

DETAILS

ATTRIBUTES

COST CATEGORIES

CURRENT ESTIMATE RESOURCES

Last changed on

Last changed by

05/23/2022 11:49 PM

rakesh.gunda-ptr@inei...

Description

Account code

* Cost source

(Varies)

Detail

* Forecast T/O qty

* UoM

* As-built lock

1.00000000000

PLS

☐

CE total cost

CE unit cost

☒ Live forecast method

\$ 0.00000000000

\$ 0.00000000000

Rollup

CE total MHrs

CE total equipment Hrs

CE labor cost/MHrs

0.00000000000

0.00000000000

\$ 0.00000000000

CE Mhr/Unit

CE Units/MHrs

* Cost segment

0.00000000000

0.00000000000

(Varies)

* Allow as-built

Pay item assignment

* Currency

None

2

CAD \$

* Quantity driver

☐ CBS contribute qty

☐ Hide in plan/Progress

Superior CI

☒ Pay item contribute qty

Selecting the Pay item contribute qty check box updates both the Current forecast (T/O) and the Update earning rules, only if Earnings rules are set to calculate based on Forecast (T/O) qty value in Pay items.

Pay item position	Pay item number	Descri...	Line num...	Row num...	Current price	Current forecast (T/O) qty
1	2	2	2	2	\$ 100.00000000	3.000000000000
2	4	D4	4	4	\$ 1,000.000000	
2.1	1		1	1	\$ 1,000.000000	0.000000000000

Pay item ID 2Description 2

Calculate earning amounts by:
☒ Forecast (T/O) qty
☐ CE total cost

CBS Position	Descri...	Pay item contrib... quantity	Earning %
3	Misc. Rev Ext...	☒	5.000000000000 %
3.1	Misc. Rev Ext...	☒	0.000000000000 %
3.1.6	B/C 8888 Osle...	☒	0.000000000000 %
3.1.6.5		☐	0.000000000000 %
3.1.6.1	8888 Osler La...	☐	15.000000000000 %
3.1.6.4	Bowen Island ...	☐	0.000000000000 %
3.1.6.2	8888 Osler Eq...	☐	0.000000000000 %
3.1.6.3	8888 Osler 3rd...	☐	0.000000000000 %
			20.000000000000 %

☐ Default Earning Rules

Deselecting the Pay item contribute qty check box in the CBS also updates both the Current forecast (T/O) and the Update earning rules.

Pay item position	Pay item number	Descri...	Line num...	Row num...	Current price	Current forecast (T/O) qty
1	2	2	2	2	\$ 100.00000000	0.000000000000
2	4	D4	4	4	\$ 1,000.000000	
2.1	1		1	1	\$ 1,000.000000	0.000000000000

Pay item ID 2Description 2

Calculate earning amounts by:
☒ Forecast (T/O) qty
☐ CE total cost

CBS Position	Descri...	Pay item contrib... quantity	Earning %
3	Misc. Rev Ext...	☐	5.000000000000 %
3.1	Misc. Rev Ext...	☐	0.000000000000 %
3.1.6	B/C 8888 Osle...	☐	0.000000000000 %
3.1.6.5		☐	0.000000000000 %
3.1.6.1	8888 Osler La...	☐	15.000000000000 %
3.1.6.4	Bowen Island ...	☐	0.000000000000 %
3.1.6.2	8888 Osler Eq...	☐	0.000000000000 %
3.1.6.3	8888 Osler 3rd...	☐	0.000000000000 %
			20.000000000000 %

☐ Default Earning Rules

4.6 ATTRIBUTES TAB

The Attributes tab allows you to tag the new cost item with user-defined entries.

1. **User-Defined Fields** –free text fields that you can type values into manually
2. **Tags** – Many of these fields are validated fields (known as tags), meaning you can choose from options in a drop-down list

1074
Erect Steel - Heavy

DETAILS ATTRIBUTES COST CATEGORIES RESOURCES

CBS tag 16
CBS tag 17
CBS tag 18
CBS tag 19
CBS tag 20
CBS tag 22
CBS tag 23
CBS tag 25
CBS user defined 1
CBS user defined 2
CBS user defined 3
CBS user defined 4
CBS user defined 5
CBS user defined 6
CBS user defined 7
CBS user defined 8
CBS user defined 9
CBS user defined 10
CBS user defined 11
CBS user defined 12
CBS user defined 13
CBS user defined 14
CBS user defined 15

Hand Place
Machine Finish
Other
Shoulder Barrier - Walls
Cut Off Pile
Splice Pile
Clear

Some of these tags and their drop-down values are defined at the organizational level and others are customizable via the Project Settings under the Configure tag list value.

4.7 COST CATEGORIES TAB

The Cost Categories tab allows you to view your current budget, actuals, live forecast and forecast remaining cost, broken down into more detailed cost categories (e.g., labor, construction equipment, supplies, materials, etc.).

The header in the Cost Categories tab shows the % **Complete**, **Live forecast method**, and the **Latest actuals in forecast values**.

DETAILS		ATTRIBUTES		COST CATEGORIES		RESOURCES
% Complete	★ Live forecast method	Latest actuals in forecast values				
297.77777778 %	Committed cost ▼	08/21/2020				
		TOTAL		PER UNIT		
Cost category	Current budget	Total cost (to date)	Current estimate	★ Live forecast	★ Forecast remaining cost	
^ Total	\$ 100.00000	\$ 30,565.15556	\$ 100.00000	\$ 31,565.15556	\$ 1,000.00000	
v Labor	\$ 0.00000	\$ 44,111.00000	\$ 0.00000	\$ 45,111.00000	\$ 1,000.00000	
v Construction...	\$ 0.41477	\$ 0.02304	\$ 0.41477	\$ 0.02304	\$ 0.00000	
v FOM Rented ...	\$ 0.04148	\$ 0.00230	\$ 0.04148	\$ 0.00230	\$ 0.00000	
v Supplies	\$ 0.00000	(\$ 14,000.00000)	\$ 0.00000	(\$ 14,000.00000)	\$ 0.00000	
v Materials	\$ 0.00000	(\$ 51.40000)	\$ 0.00000	(\$ 51.40000)	\$ 0.00000	
v Subcontract	\$ 0.00000	\$ 0.00000	\$ 0.00000	\$ 0.00000	\$ 0.00000	
v Fees	\$ 99.54376	\$ 5.53021	\$ 99.54376	\$ 5.53021	\$ 0.00000	

If you have the correct permissions, you can change the Live forecast method. You can also change the view of the Cost Categories values to show either **Total** or **Per Unit** cost.

1004 Permitss						
DETAILS		ATTRIBUTES		COST CATEGORIES		
% Complete	★ Live forecast method	Latest actuals in forecast values				
297.77777778 %	Committed cost ▼	08/21/2020				
		TOTAL		PER UNIT		
Cost category		Total cost (to date)	Current estimate	★ Live forecast	★ F	
^ Total		\$ 30,565.15556	\$ 100.00000	\$ 31,565.15556		
v Labor		\$ 44,111.00000	\$ 0.00000	\$ 45,111.00000		
v Construction...		\$ 0.02304	\$ 0.41477	\$ 0.02304		

This is also where you enter the estimated cost into the different cost categories for the plug cost source.

You can expand the labor category and enter your cost at the appropriate level (e.g., Labor Base wages). You need to enter the cost under the appropriate level of the category. For example, if you

enter the cost at the Labor category level, the cost will appear in Undefined Labor level because you did not enter it at a specific sub-category level.

DETAILS	ATTRIBUTES	COST CATEGORIES		RESOURCES	
4.1 - Erect Steel - Heavy					
Cost category	Current Budget	Total Cost (To Date)	Current Estimate	★ Live Forecast	★ Forecast Remaining Cost
▸ Total	\$800,000.00	\$0.00	\$800,000.00	\$800,000.00	\$800,000.00
▸ Labor	\$800,000.00	\$0.00	\$800,000.00	\$800,000.00	\$800,000.00
Labor Base	\$800,000.00	\$0.00	\$800,000.00	\$800,000.00	\$800,000.00
▸ Labor Burden	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
Undefined Labor	Undefined Labor		\$0.00	\$0.00	\$0.00
▸ Construction Equipment	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00

The following Step by Step walks you through adding costs to the Cost Categories tab of the Cost item details slide out panel.

Enter Costs in Cost Categories

1. Within the InEight Control main page, on the CBS tab, right click on the cost item you created.
2. Select **Cost Item Details** to open the Cost item details slide out panel.
3. Click on the **Cost Categories** sub tab.
4. Under the Current Estimate column, expand the **Labor** cost category.
5. In the Current Estimate column, enter a value in the Current Estimate column for Labor Base, then press the **Tab** key.

4.8 CURRENT ESTIMATE RESOURCES TAB

The Current Estimate Resources tab is where you can view and manage the CE resources for terminal cost items.

From the Current Estimate Resources tab you can view and manage:

- Cost item details
- Current estimate resources
- Productivity and overall settings

- Resource details

DETAILS

ATTRIBUTES

COST CATEGORIES

CURRENT ESTIMATE RESOURCES

FORECAST RESOURCES

Cost item details

Forecast T/O qty

UoM

CE total cost

CE remaining cost

CBS position

Cost source

10,000.00

CY

\$ 1,000,000.00

\$ 1,000,000.00

5.2

Detail

Current estimate resources

	Row #	Code	Description	Quantity	UoM	Work hours	CE unit cost
☒	1	C01.04	Concrete Bulk Commodities	10000	CY		0

Productivity and overall settings

Remaining

Total

Remaining hours

0.00

Remaining units/hour

0.00

Remaining hours/unit

0.00

Remaining man hours

0.00

Remaining units/man hour

0.00

Remaining man hours/unit

0.00

Resource details

C01.04

Concrete Bulk Commodities

When

Cost category

Amount

▼ Total

\$ 100.00

Billing rate

\$ 100.00

Billing rate markup

\$ 0.00

Billing rate markup %

0.00 %

Charge rate

\$ 100.00

Markup amount

\$ 0.00

Markup %

0.00 %

To see a total sum of the resources in Current estimate resources, you must have the Cost Source set to **Detail**.

DETAILS	ATTRIBUTES	COST CATEGORIES	CURRENT ESTIMATE RESOURCES	FORECAST RESOURCES	
Cost item details					
Forecast T/O qty	UoM	CE total cost	CE remaining cost	CBS position	Cost source
800.00	Ton	\$ 800,000.00	\$ 800,000.00	4.1	Detail Detail Plug
Current estimate resources					
Productivity and overall settings					
Resource details					

When the cost item’s cost source is set to **Plug**, you will not use the Current Estimate Resources tab. Instead, costs are “plugged” or entered directly into cost categories on the Cost Categories tab of the cost item.

4.8.1 Cost Driver

Each type of resource has a default cost driver. For example, Labor resources are duration driven so their default cost driver is CI Duration, meaning their costs are driven by the duration of the cost item. If you want a resource to only be assigned to a specific cost item or work activity for half the time, you can change its quantity to .5 and it will be driven by half of the cost item’s hours.

1005

Erect Steel - Light

DETAILS

ATTRIBUTES

COST CATEGORIES

CURRENT ESTIMATE RESOURCES

FORECAST RESOURCES

Cost item details

Forecast T/O qty

UoM

CE total cost

CE remaining cost

CBS position

Cost source

200.00

Ton

\$ 155,000.00

\$ 155,000.00

4.2

Detail

Current estimate resources

☐	Row #	Code	Description	Quantity	UoM	Work hours	CE unit cost
☐	1	1.C.01.1.05	Laborer	2	Each	800	
☐	2	1.C.05.1.04	Ironworker Apprentice	0.5	Each	200	
☐	3	1.C.01.1.06	Crane Operator	1	Each	400	
☐	4	1.C.05.1.03	Ironworker Journeyman	3	Each	1200	
☐	5	1.C.05.1.02	Ironworker Foreman	1	Each	400	

Updating the total quantity of a resource with CI quantity as the cost driver will not auto-update the hours.

To enter work hours manually for the employed resource, you can change the Cost Driver option to CI Quantity or Fixed.

DETAILS

ATTRIBUTES

COST CATEGORIES

CURRENT ESTIMATE RESOURCES

FORECAST RESOURCES

Cost item details

Forecast T/O qty

UoM

CE total cost

CE remaining cost

CBS position

Cost source

800.00

Ton

\$ 800,000.00

\$ 800,000.00

4.1

Detail

Current estimate resources

☐	Row #	Code	Description		CE total cost	Cost driver	Cost curve
☒	1	1.C.05.1.04	Ironworker Apprentice	45.00	\$ 216,000.00	CI Duration	Employed Cos...
☐	2	1.C.05.1.02	Ironworker Foreman	65.00	\$ 104,000.00		Employed Cos...
☐	3	1.C.05.1.03	Ironworker Journeyman	55.00	\$ 264,000.00		Employed Cos...
☐	4	1.C.01.1.05	Laborer	35.00	\$ 112,000.00		Employed Cos...
☐	5	1.C.01.1.06	Crane Operator	65.00	\$ 104,000.00		Employed Cos...

If you change the Cost Driver to CI Quantity, the fields below will not be editable. It causes the adjusted duration to become zero or read-only. However, it can be editable if it does make a cost impact.

With CI Quantity as your cost driver for your resources, you can adjust the Work Hours manually, where previously that column was read-only. For example, perhaps you want your Laborer to work specifically 80 hours. The Forecast (T/O) Qty is very significant when it comes to quantity driven resources. It determines how the cost is driven and what affects the cost of that specific line item. For example, perhaps there is a scope change and you need to change the Forecast (T/O) Qty from 900 to 350.

1074

Erect Steel - Heavy

DETAILS

ATTRIBUTES

Forecast T/O qty

900.00

UoM

Ton

CE unit cost

\$ 1,000.00

Last changed on

07/02/2025 06:51 AM

Last changed by

Toby Stow

Description

Erect Steel - Heavy

Account code

62.03.02.00

• Forecast T/O qty

900.00

• UoM

Ton

A dialog box shows to choose whether it will affect the CE unit cost or CE total cost. Typically, you keep the unit cost constant and adjust the total cost.

✕

⚠

Proportionally adjust CE unit cost or CE total cost ?

You can modify Forecast T/O qty by proportionally adjusting CE unit cost or CE total cost. Specify the value you would like to modify:

☐ CE unit cost

\$1,000.00

☒ CE total cost

\$350,000.00

Cancel

OK

Note that the Welder’s work hours adjust because they are driven by the Forecast (T/O) quantity of the cost item.

When the Cost Driver is set on Fixed, you can only update the resource’s hours by typing into the resource itself and updating the work hours directly.

Many of the numbers are tied to equations under the Productivity resources below. If you edit the numbers, it will have an impact on the resources depending on the cost driver.

4.8.2 Productivity and overall settings

On the Current Estimate Resources tab, you can manage duration and quantities for the following calculations:

	Calculation
1	Remaining hours/units
2	Remaining man hours/units
3	Remaining equipment hours/units

1069

Earthwork

DETAILS

ATTRIBUTES

COST CATEGORIES

CURRENT ESTIMATE RESOURCES

FORECAST RESOURCES

Cost item details

Forecast T/O qty

UoM

CE total cost

CE remaining cost

CBS position

Cost source

10,000.00

CY

\$ 400,000.00

\$ 400,000.00

2

Detail

Current estimate resources

	Row #	Code	Description	Quantity	UoM	Work hours	CE unit cost
☐	1	1.C.05.1.09	Civil Journeyman	2.00	Each	1,454.55	
☐	2	1.C.05.1.23	Civil Apprentice	3.00	Each	2,181.82	
☐	3	1.C.01.1.05	Laborer	3.00	Each	2,181.82	
☐	4	1.C.01.1.07	Civil Operator	2.00	Each	1,454.55	

Productivity and overall settings

Remaining

Total

1

Remaining hours

727.27

Remaining units/hour

13.75

Remaining hours/unit

0.07

2

Remaining man hours

8,000.00

Remaining units/man hour

1.25

Remaining man hours/unit

0.80

3

Remaining equipment hours

0.00

Remaining units/equipment hour

0.00

Remaining equipment hours/unit

0.00

When updating the quantity of duration driven labor resources

☒ Proportionally update Units\Man hours

☐ Proportionally update Hours

Resource details

Total duration hours (Remaining hours) are used to calculate labor and equipment resource work hours where:

- $\text{Work Hours (resource)} = \text{Hours (total duration)} \times \text{Quantity (resource)}$
- $\text{Total Remaining man hours} = \text{Sum (Labor Resource Work Hours)}$
- $\text{Total Remaining equipment hours} = \text{Sum (Equipment resource Work hours)}$

Total remaining duration hours are calculated using either the total value or one of the following unit rate options in the Productivity and overall settings section:

- Remaining hours (Duration)
 - Unit rates are proportionate to total value based on Forecast T/O qty.
 - Total man hours and equipment hours are proportionate to total hours based on labor and equipment resource quantity.
- Remaining man hours
 - Unit rates are proportionate to total value based on Forecast T/O qty.
 - Total duration Remaining hours are proportionate to total Man hours based on Labor resource quantity.
 - Total Remaining equipment hours are proportionate to total duration hours based on Equipment qty.
- Remaining equipment hours
 - Unit rates are proportionate to total value based on Forecast T/O qty.
 - Total duration hours are proportionate to total Remaining man hours based on Equipment resource quantity.
 - Total Labor hours are proportionate to total remaining duration hours based on Labor Resource qty.

When one value is entered, all other totals and unit rates in the Productivity and overall settings section are calculated based on that entry.

4.8.2.1 Updates to resource quantities

The options for the setting When updating the quantity of duration driven labor resources, control how work hours are calculated when a resource quantity is updated:

- **Proportionally update Units/Man hours** – When you update quantities in the Quantity column, this option changes the resource work hours in the Work hours column and re-calculates the total remaining man hours and corresponding unit rates in the Productivity and overall settings

section.

Current estimate resources

	Row #	Code	Description	Quantity	UoM	Work hours	CE unit cost
☐	1	1.C.05.1.09	Civil Journeyman	2.00	Each	1,454.55	
☐	2	1.C.05.1.23	Civil Apprentice	3.00	Each	2,181.82	
☐	3	1.C.01.1.05	Laborer	3.00	Each	2,181.82	
☐	4	1.C.01.1.07	Civil Operator	2.00	Each	1,454.55	

Productivity and overall settings

RemainingTotal

Remaining hours727.27

Remaining units/hour13.75

Remaining hours/unit0.07

Remaining man hours8,000.00

Remaining units/man hour1.25

Remaining man hours/unit0.80

Remaining equipment hours0.00

Remaining units/equipment hour0.00

Remaining equipment hours/unit0.00

When updating the quantity of duration driven labor resources

☒ Proportionally update Units\Man hours

☐ Proportionally update Hours

Resource details

- **Proportionally update Hours** – When you update quantities in the Quantity column, this option redistributes proportionally across the labor resources in line with the new quantities and does

Page 176 of 639

InEight Inc. | Release 26.7

not re-calculate but maintains the total remaining man hours.

Current estimate resources

	Row #	Code	Description	Quantity	UoM	Work hours	CE unit cost
☐	1	1.C.05.1.09	Civil Journeyman	2.00	Each	1,454.55	
☐	2	1.C.05.1.23	Civil Apprentice	3.00	Each	2,181.82	
☐	3	1.C.01.1.05	Laborer	3.00	Each	2,181.82	
☐	4	1.C.01.1.07	Civil Operator	2.00	Each	1,454.55	

Productivity and overall settings

RemainingTotal

Remaining hours

727.27

Remaining units/hour

13.75

Remaining hours/unit

0.07

Remaining man hours

8,000.00

Remaining units/man hour

1.25

Remaining man hours/unit

0.80

Remaining equipment hours

0.00

Remaining units/equipment hour

0.00

Remaining equipment hours/unit

0.00

When updating the quantity of duration driven labor resources

☐ Proportionally update Units\Man hours

☒ Proportionally update Hours

Resource details

4.9 FORECAST RESOURCES TAB

The Forecast Resources tab is where you can view and manage estimate resources assigned to a cost item.

From the Resources tab you can view and manage the:

- Forecast details live forecast method
- Add new resources and adjust duration-driven resources by changing their productivity
- View and adjust resource rates of assigned resources

DETAILS

ATTRIBUTES

COST CATEGORIES

CURRENT ESTIMATE RESOURCES

FORECAST RESOURCES

Forecast details

Forecast total cost

Forecast remaining cost

Forecast total MHrs

Forecast remaining MHrs

Live forecast method

Manual (ETC)

Resources

+

×

☐	Row #	Code	Description	Estim...	Remaini... qty	UOM	Remaini... work hrs
☒	1	1.C.01.1.05	Laborer	Labor	0.00	Hour	

Productivity and overall settings

Remaining hours

0.00

Remaining units/hour

0.00

Remaining hours/unit

0.00

Remaining man hours

0.00

Remaining units/man hour

0.00

Remaining man hours/unit

0.00

Remaining equipment hours

0.00

Remaining units/equipment hour

0.00

Remaining equipment hours/unit

0.00

Resource details

When i

☒ P

☐ P

Cost category	Scale 1 unit cost	Scale 2 unit cost	Scale 3 unit cost
▼ Total	\$ 35.00	\$ 30.00	\$ 40.00

Like the Details, Attributes, and Cost Categories tabs, you access the Forecast Resources tab from the Cost Item Details slide out panel.

Tasks

☐	CBS position	Description	WBS phase code
☐	1	Job Overhead	1002
☐	2	Earthwork	1069
☐			1071
☐			1073
☒			1074
☐			1005
☐			1006
☐			1084
☐			1085
☐			1086
☐			1087
☐			1088

- Copy
- Paste
- Insert copied cost items
- New cost item
- New subordinate cost item
- Delete cost item(s)
- Adjust CBS position
- Cost item details**
- Actuals details

1074

Erect Steel - Heavy

DETAILS
ATTRIBUTES
COST CATEGORIES
CURRENT ESTIMATE RESOURCES
FORECAST RESOURCES

Forecast T/O qty	UoM	CE unit cost	CE total cost	CBS position
800.00	Ton	\$ 1,000.00	\$ 800,000.00	4.1

Last changed on	Last changed by
02/22/2022 02:17 PM	Service Account

Description

Account code

* Cost source

* Forecast T/O qty

* UoM

☐ As-built lock

CE total cost

\$ 800,000.00

CE unit cost

\$ 1,000.00

☒ Live forecast method

Manual (ETC)

CE total M/Hrs

CE total equipment Hrs

CE labor cost/MHrs

The Forecast Resources tab shows as an accordion menu where you can select a specific drop down menu you want to view.

DETAILSDetailsATTRIBUTESAttributesCOST CATEGORIESCost CategoriesCURRENT ESTIMATE RESOURCESCurrent Estimate ResourcesFORECAST RESOURCESForecast Resources

Forecast detailsForecast details

ResourcesResources

	Row #	Code	Description	Estim...	Remaini... qty	UOM	Remaini... work hrs
☒	1	1.C.01.1.05	Laborer	Labor	0.00	Hour	
☐	2	1.C.01.1.06	Crane Operator	Labor	0.00	Hour	

Productivity and overall settingsProductivity and overall settings

Resource detailsResource details

4.9.1 Productivity and overall settings

If the resource’s cost driver is set to CI Duration, you can change any of the values on the Productivity tab under Adjusting duration driven resources below, and it will change the work hours of your resources without you having to do the math yourself.

DETAILS

ATTRIBUTES

COST CATEGORIES

CURRENT ESTIMATE RESOURCES

FORECAST RESOURCES

Cost item details

Current estimate resources

Productivity and overall settings

Resource details

Remaining

Total

Remaining hours

1,600.00

Remaining units/hour

0.50

Remaining hours/unit

2.00

Remaining man hours

16,000.00

Remaining units/man hour

0.05

Remaining man hours/unit

20.00

Remaining equipment hours

0.00

Remaining units/equipment hour

0.00

Remaining equipment hours/unit

0.00

When updating the quantity of duration driven labor resources

Proportionally update Units\Man hours

Proportionally update Hours

4.9.2 Resource Details

Resource Details shows the unit cost category breakdown of the selected resource listed above. The Resource rates tab expands to a unit breakdown on a selected item under resources. It is fully editable if you have the right permissions to do so.

Resource details				
1.C.05.1.04				
Ironworker Apprentice				
Cost category	Scale 1 unit cost	Scale 2 unit cost	Scale 3 unit cost	
^ Total	\$ 45.00	\$ 45.00	\$ 60.00	
✓ Labor	\$ 45.00	\$ 45.00	\$ 60.00	
✓ Construction Equipment	\$ 0.00	\$ 0.00	\$ 0.00	
✓ FOM Rented Equipment	\$ 0.00	\$ 0.00	\$ 0.00	
✓ Supplies	\$ 0.00	\$ 0.00	\$ 0.00	
✓ Materials	\$ 0.00	\$ 0.00	\$ 0.00	
✓ Subcontract	\$ 0.00	\$ 0.00	\$ 0.00	

4.9.2.1 ▲ Orphan Indicator

If you change the resource rate of one of the assigned resources, then a triangle will appear. The triangle is an **orphan indicator**. This means a value associated with this resource does not match the resource's value in the Estimated resources in the Project library. When you hover over the triangle, it will give you a summary of all the differences between the library value and the orphaned value.

Attribute	Library value	Orphan value	Last changed by	Last changed on
Total - Scale1	50.00	100.00	Susan Cappelloni	09/25/2017 02:24 PM
FOM Rented Equipm...	0.00	50.00	Susan Cappelloni	09/25/2017 02:24 PM
Undefined FOM Rent...	0.00	50.00	Susan Cappelloni	09/25/2017 02:24 PM

Row #	Code	Description	Quantity	UOM	Work Hours	CE - Unit Cost	CE - Total Cost
2	lab1	lab1	1	Each	27.78	60.00	10
3	lab1	lab1	1	Each	41.67	\$60.00	\$1,5

PRODUCTIVITY

CHARGE RATE

Unit cost charge rates

Cost category	Scale 1 unit cost	Scale 2 unit cost	Scale 3 unit cost
Total	\$70.00	\$0.00	\$0.00
Labor	\$0.00	\$0.00	\$0.00


This is shown in case you want to change the values back to match the library. If you change the values back to match the library, the triangle will disappear.

4.9.3 Cost Item Man-Hours

Aside from on the Cost Estimate Resources tab, you can also define productivity on the CBS register page. The following steps walk you through how to add the planned man-hours for a cost item from the CBS register page.

Define Cost Item Man-Hours

- 1. On your CBS register tab, make sure the Current estimate data block is displayed on the page, by selecting the **CE + CB** viewset.

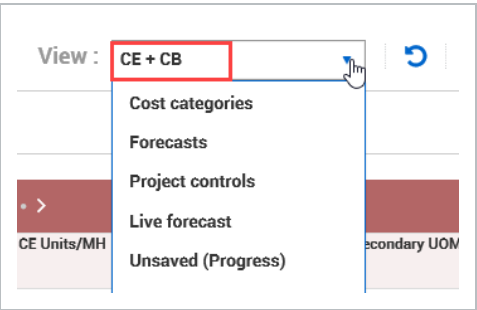

- 2. Under the CE Total MHrs column, enter **16,000** for a cost item, then press the **Tab** key. Note – If the cost item is a “detail” cost source you will not be able to manually adjust this field.

▼ Steel Structure Training Job
105099

Actions CBS ACS PAY ITEMS CHANGE REGISTER AUDIT LOG

Tasks ?

	CBS Position	Description
☐	3	Concrete
☐	▼4	Structural Steel
☐	4.1	Erect Steel - Heavy
☐	4.2	Erect Steel - Light

Task Details < >

Resource	Forecast (TO) Quantity	UOM
1	10,000.00	CY
	1,000.00	Ton
1	800.00	Ton
	1,000.00	Ton

Current estimate

CE total Mhrs	CE total cost
30,000.00	\$1,500,000.00
20,000.00	\$1,050,000.00
16,000.00	\$800,000.00
1,000.00	\$50,000.00

4.10 ISSUE TAGGING IN THE CBS

You can associate an issue to a cost item in the CBS. Issue Ids in Change have a hierarchy of issues and subordinate issues. Associated an issue to a cost item applies to parent-level issues. Child issues take on the cost item of the parent issue.

CBS ACS PAY ITEMS CHANGE REGISTER

Actions + ✎ ✕

Tasks

	✓ CBS position	Description	WBS phase code
☐	30		1 / 85
☐	31		1790
☐	32	Cost item 1 up	
☐	33	Cost item 2	
☐	34	x	
☐	35	Detail - labor	
☐	36	Detail - CE	
☐	37	Detail - other	
☐	38	Detail - mix	
☐	39	Plug	
☐	40	plug2	
☐	41	Cost item 1	01
☐	42	Cost item 2	02
☐	43	Cost item 3	03
☐	44	Cost item 4	04
☒	45		

Subtotals 804 (1 rows selected)

nt-	Last estimated actual man hours reversal	Last estimated actual equip hours reversal	Issue
0.00			
0.00			
0.00			
0.00			
0.00			
100.00			
0.00			
10.00			
0.00			
0.00			
0.00			
1.00	04/06/2021 1:18:1...	03/29/2021 3:08:7...	
0.00			
0.00			

Formula description: Document issue: N/A

When you click in the Issue column, the Assign issue dialog box is shown. The list of issues originates from the list of the issues in Change.

×

Assign issue

Search...

Select	Issue id	Issue name
☐	7	new5_copy67
☐	8	new5

Clear

Cancel

Assign

The Assign issue dialog box does not contain the full list of Issues that Change contains.

Change

NEW ISSUE

7

ISSUE LOG

POTENTIAL CO LOG

	Issue ID	PCO ID	Client CO ID	Issue name	Issue start date	Issue stat...	Assign
☐	^ 12			G Testing 2/1...	02/17/2021	Open	
☐	12.2			G Testing 2/1...	02/17/2021	New	
☐	12.1			G Testing 2/1...	02/17/2021	New	
☐	11 B			new6 (B)	11/05/2020	New	
☐	11 A			new6 (Original)	11/05/2020	New	
☐	^ 10			new6	11/05/2020	Open	
☐	10.1			new6	11/05/2020	New	
☐	9		new1	new5cj	11/04/2020	Executed	
☐	^ 8			new5	11/04/2020	Open	

If a parent issue in Change becomes a subordinate while you already have that issue assigned to a cost item in the CBS, the cost item then changes Issue ID to match the parent item that the linked issue was then relocated under. For example, if the parent issue ID was a 2 in Change and it was moved under the parent issue ID 1, then the cost item previously linked to the parent 2 changes to the parent issue 1.

4.11 LOCK BUDGET

4.11.1 Budgets vs Estimate

You can maintain an Original Budget, a Current Budget, and a Current Estimate, as is shown from the CBS tab of the Control main page, using a custom data block.

Tasks			Task Det... < + + + + >			BM Budget View < + + >		
CBS Position	Description		WBS Phase Code	Forecast TO City	UOM	O B-Total Cost	C B-Total Cost	C E-Final Cost
1	Job Overhead		1002	1.00	Lump Su..	\$250,000.00	\$250,000.00	\$250,000.00
2	Earthwork		1069	10,000.0..	CY	\$400,000.00	\$400,001.00	\$400,000.00
▼3	Concrete		1071	10,000.0..	CY	\$0.00	\$8,000.00	\$5,000.00
▼3.1	Concrete Footings		1089	1,000.00	CY	\$0.00	\$8,000.00	\$5,000.00
3.1.1	Place/Strip Footing Forms		1090	500.00	SF	\$0.00	\$8,000.00	\$5,000.00
3.1.2	Pour Footings		1091	0.00	CY	\$0.00	\$0.00	\$0.00

4.11.1.1 Original Budget

The Original Budget (OB) is a snapshot of the project plan in its original state, prior to execution. It is a baseline used for comparison as the project progresses. You cannot edit your Original Budget values; they are read-only in the CBS register, available for reference only.

Once set, the Original Budget never changes.

In the CBS register, you can find the OB values for man-hours, quantities, and costs.

Tasks			Task Det... < + + + + >			BM Budget View < + + >		
CBS Position	Description		WBS Phase Code	Forecast TO City	UOM	O B-Total Cost	C B-Total Cost	C E-Final Cost
1	Job Overhead		1002	1.00	Lump Su..	\$250,000.00	\$250,000.00	\$250,000.00
2	Earthwork		1069	10,000.0..	CY	\$400,000.00	\$400,001.00	\$400,000.00
▼3	Concrete		1071	10,000.0..	CY	\$0.00	\$8,000.00	\$5,000.00
▼3.1	Concrete Footings		1089	1,000.00	CY	\$0.00	\$8,000.00	\$5,000.00

4.11.1.2 Current Budget

The **Current Budget (CB)** is the project's operational budget, including only project changes approved through a controlled process. The Current Budget is therefore the sum of your Original Budget, plus or minus any approved changes.

See the Change Management section for more details on managing and approving budget changes.

In the CBS register, you can find CB values for planned, earned and forecasted costs, hours and productivity.

Tasks		Task Det... < + - >			BM Budget View < + - >			
CBS Position	Description	WBS Phase Code	Forecast TO City	UOM	O B-Total Cost	C B-Total Cost	Descr: Current Budget Total Cost Formula: N/A	C E-Final Cost
1	Job Overhead	1002	1.00	Lump Su..	\$250,000.00	\$250,000.00		\$250,000.00
2	Earthwork	1069	10,000.0.	CY	\$400,000.00	\$400,001.00		\$400,000.00
▼3	Concrete	1071	10,000.0.	CY	\$0.00	\$8,000.00		\$5,000.00
▼3.1	Concrete Footings	1089	1,000.00	CY	\$0.00	\$8,000.00		\$5,000.00
3.1.1	Place/Strip Footing Forms	1090	500.00	SF	\$0.00	\$8,000.00		\$5,000.00
3.1.2	Pour Footings	1091	0.00	CY	\$0.00	\$0.00		\$0.00

4.11.1.3 Current Estimate

The **Current Estimate (CE)** represents the most up to date estimate of your work. You can update your Current Estimate quantities, hours, and costs at any time in the CBS register, with no required approval process or work flow.


You can use the Current Estimate as a sand box to build out change orders and do what-if analysis to plan for potential changes, without worrying about affecting the Current or Original Budgets.

Tasks		Task Det... < + - >			BM Budget View < + - >			
CBS Position	Description	WBS Phase Code	Forecast TO City	UOM	O B-Total Cost	C B-Total Cost	Descr: Current Estimate Final Cost Formula: N/A	C E-Final Cost
1	Job Overhead	1002	1.00	Lump Su..	\$250,000.00	\$250,000.00		\$250,000.00
2	Earthwork	1069	10,000.0.	CY	\$400,000.00	\$400,001.00		\$400,000.00
▼3	Concrete	1071	10,000.0.	CY	\$0.00	\$8,000.00		\$5,000.00
▼3.1	Concrete Footings	1089	1,000.00	CY	\$0.00	\$8,000.00		\$5,000.00
3.1.1	Place/Strip Footing Forms	1090	500.00	SF	\$0.00	\$8,000.00		\$5,000.00
3.1.2	Pour Footings	1091	0.00	CY	\$0.00	\$0.00		\$0.00

All editable cells in the Current Estimate CBS grid are single click.

4.11.2 Lock Budget and Price


When you first create your project, your cost breakdown structure is unlocked, meaning you can make changes to your current estimate, but there is no locked down budget for tracking purposes. Your Original Budget and Current Budget data blocks therefore contains no values.

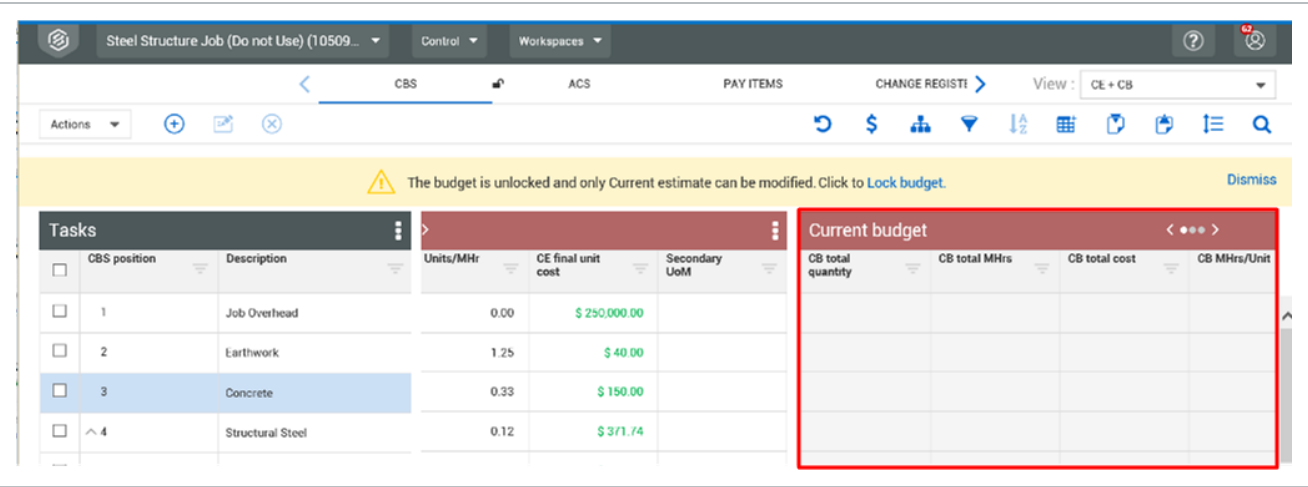

Locking your budget creates an Original and Current Budget based on your Current Estimate values. Keep in mind that:

- Your Original Budget cannot change
- Your Current Budget can only change via approved change orders. For more information, see [Change management overview](#).
- During project execution, you can compare your actual costs and man-hours to your Original and Current Budgets to track you progress


In the CBS you can lock the budget by selecting Actions > Lock/unlock budget > **Lock Budget** or **Lock project budget and price**.

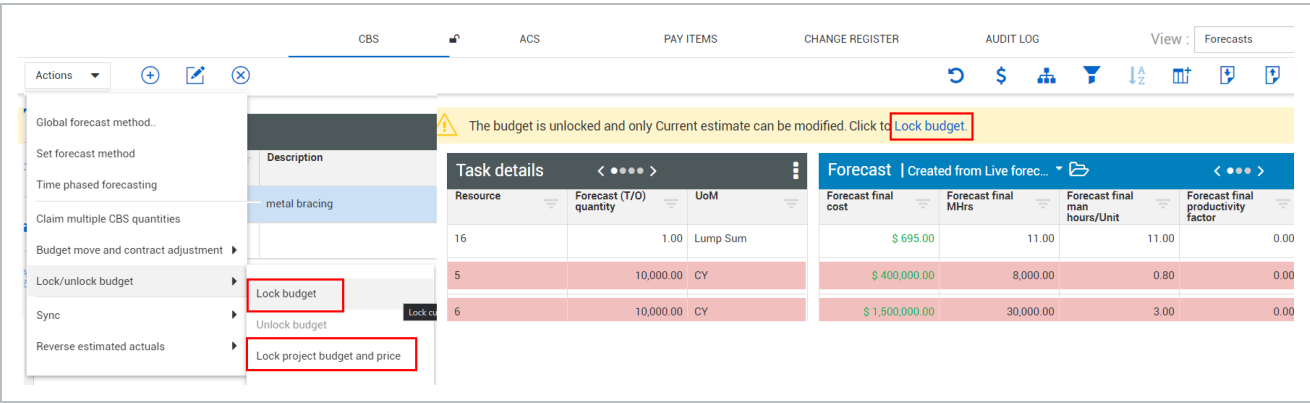

The Budget Lock Status columns then changes to a locked symbol.

☐	Pay item number	Description	Current forecast (T/O) qty	Price lock status
☐	001	Earthwork - Lab...	1.00	
☐	002	Concrete - Lab...	1.00	
☐	003	Steel - Labor & ...	1.00	

In Pay Items, you can also lock your price and budget for pay items by selecting Actions > Lock/unlock price>Lock Price or Lock project budget and price.

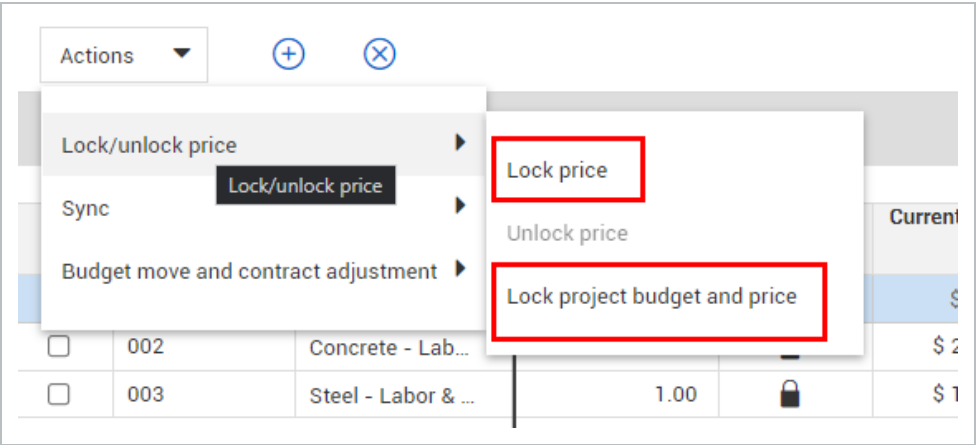


The Price Lock Status columns then changes to locked.


☐	Pay item number	Description	Current forecast (T/O) qty	Price lock status
☐	001	Earthwork - Lab...	1.00	
☐	002	Concrete - Lab...	1.00	
☐	003	Steel - Labor & ...	1.00	

4.11.3 Unlock Budget and Price

After you lock your budget, in rare instances, it might be necessary to unlock your Original and Current Budgets, though this is typically not recommended. For example, after initial import of your estimate into Control, you might need to make further adjustments to your cost breakdown structure to conform your estimate to the working plan for the project. Normally, unlocking your budget is the exception, not the rule.

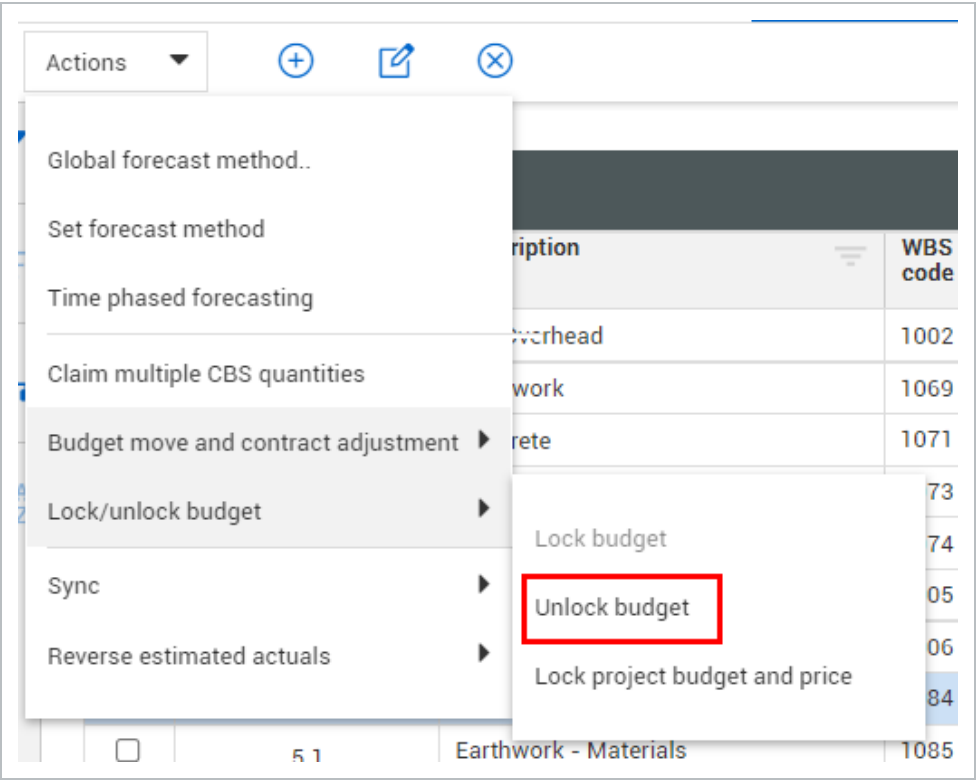

In Pay Items, like locking the budget for cost items, you unlock the price from the Actions menu.

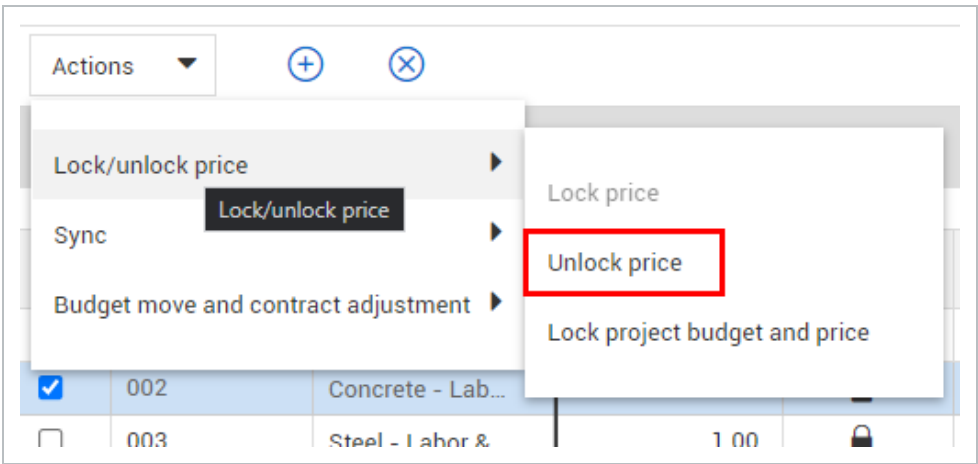

4.12 ASSIGNED VENDORS

You can assign a vendor to a cost item, and also view the assigned vendors from InEight Contract. A cost item with a vendor assigned serves two purposes. The first purpose is informative, letting the product team know a vendor is related to that cost item, either as a material supplier or as a subcontractor doing the work. The second purpose is functional, as it controls what tasks a vendor can view when logged into a daily plan in InEight Progress. The vendor will only view tasks related to the cost items/WBS phase codes with that vendor assigned to them in Control.

If a vendor is assigned via a contract, the vendor name is automatically assigned to a cost item and cannot be removed.

Tasks

☐	CBS position	Description
☐	1	Financial Results Analysis
☐	▼ 2	Misc. Rev Internal
☐	2.1	Misc. Rev Internal
☐	▼ 2.2	Escalation/Contingency
☐	2.2.1	General Project Risk
☐	▼ 2.3	Directs
☐	▼ 2.3.1	Direct Labour
☐	▼ 2.3.1.1	Grading Work
☐	2.3.1.1.1	Resurface Existing Access road
☐	2.3.1.1.2	Maintain Access Road
☐	2.3.1.1.3	Clear & Grub Bench B & West Layd...
☐	2.3.1.1.4	Type D Excavation LD/PL/CP to E...
☐	2.3.1.1.5	Road Subgrade Prep/Place/Finish...

Assigned Vendors

Assigned vendor

Finance Group Inc.

Mining Grou...Midwest Aviation

Power Cons...Engineering ...Finance Gro...

Plaza Building Co...Finance Gro...Construction Kiewi...Infrastructur...

Mexico LLC

Canada Inc

Enterprises Inc

Clicking in an Assigned vendor field lets you add new vendors. Vendors originate from the master data library for the entire organization.

Assigned Vendors

Assigned vendor

Kiewit Finance Group Inc.

Kiewit Mining Grou...Midwest

Kiewit Power Cons...Kiewit En

Plaza Building Co...Kiewit Fir

Kiewit Mexico LLC

Kiewit Canada Inc

Barrons Enterprises Inc

Vendor assignment

Search...

☐	Vendor ID	Vendor name
☐	0000001003	Mining Group Inc.
☐	0000001008	Aviation
☐	0000001013	Management Co.
☐	0000001014	Infrastructure Co.
☐	0000001022	Infrastructure Engineer...
☐	0000001035	Engineering (NC) Co
☐	0000001037	Power Constructors Co.
☐	0000001039	Finance Group Inc.
☐	0000001042	Construction Cie
☐	0000001044	Infrastructure South Co.
☐	0000001049	Building Company

Clear

Cancel

Assign

This page intentionally left blank.

CHAPTER 5 – PROGRESS MEASUREMENT

5.1 Progress measurement workflow	196
5.2 Progress Measurement Overview	196
5.2.1 Budgets vs Estimate	197
5.2.2 Earned value management terms	199
5.2.3 Productivity	202
5.2.4 Updating Forecast (T/O) Qty	203
5.2.5 Update Forecast (T/O) Qty with Plan components	205
5.3 Date Range Setup	208
5.4 Manage Actuals	211
5.5 Actuals by Sync	211
5.5.1 Sync Quantities	211
5.5.2 Sync Hours and Costs	217
5.5.3 Audit Log	221
5.6 Actuals by Import	221
5.7 Actuals by Manual Entry	226
5.7.1 Claim Quantities	228
5.7.2 Claim Man-hours	234
5.7.3 Claim Equipment Hours	235
5.7.4 Claim Cost	236
5.7.5 Add Additional Claiming entries	238
5.7.6 User-Defined Fields	238
5.8 Actuals by API	239
5.9 User-defined fields	239
5.10 Estimated Actuals	242
5.10.1 Claim Estimated Actuals in Control	244
5.10.2 Estimated Actuals from Progress	245
5.10.3 Reverse Estimated Actuals	247
5.11 Actuals History	249
5.12 Progress Control Settings	249


5.13 Vendor Work Hours from Progress251

5.13.1 Vendor MHours from Progress251

5.14 Track Open/Remaining and Total Committed Costs254

5.15 Committed cost from Contract260

5.1 PROGRESS MEASUREMENT WORKFLOW

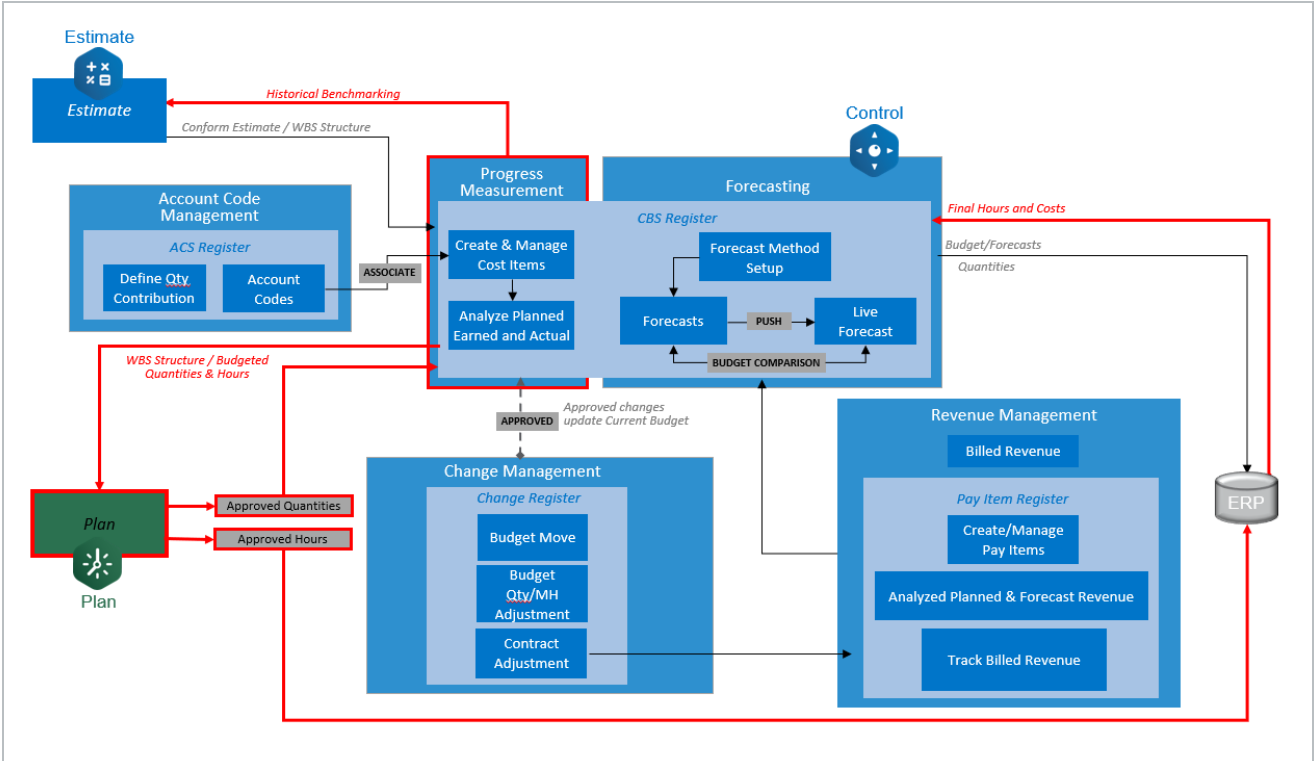

5.2 PROGRESS MEASUREMENT OVERVIEW

Progress measurement plays a key role in tracking how much work has been completed and how it aligns with contract deliverables. Payment terms are often tied to the value of work performed, making it essential to measure progress accurately. A clear and consistent approach to progress tracking helps teams manage performance, support billing, and maintain visibility throughout the life of the project.

To measure progress effectively, it’s important to understand a few key terms and how they relate to budget and performance tracking.

5.2.1 Budgets vs Estimate

In InEight Control, you can maintain an original budget, a current budget, and a current estimate. These values can be referenced in preset data blocks, or in a custom data block like the one shown below.

Tasks				Budgets			
☐	CBS position	Description	WBS phase code	OB total cost	CB total cost	CE total cost	% complete
☐	6	Electrical Systems Installation	1088	\$ 83,930.00	\$ 86,275.00	\$ 97,537.00	44.03 %
☐	6.1	Install Electrical Conduit	1089	\$ 37,400.00	\$ 37,400.00	\$ 44,880.00	60.00 %
☐	6.2	Pull Wire	1090	\$ 32,160.00	\$ 33,165.00	\$ 36,180.00	40.00 %
☐	6.3	Install Light Fixtures	1091	\$ 10,050.00	\$ 11,390.00	\$ 11,725.00	20.00 %
☐	6.4	Test Electrical Systems	1092	\$ 4,320.00	\$ 4,320.00	\$ 4,752.00	0.00 %

5.2.1.1 Original Budget

The original budget (OB) is a snapshot of the project plan in its original state prior to execution. It is a baseline used for comparison as the project progresses. You cannot edit your original budget values; they are read-only in the CBS register, available for reference only. After the original budget is set, it will not change unless you unlock it.

In the Control CBS register, you can see the OB values for man-hours, quantities, and costs.

Original budget			
OB total cost	OB total MHrs	OB total qty	OB unit cost
\$ 83,930.00	2,480.00	1.00	\$ 83,930.00
\$ 37,400.00	1,100.00	1,000.00	\$ 37.40
\$ 32,160.00	960.00	800.00	\$ 40.20
\$ 10,050.00	300.00	150.00	\$ 67.00
\$ 4,320.00	120.00	20.00	\$ 216.00

5.2.1.2 Current Budget

The current budget (CB) is the project's operational budget, including only project changes approved through a controlled process. The current budget is therefore the sum of your original budget, plus or minus any approved changes.

See [Change Management](#) for more details on managing and approving budget changes.

In the CBS register, you can access the Current budget data block and view CB values for planned, earned and forecasted costs, hours, and productivity.

Current budget < ● ● ● >					
Bud... lock status	CB total quantity	CB total Mhrs	CB total cost	CB Mhrs/Unit	CB units/Mhr
	1.00	2,550.00	\$ 86,275.00	2,550.00	0.00
	1,000.00	1,100.00	\$ 37,400.00	1.10	0.91
	825.00	990.00	\$ 33,165.00	1.20	0.83
	170.00	340.00	\$ 11,390.00	2.00	0.50
	20.00	120.00	\$ 4,320.00	6.00	0.17

5.2.1.3 Current Estimate

The current estimate (CE) represents the most up-to-date estimate of your work. You can update your current estimate quantities, hours, and costs at any time in the CBS register, with no required approval process or workflow.

You can use the current estimate as a sand box to build out change orders and do what-if analysis to plan for potential changes, without worrying about affecting the current or original budgets.

In the CBS register, you can access the Current estimate data block to view a variety of columns for measuring and analyzing the progress of your project.

Current estimate < ● ● ● >				
CE total Mhrs	CE total cost	CE Mhrs/unit	CE units/Mhr	CE unit cost
2,783.29	\$ 97,537.00	2,783.29	0.00	\$ 97,537.00
1,275.00	\$ 44,880.00	1.06	0.94	\$ 37.40
1,042.65	\$ 36,180.00	1.16	0.86	\$ 40.20
337.90	\$ 11,725.00	1.93	0.52	\$ 67.00
127.74	\$ 4,752.00	5.81	0.17	\$ 216.00

5.2.2 Earned value management terms

5.2.2.4 Planned Value (PV)

Planned Value (PV) is the costs and hours you have estimated and scheduled for the project. Think of PV as your approved budget of scheduled items. In Control, your PV includes the following columns:

- CE total Cost
- CE total MHrs
- CB total cost
- CB total MHrs

Planned Value 03/24/2025 to 08/27/2025 						< • >	
CE total cost	CE total MHrs	CB total MHrs	CB total cost	Start	Finish		
\$ 97,537.00	2,783.29	2,550.00	\$ 86,275.00	03/01/2025	11/05/2025		
\$ 44,880.00	1,275.00	1,100.00	\$ 37,400.00	07/01/2025	07/31/2025		
\$ 36,180.00	1,042.65	990.00	\$ 33,165.00	08/01/2025	08/25/2025		
\$ 11,725.00	337.90	340.00	\$ 11,390.00	08/25/2025	09/15/2025		
\$ 4,752.00	127.74	120.00	\$ 4,320.00	09/15/2025	09/25/2025		

5.2.2.5 Earned Value (EV)

Earned Value (EV) measures the amount of money you merit in return for the work performed up to that point. You can use EV to measure how much of your planned costs and hours you should have spent so far, according to the percent of work completed. Earned Value uses formula *Planned Value × % of work completed = Earned Value*.

In InEight Control, your EV includes the following columns:

- CE cost earned
- CE MHrs earned
- CB cost earned
- CB MHrs earned

Earned Value 03/24/2025 to 08/27/2025				
CE cost earned	CE Mhrs earned	CB cost earned	CB Mhrs earned	% complete
\$ 43,745.00	1,249.64	\$ 37,984.00	1,124.00	44.03 %
\$ 26,928.00	765.00	\$ 22,440.00	660.00	60.00 %
\$ 14,472.00	417.06	\$ 13,266.00	396.00	40.00 %
\$ 2,345.00	67.58	\$ 2,278.00	68.00	20.00 %
\$ 0.00	0.00	\$ 0.00	0.00	0.00 %

5.2.2.6 Schedule Performance Index

Schedule performance index (SPI) measures how close the work is being completed according to the designated schedule. It uses the formula $CB \text{ cost earned} \div CB \text{ planned value (to date)}$.

SPI < • >			
SPI	CB cost earned	CB planned value (to date)	
0.60	\$ 37,984.00	\$ 62,978.39	
0.74	\$ 22,440.00	\$ 30,161.29	
0.61	\$ 13,266.00	\$ 21,785.81	
0.28	\$ 2,278.00	\$ 8,104.84	
0.00	\$ 0.00	\$ 2,926.45	

The SPI calculation uses the time-phased budget values as planned values. To accommodate the time-phased budget values, the planned value includes the cumulative time-phased budget planned value to date.

5.2.2.7 Actual Cost (AC)

Actual cost (AC) refers to the costs you incur when you perform the work. You can view AC in the **Actual cost (to date)** column.

Actuals 03/24/2025 to 09/05/2025					
Actual cost (to date)	Actual MHrs (to date)	Actual qty (to date)	Actual MHrs/unit (to date)	CB MHrs G/L (to date)	CB actual cost G/L (to date)
\$ 37,680.00	1,236.00	0.44	2,807.39	-112.00	\$ 304.00
\$ 21,884.00	740.00	720.00	1.03	-80.00	\$ 556.00
\$ 13,518.00	430.00	360.00	1.19	-34.00	(\$ 252.00)
\$ 2,278.00	66.00	35.00	1.89	2.00	\$ 0.00
\$ 0.00	0.00	0.00	0.00	0.00	\$ 0.00

5.2.2.8 Variance

Variance is the difference between EV and AC and uses formula *Earned Value - Actual Cost = Variance*.

Variance indicates if you are performing better or worse than planned up to that point. Control uses the term Gain/Loss (G/L) rather than variance, shown in the following columns:

- CE actual cost G/L (to date)
- CE MHrs G/L (to date)
- CB actual cost G/L (to date)
- CB MHrs G/L (to date)

5.2.2.9 Remaining

Remaining is a general finance term for money that is not yet used. Control uses the formula *Planned Value - Actual Cost = Remaining Value* to calculate remaining cost.

In other words, remaining cost is the difference between what you originally planned and what you have spent so far, to help you understand how much cost or how many man-hours you have left.

The table below summarizes each EVM term with its equivalent term in Control and what it measures.

Term	InEight Control Term	What it measures
Planned Value (PV)	CE total cost CE total MHrs CB total cost CB total MHrs	Budget of scheduled values
Earned Value (EV)	CE cost earned CE MHrs earned CB cost earned	Planned value × percent complete

Term	InEight Control Term	What it measures
	CB MHrs earned	
Actual Cost (AC)	Actual cost (to date) Actual MHrs (to date)	Actual ÷ expended values
Variance	CE actual cost G/L (to date) CE MHrs G/L (to date) CB actual cost G/L (to date) CB MHrs G/L (to date)	Difference between earned value and actual cost
Remaining	Remaining qty CE remaining cost CB remaining cost CB remaining qty	Difference between planned value and earned value

The following displays planned vs. earned vs. actual values within a custom data block of the CBS register of InEight Control:

		PV - EV - AC								
Description	WBS phase code	CB total cost	CB cost earned	Actual cost (to date)	CB total MHrs	CB MHrs earned	Actual MHrs (to date)	CB total quantity	CB earned qty	Actual qty (to date)
Electrical Systems Installation	1088	\$ 86,275.00	\$ 37,984.00	\$ 37,680.00	2,550.00	1,124.00	1,236.00	1.00	0.44	0.44
Install Electrical Conduit	1089	\$ 37,400.00	\$ 22,440.00	\$ 21,884.00	1,100.00	660.00	740.00	1,000.00	600.00	720.00
Pull Wire	1090	\$ 33,165.00	\$ 13,266.00	\$ 13,518.00	990.00	396.00	430.00	825.00	330.00	360.00
Install Light Fixtures	1091	\$ 11,390.00	\$ 2,278.00	\$ 2,278.00	340.00	68.00	66.00	170.00	34.00	35.00
Test Electrical Systems	1092	\$ 4,320.00	\$ 0.00	\$ 0.00	120.00	0.00	0.00	20.00	0.00	0.00

5.2.3 Productivity

If you are the contractor building a project, you will need to monitor the performance of your crews, including how productive they are and how much they are being paid.

Productivity is a measure of effectiveness: the rate of output per unit of input. This can be measured with the following equation: *Productivity = Earned MH ÷ Actual MH*.

You can view productivity values in the following columns:

- CB productivity factor
- CE productivity factor

5.2.3.10 Compensation Factor (CF)

Compensation is the amount of money paid to an employee for their hours worked. Compensation factor is a numerical value comparing the budgeted compensation to the actual compensation. For example, if you had budgeted for work to be completed by master electricians, but you actually used 2nd year apprentices (making a lower wage), then that change would be reflected in the compensation factor. In InEight Control, compensation factor is shown as **Compensation factor (to date)**. You can calculate compensation factor using formula *Compensation Factor = Budgeted MH Cost ÷ Actual MH Cost*.

5.2.3.11 Labor Efficiency Index (LEI)

Labor efficiency index (LEI) is a numerical value assigned to indicate the effectiveness of resource utilization. In Control, it is shown as **LEI (to date)**. You can calculate LEI using formula *LEI = Productivity ÷ Compensation Factor*.

If LEI is greater than 1, it means that you are using your resources effectively. If LEI is lower than 1, it means your resources are being used poorly.

5.2.4 Updating Forecast (T/O) Qty

The Forecast (T/O) qty represents the total amount of work or materials expected to be completed for a cost item by the end of the project. This value can be updated as the project progresses and represents the current estimate of total quantity, comparable to the original or current budget quantity.

There are a number of ways to update the Forecast (T/O) qty:

1. Direct entry in the CBS
2. Rolldown from assigned pay item (need to have this setting enabled)
3. Rolldown from parent cost item (Qty driver is **Superior CI**)
4. Rollup from subordinate cost items (**Contribute qty** is checked)
5. Cost item import
6. Cost item API

When you update the Forecast (T/O) qty, you are prompted to update either the CE unit cost or CE total cost. You can also choose to update either the CE labor cost/Mhr or CE total MHrs, and either CE construction equipment cost/hr or CE total equipment hrs (if applicable).



Proportionally adjust CE unit cost or CE total cost

?

You can modify Forecast T/O qty by proportionally adjusting CE unit cost or CE total cost. Specify the value you would like to modify:

☐ CE unit cost

\$216.00

☐ CE total cost

\$4,752.00

Cancel

OK

Updating the Forecast (T/O) qty adjusts the remaining quantity for a cost item, which in turn updates the forecast values. Since forecast is calculated as *Remaining Quantity × Selected Unit Cost*, any change to the Forecast (T/O) qty directly affects the forecasted cost. This also impacts the % Complete, which is calculated as *Quantity Claimed ÷ Forecast (T/O) Qty*. As a result, earned value metrics and forecasted revenue values are updated to reflect the new progress and cost expectations.


5.2.4.12 Forecast (T/O) - CB qty delta column

The Forecast (T/O) - CB qty delta column shows you the difference between the Forecast (T/O) quantity and the current budget total quantity columns.

The calculation for this formula is *Forecast (T/O) qty - CB total quantity*.

Tasks				Task details - LK	
☐	CBS position	Description	WBS phase code	Forecast (T/O) qty	Forecast (T/O) - CB qty delta
☒	6	Electrical Systems Installation	1088	1.00	0.00
☐	6.1	Install Electrical Conduit	1089	1,200.00	200.00
☐	6.2	Pull Wire	1090	900.00	75.00
☐	6.3	Install Light Fixtures	1091	175.00	5.00
☐	6.4	Test Electrical Systems	1092	22.00	2.00

You can filter for cost items with a delta greater than 0 when you want to align the Forecast T/O Quantity and CB total quantity.

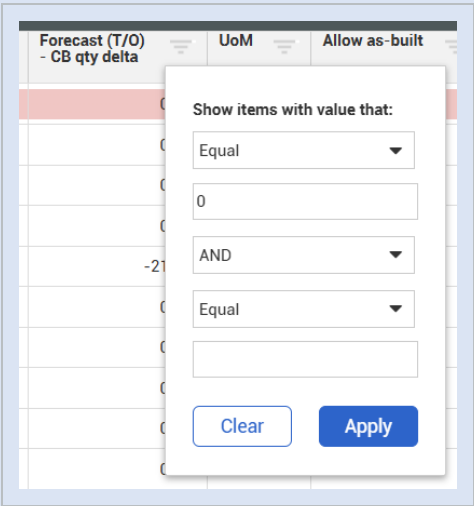

5.2.5 Update Forecast (T/O) Qty with Plan components

The **Plan component total qty** column represents the planned quantities defined in InEight Plan – essentially, what the team expects to install or complete based on the scope and schedule. Based on details from the field, these planned quantities may differ from the Forecast (T/O) quantity defined in Control.

You can compare planned quantities with the current forecast in the following columns:

- **Plan component total qty**

This allows you to identify discrepancies and make adjustments as needed.

Task details		Actuals 03/24/2025 to 09/05/2025			
Forecast (T/O) qty	UoM	Actual qty (to date)	Plan component total qty	Forecast (T/O) - Plan component qty	Actual MHrs/unit (to date)
1.00	Ea	0.44			2,807.39
1,200.00	LF	720.00	1,440.00	-240.00	1.03
900.00	LF	360.00	900.00	0.00	1.19

In InEight Plan, cost items from Control are associated to more detailed components. Each component has a planned quantity and can also capture actuals as installed quantities. Multiple components may roll up to a single cost item.

For example, the Install Conduit cost item is assigned to WBS phase code 1139 in the CBS. In Plan, this cost item is represented by two components:


- Conduit Material: 150 units
- Install Conduit: 120 units

Component details				
	Name	Claiming scheme	Quantity	WBS
☐	Road Subgrade	Road Subgrade	293.60000	1008
☒	Conduit material	Conduit	150.00000	1139
☒	Install conduit	Electrical	120.00000	1139


Together, these total 270 units, which appears in Control as the Plan component total quantity for the cost item.

Tasks				Actuals 11/17/20
☐	CBS position	Description	WBS phase code	Plan component total qty
☒	5	Install conduit	1139	270.00

To align the forecast with the planned scope, use the **Update Forecast (T/O) qty with Plan component total qty** option under the Actions drop-down menu. This copies the Plan quantity directly into the Forecast (T/O) qty field.

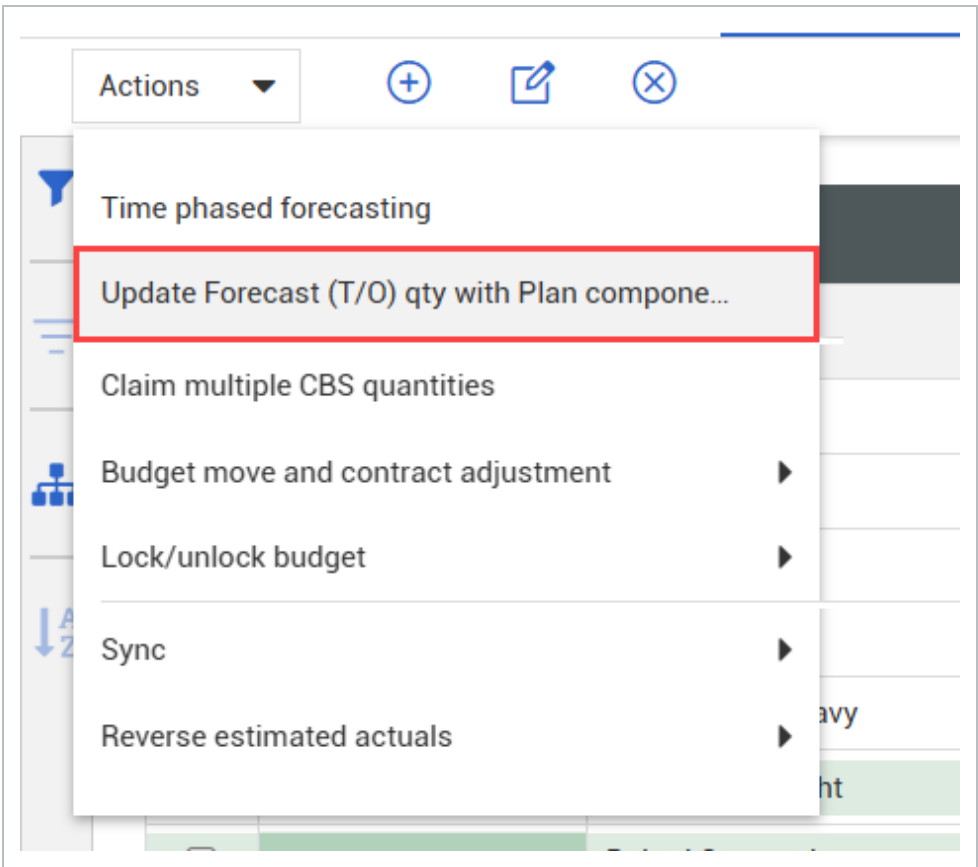

You can also access this option from the cost item menu.

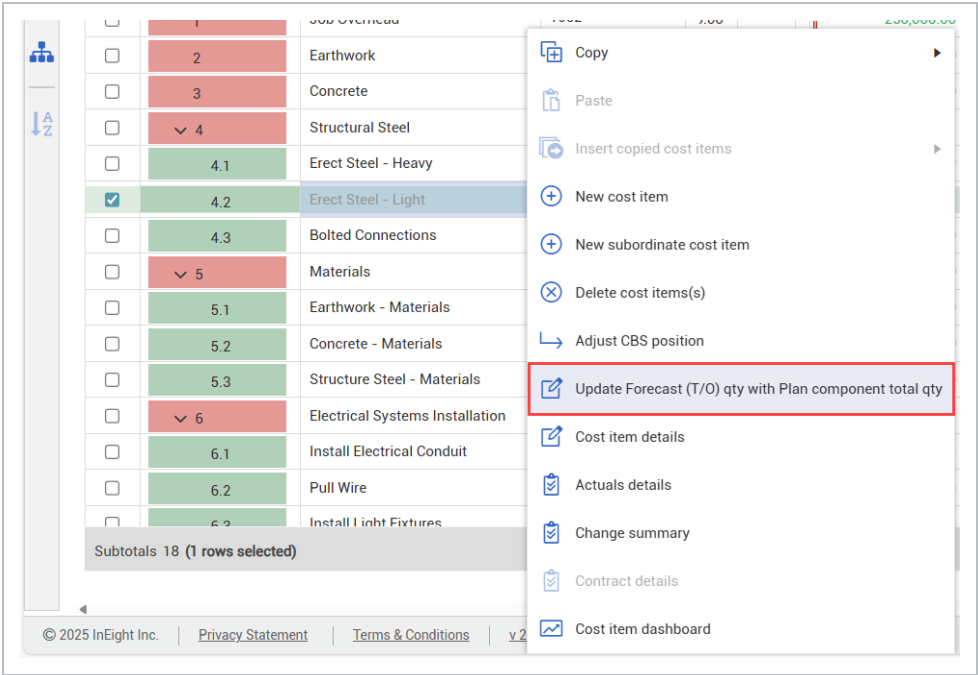


5.3 DATE RANGE SETUP


InEight Control gives you flexibility in the form of a Date Range option. The following Step by Step walks through how the Date Range setup feature works.

Date Range Setup

1. Click the **View drop-down** to change your view.



2. Select the **Progress** viewset from the View drop-down list.

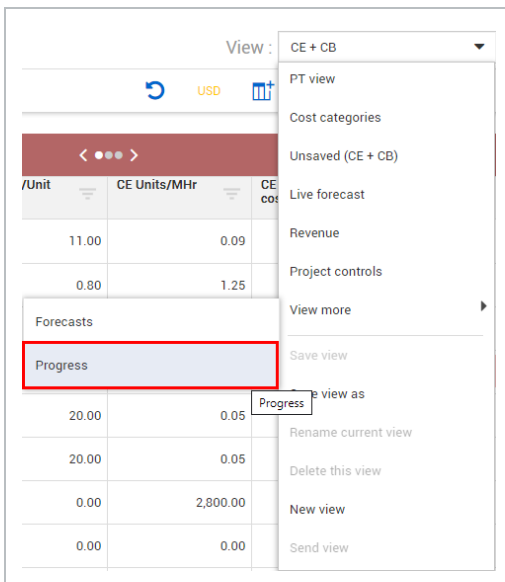


3. In the Actuals data block, select the **left calendar field** on the date range chooser and choose the first day of this month.

Actuals							6/15/2018 to 7/3/2018		< ● ● ● >	
Qty complete (to date)	June 2018						MHrs G/L (to date)	Total cost (to date)		
	Su	Mo	Tu	We	Th	Fr				
	27	28	29	30	31	1	2	0.00		\$ 0.00
	3	4	5	6	7	8	9	0.00		\$ 0.00
	10	11	12	13	14	15	16	0.00		\$ 0.00
	17	18	19	20	21	22	23	0.00		\$ 0.00
	24	25	26	27	28	29	30	0.00		\$ 0.00
	1	2	3	4	5	6	7	0.00		\$ 0.00
	Tuesday, July 03, 2018									
	0.00		0.00		0.00		0.00			\$ 0.00


- To manually select your date range, click into the date cells along the header of the Actuals data block and select your desired to and from dates
4. Select the **right calendar field** on the date range chooser and select the last day of this month.
 5. Select the **calendar** icon.

Actuals					6/15/2018 to 7/3/2018		< ● ● ● >	
	Qty complete (to date)	MHrs/Unit (to date)	CB MHrs G/L (to date)	Total cost (to date)				
	0.00	0.00	0.00	\$ 0.00				
	0.00	0.00	0.00	\$ 0.00				

6. Select **Last month end** from the calendar.

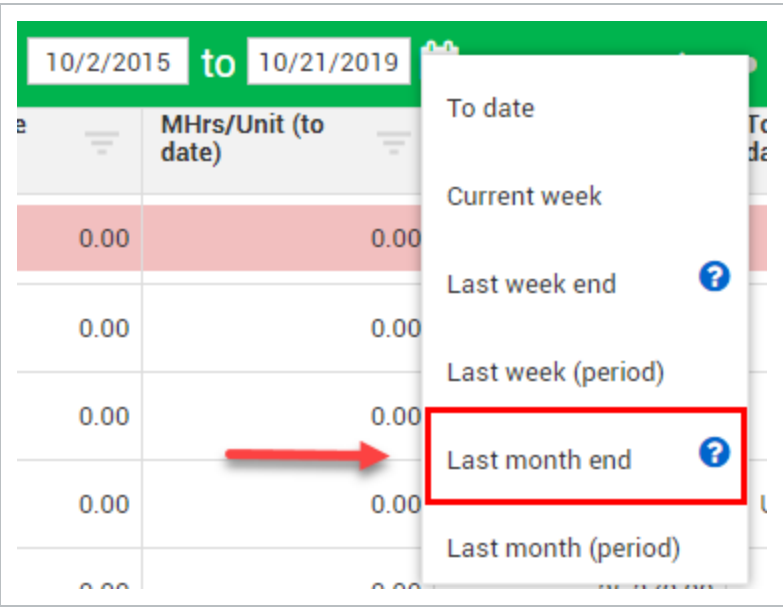

- To select your date range from the pre-set list, click on the **calendar** icon within the Actuals data block header and select the desired date option

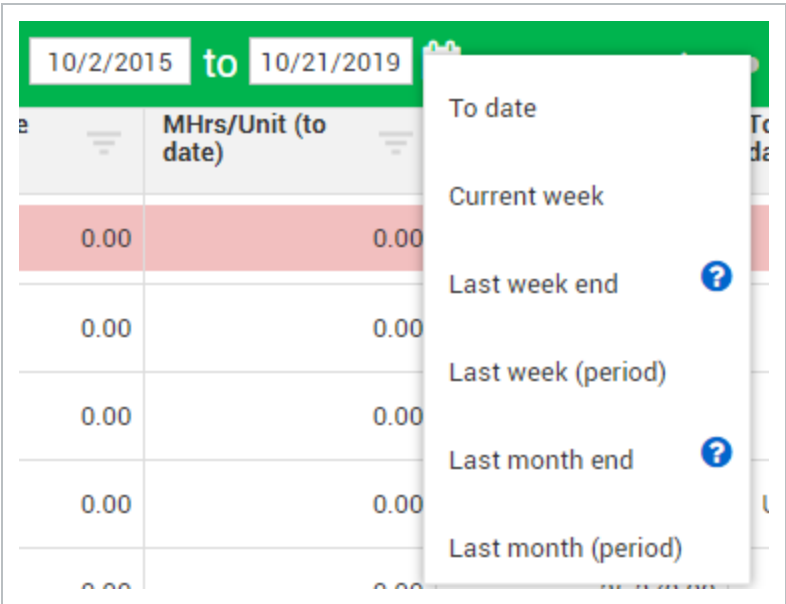

Both week and month end date rules are determined during project setup within the Fiscal Calendar setting. For more information, see the [Fiscal calendar](#) setting topic.

5.4 MANAGE ACTUALS

In Control, you can choose from four methods for tracking actual values:

- Sync – Lets you connect directly with other systems to update data in real time.
- Import – Allows you to upload spreadsheet data.
- Manual entry – You can input data directly into the system.
- API – Allows you to connect data from external sources, such as an ERP.

These methods help ensure that project records are accurate and up to date. The following topics provide more details on methods for managing actuals:

- [Actuals by Sync](#)
- [Actuals by Import](#)
- [Actuals by Manual Entry](#)
- [Actuals by API](#)

5.5 ACTUALS BY SYNC

Update Control data in real time by connecting with InEight applications and other external systems.

5.5.1 Sync Quantities


A quantities sync lets you to bring actuals from other InEight applications into Control. Quantities are brought into Control through a Get Quantities sync. The Actual qty (to date) column is updated when the sync is complete.

Actuals 05/30/2025 to 06/26/2025			
Actual qty (to date)	Actual MHrs/unit (to date)	CB MHrs G/L (to date)	
0.17	122.77	0.00	
1.00	0.00	0.00	
0.28	0.00	0.00	
0.53	0.00	0.00	
750.00	0.00	0.00	
200.00	0.00	0.00	
1.00	0.00	0.00	
0.00	0.00	0.00	


Sync operations are accessed from the Actions menu in the CBS.

Performing a Get Quantities Sync


1. From the Actions menu, choose **Sync > Get quantities**.

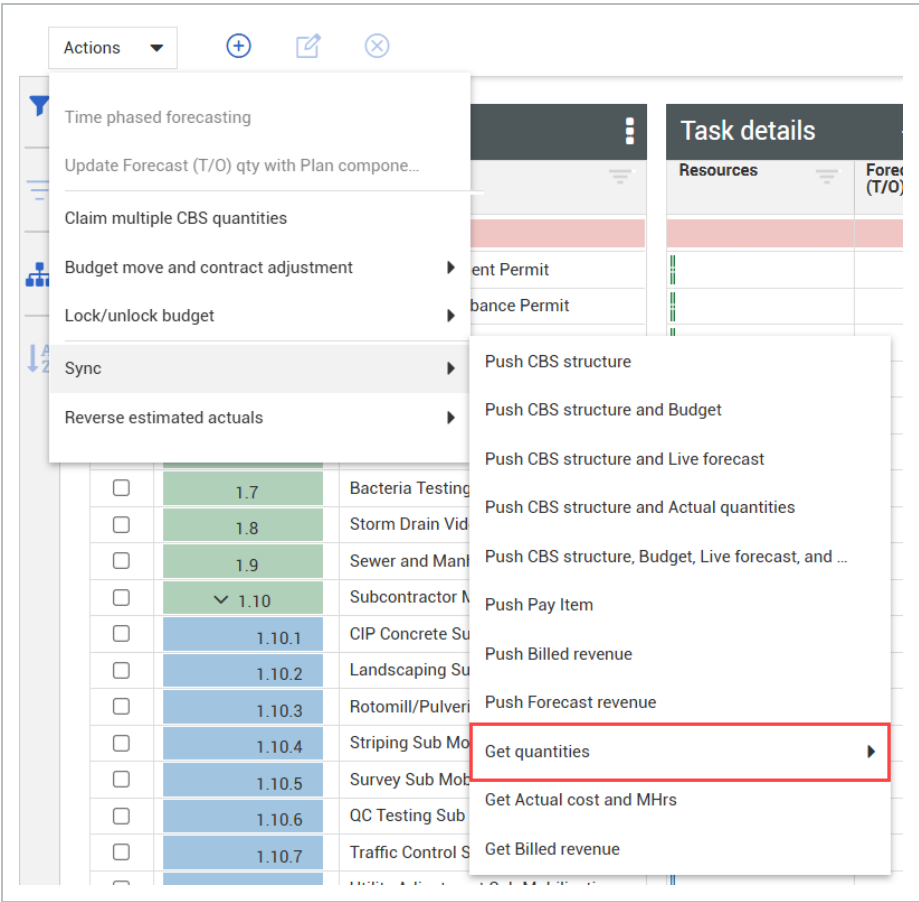

2. Choose the time period for the sync (Through previous pay period or Job to date).

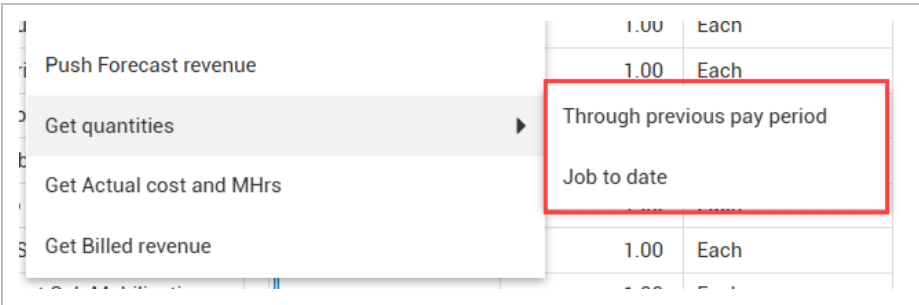

3. A status message notifies you that the sync has initiated.




5.5.1.1 Types of Get Quantities Syncs

Depending on your project configurations, the Get Quantities sync can bring in values from InEight Design, InEight Plan, or InEight Contract. Each of these applications tracks quantities differently, depending on its role in the project lifecycle.


InEight Design

In InEight Design, engineering deliverables are broken down and tracked as scope items. As work on scope items is completed, team members can claim partial or total quantity values. Scope items are linked to cost items through the WBS phase code. As a result of a Get Quantities sync, scope item quantities update the actual quantity for their associated cost items.

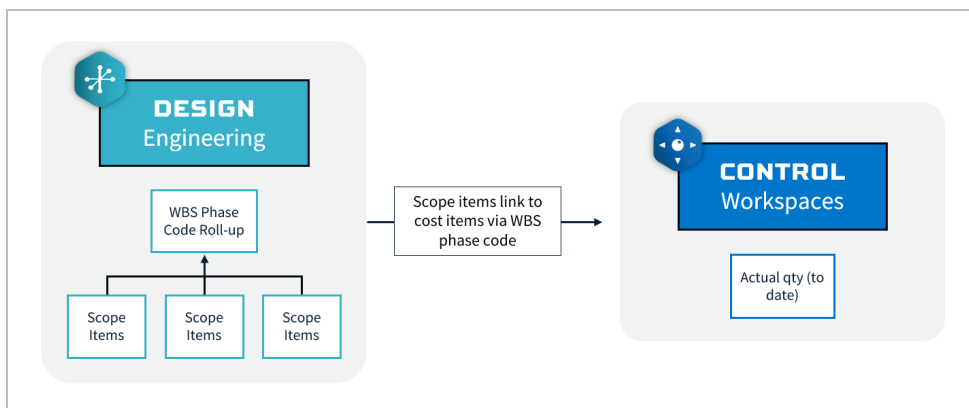


InEight Plan

Quantities from InEight Plan represent completed progress in the field. Quantities can be captured directly in the Quantity Tracking module, or they can be captured through approved daily plans from InEight Progress. Components are linked to cost items through the WBS phase code. As a result of a Get Quantities sync, component quantities update the actual quantity for their associated cost items.

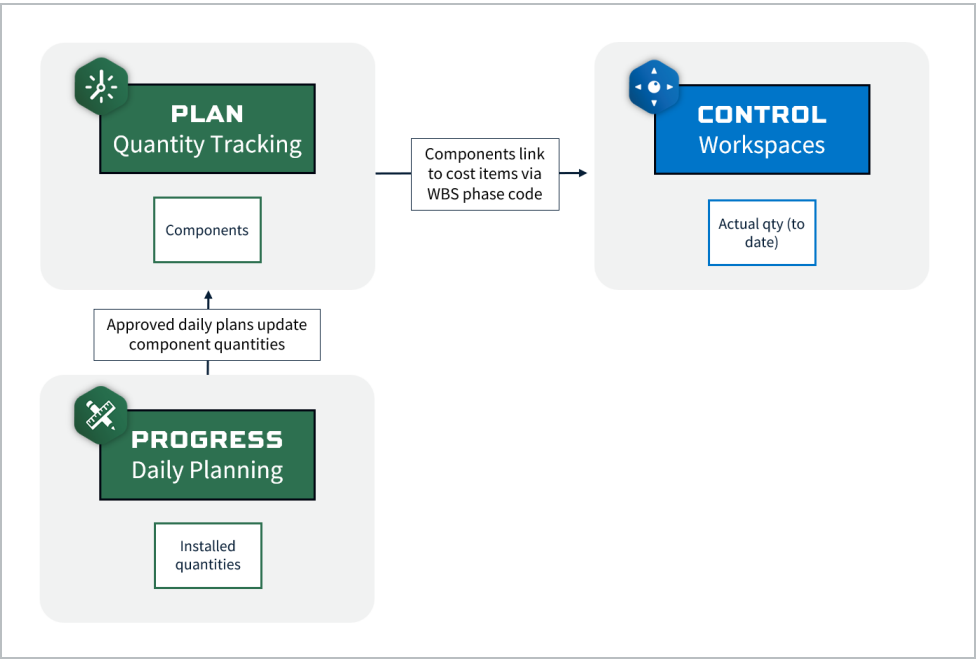


InEight Contract

Quantities from InEight Contract represent completed progress associated with a third-party contract. Contract line items can be broken down into schedule of value items to track field progress. These SOV items can be claimed directly in InEight Contract, or they can be claimed as contract components in InEight Plan. SOV items are linked to cost items through the WBS phase code. As a result of a Get Quantities sync, SOV quantities update the percent complete and actual quantity for their associated cost items.

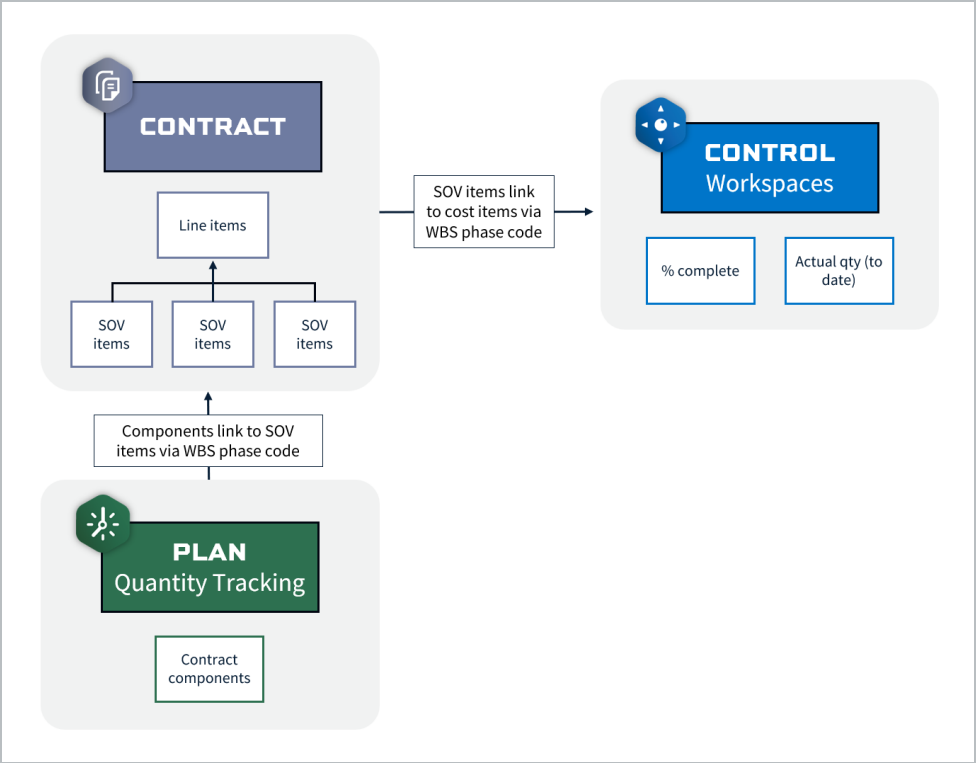

To update complete from InEight Contract, you must enable the settings for the project in Control > Project Tracking > **Actuals**. Switch the **Update % complete from Contract** toggle to *On*.

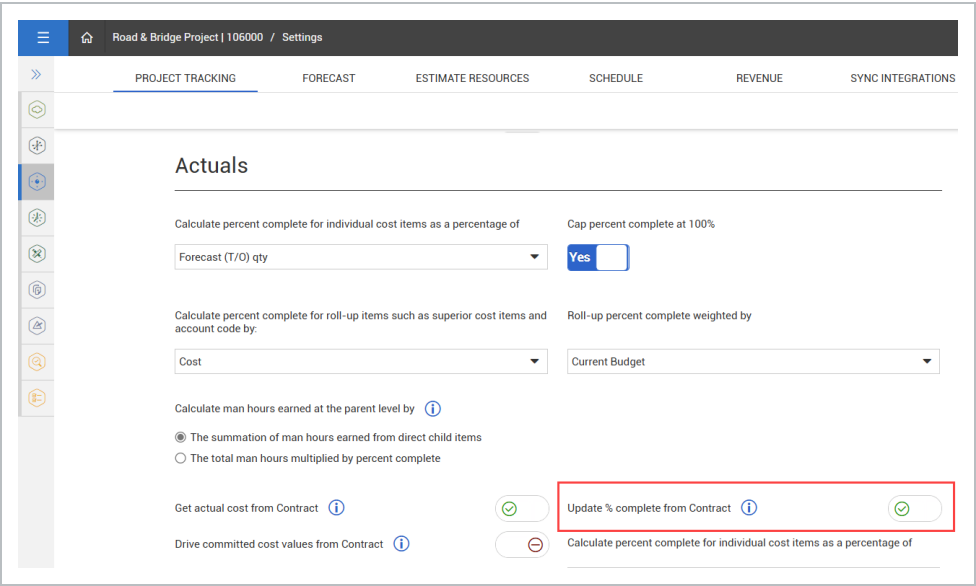

After the Update % complete from Contract setting is enabled, select from the **Calculate percent complete for individual cost items as a percentage of** drop-down list to define how you want to calculate the percent complete for cost items.

Update % complete from Contract 



Calculate percent complete for individual cost items as a percentage of

Current budget total cost

Current budget total cost

Committed total cost

Forecast total cost

Current estimate total cost

The calculation for this option is: (updated % complete on the cost item) = (SOV unit price) x (Claimed qty in Contract or Plan) ÷ (Denominator in settings). Actual qty (to date) = % complete * Forecast (T/O) qty OR CB total qty (depending on settings).


5.5.2 Sync Hours and Costs

If your project uses external systems to capture man-hours and costs, those values can be brought into Control through a sync. If your project uses an ERP system, you can bring in man-hours and costs by performing a Get Actual Cost and MHrs sync. If you have values tracked through contracts, you can enable project settings to bring those values in from InEight Contract. Hours and costs brought into Control through a sync update which updates the Actual cost (to date) and Actual MHrs (to date) columns.


Actuals 05/30/2025 to 06/26/2025	
Actual cost (to date)	Actual MHrs (to date)
\$ 583,998.84	1,935.50
\$ 524,328.84	1,824.00
\$ 0.00	0.00
\$ 104,100.00	0.00
\$ 12,800.00	0.00
\$ 62,375.00	1,800.00

ERP

After man-hours and costs are verified in your ERP system, you can initiate a sync to bring those values into Control. Similar to the Get Quantities sync, the Get Actual Cost and MHrs sync is accessed from the Actions menu.

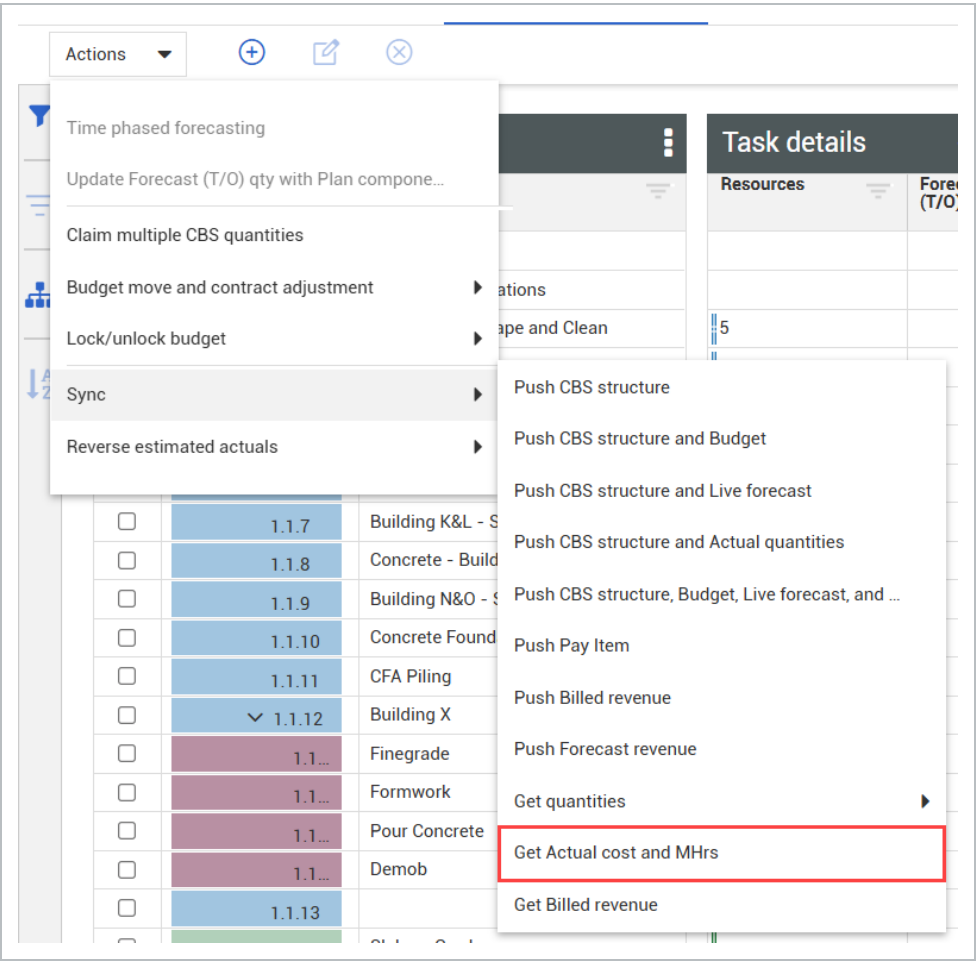

If your project captures work hours through InEight Progress, those hours and their associated costs are approved in Progress before being sent to the ERP.

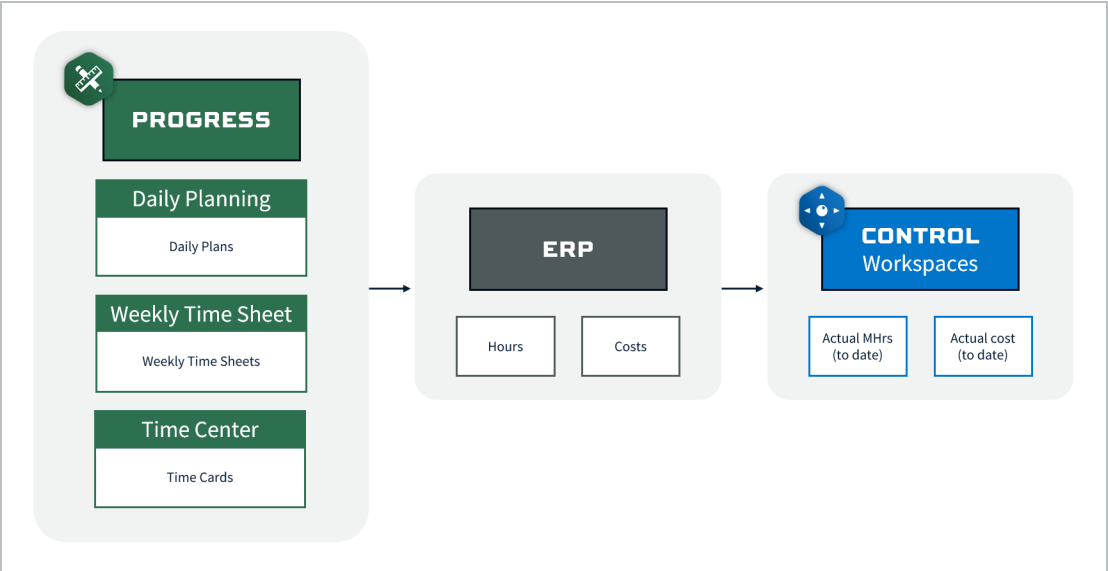

InEight Contract


InEight Contract can record actual costs in the form of goods receipts, accruals, invoice receipts, or payment forms. You can configure your project settings to pull these actual costs into Control through a batch process.

In project settings, under Control > Project Tracking > **Actuals**, switch the **Get actual cost from Contract** toggle to *On*.

The screenshot shows the 'Actuals' configuration page. The left sidebar has a 'PROJECT TRACKING' tab selected. The main content area has a title 'Actuals' and several settings:

- Calculate percent complete for individual cost items as a percentage of:** A dropdown menu is set to 'Forecast (T/O) qty'. To the right, there is a 'Cap percent complete at 100%' label and a 'Yes' toggle which is turned on.
- Calculate percent complete for roll-up items such as superior cost items and account code by:** A dropdown menu is set to 'Cost'. To the right, there is a 'Roll-up percent complete weighted by' label and a dropdown menu set to 'Current Budget'.
- Calculate man hours earned at the parent level by:** Two radio button options are present:
 - ☒ The summation of man hours earned from direct child items
 - ☐ The total man hours multiplied by percent complete
- Get actual cost from Contract:** This toggle is highlighted with a red box and is turned on, indicated by a green checkmark.
- Update % complete from Contract:** This toggle is turned off, indicated by a grey circle with a minus sign.
- Drive committed cost values from Contract:** This toggle is turned off, indicated by a grey circle with a minus sign.

After you enable this setting, Contract values update the actual cost for the associated cost items. Note that it may take up to 15 minutes for the background batch process to complete.

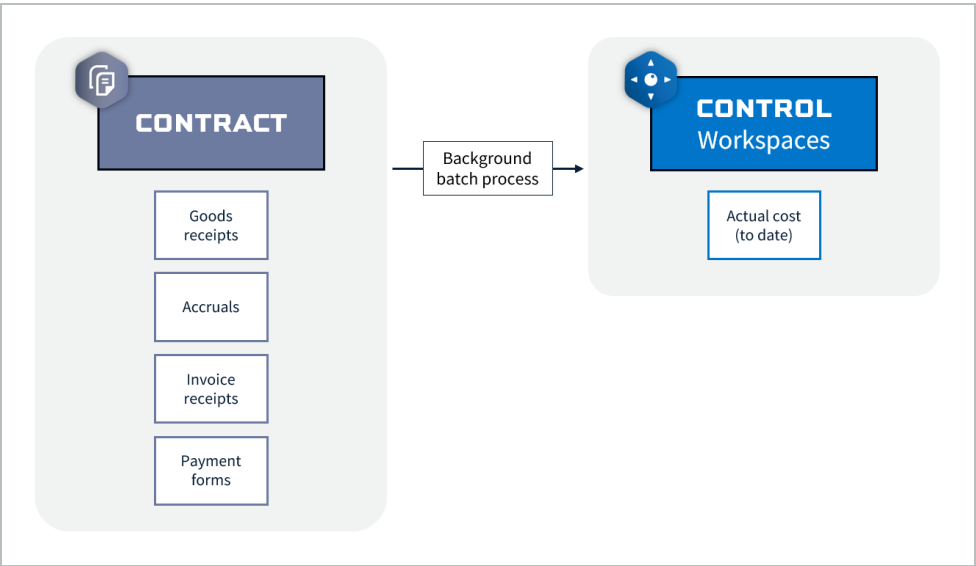

5.5.3 Audit Log

You can check the status of a sync in the Audit Log on the Integration tab.


CBS ACS PAY ITEMS CHANGE REGISTER AUDIT LOG								
Actions								
	☐	Audit ID	Interface	Status	Processing details	Start	Finish	Log Handle
CBS	☐	2150	Quantities - Job to date	Succeeded	2 of 2	10/16/2024 12:15 PM	10/16/2024 12:15 PM	3941e926-52ed-461c-bc23-1f48d56f41cb
ACS	☐	1710	Budget	Failed	Failed at 1	03/10/2023 12:33 PM	03/10/2023 12:48 PM	ef916a4f-5ed8-4563-8ed7-7fe1fa37b3a
Pay Items	☐	1709	CBS	Succeeded	4 of 4	03/10/2023 12:33 PM	03/20/2023 05:30 AM	6eae0491-75b8-4f3f-8908-a1bfb1bffd4
Integration	☐	1706	Quantities - Job to date	Succeeded	2 of 2	02/23/2023 12:26 PM	02/23/2023 12:26 PM	307397f1-889a-4eeb-b9d5-a14ee876543a
	☐	1705	Quantities - Job to date	Succeeded	2 of 2	02/23/2023 12:04 PM	02/23/2023 12:04 PM	43c1d5ec-d32f-4357-bf70-90edf8d375bf
Import history	☐	1704	Quantities - Job to date	Succeeded	2 of 2	02/23/2023 11:49 AM	02/23/2023 11:49 AM	5f805bec3-8d6f-45e1-a269-283a6f43742c
	☐	1661	ActualMHCost	InProcess	0 of 3	12/07/2022 03:26 PM		de1ffe21-8ae0-41f1-8399-e93c29a86b56

5.6 ACTUALS BY IMPORT

You can import actual costs, man-hours and quantities by using an Excel or CSV file.

An actuals import is similar to claiming actuals in Control. After you upload a spreadsheet containing actuals, those values are added to any existing actuals for the specified cost items. Your spreadsheet values should represent new claiming on a cost item rather than the total sum to date.

From the CBS tab in Control Workspaces, you can access the Import function by clicking the **Import** icon, and then selecting **Actuals**.

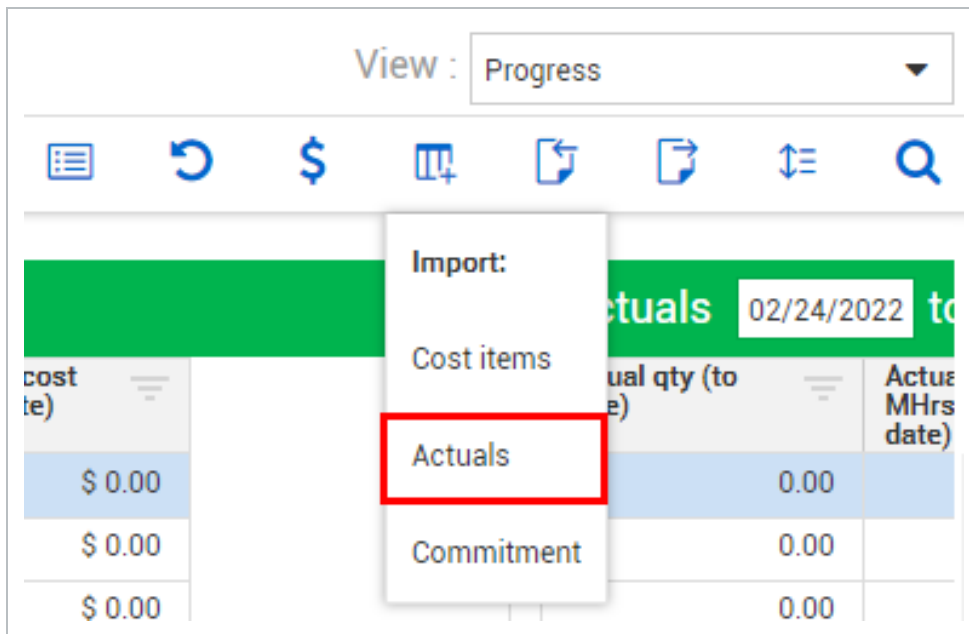

After you add the import file, you can select the matching criteria in the Map columns dialog box. The Map columns dialog box has a select number of Control fields which pertain to actuals. The table below shows details of the available fields.


Control field	Details
WBS phase code	The unique WBS phase code. Can be used as the cost item matching criteria. Required to select this or CBS position as the cost item matching criteria.
CBS position	The position in the CBS hierarchy. Can be used as the cost item matching criteria. Required to select this or WBS phase code as the cost item matching criteria.
Posting date	Required field. Control will prompt you to specify the date format used in your import file.
Notes	Text field for any notes that pertain to this specific claiming update.
Claimed quantities	Quantities in this field will be added to the Actual qty (to date) field for the specified cost items.
Number of man hours	Values in this field will be added to the Actual Mhrs (to date) field for the specified cost items.
Number of equipment	Values in this field will be added to the Actual eqp hrs (to date) field for

Control field	Details
hours	the specified cost items.
Cost	Values in this field will be added to the Actual cost (to date) field for the specified cost items.
Cost categories	You can download a list of your project's cost categories from the Import actuals data dialog box. The values in the import file must match the Control values exactly.
Actuals user defined 1-2	Use these fields to enter dates based on customized field labels set up in Platform > Suite Administration > Custom labels.
Actuals user defined 3-6	Use these free text fields to enter any variable attribute based on customized field labels set up in Platform > Suite Administration > Custom labels.
Estimate Resource	You can specify estimate resources to be included with this claiming update. Use the resource code for the estimate resource as the value for this field. This update will be visible from the Actuals Details tab in Actuals History.


Follow the steps below to import actuals.

Import Actuals

1. Prepare the import file.
2. From the CBS, click Import > **Actuals**.

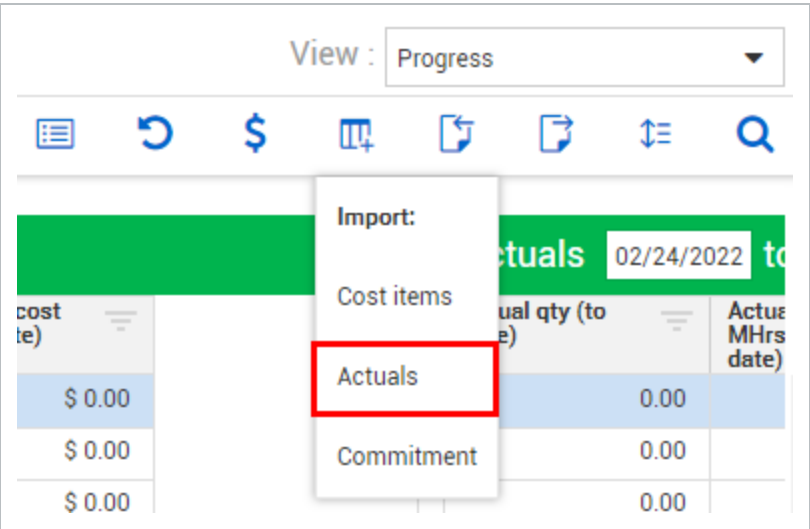

3. In the Import actuals data dialog box, add the import file, and then select the cost item matching criteria.

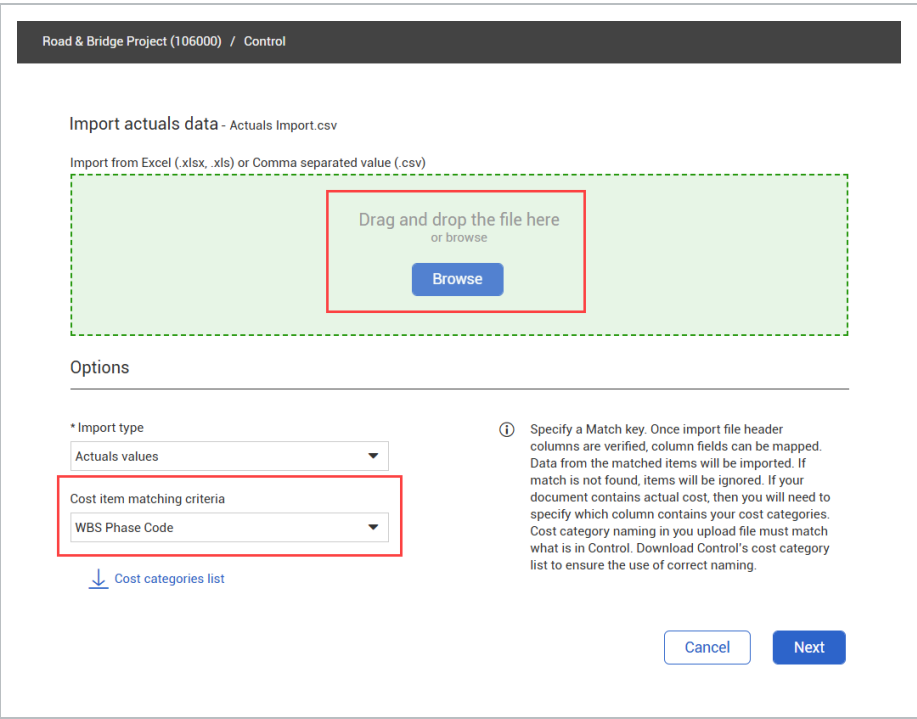

4. Map the Control fields to the file columns.

Import actuals data - Actuals Import.csv

Map columns

Template

Unsaved template

Control field	Mapped	File columns
Tasks		
* WBS phase code	q	WBS phase code
CBS position		only used if matching
Actuals		
* Posting date	✓	Date
Notes		Blank-do not import
Claimed quantities	✓	Actual qty (to date)
Number of man hours	✓	MHrs
Number of equipment hours	✓	Equipment
Cost	✓	Cost

* Required fields

Reset

Cancel

Back

Next

5. Select the date format used in the import file.

Mapped

File columns

Select date...

MM/DD/YYYY


Choose date format currently displayed in file. Selected format will be converted to match user settings.

Cancel

Back

Next

6. The import file will be checked for errors. If the file contains no errors, click **Next**.
If the import contains errors, download the error file for more information.
7. Click **Import now** to complete the import.

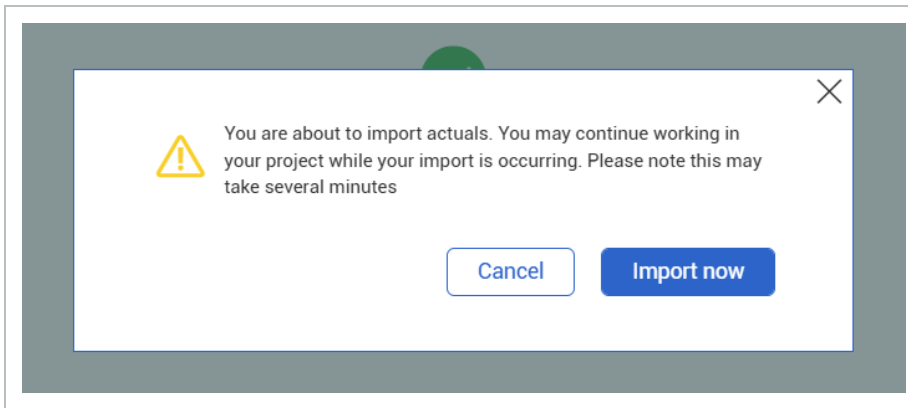

Visit [Cost Item Excel Import](#) for more information on performing an import.


5.7 ACTUALS BY MANUAL ENTRY

In some situations, you may need to enter actuals directly in InEight Control. This can be helpful when field data is delayed, incomplete, or needs correction. Manual entry also gives you greater flexibility when tracking progress tied to lump sum or indirect costs, or when values include confidential or sensitive data.


The steps below outline how to claim actuals by manual entry.

Claim Actuals by Manual Entry

- 1. From the CBS, right-click a cost item, and then select **Actuals details**.

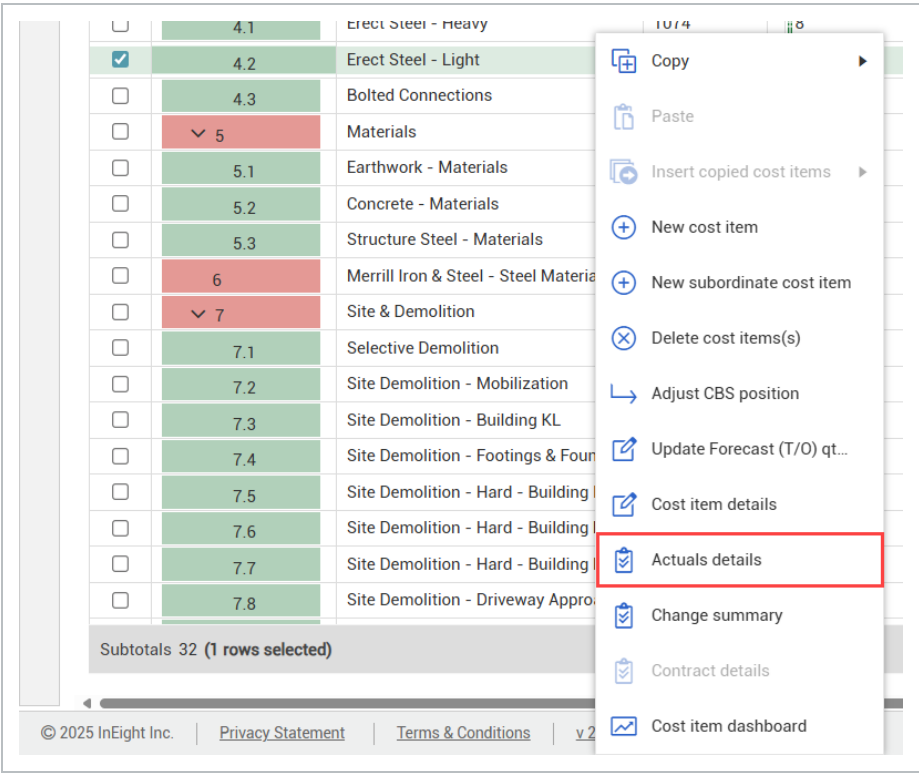

- 2. On the Claim Actuals tab of the slide-out panel, select the type of actuals from the tabs on the left.

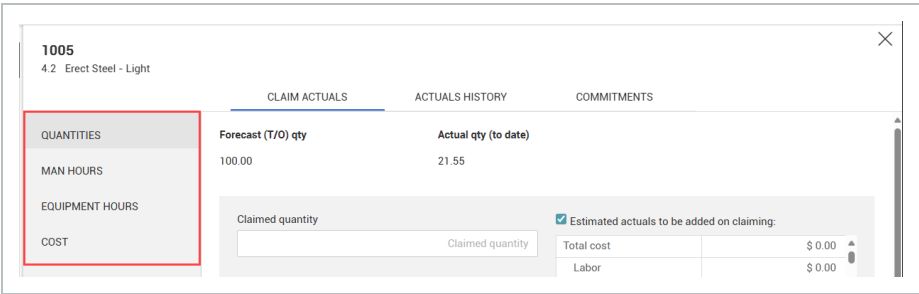

- 3. Enter the quantity, hours, or cost to be claimed.

CLAIM ACTUALS

ACTUALS HISTORY

COMMITMENTS

QUANTITIES

MAN HOURS

EQUIPMENT HOURS

COST

Forecast (T/O) qty

100.00

Actual qty (to date)

21.55

Claimed quantity

15.00

Posted date

06/30/2025

Estimated actuals to be

Total cost

Labor

Construction Equipmen

ENM Rented Equipment

4. Enter additional details as needed.

CLAIM ACTUALS

ACTUALS HISTORY

COMMITMENTS

Posted date

06/30/2025

Start date

06/23/2025

Area

South

Actuals user defined 5

Actuals user defined 5

Estimate resource

Estimate resource

Notes

Notes

Finish date

06/27/2025

Actuals user defined 4

Actuals user defined 4

Actuals user defined 6

Actuals user defined 6

5. When finished, click **Apply**.

5.7.1 Claim Quantities

Track completed progress progress on a cost item by entering a claim on the Quantities tab in the Actuals details slide-out panel.

Before claiming quantities for a cost item, make sure the *Hide in Plan, Progress, and Design* column is checked. This option prevents conflicts by making the cost item unavailable for claiming outside of Control.

Tasks

☐	CBS position	Description	WBS phase code
☐	2	Construction	1011
☐	2.1	Bridge Work	1012

Task details

Hide in Plan, Progress, and Design	Is terminal
☐	☐
☒	☐

See the table below for details on the available fields on the Quantities tab.

CLAIM ACTUALS

ACTUALS HISTORY

COMMITMENTS

QUANTITIES

MAN HOURS

EQUIPMENT HOURS

COST

Forecast (T/O) qty

Actual qty (to date)

4,331.00

2,576.45

Claimed quantity

Posted date

Claimed quantity

07/01/2025

Actuals user defined 1

Actuals user defined 2

Actuals user defined 3

Actuals user defined 4

Actuals user defined 5

Actuals user defined 6

Estimate resource

Estimate resource

Notes

4000

Notes

Field	Details
Forecast (T/O) qty	Shows the forecast takeoff quantity for the cost item.
Actual qty (to date)	Shows the actual quantity claimed to date for the cost item.
Claimed quantity	Required field. Enter the quantity you wish to claim for this entry.
Posted date	Select a posting date for this claiming entry.
Actuals user defined 1-2	Use these fields to enter dates based on customized field labels set up in Platform > Suite Administration > Custom labels .
Actuals user defined 3-6	Use these free text fields to enter any variable attribute based on customized field labels set up in Platform > Suite Administration > Custom labels .

(continued)

Field	Details
Estimate resource	You can select a resource from the Project library. You can only select one resource per entry.
Notes	Enter any notes pertinent to this claiming entry.

You can enter negative quantities when claiming in Control.

5.7.1.1 Claim quantities for multiple cost items

Select Claim quantities for multiple cost items to claim actuals for multiple cost items on the same posting date. The Claim quantities for multiple cost items window shows the same fields that are found on the Quantities claiming tab in a grid format.

Claim quantities for multiple cost items

Load template

Save as template

Note: Cost items that cannot be claimed are not displayed in this list.

Posted date

07/01/2025

Claim multiple actuals:

Action	CBS position	WBS phase code	Description	CE UoM	Forecast (T/O) qty	CB - total quantity	Actual qty (to date)	Claimed quantity	Acti defi
⊖	1.1.6	1007	Drainage - System	LF	4,331.00	0.00	2,576.45	0.00	

⊕

Add cost item

Cancel

Claim

Follow the steps below to complete a manual claim for multiple cost items.

Claim Quantities for Multiple Cost Items

1. From Claim Actuals > Quantities of the Actuals Details slide-out panel, click **Claim quantities for multiple cost items**.

Notes

4000

Notes

+

Add claimed quantity

Claim quantities for multiple cost items

Cancel

Apply

2. Select the posting date for this claim.

Claim quantities for multiple cost items

Load template Save as template

Note: Cost Items that cannot be claimed are not displayed in this list.

Posted date
07/01/2025

SU	MO	TU	WE	TH	FR	SA	Description	CE UoM	Forecast (T/O) qty	CB - total quantity	Actual qty (to date)
29	30	1	2	3	4	5	Drainage - System	LF	4,331.00	0.00	2,576.45
6	7	8	9	10	11	12					
13	14	15	16	17	18	19					
20	21	22	23	24	25	26					
27	28	29	30	31	1	2					
3	4	5	6	7	8	9					

TUESDAY, JULY 1, 2025

Cancel Claim

3. Click **Add cost item** to add additional cost items to claim on this posting date.

Claim quantities for multiple cost items

Load template Save as template

Note: Cost items that cannot be claimed are not displayed in this list.

Posted date
07/01/2025

Claim multiple actuals:

Action	CBS position	WBS phase code	Description	CE UoM	Forecast (T/O) qty	CB - total quantity	Actual qty (to date)	Claimed quantity	Act defi
-	1.1.6	1007	Drainage - System	LF	4,331.00	0.00	2,576.45	0.00	

+ Add cost item

Cancel Claim

4. Click the checkbox to select cost items. When you are finished, click **Add**.

Add CBS items

Notes : Cost items that cannot be claimed are not displayed in this list .

Search...

Tasks

☐	CBS position	WBS phase code	Descrip...	CE UoM	Forecast (T/O) qty	CB - total quantity	Actual qty (to date)	Claimed quantity
☐	1.1.1	1002	Structural So...	SF	35,210.00	0.00	29,150.00	0
☐	1.1.2	1003	Walls - SB Ra...	SF	13,000.00	0.00	13,000.00	0
☐	1.1.3	1004	Structural - S...	SF	640.00	0.00	640.00	0
☐	1.1.4	1005	Traffic Model ...	LF	2,454.00	0.00	2,208.60	0
☒	1.1.5	1006	Roadway - Cl...	LF	3,000.00	0.00	2,550.00	0
☐	1.1.7	1008	Landscape - ...	Acre	1.00	0.00	1.00	0
☐	1.1.8	1009	D16 408 Permit	Each	1.00	0.00	1.00	0
☐	1.1.9	1010	Geo Report	Each	2.00	0.00	2.00	0
☒	2.1.1	1013	Erect Structur...	Ton	1,500.00	0.00	0.00	0

2 items selected

Cancel

Add

5. Click inside the **Claimed quantity** field to enter a quantity for each cost item.

Claim quantities for multiple cost items

Load template

Save as template

Note: Cost items that cannot be claimed are not displayed in this list.

Posted date

07/01/2025

Claim multiple actuals:

Description	CE UoM	Forecast (T/O) qty	CB - total quantity	Actual qty (to date)	Claimed quantity	Actuals user defined 1	Actuals user defined 2
Drainage - System	LF	4,331.00	0.00	2,576.45	1,000.00		
Roadway - Civil Design	LF	3,000.00	0.00	2,550.00	500.00		
Erect Structural Steel for Bridges	Ton	1,500.00	0.00	0.00	300		

Add cost item

Cancel

Claim

6. Enter additional details as necessary.

Claim quantities for multiple cost items

Load template

Save as template

Note: Cost items that cannot be claimed are not displayed in this list.

Posted date

07/01/2025

Claim multiple actuals:

Actuals user defined 2	Actuals user defined 3	Actuals user defined 4	Actuals user defined 5	Actuals user defined 6	Estimate resource	Notes
						Storm event on 6/30

Add cost item

Cancel

Claim

7. When finished, click **Claim**.

Note that you can also claim quantities for multiple cost items by selecting the cost items in the CBS register, and then opening the Actions menu and choosing **Claim multiple CBS quantities**.

Actions

Update Forecast (T/O) qty with Plan compone...

Claim multiple CBS quantities

Budget move and contract adjustment

Lock/unlock budget

Sync

			WBS phase code
			1000
		d Bridge	1001
		Bound Ramp/Bri...	1002
		o/Bridge	1003
☐	1.1.3	Structural - SB Ramp/Bridge Misc ...	1004
☒	1.1.4	Traffic Model - Development/Anal...	1005
☒	1.1.5	Roadway - Civil Design	1006
☒	1.1.6	Drainage - System	1007
☐	1.1.7	Landscape - SB Ramp/Bridge	1008

5.7.2 Claim Man-hours

Claim work hours for a specific employee or for a crew on the Man Hours tab in the Actuals details slide-out panel.

To claim hours for a crew, enter the total number of hours worked in the Number of hours field and leave the Employee name and Employee ID number fields blank.

See the table below for details on the available fields on the Man Hours tab.

CLAIM ACTUALS

ACTUALS HISTORY

COMMITMENTS

QUANTITIES

MAN HOURS

EQUIPMENT HOURS

COST

CE total MHRs

MHRs(to date)

12,000.00

0.00

Number of hours

Posted date

Employee name

Employee ID number

Actuals user defined 1

Actuals user defined 2

Actuals user defined 3

Actuals user defined 4

Actuals user defined 5

Actuals user defined 6

Estimate resource

Notes

4000

Field	Details
CE total MHRs	Shows the Current Estimate total man-hours for the cost item.
MHRs (to date)	Shows the actual man-hours claimed to date for the cost item.
Number of hours	Required field. Enter the hours you wish to claim for this entry.
Posted date	Select a posting date for this claiming entry.
Employee name	If entering hours for a single employee, enter the employee name. Make sure that the entry matches the name in the employee record.
Employee ID	If entering hours for a single employee, enter the ID number. Make sure that the entry matches the ID number in the employee record.

Field	Details
Actuals user defined 1-2	Use these fields to enter dates based on customized field labels set up in Platform > Suite Administration > Custom labels .
Actuals user defined 3-6	Use these free text fields to enter any variable attribute based on customized field labels set up in Platform > Suite Administration > Custom labels .
Estimate resource	You can select a resource from the Project library. You can only select one resource per entry.
Notes	Enter any notes pertinent to this claiming entry.

5.7.3 Claim Equipment Hours

Claim hours for an equipment item on the Equipment Hours tab in the Actuals details slide-out panel. See the table below for details on the available fields on the Equipment Hours tab.

CLAIM ACTUALS

ACTUALS HISTORY

COMMITMENTS

QUANTITIES

MAN HOURS

EQUIPMENT HOURS

COST

CE total equipment Hrs

Equipment Hrs (to date)

1,800.00

0.00

Equipment ID #

Posted date

Equipment ID #

07/01/2025

Hours used

Hours used

Actuals user defined 1

Actuals user defined 2

Actuals user defined 3

Actuals user defined 4

Actuals user defined 5

Actuals user defined 6

Estimate resource

Notes

Notes

4000

Field	Details
CE total equipment Hrs	Shows the Current Estimate total man-hours for the cost item.

Field	Details
Equipment Hrs (to date)	Shows the actual equipment hours claimed to date for the cost item.
Equipment ID #	You can enter the ID for the equipment item. Make sure that the entry matches the ID number in the equipment record.
Posted date	Select a posting date for this claiming entry.
Hours used	Required field. Enter the hours you wish to claim for this entry.
Actuals user defined 1-2	Use these fields to enter dates based on customized field labels set up in Platform > Suite Administration > Custom labels .
Actuals user defined 3-6	Use these free text fields to enter any variable attribute based on customized field labels set up in Platform > Suite Administration > Custom labels .
Estimate resource	You can select a resource from the Project library. You can only select one resource per entry.
Notes	Enter any notes pertinent to this claiming entry.

5.7.4 Claim Cost

Claim cost for a cost item on the Cost tab in the Actuals details slide-out panel. See the table below for details on the available fields on the Cost tab.

CLAIM ACTUALS

ACTUALS HISTORY

COMMITMENTS

QUANTITIES

MAN HOURS

EQUIPMENT HOURS

COST

CE total cost

Actual cost (to date)

\$ 50,000.00

\$ 5,221.75

Claimed cost

Claimed cost

Cost category

Posted date

07/01/2025

Actuals user defined 1

Actuals user defined 2

Actuals user defined 3

Actuals user defined 3

Actuals user defined 4

Actuals user defined 4

Actuals user defined 5

Actuals user defined 5

Actuals user defined 6

Actuals user defined 6

Estimate resource

Notes

4000

Notes

Field	Details
CE total cost	Shows the Current Estimate total cost for the cost item.
Actual cost (to date)	Shows the actual cost claimed to date for the cost item.
Claimed cost	Required field. Enter the cost you wish to claim for this entry.
Cost category	Required field. Select the cost category for this entry.
Posted date	Select a posting date for this claiming entry.
Actuals user defined 1-2	Use these fields to enter dates based on customized field labels set up in Platform > Suite Administration > Custom labels .
Actuals user defined 3-6	Use these free text fields to enter any variable attribute based on customized field labels set up in Platform > Suite Administration > Custom labels .
Estimate resource	You can select a resource from the Project library. You can only select one resource per entry.
Notes	Enter any notes pertinent to this claiming entry.

5.7.5 Add Additional Claiming entries

You can record separate claiming entries for a single cost item from the Actuals Details slide-out panel. Click the Add icon from the bottom of the slide-out panel to add additional entry fields.

The screenshot shows a slide-out panel for recording actuals. At the top, there is a 'Notes' section with a text area and a character count of 4000. Below this, there are two buttons: 'Add claimed quantity' (highlighted with a red box) and 'Claim quantities for multiple cost items'. At the bottom right, there are 'Cancel' and 'Apply' buttons.

5.7.6 User-Defined Fields

There are 6 user-defined fields you can use when you claim actuals in Control. These field labels can be customized to fit your business practices. Examples of custom labels include “Start Date”, “Area”, or “Category”. An additional field is available to select a resource from the Project library.

The screenshot shows a slide-out panel for recording actuals. It includes several input fields: 'Number of hours' (with a placeholder 'Number of hours'), 'Posted date' (with a date picker showing 07/01/2025), 'Employee name' (with a placeholder 'Employee name'), and 'Employee ID number' (with a placeholder 'Employee ID number'). Below these, there are six 'Actuals user defined' fields, numbered 1 through 6, each with a placeholder and a date picker icon. At the bottom, there is an 'Estimate resource' field with a placeholder 'Estimate resource'. At the very bottom, there is a 'Notes' section with a text area and a character count of 4000.

Custom labels for the user-defined fields can be set up in Platform > Suite Administration > **Custom labels**.

User-defined field	Type	Description
Actuals user defined 1-2	Date	Use this field to enter dates, such as start and finish dates.
Actuals user defined 3-6	Free text	Use these fields to enter any variable attribute based on your business processes.
Estimate resource	Choice	Select a resource from the Project library. You can only select one resource per transaction.

5.8 ACTUALS BY API

Your organization can set up API integrations to synchronize actuals between InEight Control and an ERP or other external system. Refer to the [Control Integration Specification](#) document for more details.

5.9 USER-DEFINED FIELDS

There are 6 user-defined fields you can use when you claim actuals in Control. An additional field is available to select a resource from the Project library. The fields are available in Actual Details > **Claim Actuals** tab slide-out panels for Quantities, Man Hours, Equipment Hours, and Cost. The following fields are available:

User defined field	Type	Description
Actuals user defined 1-2	Date	You can use to enter dates such as start and finish dates among other entries.
Actuals user defined 3-6	Free text	You can enter any variable attribute based on your business processes.
Estimate resource	Choice	You can select a resource from the Project library. You can only select one resource per transaction.

CLAIM ACTUALS

ACTUALS HISTORY

COMMITMENTS

QUANTITIES

MAN HOURS

EQUIPMENT HOURS

COST

Forecast (T/O) qty

Actual qty (to date)

3,322.49000000000

1,323.49000000000

Claimed quantity

Posted date

Claimed quantity

07/31/2024

Actuals user defined 1

Actuals user defined 2

Actuals user defined 3

Actuals user defined 4

Actuals user defined 5

Actuals user defined 6

Estimate resource

Notes

4000

You can customize the field labels to fit your business practices in Platform > Suite Administration > **Custom labels**. For example, you can name Actuals user defined 3 to Area, and Actuals user defined 4 to Category.

The user-defined fields are available to use in Actions > **Claim multiple CBS quantities** dialog box. You can click in a field and enter data, including selecting an Estimate resource in the Estimate resource field. The fields can also be viewed in Actuals History tab.

You can import claim actuals and use the user-defined fields as mapped fields in the CBS Microsoft Excel import.

Page 240 of 639

InEight Inc. | Release 26.7

Import actuals data - InEight Control Columns List (9).xlsx

Map columns

Template

Unsaved template

Control field	Mapped	File columns
Cost		Blank-do not import
Cost categories		Blank-do not import
Actuals user defined date 1	✓	Start Date
Actuals user defined date 2	✓	End Date
Area	✓	Area
Actuals user defined 4		Blank-do not import

* Required fields

Reset

Cancel

Back

Next

For more information about importing actuals, see [Actuals by Import](#).

5.10 ESTIMATED ACTUALS

Estimated actuals lets you track costs, quantities, man-hours, and equipment hours on a cost item before these values are validated through the ERP system. This provides more up-to-date visibility on progress and increases forecast accuracy. Estimated actuals can be generated in Control through quantity claims, or brought in from approved daily plans in Progress. After actuals are validated in the ERP system, you can reverse the estimated actuals and maintain the confirmed actuals.

To view estimated actuals in Control, you must first enable the feature in Control's project settings. To enable, go to the Project Tracking tab in settings, and under Estimated actuals, switch the **Turn on estimated actuals** toggle to *ON*, and then select the applicable cost categories under Control and Progress.

For each cost category, we recommend enabling the setting for either Control or Progress only. We don't recommend enabling the setting for both applications at the same time.

Turn on estimated actuals: ☒

Actual type	Enable estimated actuals for:	
	Control	Progress
Labor cost	☐	☒
Labor man hours	☐	☒
Construction Equipment cost	☐	☒
Construction equipment hours	☐	☒
FOM Rented Equipment cost	☐	
Supplies cost	☒	
Materials cost	☒	
Subcontract cost	☒	
Fees cost	☐	
Allowance cost	☐	
G & A cost	☐	
Undefined cost	☐	

When you enable estimated actuals, you can add relevant columns to a data block to view estimated actuals.

Estimated Actuals											
Confirmed actual cost	Confirmed actual equipment	Confirmed actual man hours	Confirmed actual qty	Estimated actual cost	Estimated actual equipment	Estimated actual man hours	Estimated actual qty	Last estimated actual cost	Last estimated actual eqp hours reversal	Last estimated actual man hours reversal	
\$ 0.00	0.00	0.00	0.00	\$ 0.00	0.00	0.00	0.00				
\$ 92,300.00	0.00	2,030.00	2,150.00	\$ 0.00	0.00	0.00	0.00				
\$ 103,500.00	0.00	1,890.00	695.00	\$ 0.00	0.00	0.00	0.00				
\$ 76,300.00	0.00	1,620.00	0.00	\$ 33,537.35	151.00	580.50	0.00				
\$ 51,300.00	0.00	1,060.00	80.00	\$ 26,761.60	120.00	500.00	0.00				
\$ 20,500.00	0.00	400.00	21.00	\$ 6,054.00	11.00	0.00	0.55	05/14/2025 3:...		05/14/2025 3:13.5...	
\$ 4,500.00	0.00	160.00	44.00	\$ 721.75	20.00	80.50	0.00	05/06/2025 1:...			


The following table shows columns related to estimated actuals.

Column	Description
Confirmed actual cost	The expended cost verified through the ERP system.
Confirmed actual equipment	The expended equipment cost verified through the ERP system.
Confirmed actual man hours	The number of labor hours verified through the ERP system.
Confirmed actual qty	The cost item quantity verified through the ERP system.
Estimated actual cost	Recorded actual cost that has not yet been confirmed through the ERP system.
Estimated actual equipment	Recorded equipment cost that has not yet been confirmed through the ERP system.
Estimated actual man hours	Recorded labor hours that have not yet been confirmed through the ERP system.
Estimated actual qty	Recorded cost item quantity that has not yet been confirmed through the ERP system.
Last estimated actual cost reversal	The date and time the last Reverse estimated actuals > Reverse estimated actual cost action was performed.
Last estimated actual man hours reversal	The date and time the last Reverse estimated actuals > Reverse estimated actual man-hours and labor cost action was performed.
Last estimated actual eqp hours reversal	The date and time the last Reverse estimated actuals > Reverse estimated actual equipment hours and construction cost action was performed.


5.10.1 Claim Estimated Actuals in Control

Claim Estimated Actuals

1. From the CBS, right-click a cost item, and then select **Actuals details**.

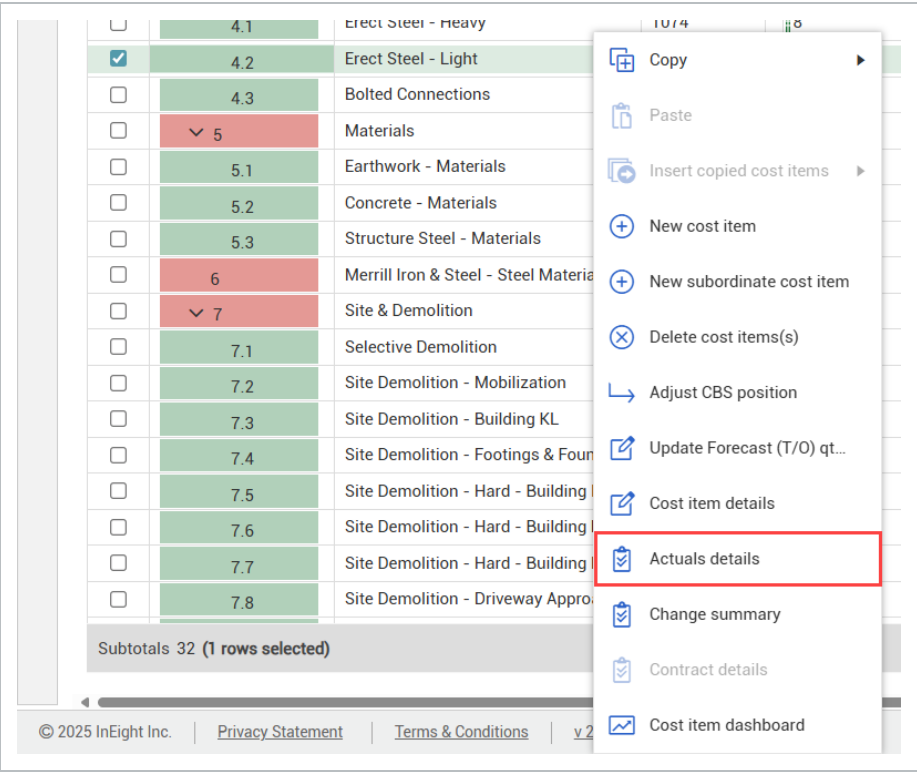

2. From the Quantities tab, enter a claimed quantity.

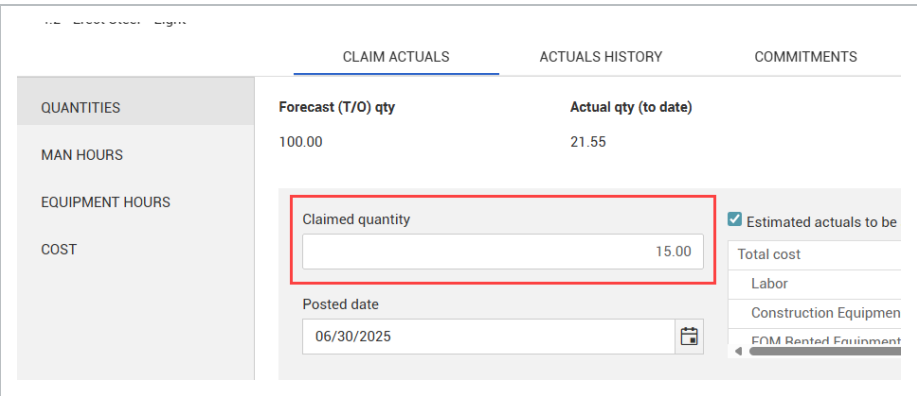

3. When you select Estimated actuals to be added on claiming, cost category values automatically populate based on the claimed quantity entered using Current Estimate unit rates.

Claimed quantity: 15.00

Posted date: 07/01/2025

☒ Estimated actuals to be added on claiming:

Total cost	\$ 375.00
Labor	\$ 375.00
Construction Equipment	\$ 0.00
FOM Rented Equipment	\$ 0.00

4. Click **Apply** when you are done.

The estimated values for the cost item can now be viewed in the relevant columns.

Estimated Actuals						
Confirmed actual cost	Confirmed actual man hours	Confirmed actual qty	Estimated actual cost	Estimated actual equipment	Estimated actual man hours	Estimated actual
\$ 0.00	0.00	0.00	\$ 0.00	0.00	0.00	
\$ 92,300.00	2,030.00	2,150.00	\$ 0.00	0.00	0.00	
\$ 103,500.00	1,890.00	695.00	\$ 0.00	0.00	0.00	
\$ 0.00	0.00	0.00	\$ 0.00	0.00	0.00	
\$ 76,300.00	1,620.00	0.00	\$ 28,703.85	140.00	610.50	
\$ 51,300.00	1,060.00	80.00	\$ 26,761.60	120.00	500.00	
\$ 20,500.00	400.00	21.00	\$ 1,220.50	0.00	30.00	
\$ 4,500.00	160.00	44.00	\$ 721.75	20.00	80.50	

5.10.2 Estimated Actuals from Progress

With the correct settings enabled, estimated actuals can be brought in from Progress based on approved daily plans. Estimated labor and equipment hours from Progress are calculated as approved hours multiplied by the operational rate codes.

This calculation differs from estimated actuals claimed in Control, which are based on claimed quantities multiplied by the current estimate unit rate.

Note in the example below, prior to the creation of a new daily plan, the estimated actuals for this cost item have a value of 0.

Steel Structure Training Job 211... / Control / Workspaces

CBS

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

View: Unsaved (Progress)

Actions

Tasks

<

In Progress, labor hours and equipment hours are tracked on the Time Sheet tab of a daily plan.

Steel Structure Training Job 2 | 1...

/ Progress / Daily planning

Daily Plans

>

Erect Steel Module 12 - 05/14/2025 (Execution) - Plan ID 63

OVERVIEW

DETAILS

TIME SHEET

QUANTITIES

NOTES / ISSUES

+

Add tasks and resources

+

Add maintenance

-

Clear hours

1005

Erect Steel - Light

:32

:

11

Alejandro Ramirez

Laborers - Laborer Journeyman

IN8-10023

MH :8

ST: 8

Maria Popova

Iron Worker - Iron Worker (Stru...

IN8-10013

MH :8

ST: 8

Grove-RT880E Crane

MC-10000000

MH :8

Operated: 8

Quantities are tracked on the Quantities tab of a daily plan.

Complete	Claim %	Step	Quantity	UoM	To date quantity	Planned quantity	Installed quantity
☒		15 Shakeout/Transport	0.30000	Ton	0	0	0.30000
☒		45 Erect/Bolt Up	0.30000	Ton	0	0	0.30000
☒		30 Final Torque	0.30000	Ton	0	0	0.30000
☐		10 QC Verification	0.30000	Ton	0	0	0
		Component total	0.30000	Ton	0.00000	0.00000	0.27000

After the daily plan is submitted and approved in Progress, the estimated actuals values automatically update in Control.

Tasks	CBS position	Description	WBS phase code	Confirmed actual cost	Confirmed actual equipment	Confirmed actual man hours	Confirmed actual qty	Estimated actual cost	Estimated actual equipment	Estimated actual man hours	Estimated actual qty	Last estimated actual cost
☐	1	Job Overhead	1002	\$ 0.00	0.00	0.00	0.00	\$ 0.00	0.00	0.00	0.00	
☐	2	Earthwork	1069	\$ 92,300.00	0.00	2,030.00	2,150.00	\$ 0.00	0.00	0.00	0.00	
☐	3	Concrete	1071	\$ 103,500.00	0.00	1,890.00	695.00	\$ 0.00	0.00	0.00	0.00	
☐	4	Bolted Connections	1110	\$ 0.00	0.00	0.00	0.00	\$ 0.00	0.00	0.00	0.00	
☐	5	Structural Steel	1073	\$ 76,300.00	0.00	1,620.00	0.00	\$ 34,247.35	151.00	612.50	0.00	
☐	5.1	Erect Steel - Heavy	1074	\$ 51,300.00	0.00	1,060.00	80.00	\$ 26,761.60	120.00	500.00	0.00	
☒	5.2	Erect Steel - Light	1005	\$ 20,500.00	0.00	400.00	21.00	\$ 6,764.00	11.00	32.00	0.55	05/14/2025 2...
☐	5.3	Bolted Connections	1006	\$ 4,500.00	0.00	160.00	44.00	\$ 721.75	20.00	80.50	0.00	05/06/2025 1...
☐	6	Materials	1084	\$ 604,400.00	0.00	0.00	0.00	(\$ 250,000.00)	0.00	0.00	0.00	

Estimated actuals values are only general estimates. They are not confirmed until synced with an ERP or an external payroll system.


5.10.3 Reverse Estimated Actuals

After actuals are reviewed and confirmed in your ERP system, they are brought into Control through a sync. These values are then reflected as “confirmed” actuals. Following this process, you can reverse the estimated actuals, since the confirmed actuals now reflect the most up-to-date information.


If you keep the estimated values without reversing after syncing with the ERP system, those values are detected as double values.

Reverse Estimated ACTuals

- 1. From the CBS, select the cost items which have recorded estimated actuals.
- 2. From the Actions menu, select **Reverse estimated actuals**, and then select the appropriate type of reversal.

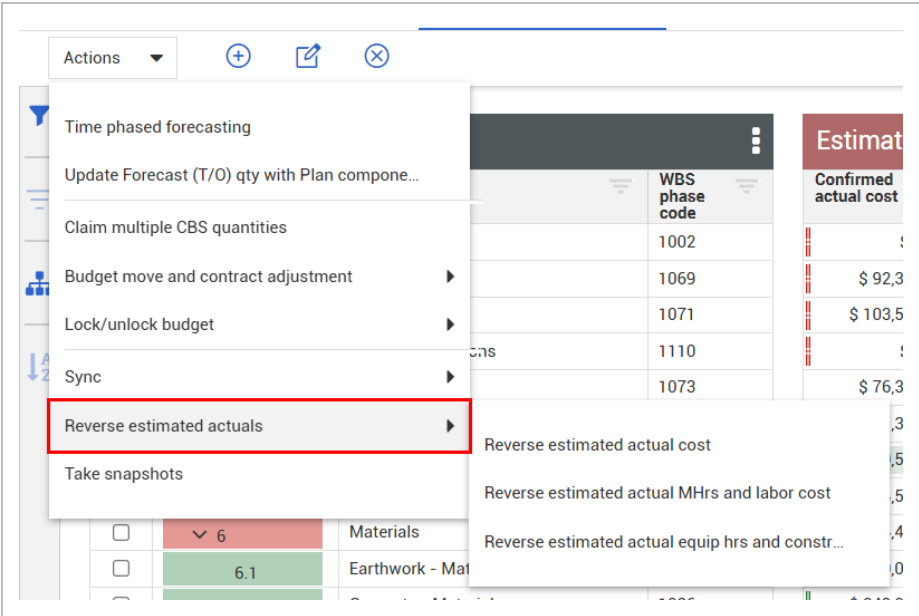

- 3. Click **Yes** to confirm the reversal.

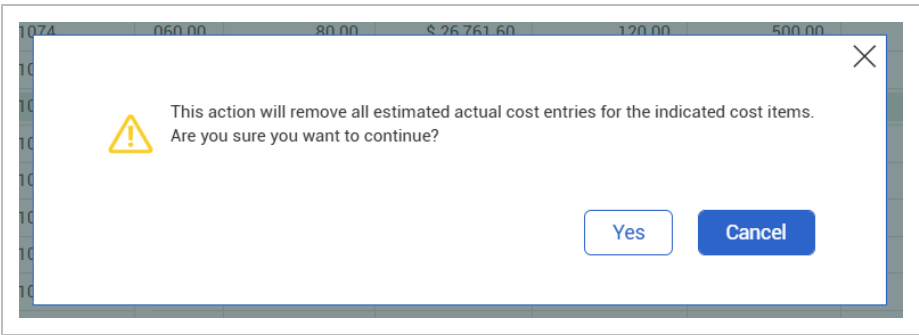


- 4. In the CBS, the estimated values are reset to 0.

5.11 ACTUALS HISTORY

Once progress is tracked against a cost item, you can view its actuals claim history. You can view actuals history of a cost item by right clicking on a cost item and selecting **Actuals details** from the menu. On the resulting slide out panel, you can view the history of when actual quantities, costs, and man-hours were posted by clicking on the Actuals History tab of the cost item.


The Actuals history tab displays and groups the actual claim history by posting date. Within in each posting date folder you can view as-built progress details of quantity, cost, man-hours, and equipment hours of the specific cost item selected in the CBS.

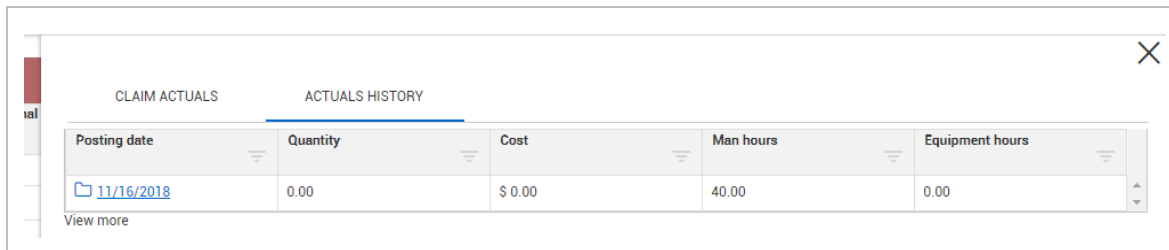

Posting date	Quantity	Cost	Man hours	Equipment hours
11/16/2018	0.00	\$ 0.00	40.00	0.00

View more

In addition, by clicking on the posting date link, you can view more specific claim history details such as actuals type, cost category, employee change by, and notes.



Posting date	Actuals type	Actuals completed	Cost category	Changed by	Notes
11/16/2018	Man Hours	40.00		Control - [Paul Bennion]	

View more

5.12 PROGRESS CONTROL SETTINGS

InEight Control integrates with several other programs. Within the tool, a few specific columns allow you to manage the information that is sent to other InEight applications and to your ERP system. Below is a table of the key columns and their functions.

Column Name	Function
Allow as-built	Allows you to choose whether a cost item accepts actual cost, quantities, both, or none. Once this item receives actual costs, quantities, or man-hours, this setting cannot be adjusted (changed from All to None).

Column Name	Function
As-built lock	Once you lock the ERP status, your ERP does not allow the WBS to be progressed. Example use cases for locking ERP status: • Work will not begin for two more years • Foreman is not allowed to claim more quantity because work is 100% complete • Work is complete and you do not want people mistakenly charging cost to completed to cost items
Hide in Plan, Progress, and Design	Allows the user to choose whether to have a cost item available to use in InEight Plan, InEight Progress, and InEight Design. Example use case for using the hide feature: • Indirect staff cost codes should not be available for direct labor to charge. For more information, see Hide in Plan, Progress, and Design.

The steps below walk you through the various columns and discuss options for changing the settings.

Progress Control Settings

For this step you will need to have a subordinate available to use.

1. On the Control main page CBS tab, select the **Progress** view.
2. Navigate to the **Task Details** data block.
3. Select the second **Data Panel** in the Task Details data block.
4. Double click in the **Allow as-Built** field of the subordinate cost item and select the drop-down arrow.
5. Select **All**.
6. Navigate to the **Third Panel** of the Task Detail data block.
7. Select the **Hide in Plan, Progress, and Design** check box of the cost item.

5.13 VENDOR WORK HOURS FROM PROGRESS

5.13.1 Vendor MHrs from Progress

You can see the subcontract man-hours in Control for cost items that derive from InEight Progress. Subcontract performance can be tracked in Progress with data coming into Control for increased transparency, improved monitoring, and analysis.

In addition to assigning a vendor to a cost item, and viewing the assigned vendors from InEight Contract, you can also see the claimed MHrs originating from Progress in Control > **Workspaces**, upon approval in Progress.

After the claimed vendor hours are approved in Progress, the Actual vendor MHrs (to date) and Actual columns populate with the claimed hours. This helps to find and focus on the true causes of any issues and support the ongoing work in the best way possible.

103614 | PATH Substation / Control / Workspaces

CBS

ACS

PAY ITEMS

Actions

Tasks

CBS position

Description

6

Roofing Vendor

Vendor

Assigned vendor

Actual vendor MHrs (to date)

Actual MHrs (to date)


Hide in Plan and Progress

Independent Roofing Co Inc


20.0000000000

0.0000000000

The Actuals Details slide-out panel shows the number of hours worked by the assigned vendor.

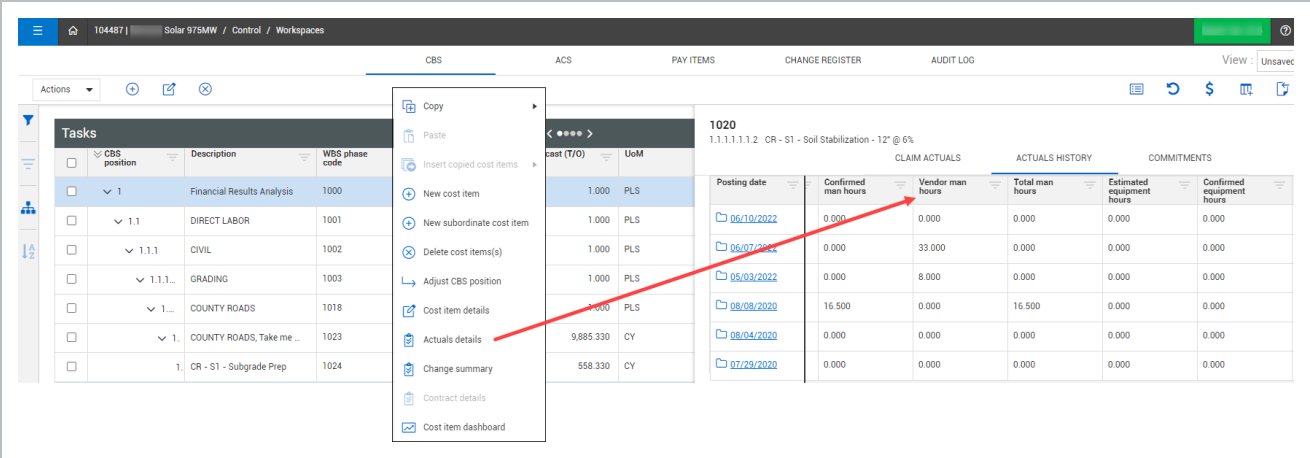

In Progress > Daily Plans > **Timesheet**, the new Vendor tab lets you choose which vendors to include on your daily time sheet as selected vendors to claim hours.

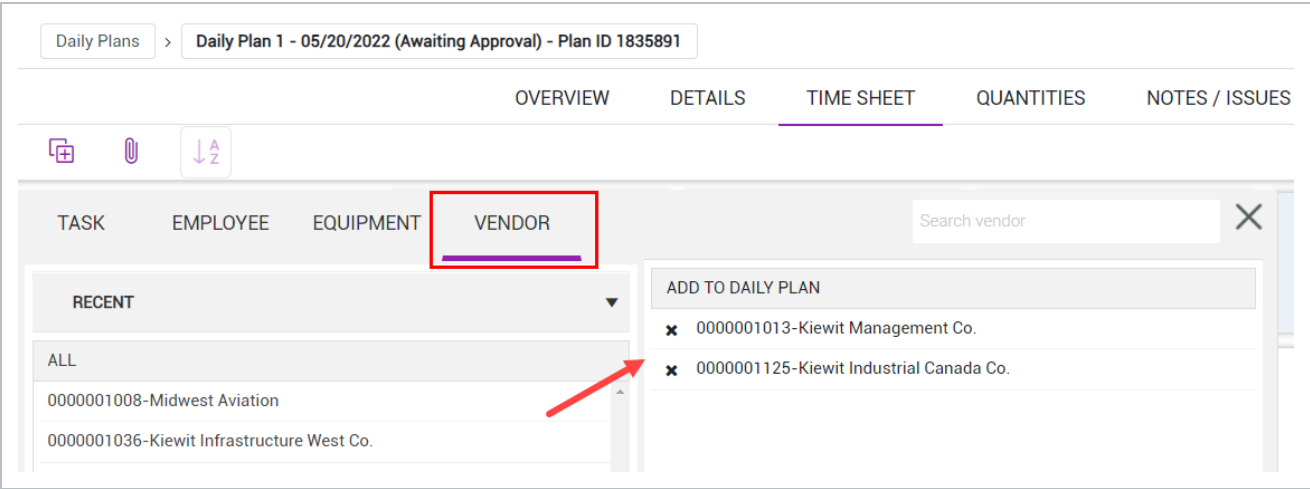

Only those vendors that are assigned in Control > Workspaces can claim hours against a timesheet Progress's daily plan. In Progress, if a vendor is not assigned to a cost item in Control, the vendor hours task block is disabled and hours cannot be claimed.

103614 | - PATH Substation / Progress / Daily plan

Daily Plans

> Install Roof - 04/07/2022 (Awaiting Approval) - Plan ID 1835468

+

Add tasks and resources

-

Clear hours

2002

Install Roof

Construction

0000001042

Σ: 0

Independent Roofi...

0010000758

Σ: 20

Midwest Aviation

0000001008

Σ: 0

ST 10

OT 5

DT 5

Vendor not assigned in Control

Vendor is assigned in Control

Vendor not assigned in Control

If a vendor is assigned to a cost item in Control, the vendor can claim actual hours.

InEight Inc. | Release 26.7

Page 253 of 639

The screenshot displays a software interface for tracking vendor hours. A modal dialog titled "Vendor hours" is open, showing details for the task "2002 - Install Roof" assigned to the vendor "758 Independent Roofing Co Inc". The dialog contains a table for "Time calculations" with columns for "Planned" and "Actual" hours. The "Actual" column shows 10 for ST (Standard Time), 5 for OT (Overtime), and 5 for DT (Double Time), totaling 20 hours. The background shows a task list with "2002 Install Roof" selected.

Time calculations	Planned	Actual
ST		10
OT		5
DT		5

Total vendor hours: 20

Number of employees:

Buttons: Clear, Cancel, Done

Note that the Actual vendor MHrs (to date) are recorded and reported on separately from the self-perform work hours that are recorded in the Actual MHrs (to date) fields.

5.14 TRACK OPEN/REMAINING AND TOTAL COMMITTED COSTS

Additional information about purchase orders and contracts (for any particular task) can be viewed and updated within CBS columns. This provides users with a more comprehensive data set in one location.

Committed costs are the purchase orders or subcontract commitments that a cost item may have against it. To determine open and total commitments, look at the agreed or pending purchase order amounts that are associated to any particular cost item. This information is typically exported from your ERP or accounting system.

Open/Remaining committed cost: Total committed cost - Actual cost (amount that still needs to be paid for a cost item).

Total committed cost: The summation of all purchase order and/or contract obligation amounts assigned to a cost item.


Open/Remaining committed cost adjustment: A debit or credit to the existing Open committed/Remaining cost value.

New open committed cost: Open/Remaining committed cost + Open/Remaining committed cost adjustment.

However, there is also the option to use a generic API to push committed cost values into InEight Control. If your organization does not have an ERP system, you can configure the endpoints in APIM and push over your committed cost values.


Viewing Open/Remaining and Total Committed Costs

1. On the CBS register tab, select the **Group Columns** icon to the right of the page. The icon will turn yellow when turned on.

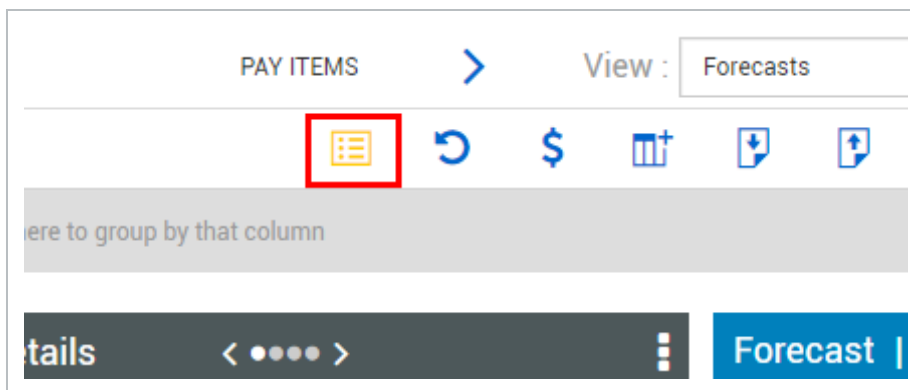


- Tasks, Task details and Commitments data block need to be present on this screen
- If the Commitments data block has not been created, create a custom data block using the Data Icon and include columns Remaining committed cost, and Total committed cost. Insert this data block into your view.


2. Drag the **UOM** column from the Task details data block, and drop it into the grey bar area

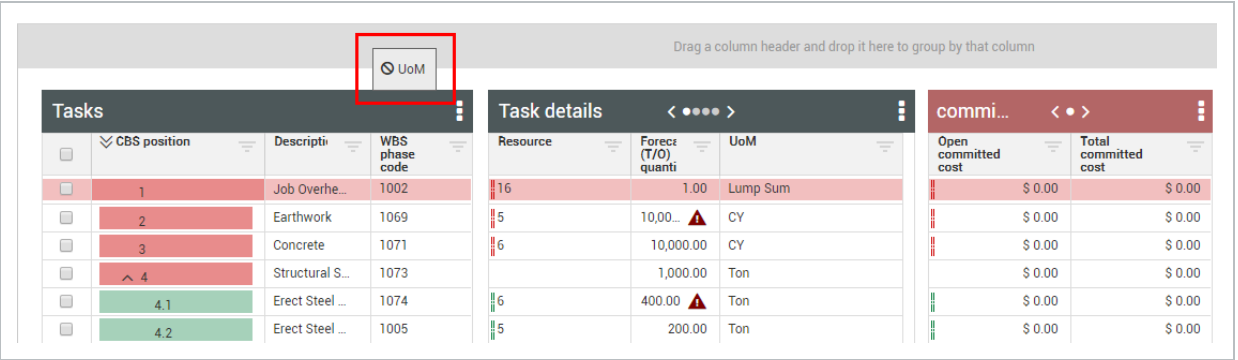

- Notice how UOM's are now visible by groups.

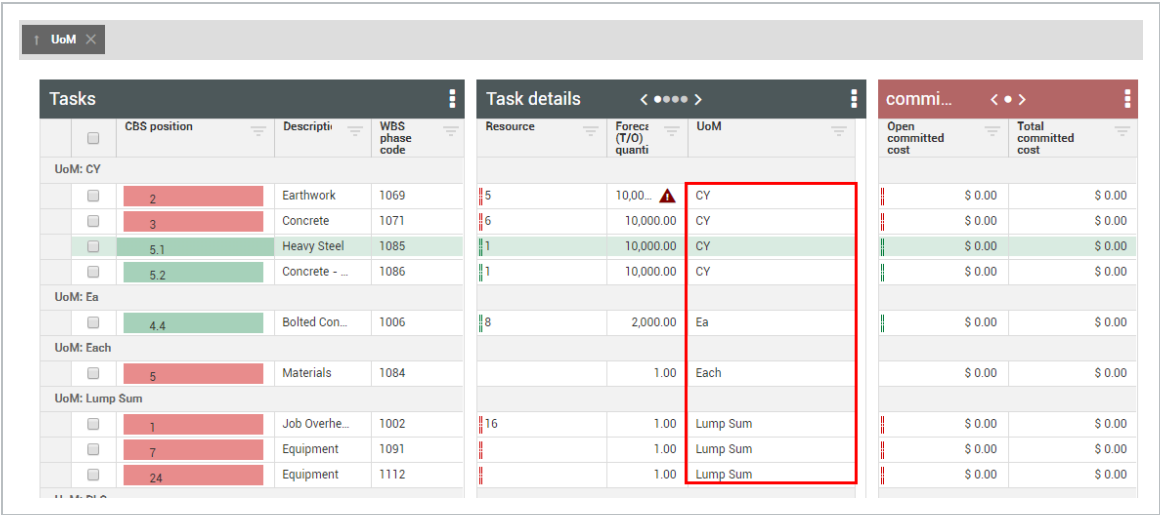

3. To view a more granular level of information, navigate into the **context menu** for a cost item, and select **Actuals details**.

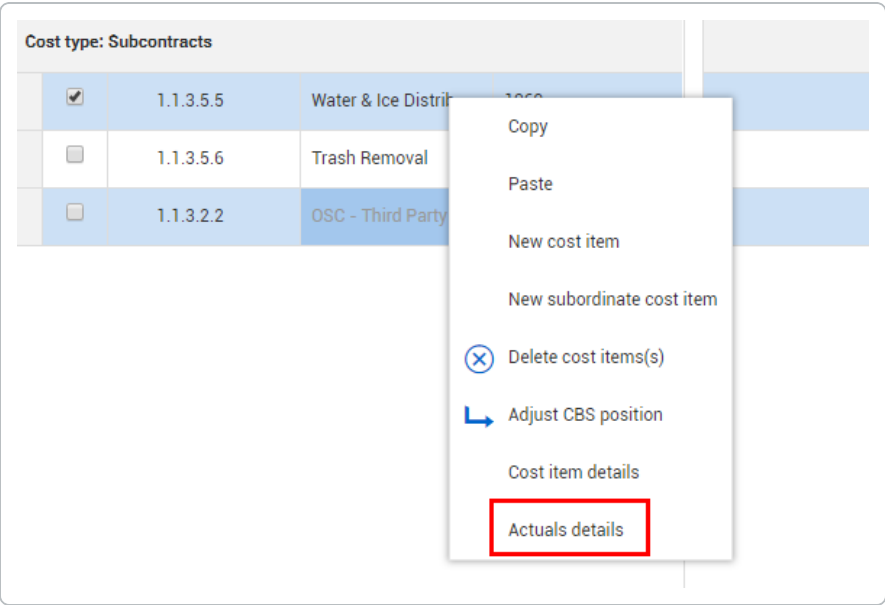

4. Once in the Actuals details, navigate to the Commitments tab.
- Here is a more concentrated view of the cost category breakdown of the Open and Total commitments
 - It's also possible to update information. *For example:* the below cost item for Water & Ice Distribution, the New total committed cost is showing that a contract was signed

for \$1,267.87.

1069 1.1.3.5.5 Water & Ice Distribution					
CLAIM ACTUALS		ACTUALS HISTORY		COMMITMENTS	
Open committed cost		Total committed cost			
\$ 700.00		\$ 1,267.87			
Cost category	Open committed cost adjustment	New open committed cost	Total committed cost adjustment	New total committed cost	
^ Total	\$ 0.00	\$ 700.00	\$ 0.00	\$ 1,267.87	
v Labor	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	
v Construction Equipment	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	
v FOM Rented Equipment	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	
v Supplies	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	
v Materials	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	
v Subcontract	\$ 0.00	\$ 700.00	\$ 0.00	\$ 1,267.87	

- There is \$700.00 left remaining to pay the full \$1,267.87 subcontract, as shown in the New open committed costs column

1069 1.1.3.5.5 Water & Ice Distribution					
CLAIM ACTUALS		ACTUALS HISTORY		COMMITMENTS	
Open committed cost		Total committed cost			
\$ 700.00		\$ 1,267.87			
Cost category	Open committed cost adjustment	New open committed cost	Total committed cost adjustment	New total committed cost	
^ Total	\$ 0.00	\$ 700.00	\$ 0.00	\$ 1,267.87	
v Labor	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	
v Construction Equipment	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	
v FOM Rented Equipment	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	
v Supplies	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	
v Materials	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	
v Subcontract	\$ 0.00	\$ 700.00	\$ 0.00	\$ 1,267.87	

- Assuming a bill of \$100.00 was just paid, it's possible to update the Open committed cost adjustment field with this value. Notice how the New open/remaining committed cost decreases to \$600.00, after making an adjustment of \$-100.00 to the Open committed cost adjustment field.

1069
1.1.3.5.5 Water & Ice Distribution

CLAIM ACTUALS ACTUALS HISTORY COMMITMENTS

Open committed cost	Total committed cost			
\$ 700.00	\$ 1,267.87			

Cost category	Open committed cost adjustment	New open committed cost	Total committed cost adjustment	New total committed cost
^ Total	(\$ 100.00)	\$ 600.00	\$ 100.00	\$ 1,367.87
v Labor	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00
v Construction Equipment	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00
v FOM Rented Equipment	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00
v Supplies	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00
v Materials	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00
v Subcontract	(\$ 100.00)	\$ 600.00	\$ 100.00	\$ 1,367.87

5. Select **Apply** to apply the above changes.

Tasks				Task details			Commi...	
	CBS position	Description	WBS phase code	Forecast (T/O) quantity	UoM	Cost type	Open committed cost	Total committed cost
Cost type: Subcontracts								
☐	1.1.3.2.2	OSC - Third Party I...	1054	13.00	MWk	Subcontracts	\$ 7,525.23	\$ 13,000.00
☒	1.1.3.5.5	Water & Ice Distrib...	1069	3,489.55	DMH	Subcontracts	\$ 600.00	\$ 1,367.87
☐	1.1.3.5.6	Trash Removal	1070	3,489.55	DMH	Subcontracts	\$ 309.00	\$ 873.24


6. Back on the CBS, you can now see your new updated values for this cost item.

Both the Open/Remaining committed cost and the Total committed cost values can be edited in the Actuals details slideout > Commitments tab (with the right permissions).

5.15 COMMITTED COST FROM CONTRACT

When the Drive committed cost values setting is on, your committed cost is then derived from Contracts.

When the switch is off, your committed cost is driven from the ERP. Regardless of the state of the switch, you can always manually enter your committed cost directly in the product or via a Microsoft Excel import.

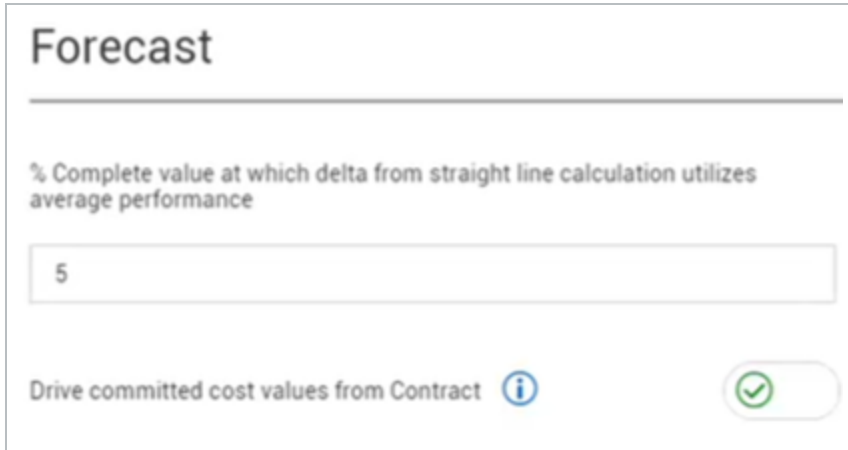

With the setting on, all of your committed cost values initially zero out, and then pull over all of your committed cost values that exist in InEight Contract.

For example, if you have a cost item that is associated with a contract, those values are pulled over from Contract and populate the total committed cost and open/remaining committed cost columns.

The calculation is *Forecast final cost = your Total committed cost; Forecast remaining cost = your Open/Remaining Committed Cost.*

In a contract on the Line items tab, change your view to Progress. Take note of the WBS phase code and then view the Gross amount. The gross amount for the cost item is the exact amount for the total committed cost, which includes your line item amount, plus tax.

Total gross amount is your line item amount plus tax. That is going to be your total committed cost value. The calculation for that: *Total committed cost = Line item amount + Tax* (this is also called Gross amount in Contract)

If you have a cost item that is associated with multiple line items in a single contract or across multiple contracts, the total committed cost for that cost item is the gross amount for all the line items that cost item is associated with.

If the WBS element is associated to three different line items, the sum of those three gross amounts is the total committed cost value. A best practice is to associate a single cost item to a single line item.

To get your Open/Remaining Committed Cost, calculate what you still have to pay for your remaining commitments. It is your total committed costs minus what you have already paid. You track payments in contract in three different ways:

- goods receipts
- accruals
- invoices

Invoices are generated in your payment forms.


The calculation is *Open/Remaining Committed Cost = Total committed cost - Max(Goods receipt amount, Invoice amount) - Accrual amount*.

This page intentionally left blank.

CHAPTER 6 – ACCOUNT CODES

6.1 Account codes workflow	263
6.2 Account Code Assignment	264
6.3 Quantity Contribution	264
6.3.1 ACS Navigation	265
6.3.2 Account Code Quantity	266
6.3.3 Quantity Contributors	267
6.3.4 ACS Unit of Measure Toggle	268
6.3.5 Account Code Quantity Conversions	269
6.3.6 Notes Column	271
Review	272
Summary	272

6.1 ACCOUNT CODES WORKFLOW

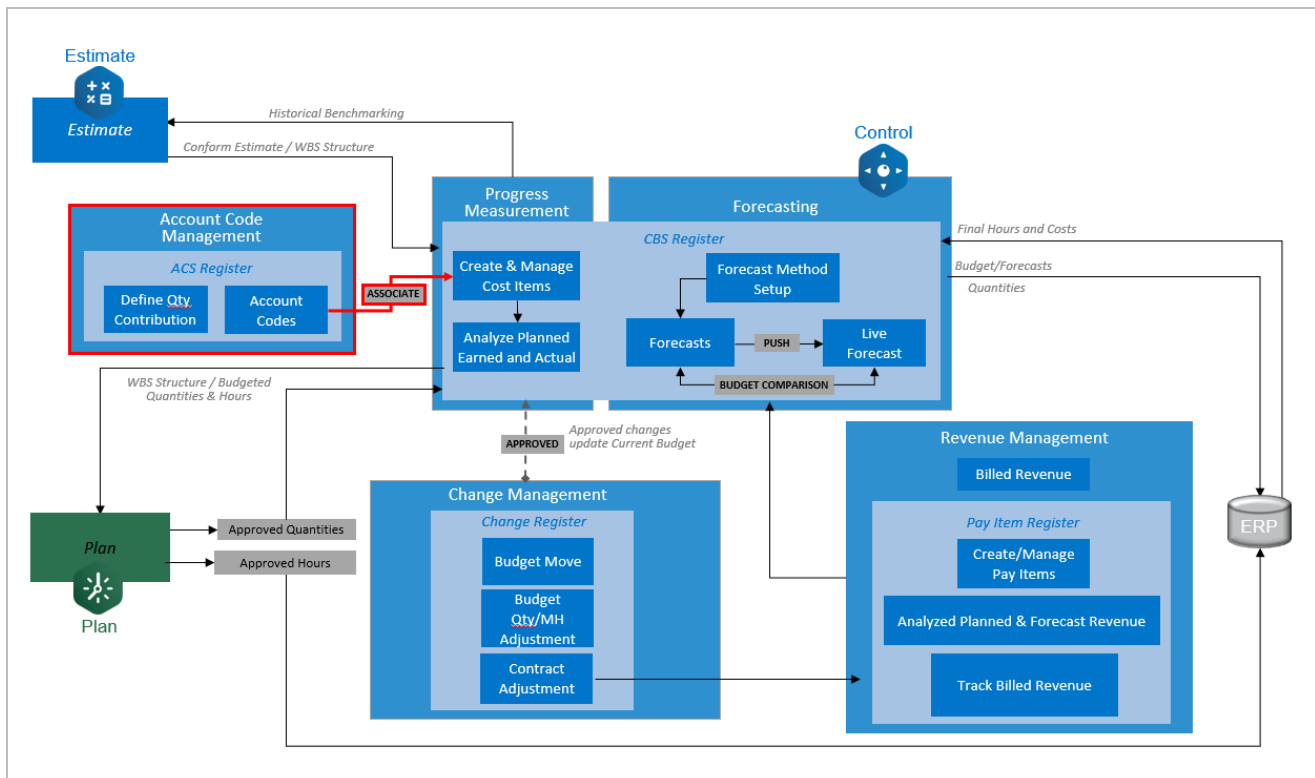

6.2 ACCOUNT CODE ASSIGNMENT

Account codes can only be assigned to terminal items. Parents cannot have an account code.

Assign Account Codes to Cost Items

1. From within the Control Workspaces page of a project, select the **CBS** tab to view your Cost Breakdown Structure.
2. From the View menu, select the **Project Controls** view by first selecting View more, if not already displayed.
3. Within the Task Details data block, click on the right arrow to progress to the Account Code column.
4. For a cost item you wish to have an Account Code assigned, double click in the Account Code cell for that cost item.
5. Use the search box to find the account code to assign, then click **Select**, and then click **Assign**.

6.3 QUANTITY CONTRIBUTION

At the project level, you can manage account codes under the ACS tab from the Control Workspaces page. On the ACS tab, you can see the account codes assigned to your cost items, along with the related parent account codes, with account code details and quantity contributors.

Other budget information is automatically pulled into the ACS Details data block including, Total Cost, Unit Cost, Unit Rates, Primary and Secondary Quantity Ratios, Quantities Complete, and Account Code Tags. To access this information, click the right arrow to view the second, third and fourth panels of the data block.

CBS

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

View : Unsaved (Quantity Managem...

Actions

ACS

ACS details

ACS qty contributors

Account code	Descri...	Primary Qty	Primary UoM	Auto-quantity (Primary)	Notes	Forecast total cost	Forecast total Mhrs	Contribute Primary to Primary	Contribute Primary to Secondary
99	Change Order...	1.000000000000	PLS	☐		\$187,829,311.97999998927	3,535,755.04678499978	☐	☐
99.09	Back charges	0.000000000000	PLS	☐		\$187,829,311.97999998927	3,535,755.04678499978	☐	☐
99.09.02	Back charges ...	1.000000000000	PLS	☐		\$209,963,377.59999999404	3,535,755.04678499978	☐	☐
99.09.02.002	Back charges ...	1.000000000000	PLS	☐		\$209,963,377.59999999404	3,535,755.04678499978	☐	☐
99.09.04	Back charges ...	0.000000000000	PLS	☐		(\$22,134,065.62000000104)	0.000000000000	☐	☐
99.09.04.002	Back charges ...	1.000000000000	PLS	☐		\$200.000000000000	0.000000000000	☐	☐
99.09.06	Back charges ...	0.000000000000	PLS	☐		\$0.000000000000	0.000000000000	☐	☐
99.09.06.002	Back charges ...	1.000000000000	PLS	☐		\$0.000000000000	0.000000000000	☐	☐

6.3.1 ACS Navigation

The ACS tree lets you easily navigate up and down your ACS structure and also provides a way to filter down to a subset in the structure. Open the ACS tree slide-out panel by clicking on the ACS tree icon on the side toolbar.

<

ACS

PAY ITEMS

CHANGE REGISTER >

View : Unsaved (Project Controls)

Actions

ACS tree

Expand all Collapse all

20 Job Related Overhead

51 Grading

61 Concrete

62 Metals

62.03 Structural Steel and Connections

62.03.02 Structural Steel Industrial St(...)

62.03.02.004 Structural Steel Industria(...)

62.03.02.004.02 Structural Steel Indust(...)

62.03.02.004.06 Structural Steel Indust(...)

62.03.02.006 Structural Steel Industria(...)

ACS

ACS details

Account code	Description	Primary Qty
20	Job Related Overhead	1.00
51	Grading	1.00
61	Concrete	10,000.00
62	Metals	0.00
62.03	Structural Steel and Connections	0.00
62.03.02	Structural Steel Industrial Structures	600.00
62.03.02.004	Structural Steel Industrial - Erect Steel	600.00
62.03.02.004.02	Structural Steel Industrial - Erect Steel - Li...	200.00
62.03.02.004.06	Structural Steel Industrial - Erect Steel - H...	400.00
62.03.02.006	Structural Steel Industrial - Bolted Connec...	2,000.00

Similar to the CBS color coded hierarchy, the ACS gives you the option to differentiate your account codes by color. Click on the ACS data block ellipsis to select this option to help you identify which level of the hierarchy a specific account code is located.

Account code	Description	Filter	Auto-quantity (Primary)	Forecast total Mhrs
20	Job Related Overhead		☒	0.00
51	Grading		☐	8,000.00
61	Concrete		☒	30,000.00
62	Metals		☒	4,999.10
62.03	Structural Steel and Connections		☒	4,999.10
62.03.02	Structural Steel Industrial Structures		☐	4,999.10
62.03.02.004	Structural Steel Industrial - Erect Steel		☐	4,000.00
62.03.02.004.02	Structural Steel Industrial - Erect Steel - Li...		☒	4,000.00
62.03.02.004.06	Structural Steel Industrial - Erect Steel - H...		☐	0.00
62.03.02.006	Structural Steel Industrial - Bolted Connec...		☒	999.10

6.3.2 Account Code Quantity

There are two methods for defining primary and secondary quantities for your account codes:

- Manual entry in the Primary Qty and Secondary Qty fields
- Using the auto-quantity feature to have them automatically inherit the quantities of any cost items that have the same unit of measure as the assigned account code

Define Account Code Quantity

1. From the Workspaces page of the Steel Structure Job, select the **CE + CB** viewset from the View drop-down list.
2. In the Current Estimate data block, double click in the **Secondary UoM** field for a cost item you assigned an account code to.
3. Select a Secondary UoM from the drop-down list different than the cost item's primary UoM.
4. Click the **side arrow** to navigate to the Secondary Qty column.
5. Double click in the **Secondary Qty** field for your cost item and enter a value.
6. Select the **ACS** tab.
7. In the Primary Qty field for the account code assigned to the cost item you just changed and type in a quantity value.
8. For your account code, check the **Auto-quantity (Primary)** check box.

- To view what cost items are assigned to the account code, right click on your account code and select **ACS item details**.

If you have the account code slideout open and want to open a different account code's item details, you can select a different account code. The details slideout updates to the current account code's details. You no longer have to exit out of one ACS item only to right click and select ACS details slide out to open another.

6.3.3 Quantity Contributors

Within your project, you can specify how primary and secondary quantities contribute to your account codes. Specifically, you can indicate how:

- Cost item primary and secondary quantities contribute to assigned account code primary and secondary quantities
- Child account code primary and secondary quantities contribute to parent account code primary and secondary quantities

For both cost item and account code contributions you can have quantities roll up:

- Primary quantity to primary quantity
- Primary quantity to secondary quantity
- Secondary quantity to secondary quantity

Account codes will only automatically inherit quantities from cost items/account codes using the same unit of measure.

6.3.3.1 Contribution Options - Cost Item to Account Code

From the ACS item details slide out panel, you can specify how cost item quantities roll up to the account code that is assigned to it, by selecting the appropriate checkbox. The total of the contributing cost item(s)'s quantities will roll up to become the account code quantity.

ACS item details							- Structural Steel Industrial - Erect Steel - Light (0-19 lb/LF)		
CBS position code	Description	WBS phase code	UoM	Forecast (T/O...	CE final Mhrs	CE total cost	Primary to Prim...	Primary to Seco...	Secondary to Seco...
4.2	Erect Steel - Light	1005	Ton	200.00	4000	200,000.00	☒	☐	☐

6.3.3.2 Contribution Options - Child Account Code to Parent Account Code


On the ACS page, in the ACS qty contributors data block, you can specify how child account code quantities will roll up to their parent account codes by selecting the appropriate checkbox.

ACS		ACS details < ● ● ● >			ACS qty contributors		
Account code	Description	Primary Qty	Primary UoM	Auto-quantity (Primary)	Contribute Primary to Primary Qty	Contribute Primary to Secondary ...	Contribute Secondary to secondary Qty
20	Job Related Overhead	0.000000000...	MWk	☒	☐	☐	☐
51	Grading	1.000000000...	PLS	☐	☐	☐	☐
61	Concrete	10000.00000...	CY	☒	☐	☐	☐
^ 62	Metals	0.000000000...	Ton	☐	☐	☐	☐
^ 62.03	Structural Steel and Connectio...	0.000000000...	Ton	☒	☐	☐	☐
^ 62.03.02	Structural Steel Industrial Stru...	0.000000000...	Ton	☐	☐	☐	☐
^ 62.03.02.004	Structural Steel Industrial - Ere...	1000.0000000...	Ton	☐	☐	☐	☐
62.03.02...	Structural Steel Industrial - Ere...	200.00000000...	Ton	☒	☒	☐	☒
62.03.02...	Structural Steel Industrial - Ere...	800.00000000...	Ton	☒	☒	☐	☒

6.3.4 ACS Unit of Measure Toggle

In the ACS register, you can toggle different Unit of Measures. The Unit of Measure toggle has three different options:

- As entered Unit of Measure
- English (Imperial Unit of Measure)
- Metric

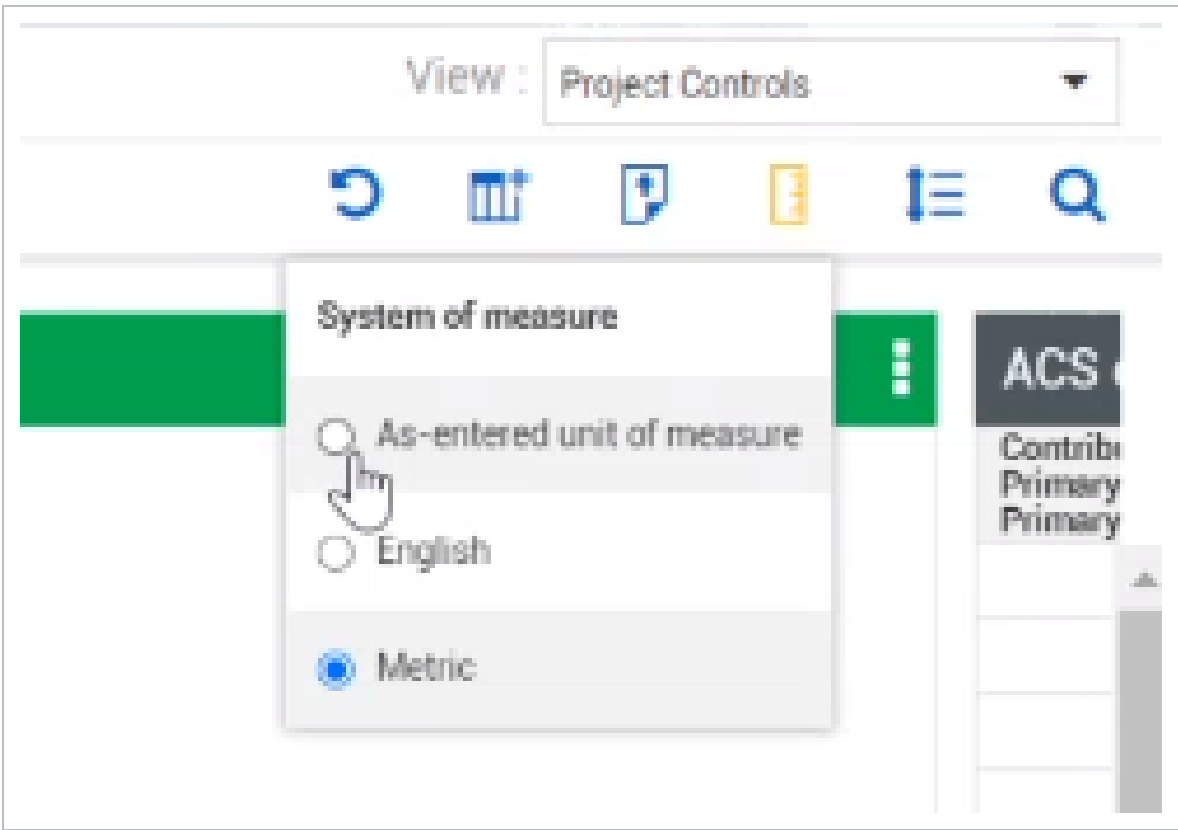

If you want to display and edit in liters instead of gallons for example, you would select the ruler icon in the top right corner of the ACS register, and then select Metric. The quantity amount converts in the browser and displays in the alternate unit of measure.

6.3.5 Account Code Quantity Conversions

Cost items that are tracked in one unit of measure can be tracked in another UoM. For example, cost items that are tracked in a metric UoM can contribute to account codes tracked in imperial UoM. This saves time in maintaining account code quantities, as project team members do not have to perform quantity conversions manually. Data accuracy is also ensured since any manual errors are eliminated from the conversion process.

In this example, CBS item Asphalt Paving and Break Removal contains a Forecast quantity of 3,000 with a UoM of Square Meter.

Tasks			Task details		
	CBS position	Description	Resource	Forecast (T/O) quantity	UoM
	1.1.1.2	Removals and De...		1.00	PLS
	1.1.1.2.1	Excavate Native t...	3	42,000.00	m3
	1.1.1.2.2	Asphalt Paving Br...	3	3,000.00	Square Meter
	1.1.1.2.3	Concrete Removal		1.00	PLS

In the ACS, you can display the Primary UoM Alternate System column to see what UoM is needed to track cost items in, so they contribute to your account codes. The Auto-quantity column is set up so that quantities are summing up the CBS. The Primary Qty of 3,587.97 is automatically populated. There is no further action to allow this value to roll up to the account code.


ACS		ACS details			
Account code	Description	Primary Qty	Primary UoM	Auto-quantity (Primary)	Primary UoM alternate system of...
50.03.02.002	Paving Removal - ...	3,587.97	Square Yard	☒	Square Meter
50.03.02.002.02	Break - Asphalt P...	3,224.10	Square Meter	☒	Square Meter
50.03.02.004	Paving Removal - ...	0.00	Square Meter	☒	Square Meter
50.03.12	Concrete Removal	0.00	Cubic Meter	☒	Cubic Meter
50.03.12.002	Concrete Removal...	0.00	Cubic Meter	☒	Cubic Meter
50.03.12.002.05	Concrete Removal...	290.82	Cubic Meter	☒	Cubic Meter

The system will automatically take the Forecast Qty in the CBS, and convert that number to the value shown in the Primary Qty field displayed in the ACS. In the above example, the CBS Forecast Qty of 3,000 in square meters is being converted to the 3,587.97 square yards, as shown in the ACS.


3000	=	3587.97
Square meter		Square yard

6.3.6 Notes Column

A Notes column is available for you to add to a new or existing data block. The Notes column lets you add commentary to any of the ACS records.

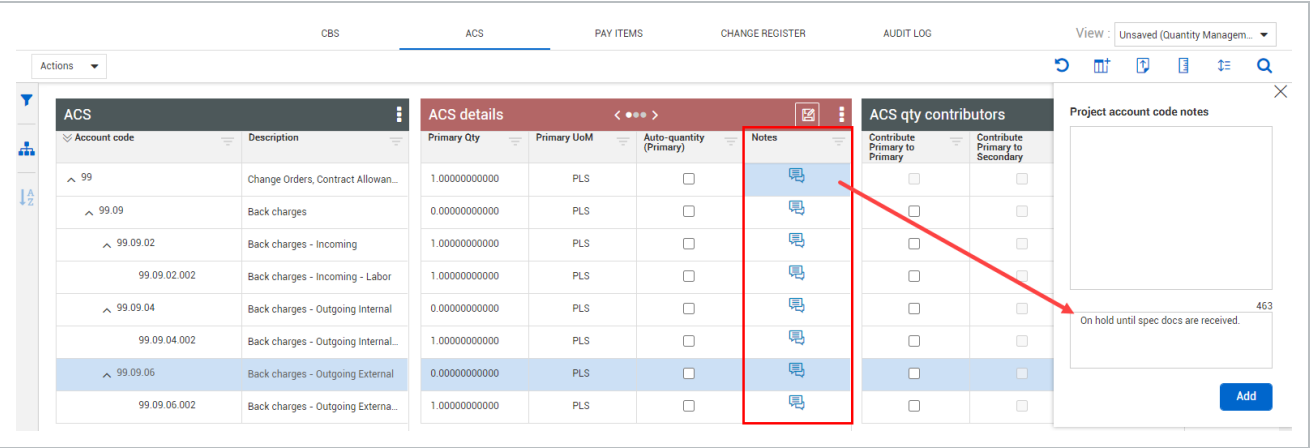

After notes are added to a record, the Notes column populates with the number of comments that are currently added to each record.

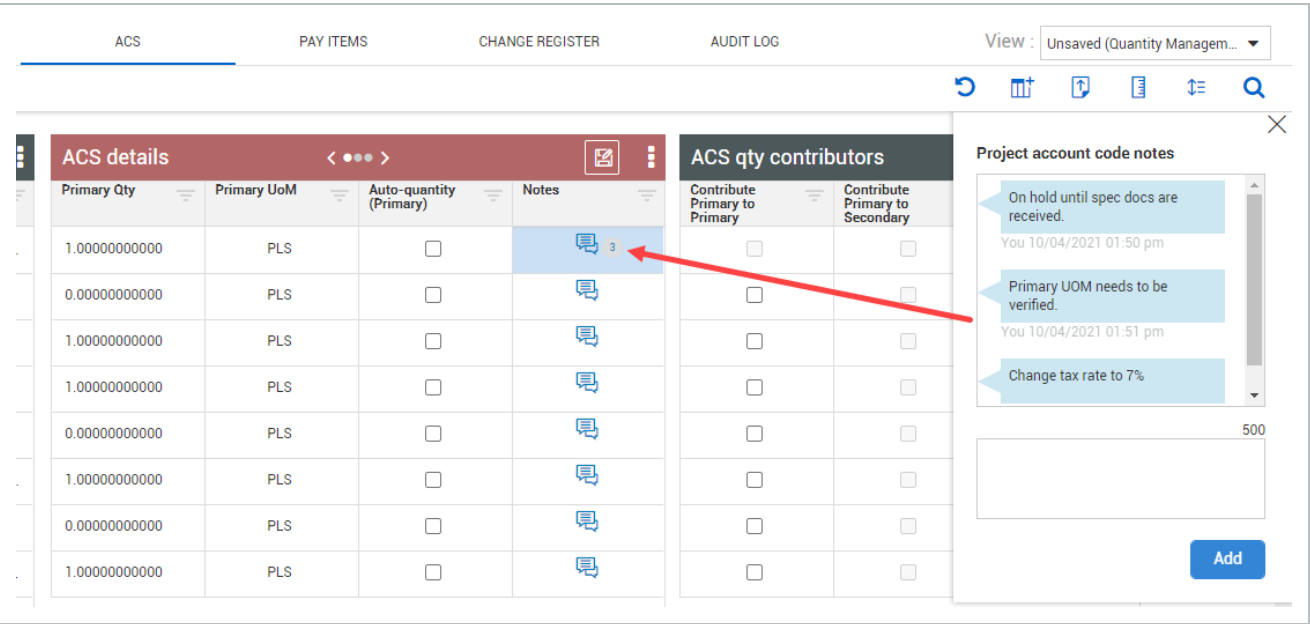

Review

1. Which of the following are account codes used to track?
 - a. Quantity
 - b. Budget
 - c. Account Code Tags
 - d. Unit Costs
 - e. a, b, and d
 - f. All of the above
2. Manual entry in the Primary Qty and Secondary Qty fields is one of the methods for defining primary and secondary quantities for _____?
 - a. Change Attribute
 - b. UOM's
 - c. Account Codes
 - d. Unit Rates
 - e. Total Cost

Summary

As a result of this lesson, you can:

- Assign account codes to cost items
- Define the quantity contribution for each account code
- Review and analyze the audit log

CHAPTER 7 – FORECASTING

7.1 Forecasting workflow	274
7.2 Forecasting overview	275
7.2.1 Private forecasts	275
7.2.2 Shared forecasts	275
7.2.3 Live forecast	276
7.3 Forecast management	276
7.3.1 Forecast data block	276
7.3.2 Push to shared forecast	280
7.3.3 Compare forecasts	281
7.3.4 Live forecast data block	282
7.4 Fiscal Calendar	283
7.5 Forecast Methods	285
7.5.1 Forecast Method Assignment	286
7.6 Manual Forecasting	298
7.6.1 EAC vs. ETC	298
7.6.2 Manual EAC (Estimate at Complete) Forecast	299
7.6.3 Manual ETC (Estimate to Completion) Forecast	305
7.7 Time Phased Forecasting	307
7.7.1 TPF Register	310
7.7.2 Auto Distribute	310
7.7.3 Manual Time Phased Forecast	311
7.7.4 Static manual time phased forecasting (TPF)	315
7.7.5 Time Phased Forecast Settings	317
7.7.6 Time Phased Forecast Prerequisites	320
7.7.7 Time Phased Forecast View	320
7.7.8 Time Phased Forecast Microsoft Excel import	323
7.7.9 Column Chooser	328
7.7.10 Audit Log	329
7.8 Push to Live Forecasts	329
7.8.1 Time phased forecast push to live	330

7.9 Live Forecast Snapshot

333



7.9.1 Snapshot settings

334

7.9.2 Manage snapshots

334

7.1 FORECASTING WORKFLOW

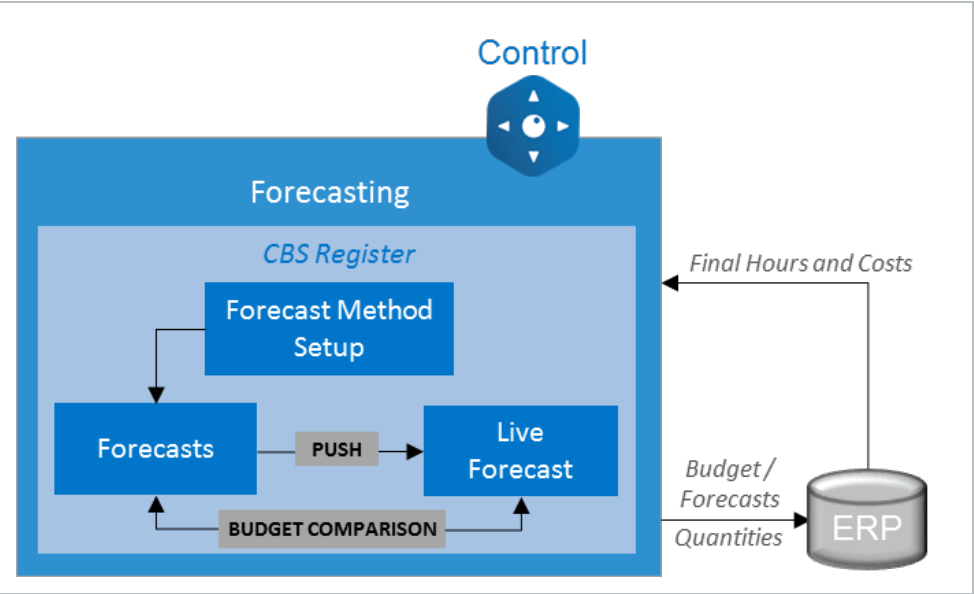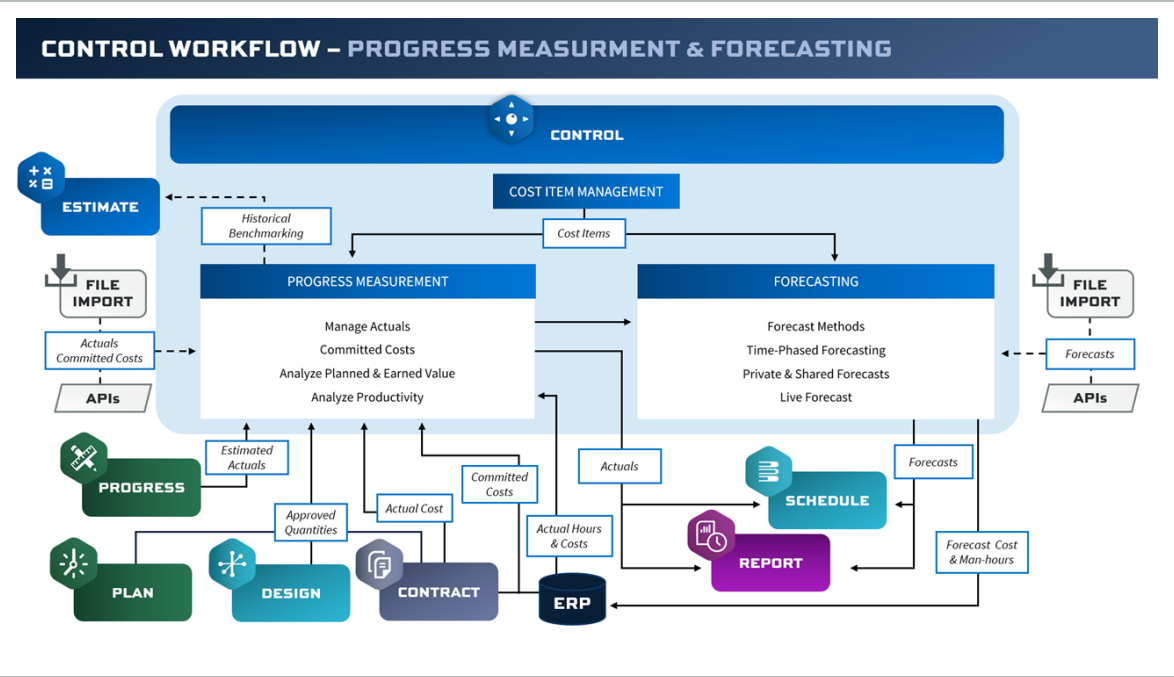

7.2 FORECASTING OVERVIEW

Forecasting in InEight Control is the process of predicting project costs and progress based on current data and trends. Accurate forecasting helps project teams stay on budget and make informed decisions.

Depending on the size of your project, multiple engineers may be involved in forecasting tasks. For example, a large team might divide responsibilities by discipline, with discipline-specific field engineers preparing data for the project manager.

Control supports collaborative forecasting by allowing users to create and save their own forecasts without affecting others' work. These forecasts can then be shared and combined to build the official project forecast.

7.2.1 Private forecasts

Private forecasts give you flexibility to explore outcomes without impacting the official project data. In Control Workspaces, you can create multiple private forecasts to:

- Test different forecasting methods.
- Explore what-if scenarios (e.g., changes in labor rates or material costs).
- Compare alternative approaches before sharing with the team.

Private forecasts are visible only to you until you choose to share them. This makes them ideal for refining your work before contributing to a shared or live forecast.

7.2.2 Shared forecasts

Shared forecasts allow collaboration among team members. You can create up to five shared forecasts, which are automatically visible to all members assigned to the project. A shared forecast lets you do the following:

- Joint editing and review of forecast data.
- Real-time updates visible to everyone sharing the forecast.
- Preparing a consensus forecast before pushing it to the Live forecast.

Any member with the appropriate permissions can edit a shared forecast.

7.2.3 Live forecast

The Live forecast is the official project forecast used for financial reporting. It is automatically shared with all project members and managed through its own data block.

- Data from private or shared forecasts can be pushed to the Live forecast to keep it current.
- Only users with the appropriate permissions can update the Live forecast.

Live forecast Current live forecast < ● ● ● ● > 10/15/2025					
Forecast total cost	Forecast total Mhrs	Forecast total Mhrs/unit	Forecast total productivity	Forecast total unit cost	Forecast method
\$ 250,000.00	0.00	0.00	0.00	\$ 250,000.00	Current estimate
\$ 406,300.00	8,310.00	0.83	0.96	\$ 40.63	Current estimate
\$ 1,499,250.00	29,805.00	2.98	1.01	\$ 149.93	Current estimate
\$ 1,056,600.00	21,226.00	21.23	0.99	\$ 1,056.60	Rollup
\$ 800,300.00	16,040.00	19.95	1.00	\$ 995.40	Current estimate
\$ 202,500.00	4,040.00	20.00	0.99	\$ 1,002.48	Current estimate
\$ 53,800.00	1,146.00	0.57	0.87	\$ 26.74	Current estimate
\$ 1,749,400.00	0.00	0.00	0.00	\$ 1,749,400.00	Rollup
\$ 250,000.00	0.00	0.00	0.00	\$ 25.00	Current budget
\$ 999,000.00	0.00	0.00	0.00	\$ 99.90	Current budget
\$ 500,400.00	0.00	0.00	0.00	\$ 500.40	Current budget

7.3 FORECAST MANAGEMENT

Control uses three data blocks for forecasting:

- Forecast – Enter and adjust forecast values.
- Forecast delta – Compare two forecasts side by side.
- Live forecast – displays the official project forecast.

7.3.1 Forecast data block

All forecasting adjustments are made in the Forecast data block. This block includes a variety of columns that show cost, man-hours, and productivity, as well as forecast methods.

When you first access the Forecast data block, either by opening the Forecasts view or by adding the data block to your view, it will show several options for loading a forecast. Select **New private forecast** or **New shared forecast** to load a new forecast based off the Live forecast. You can also select an existing forecast under Recent.

Forecast

Create new

+ New private forecast

+ New shared forecast

Recent

	Name	Last Viewed
🔗	Team Forecast Shared	11/20/2025 11:25:50 AM
🔒	LK Forecast Private	11/20/2025 11:14:50 AM
🔒	Created from Live forecast 11/20/2025 11:11:35 AM Private	11/20/2025 11:11:35 AM

Load More

After you make your selection, the data block populates.

Forecast							
🔗 Created from Live forecast 0...		< ● ● ● >		🔄 09/02/2025			
🔗 Forecast total cost	🔗 Forecast total Mhrs	🔗 Forecast total Mhrs/unit	🔗 Forecast total productivity	🔗 Forecast total unit cost	🔗 Forecast remaining cost	🔗 Forecast method	
\$ 250,000.00	0.00	0.00	0.00	\$ 250,000.00	\$ 250,000.00	Current estimate	
\$ 406,300.00	8,310.00	0.83	0.96	\$ 40.63	\$ 314,000.00	Current estimate	
\$ 1,499,250.00	29,805.00	2.98	1.01	\$ 149.93	\$ 1,395,750.00	Current estimate	
\$ 1,150,300.00	23,100.00	23.10	0.91	\$ 1,150.30	\$ 1,074,000.00	Rollup	
\$ 896,300.00	17,960.00	19.96	0.89	\$ 995.89	\$ 845,000.00	Current estimate	
\$ 200,500.00	4,000.00	20.00	1.00	\$ 1,002.50	\$ 180,000.00	Current estimate	
\$ 53,500.00	1,140.00	0.57	0.88	\$ 26.75	\$ 49,000.00	Current estimate	
\$ 1,749,400.00	0.00	0.00	0.00	\$ 1,749,400.00	\$ 1,145,000.00	Rollup	
\$ 250,000.00	0.00	0.00	0.00	\$ 25.00	\$ 150,000.00	Current budget	
\$ 999,000.00	0.00	0.00	0.00	\$ 99.90	\$ 650,000.00	Current budget	
\$ 500,400.00	0.00	0.00	0.00	\$ 500.40	\$ 345,000.00	Current budget	

You can adjust the forecast by entering values directly into the data block cells.

Forecast Created from Live fore...		
Forecast total cost	Forecast total Mhrs	
\$ 250,000.00	0.00	
\$ 406,300.00	8,310.00	
\$ 1,499,250.00	29,805.00	
\$ 331,141.02	6,686.00	
\$ 74,841.02	1,500.00	
\$ 202,500.00	4040	
\$ 53,800.00	1,146.00	

To view or adjust cost categories for a cost item, click the **View cost categories icon** inside a cell. This opens the Cost Categories tab of the cost item details slide-out panel.

Forecast Created from Live fore...

Forecast total cost	Forecast total Mhrs
\$ 74,841.02	
\$ 202,500.00	4040
\$ 53,800.00	

WBS phase code

1002

1069

1071

1073

1074

1005

1006

1084

1085

1086

1087

1005

Erect Steel - Light

DETAILS

ATTRIBUTES

COST CATEGORIES

CURRENT ESTIMATE RESOURCES

FORECAST RESOURCES

% complete 9.90 %

Live forecast method

Latest actuals in forecast values


Current estimate

10/15/2025

Total Per unit

Cost category	Current budget	Actual cost (to date)	Current estimate	Forecast	Forecast remaining cost	Billing rate markup amount
Total	\$ 200,000.00	\$ 20,500.00	\$ 202,000.00	\$ 202,500.00	\$ 182,000.00	\$ 0.00
Labor	\$ 200,000.00	\$ 20,500.00	\$ 202,000.00	\$ 202,500.00	\$ 182,000.00	\$ 0.00
Construction...	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00
FOM Rented ...	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00

The drop-down menu in the Forecast data block gives you options for managing your forecasts. The image and table below show the option details.

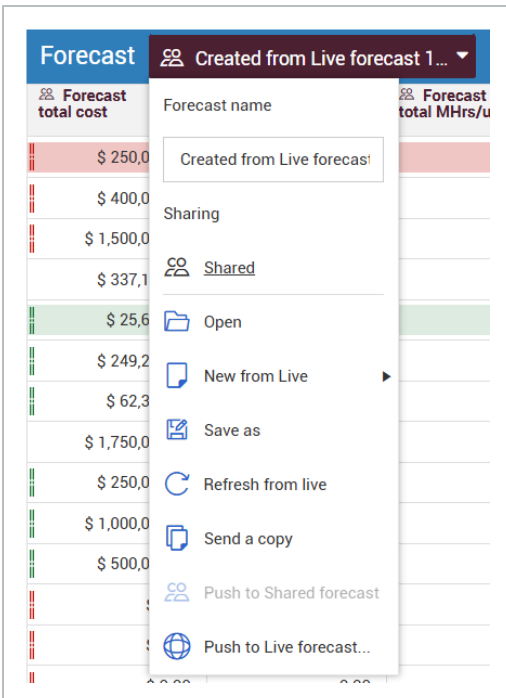

Menu Option	Details
Forecast name	Enter a name for the current forecast.
Sharing	Click to select Shared or Private access to this forecast. You can also send a copy of this forecast to team members.
Open	Load a saved or shared forecast. You can also delete saved forecasts.
New from Live	Create a new private or shared forecast from the Live forecast.
Save as	Save a copy of this forecast.
Refresh from live	Overwrite forecast values with the Live forecast values on selected cost items.
Send a copy	Send a snapshot of this forecast to specific users.
Push to Shared forecast	Overwrite values in a shared forecast with values from this forecast for selected cost items. See below for more details.
Push to Live forecast	Overwrite Live forecast values with values from this forecast for selected cost items. See Push to Live forecast for more details.

7.3.2 Push to shared forecast

Changes made to a private forecast can be pushed to a shared forecast.

Push to shared forecast

1. From the private forecast data block, select the cost items with updated values.
2. Open the data block drop-down menu, and then select **Push to Shared forecast**.

The screenshot shows the 'Tasks' table with columns: CBS position, Description, and WBS phase code. The 'Forecast' panel on the right shows a list of forecast items with their total costs. A dropdown menu is open from the 'Forecast' panel, showing options like 'Private', 'Open', 'New from Live', 'Save as', 'Refresh from live', 'Send a copy', 'Push to Shared forecast', and 'Push to Live forecast...'. The 'Push to Shared forecast' option is highlighted with a red box.

CBS position	Description	WBS phase code
1	Job Overhead	1002
2	Earthwork	1069
3	Concrete	1071
4	Structural Steel	1073
4.1	Erect Steel - Heavy	1074
4.2	Erect Steel - Light	1005
4.3	Bolted Connections	1006
5	Materials	1084
5.1	Earthwork - Materials	1085
5.2	Concrete - Materials	1086
5.3	Structure Steel - Materials	1087
6	Merrill Iron & Steel - Steel Material	1088

Forecast total cost
\$ 250,0
\$ 406,3
\$ 1,499,2
\$ 1,062,8
\$ 748,4
\$ 260,6
\$ 53,8
\$ 1,749,4
\$ 250,0
\$ 999,0
\$ 500,0

3. A dialog box opens where you can review the changes. Select a shared forecast from the drop-down menu.

The dialog box contains a table with the following data:

CBS position	Description	WBS phase code	Forecast total cost	Forecast total Mhrs	Cost difference	Mhrs difference
4.1	Erect Steel - H...	1074	\$ 748,410.22	15,000.00	(\$ 51,889.78)	-1,040.00
4.2	Erect Steel - LI...	1005	\$ 202,500.00	4,040.00	\$ 58,143.56	1,160.00
			\$ 1,002,800.00	20,080.00	\$ 1,009,053.79	20,200.00
					\$ 6,253.79	\$ 120.00

The dropdown menu shows 'Shared Forecast 2' and 'Shared Forecast 1'. The 'Yes' button is highlighted.

4. Review the changes, and then click **Yes** to finish. The updated values now show in the shared forecast.

Forecast Shared Forecast 1		
Forecast total cost	Forecast total MHrs	Forecast total MHrs/unit
\$ 250,000.00	0.00	0.00
\$ 406,300.00	8,310.00	0.83
\$ 1,499,250.00	29,805.00	2.98
\$ 1,062,853.79	21,346.00	21.35
\$ 748,410.22	15,000.00	18.66
\$ 260,643.56	5,200.00	25.74
\$ 53,800.00	1,146.00	0.57

7.3.3 Compare forecasts

You can compare forecasts by adding the Forecast delta data block to your view and then selecting two forecasts in the data block header to compare.

Forecast delta Ma... Liv...			
Forecast total cost	Forecast total MHrs	Forecast total MHrs/unit	Forecast product factor
\$ 0.00	0.00		0.00
\$ 0.00	0.00		0.00
\$ 0.00	0.00		0.00
\$ 6,253.79	12		-0.01
(\$ 51,889.78)	-1		0.07
\$ 58,143.56	1,160.00	5.74	-0.22

The Forecast delta data block displays any deltas between the selected forecasts.

- Values in black indicate equal values between the selected forecasts.
- Values in green indicate a higher value than the corresponding value in the other forecast.
- Values in red indicate a lower value than the corresponding value in the other forecast.


Forecast delta  Ma...  Liv...  10/15/2025 					
Forecast total cost	Forecast total Mhrs	Forecast total Mhrs/unit	Forecast total productivity factor	Forecast total unit cost	Forecast remaining cost
\$ 0.00	0.00	0.00	0.00	\$ 0.00	\$ 0.00
\$ 0.00	0.00	0.00	0.00	\$ 0.00	\$ 0.00
\$ 0.00	0.00	0.00	0.00	\$ 0.00	\$ 0.00
\$ 6,253.79	120.00	0.12	-0.01	\$ 6.25	\$ 6,253.79
(\$ 51,889.78)	-1,040.00	-1.29	0.07	(\$ 64.54)	(\$ 51,889.78)
\$ 58,143.56	1,160.00	5.74	-0.22	\$ 287.84	\$ 58,143.56
\$ 0.00	0.00	0.00	0.00	\$ 0.00	\$ 0.00

7.3.4 Live forecast data block

Access the Live forecast data block to view official project forecast values. Users with the correct permissions can make updates directly in the data block.


Live forecast  Current live forecast  09/02/2025 					
Forecast total cost	Forecast total Mhrs	Forecast total Mhrs/unit	Forecast total productivity	Forecast total unit cost	Forecast method
\$ 312.50	0.00	0.00	0.00	\$ 312.50	Current estimate
\$ 406,300.00	8,310.00	0.83	0.96	\$ 40.63	Current estimate
\$ 1,499,250.00	29,805.00	2.98	1.01	\$ 149.93	Current estimate
\$ 475,850.00	9,560.00	9.56	2.20	\$ 475.85	Rollup
\$ 346,300.00	6,960.00	19.89	2.30	\$ 989.43	Current estimate
\$ 125,050.00	2,440.00	20.00	1.64	\$ 1,025.00	Average performan...
\$ 4,500.00	160.00	4.00	6.25	\$ 112.50	Current estimate
\$ 1,749,400.00	0.00	0.00	0.00	\$ 1,749,400.00	Rollup

Additionally, you can access previous Live forecast snapshots from the drop-down menu.

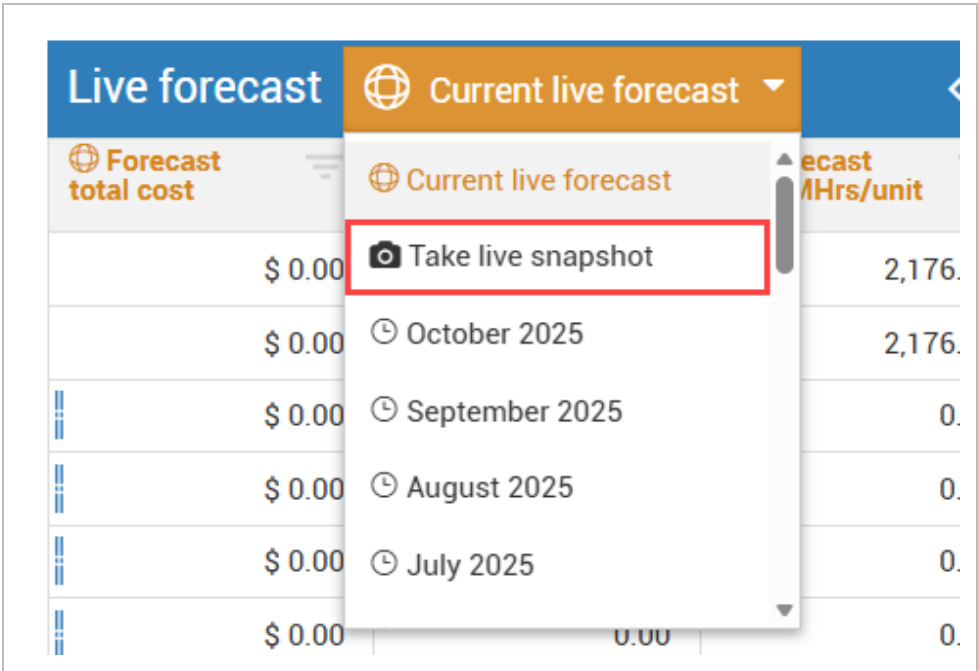

7.4 FISCAL CALENDAR

Control has built-in settings that automatically set the actuals in the forecasting-related data blocks to match your company’s month end calendar.

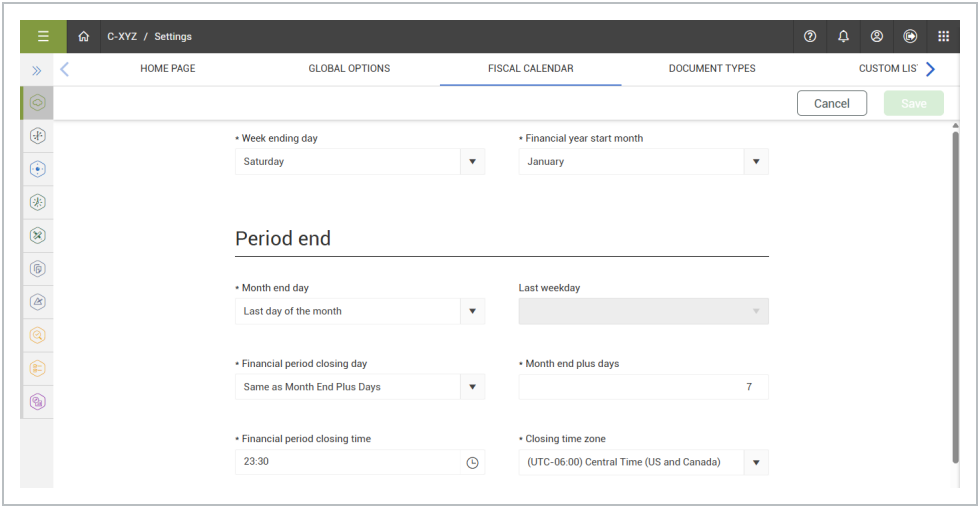

The fiscal calendar settings include a suspended period for you to finalize your forecast numbers without incurring any new actuals.

Period end

* Month end day

Last day of the month

Last weekday

Select one

* Financial period closing day

Same as Month End Plus Days

* Month end plus days

8

* Financial period closing time

23:30

* Closing time zone

(UTC-06:00) Central Time (US and Canada)

During the suspended period, your numbers are frozen, allowing you to finish month end reporting without worrying about the numbers changing. Any new actuals accumulated during the suspended period will populate once the suspended period is over.

The Live forecast data block contains a Current live forecast label in its header. The Current live forecast label reminds you that the values in the Live forecast data block are only for the current period, as defined in the organization settings.

Live forecast	Current live forecast					09/02/2025
Forecast total cost	Forecast total MHrs	Forecast total MHrs/unit	Forecast total productivity	Forecast total unit cost	Forecast method	
\$ 312.50	0.00	0.00	0.00	\$ 312.50	Current estimate	
\$ 406,300.00	8,310.00	0.83	0.96	\$ 40.63	Current estimate	
\$ 1,499,250.00	29,805.00	2.98	1.01	\$ 149.93	Current estimate	
\$ 475,850.00	9,560.00	9.56	2.20	\$ 475.85	Rollup	
\$ 346,300.00	6,960.00	19.89	2.30	\$ 989.43	Current estimate	
\$ 125,050.00	2,440.00	20.00	1.64	\$ 1,025.00	Average performan...	

Fiscal calendar settings are configured in your organization settings. See the following table for details on fiscal calendar options.

Field Name	Purpose
Week ending day	Determines which day of the week is the final day.
Financial year start month	Allows the financial year-end to be different from the calendar year-end.

Field Name	Purpose
Month end day	Determines what the final day of the month is.
Last weekday	Sets the day for the above setting.
Financial period closing day	Allows you to set the financial period to end on the same day or allow a period to close out the finances.
Month end plus days	Sets the number of closing days.
Financial period closing time	Sets the time when the forecast actuals will be reset to the next period.
Closing time zone	Sets the closing time zone.
Project fiscal calendar settings	Enable this setting to allow different fiscal calendar settings at the project level.

7.5 FORECAST METHODS

The Forecast Method establishes the appropriate forecast unit cost, which is used to calculate the total forecast cost. The Forecast Method applies to individual cost items and can be changed at any time.

You can use several forecast production methods to calculate the cost of the remaining work associated with a cost item. This enables the control of forecasting on a cost item by cost item basis by controlling the calculation of the cost of the remaining work. The different methods available for forecasting are:

Forecast Methods

Method	Calculation	Apply to
Current Budget (CB)	Actual Total cost + (Current budget unit cost * Quantity remaining)	Terminal or superior cost items
Current Estimate (CE)	Actual Total cost + (Current estimate unit cost * Quantity remaining)	Terminal or superior cost items
Average Performance	Actual Total cost + (Actual unit cost * Quantity remaining)	Terminal or superior cost items

Forecast Methods (continued)

Method	Calculation	Apply to
Manual	Manually entered forecast value	Terminal or Superior cost items
Rollup	The sum of subordinate forecast values	Superior cost items
Committed Cost	Actual Total cost + Open/Remaining committed cost	Terminal or superior cost items
None	The Forecast total cost will be 0	Terminal or superior cost items
Contract	Line item gross amount + Draft vendor change order amount + Remaining to buy (value allocated to the first line item in the contract)	Terminal or superior cost items
Detailed ETC	Actual Total cost + sum (Forecast remaining cost) for all assigned forecast resources.	Terminal cost items
Static manual time phased forecasting (TPF)	The sum of the manually distributed time phased forecast cost.	Terminal or superior cost items
Custom (customer specified)	Calculation specified by customer.	Terminal or superior cost items

7.5.1 Forecast Method Assignment

There are three different ways to assign a forecast method:

- Globally to all cost items in the project
- Selection of multiple cost items
- Individual cost item

7.5.1.1 Global Forecast Method

From the Actions menu, you can set the forecast method globally for all the cost items within the project.

The Global forecast method only applies to the forecasted items of the user who performs the function. It does not apply to other users in the project.

The following steps walk you through applying a global Forecast Method.

Set Global Forecast Method

1. From the CBS tab register, select the **View** menu.
2. Select the Project Controls viewset.
3. Click on the Actions drop-down menu and select Global Forecast Method.
4. Select the **Current Budget** Forecast Method.
5. Click **Apply**.

Only **terminal** cost items will adjust per the global Forecast Method selected. The parent item Forecast Method will stay as **Rollup**.

6. Click **Yes** on the prompt that appears.

7.5.1.2 Forecast Method for Selected Items

You can also set the forecast method for selected cost items, as shown in the steps below.

Set the Forecast Method for Selected Items

1. In the Tasks data block, select the **check box** next to the desired tasks.

MENU

Control

\$100000 - PKS Inc

Steel Structure Training Job

100098

View :Forecasts

Actions

CBS

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

Tasks

CBS Position

Description

1

Job Overhead

2

Earthwork

3

Concrete

*4

Structural Steel

4.1

Erect Steel - Heavy

4.2

Erect Steel - Light

4.3

Bolted Connections

*5

Materials

5.1

Earthwork - Materials

5.2

Concrete - Materials

5.3

Structure Steel - Materials

Task Det... < + + + >

WBS Phase Code

Forecast at TO City

UOM

1000

1.00

Lump Su.

1001

10,000.00

CY

1002

10,000.00

CY

1003

1,000.00

Ton

1004

800.00

Ton

1005

200.00

Ton

1006

2,000.00

Ea

1007

1.00

Each

1008

10,000.00

CY

1009

10,000.00

CY

1010

1,000.00

Ton

Forecast | Created from Live foreca... < + + + >

Forecast Final Cost

Forecast Final MH

Forecast Final Man Hour/Unit

Forecast Final PF

Forecast Final Unit Cost

Forecast Method

\$250,000.00

0.00

0.00

0.00

\$250,000.00

Current estimate

\$400,000.00

8,000.00

8.80

1.00

\$40.00

Current estimate

\$1,500,000.00

30,000.00

3.00

1.00

\$150.00

Current estimate

\$1,050,000.00

20,000.00

20.00

1.00

\$1,050.00

Rollup

\$800,000.00

16,000.00

20.00

1.00

\$1,000.00

Current estimate

\$200,000.00

4,000.00

20.00

1.00

\$1,000.00

Current estimate

\$50,000.00

0.00

0.00

0.00

\$25.00

Current estimate

\$1,750,000.00

0.00

0.00

0.00

\$1,750,000.00

Rollup

\$250,000.00

0.00

0.00

0.00

\$25.00

Current estimate

\$1,000,000.00

0.00

0.00

0.00

\$100.00

Current estimate

\$500,000.00

0.00

0.00

0.00

\$500.00

Current estimate

Forecast | Created from Live foreca... < + + + >

Forecast Final Cost

Forecast Final MH

Forecast Final Man Hour

\$250,000.00

0.00

\$400,000.00

8,000.00

\$1,500,000.00

30,000.00

\$1,050,000.00

20,000.00

\$800,000.00

16,000.00

\$200,000.00

4,000.00

\$50,000.00

0.00

\$1,750,000.00

0.00

\$250,000.00

0.00

\$1,000,000.00

0.00

\$500,000.00

0.00

Subtotals

11

\$4,950,000.00

58,000.00


\$4,950,000.00

58,000.00


©2017 InEight Inc Privacy and Terms | Build: TRN-WEB 2.0.6352 34563 | User: Kris Pooley <kris.pooley@ineight.com>

INEIGHT

2. Select the **Actions** drop-down menu and select **Set Forecast Method**.

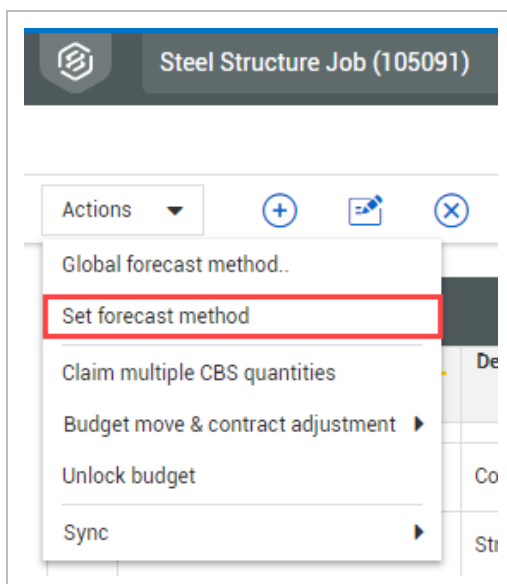

3. On the resulting slide out panel, select your desired Forecast Method and click **Apply**.

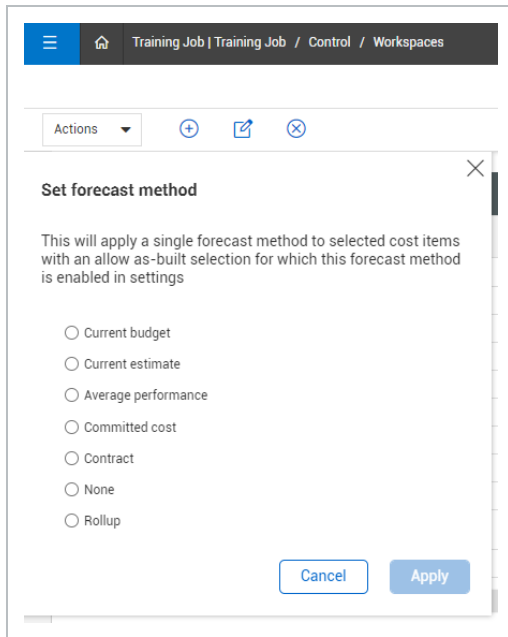

7.5.1.3 Forecast Method for Individual Items

You may need to change the forecast method for a single cost item. The following Step by Step walks you through how to do so.

Set the Forecast Method for Individual Items

1. In the **Forecast** data block, locate the **Forecast Method** column.
2. Double click on the Forecast Method field for the your desired cost item.

- A dropdown menu appears where you can select your Forecast Method from a list

Tasks	CBS Position	Description	Final	Forecast Final MH	Forecast Final Man-Hours/Unit	Forecast Final Productivity Factor	Forecast Final Unit Cost	Forecast Method	Forecast Method
1		Job Overhead	50,000.00	0.00	0.00	0.00	\$250,000.00	Current budget	\$C
2		Earthwork	00,000.00	8,000.00	0.80	1.00	\$40.00	Current budget	\$C
3		Concrete	00,000.00	30,000.00	3.00	1.00	\$150.00	Current budget	\$C
4		Structural Steel	83,768.50	19,977.80	19.98	1.00	\$1,983.77	Current estimate	\$C
...		Erect Steel - Heavy	34,158.50	15,985.60	19.98	1.00	\$1,167.70	Average performance	\$C
...		Module 01 - Erect Steel Heavy	00,000.00	0.00	0.00	0.00	\$1,000.00	None	\$C

7.5.1.4 Average Performance Forecast Method

The average performance forecast method lets you use actuals for a specific time frame range to determine the unit cost and rate for the remaining work when calculating the remaining forecast. Forecasting using average performance lets you forecast the remainder of work based off completed work.

When Average performance is selected as the forecast method in the CBS, you can click the value in the Average performance settings column and select a date range to use for the actual rate of completion for the remainder of work.

This feature lets you identify a length of time you want to utilize a cost item's hours and quantities to determine the install rates for the remaining work.

Click an Average Performance Settings CBS record to access the Average Performance Settings window.

Setting	Usage notes
Calculate average performance over all dates	The average performance for the cost item takes all the dates into account when calculating its average performance.
Calculate average performance based on most recent	You can determine how many weeks or months to calculate the average performance for a cost item. For example, you determine that the last 2 weeks performance best represents how to progress, then you would calculate two weeks of average performance.

Setting	Usage notes
Calculate average performance over a specified range	Selecting a date range uses only the specified time range for calculating the average performance.
Calculate average performance from date	You can select a specific date to calculate average performance. After the learning period for the selected cost item is complete, you can use the average performance for a specific date and onward.

The screenshot displays the 'Average performance settings' dialog box over a software interface. The dialog box contains the following options:

- ☒ Calculate average performance over all dates
- ☐ Calculate average performance based on most recent: (1 Weeks)
- ☐ Calculate average performance over a specified range: (From 12/31/1752 To 12/19/2022)
- ☐ Calculate average performance from date: (12/31/1752)

A tooltip for the 'most recent' option indicates: 'This will be up to date through the most recent week ending date'. The background interface shows a table with columns for various forecast metrics.

The average performance settings can also be accessed in the cost item details slide-out panel.

Tasks

	CBS position	Description
☐	1	Financial Results ...
☐	2	Misc. Rev Internal
☐	2.1	Misc. Rev Internal
☐	2.2	Escalation/Contin...
☐	2.2.1	General Project Ri...
☐	2.3	Directs
☐	2.3.1	Direct Labour
☐	2.3.1.1	Grading Work
☒	2.3.1.1.1	Resurface Existin...
☐	2.3.1.1.2	Maintain Access ...
☐	2.3.1.1.3	Clear & Grub Benc...
☐	2.3.1.1.4	Type D Excavatio...
☐	2.3.1.1.5	Road Subgrade Pr...
☐	2.3.1.1.6	Culverts & Riprap ...
☐	2.3.1.1.7	Rock / Boulder Ex...
☐	2.3.1.1.8	Sump Excavation ...
☐	2.3.1.2	PreCast Blocks & ...
☐	2.3.1.2.1	Set / Place Pre-C...
☐	2.3.1.2.2	Drill / Install / Gro...
☐	2.3.1.2.3	Build & Move Anc...
☐	2.3.1.2.4	Test Anchors
☐	2.3.1.2.5	Relocate Existing ...
☐	2.3.1.2.6	Anchor Re-Tensio...
☐	2.3.1.2.7	Anchor Block Re-I...

Subtotals 151 (1 rows selected)

Actuals

Actual qty (to date)
2

1004

Resurface Existing Access road

DETAILS

Description

Resurface Existing Access road

Forecast T/O qty

CE total cost

\$ 5,803.84

CE total MHrs

103.20

CE MHR/Unit

0.02

Allow as-built

All

As-built lock

Hide in Plan, Progress, and P

NT ESTIMATE

SOURCES

FORECAST RESOURCES

Cost source

Detail

Live forecast method

Average performance

Average performance settings

To date

☐ Calculate average performance over all dates

☐ Calculate average performance based on most recent:

1 Weeks

☒ Calculate average performance over a specified range:

From 11/22/2018

To 01/10/2023

☐ Calculate average performance from date:

11/22/2018

Apply

As an example, if you choose to calculate the average performance based on the most recent three weeks, the Forecast remaining cost and Forecast remaining MHrs change based off the cost item’s performance from the last three weeks.

Actions

Tasks

	CBS position	Description
☐	1	Financial
☐	2.1.1.1	Site ...
☒	2.1.1.1.1	Site ...

CHANGE REGISTER

AUDIT LOG

12/09/2022

Forecast total cost	Forecast remaining MHrs	Average performance settings	Forecast remaining cost	Forecast method
\$ 0.00	0.000		\$ 0.00	Current estimate
\$ 2,469,443.93	-2.409		(\$ 101.66)	Rollup
\$ 2,452,434.31	0.000	Last 3 weeks	\$ 0.00	Average performan...

The Forecast method and Average performance settings changes are also shown in the cost item details slide-out panel.

1396

Site Maintenance Crew

DETAILS

Forecast T/O qty

UoM

75,181.000

MH

Last changed on

Last ch

12/16/2022 09:54 AM

Description

Site Maintenance

* Forecast T/O qty

CE total cost

CE total MHrs

↶

\$

🏠

📄

📄

⬆️

🔍

✕

CURRENT ESTIMATE
RESOURCES

FORECAST RESOURCES

CBS position

2.1.1.1.1

* Cost source

Detail

🌐 Live forecast method

Average performance

Average performance settings

Last 3 weeks

CE labor cost/MHrs

7.5.1.5 Committed Cost Forecast Method

Committed Costs are obligations made for contract work or purchase orders that you have agreed to pay for. The Committed Cost forecast method provides you with the ability to use committed cost information to forecast your cost at completion.

Forecast final unit cost	Forecast remaining cost	Forecast method
(\$ 120,539,221.43)	(\$ 122,907,115.92)	Rollup
(\$ 142,040,228.20)	(\$ 142,445,305.28)	Rollup
(\$ 12,535.89)	(\$ 129,212.48)	Rollup
\$ 118.05	\$ 10,805.00	Committed cost
\$ 43.88	\$ 8,676.00	
\$ 9.18	\$ 0.00	
(\$ 14,869.35)	(\$ 148,693.48)	
\$ 0.00	\$ 0.00	
\$ 0.00	\$ 0.00	

Forecasting cost items can be done in the live or private forecast, and can be forecasted at the parent or terminal levels. The Committed Cost Forecast method can only be used when cost items have an Allow as-built of All or Costs. When the Allow as-built values are set to None or Quantities, this forecast method cannot be used because cost and committed costs cannot be claimed.

The Committed Cost forecast is mostly utilized on cost items that are driven from purchase orders or contracts. It is not used when you're claiming quantities. For example, this forecast method isn't suitable for direct labor items where quantities are claimed to generate progress and crew performance. This forecast method works well for cost items that are tied to a contract or PO.

When Open/Remaining Committed Cost values are being entered, these values will also update the forecast values in the CBS. There is also an integration available that allows you to import committed cost data from your ERP, instead of manually entering in the data. For more information on Commitment Costs, visit subject Track Open/Remaining and Total Committed Costs within this topic3.3 Cost Items on page 99

The following columns will help you view the Committed Cost forecast method:

Forecast total cost: Forecast cost at completion which is equal to the Open/Remaining committed cost plus any Actual cost to date.

Forecast remaining cost: This is the amount of money that remaining to be paid out. This column is equal to the Open/Remaining Committed Cost.


Tasks		< ● ● ● >		Forecast Created from Live forec... 03/09/2020						
CBS position	Description	As-built lock	Allow as-built	Forecast final man hours/Unit	Forecast final cost	Forecast final productivity factor	Forecast final Mhrs	Forecast final unit cost	Forecast remaining cost	Forecast method
1.1.1.1	Permits	☐	All	1.00	\$ 11,805.00	2,323.00	1.00	\$ 118.05	\$ 10,805.00	Committed cost

The Committed cost forecast method is most commonly used for costs that are associated to a purchase order tracked through an ERP system. This method doesn't focus on quantities or percent complete, but rather the progression of costs paid towards the final agreed upon PO value.”


7.5.1.6 Contract Forecast Method

Using this forecast method, you can forecast by Contract values. This forecast method is only available in the forecast drop down for cost items that are assigned to a Contract.

Any modifications that you make in Contract automatically updates and comes into Control.

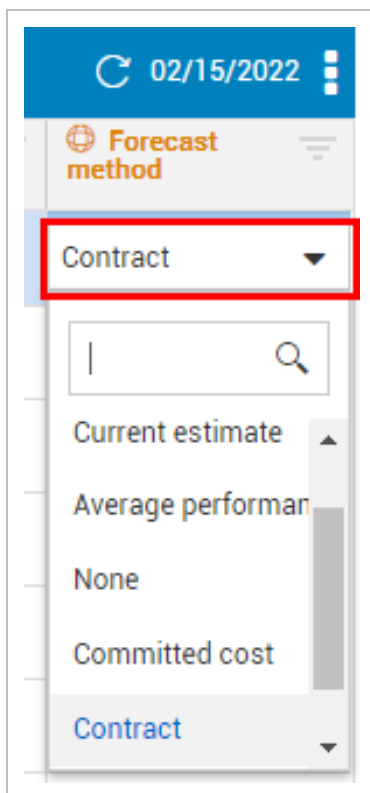

When a cost item is assigned to a contract, you have the option of adding the read-only column **Number of contracts** to your CBS. This column is an integer value that counts the number of contracts a particular cost item is associated to. You have to go into Contracts to see which Contract your cost item is associated to.

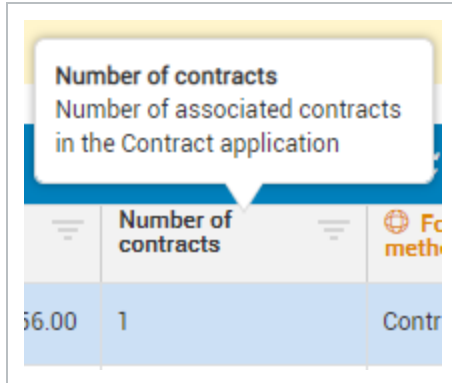

If the **Number of contracts** column is set to zero, the Contract Forecast Method becomes unavailable from the Live Forecast, Private Forecast, and the Cost Item Details slideout drop down for Live Forecast Method on the Details tab.

Contract Forecast Method pulls the cost that is associated to a specific cost item from Contracts. Cost items can be associated to the following if using Contract Forecast Method:

- Many different Contracts
- Many different line items across different Contracts

The cost item's Forecast Final Cost value sums up the line item amounts of all cost that is associated to a cost item from Contract.

Unapproved Contract Line Items

The line item price is included in the associated cost item's Contract forecast method when creating new line items in a Contract vendor change order.

After a new line item is saved, a batch process is initiated in the background that sends the line item's net price over to Control.

Actions

Line item II

Add existing line item

Add new line item

New

From master agreement

Add new line item

Contracts > 7400007066 - contract 1 >

Cancel

Save and new

Save

Line item details

Type

Material

Description

Hint: type 'abc'

Quantity & pricing

* Quantity

1.000

* UoM

Each

* Unit price

\$ 400.00

* Per

1.000 Each

Hint: type 'abc'

Is taxable

☒

Pricing

Value \$

The net price from Contract shows in Control’s forecast total cost column, which also includes the tax from draft pending vendor change orders.

Contracts > 7400007066 > 2 - 2 CAD \$

VCO total

Remaining amount to allocate

\$ 0.00

\$ 0.00

Actions

Cost center

WBS code

GL account

1102 - Gen...

521320 - Supplies-C...

Contract

responsible party

Vendor CO status

Approval status

Draft

Not applicable

Table with 6 columns: Unit price, Net price, Tax, Retention, Quantity, Total revision. Row 1: \$ 400.00, \$ 400.00, \$ 0.00, \$ 0.00, 1.000, \$ 0.00. Row 2: \$ 400.00, \$ 0.00, \$ 0.00, \$ 0.00, 1.000, \$ 0.00.

Table with 2 columns: Description, WBS phase code. Rows: Financial Results Analysis (1000), New 1 (1139), New 2 (1140), Misc. Rev Internal (1103), Misc. Rev Internal (1104), Escalation/Contingency (1101), General Project Risk (1102).

Control

Forecast method

Forecast total cost

Current estimate

Rollup

None

Rollup

Manual (EAC)

Rollup

Contract

\$ 0

\$ 0

\$ 0

\$ 2,402,829

\$ 0

\$ 1,000

\$ 1,000

Forecast total cost was previously \$600

7.5.1.7 Custom Forecast Method

The Custom forecast method lets you specify a calculation for a forecast cost and manhours. For more information, refer to [Project Control settings](#) where Custom forecast methods can be configured.

- Scheduling
- Administration
 - Account Code Structure (ACS)
 - InEight Control Interfaces
 - Control Settings
 - Roles & Permissions
 - Project Settings**

Custom Forecast method calculations

You can create custom forecast methods at both the project and organization levels by configuring your own calculations.

To create a custom Forecast Method, click Add custom forecast method, and then enter the Forecast Method Name, Forecast Total Cost and Forecast Total Mhrs calculations. You can create a maximum of 10 custom organization and project level forecast methods each at one time.

Select the **Formula** icon to choose fields to include in your forecast formula.

- Project Tracking (organization & project level)
 - Tasks
 - Actuals
 - Estimated Actuals
 - Enabling actuals for Progress
 - Enabling actuals for Control
 - Estimated actuals process overview
 - Reversing estimates
 - Reversing Estimated Actuals
 - Time Phasing budget
- Forecast (organization & project level)
 - Time Phasing
 - Forecast
 - Custom Forecast method calculations**
 - Enable Forecast methods based on
 - Allow as-built selections
- Estimate Resources (organization & project level)
- Schedule (organization & project level)
- Revenue (project level)
 - Revenue and Cost Timing
 - Billing method default earnings rules
 - Pay item forecast takeoff quantity rollups
 - Pay item forecast takeoff quantity roll down
 - Markup
- Sync Integrations (project level)
- Others (project level)
 - Required Cost Items
 - Decimal Precision
- Others (org level)

7.6 MANUAL FORECASTING

Scenario

Assume you have a structural steel installation code being performed by a subcontractor. They have notified the project team that the material cost of the steel has gone up due to a change of thickness of some of the column base plates. You will need to forecast an increase in the total subcontract cost of the code to reflect this change.

You also receive an update from the concrete superintendent that the code for a concrete pouring operation will now be using journeymen instead of apprentice concrete finishers. He has provided the total and you will update the total cost and the labor cost per man-hour.


7.6.1 EAC vs. ETC

You can manually enter forecast values for both your Estimate at Completion (EAC) and Estimate to Completion (ETC) values.

Control uses different descriptions than EAC and ETC as indicated below.

Forecast Term	Control Term	What it measures
Estimate at Completion (EAC)	Forecast Final Cost Forecast Final MHrs	As-built + (Forecast Unit Cost x Quantity Remaining)
Estimate to Completion (ETC)	Forecast Remaining Cost Forecast Remaining Man Hour	Forecast Unit Cost x Quantity Remaining

The image below illustrates what EAC and ETC measure:

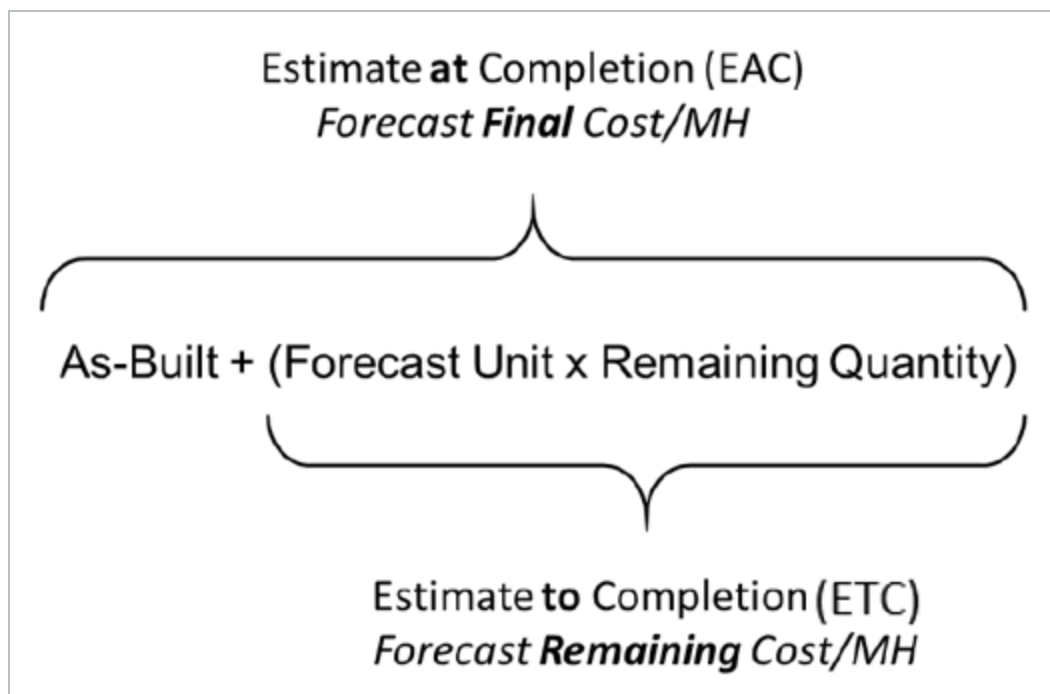

7.6.2 Manual EAC (Estimate at Complete) Forecast

You can use the Manual (Estimate at Completion) Forecast Method to make a simple, quick adjustment to the calculated forecast numbers, or to forecast the cost of the work remaining, while ignoring actual costs in the calculation of the forecast.

When you enter a forecast cost at the total level, you can have forecast costs:

- Distributed to the cost categories, or
- Back calculated if forecast man-hours are adjusted

To set the forecast total or EAC forecast, type a value into one of the following cells within the forecasting data block:

- Forecast final cost
- Forecast final MHrs
- Forecast Final Man-hours per Unit
- Forecast Productivity Factor
- Forecast Final Cost per Unit

The next two Step by Steps walk you through how to define the Manual (EAC) forecast by adjusting the Forecast Final Cost and the Forecast Final Man-Hours.

Manually Adjust Forecast Final Cost

1. In the Forecast data block, double click the **Forecast Final Cost** cell for a cost item.
 - This will allow you to edit the dollar value manually

MENU

Control

\$1,000,000 - PK3 loc

Steel Structure Training Job

1005096

View : Forecasts

ActionsCBSACS

PAY ITEMSCHANGE REGISTERAUDIT LOG

Tasks

CBS PositionDescription

1Job Overhead

2Earthwork

3Concrete

*4Structural Steel

4.1Erect Steel - Heavy

4.2Erect Steel - Light

4.3Bolted Connections

*5Materials

5.1Earthwork - Materials

5.2Concrete - Materials

5.3Structure Steel - Materials

WBS Phase CodeForecast at TO QtyUOM

10001.00Lump Su.

100110,000.00CY

100210,000.00CY

10031,000.00Ton

1004800.00Ton

1005200.00Ton

10062,000.00Ea

10071.00Each

100810,000.00CY

100910,000.00CY

10101,000.00Ton

Forecast | Created from Live forecast

Forecast Final CostForecast Final MHForecast Final Man Hour/UnitForecast Final PFForecast Final Unit CostForecast Method

\$250,000.000.000.000.00\$250,000.00Current estimate

\$400,000.008,000.000.801.00\$40.00Current budget

\$1,500,000.0030,000.003.001.00\$150.00Current estimate

\$1,000,000.0020,000.0020.001.00\$1,000.00Rollup

\$800,000.0016,000.0020.001.00\$1,000.00Current budget

\$200,000.004,000.0020.001.00\$1,000.00Current budget

\$0.000.000.000.00\$0.00Average performan...

\$1,750,000.000.000.000.00\$1,750,000.00Rollup

\$250,000.000.000.000.00\$25.00Current estimate

\$1,000,000.000.000.000.00\$100.00Current estimate

\$500,000.000.000.000.00\$500.00Current estimate

Forecast Final CostForecast Final MHForecast Man Hour

\$250,000.000.00

\$400,000.008,000.00

\$1,500,000.0030,000.00

\$1,000,000.0020,000.00

\$800,000.0016,000.00

\$200,000.004,000.00

\$0.000.00

\$1,750,000.000.00

\$250,000.000.00

\$1,000,000.000.00

\$500,000.000.00

Subtotals11

\$4,900,000.0058,000.00

\$4,950,000.0058,000.00

©2017 InEight Inc Privacy and Terms | Build: TID-WEB 2.0.6352.34563 | User: Kris Pooley <kris.pooley@ineight.com>

INEIGHT

2. Change this value to **125,000**.

Control

6100000 - PK3 Inc

Steel Structure Training Job

105098

View: Forecasts

Actions

CBS

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

Tasks

CBS Position

Description

1

Job Overhead

2

Earthwork

3

Concrete

4

Structural Steel

4.1

Erect Steel - Heavy

4.2

Erect Steel - Light

4.3

Bolted Connections

5

Materials

5.1

Earthwork - Materials

5.2

Concrete - Materials

5.3

Structure Steel - Materials

Task Det...

< >>>

WBS Phase Code

Forecast to City

UOM

1000

1.00

Lump Su.

1001

10,000.00

CY

1002

10,000.00

CY

1003

1,000.00

Ton

1004

800.00

Ton

1005

200.00

Ton

1006

2,000.00

Ea

1007

1.00

Each

1008

10,000.00

CY

1009

10,000.00

CY

1010

1,000.00

Ton

Forecast | Created from Live foreca...

< >>>

Forecast Final Cost

Forecast Final MH

Forecast Final Man Hour/Unit

Forecast Final PF

Forecast Final Unit Cost

Forecast Method

\$250,000.00

0.00

0.00

0.00

\$250,000.00

Current estimate

\$400,000.00

8,000.00

0.80

1.00

\$40.00

Current budget

\$1,500,000.00

30,000.00

3.00

1.00

\$150.00

Current estimate

\$1,000,000.00

20,000.00

20.00

1.00

\$1,000.00

Rollup

\$800,000.00

16,000.00

20.00

1.00

\$1,000.00

Current budget

\$200,000.00

4,000.00

20.00

1.00

\$1,000.00

Current budget

\$0.00

0.00

0.00

0.00

\$0.00

Average performan...

\$1,750,000.00

0.00

0.00

0.00

\$1,750,000.00

Rollup

\$250,000.00

0.00

0.00

0.00

\$25.00

Current estimate

\$1,000,000.00

0.00

0.00

0.00

\$100.00

Current estimate

125000

0.00

0.00

0.00

\$500.00

Current estimate

Forecast | Created from Live foreca...

< >>>

Forecast Final Cost

Forecast Final MH

Forecast Final Man Hour

\$250,000.00

0.00

\$400,000.00

8,000.00

\$1,500,000.00

30,000.00

\$1,050,000.00

20,000.00

\$800,000.00

16,000.00

\$200,000.00

4,000.00

\$500,000.00

0.00

\$1,750,000.00

0.00

\$250,000.00

0.00

\$1,000,000.00

0.00

\$500,000.00

0.00

Subtotals

11

\$4,900,000.00

58,000.00

\$4,950,000.00

58,000.00

©2017 InEight Inc Privacy and Terms | Build: TRN-WEB 2.0.6352.34563 | User: Kris Pooley <kris.pooley@ineight.com>

INEIGHT

To revert to the original value when manually typing into the cell, press the Escape (Esc) key.

All other cost categories proportionally adjust automatically once the labor is adjusted.


In the Forecast data block, blue dots indicate what the forecast driver is. A forecast driver is the manually edited value that the Forecast Final Cost is based off.

InEight Inc. | Release 26.7


Page 301 of 639

Forecast Created	
Forecast Final Cost	
 \$250,000.00	
 \$400,000.00	
 \$1,500,000.00	
\$1,000,000.00	
 \$800,000.00	
 \$200,000.00	
 \$0.00	
\$1,375,000.00	
 \$250,000.00	
 \$1,000,000.00	
 \$125,000.00 	

In the *Live forecast data block, orange triangles will appear in the top right-hand corner of the cell. These indicate what the forecast driver is and give a detail of the change when hovered over.

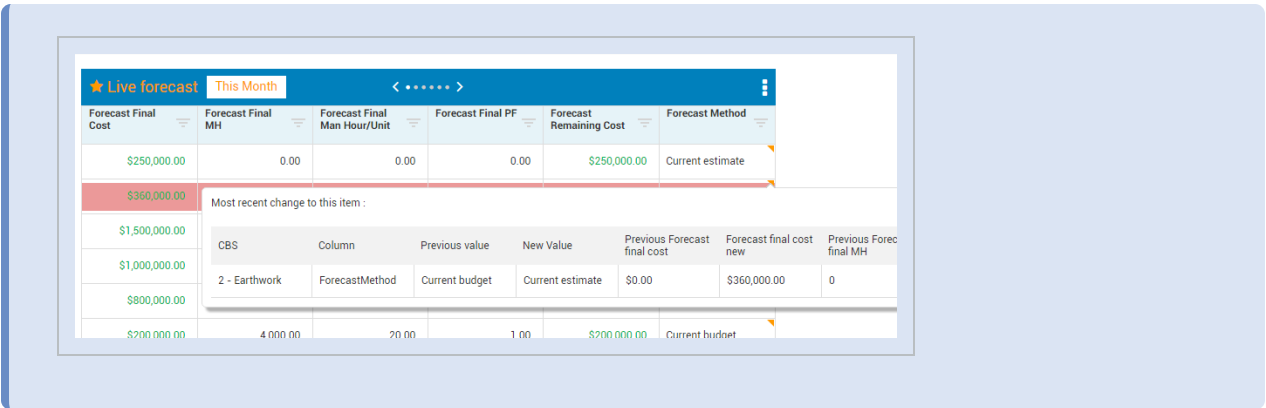

3. Hover over the **Forecast Final Cost** cell of the value you entered and select the **View cost categories** pop-up.

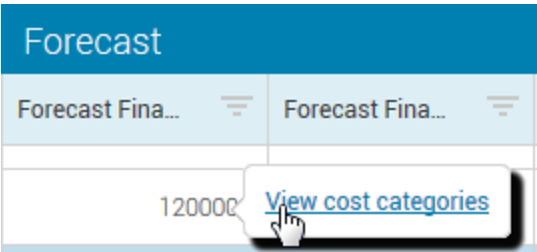

- You can see the adjustments that were made by cost category

7.6.2.1 Proportional Adjustment

As you make changes, you may receive a prompt asking you how you would like to adjust other values affected by your change. For example, when you change your Forecast Final Cost, this will affect either:

- Forecast Final MH or
- Forecast Final \$/MH

✕

Proportionally adjust Forecast Final MH or Forecast Final \$/MH ?

The Forecast Final Cost can be modified by proportionally adjusting Forecast Final MH or Forecast Final \$/MH. Specify the value you would like to modify:

☐ Forecast Final MH

0.000000000000

☐ Forecast Final \$/MH

0.000000000000

Cancel

OK

While one of those values will remain constant, the other will adjust as indicated in the table below:

Forecasting - Proportional Adjustment Example	
Action	Result
Original Forecasted Values	Forecast Final Cost = \$1000 Forecast Final MH = 100 Forecast Final \$/MH = 10
Manually adjust Forecast Final Cost	Forecast Final Cost changes from \$1000 to \$2000
Resulting adjustment Option 1: Adjust Forecast Final MH	Forecast Final Cost / Original Forecast Final \$/MH = Adjusted Forecast Final MH $\$2000 / 10 = 200 \text{ MH}$
Resulting adjustment Option 2: Adjust Forecast Final \$/MH	Forecast Final Cost / Original Forecast Final MH = Adjusted Forecast Final \$/MH $\$2000 / 100 = 20/\text{MH}$

7.6.3 Manual ETC (Estimate to Completion) Forecast

The Manual ETC (Estimate to Completion) forecast method can be used to make an adjustment to forecast the unit cost of the work remaining and adding it to the as-built costs in the calculation of the forecast.

To set the forecast remaining or ETC (Estimate to Complete) forecast, type a value into one of the following cells within the forecasting data block:

- Forecast Remaining Labor Cost/MHr
- Forecast Remaining Labor Cost
- Forecast Remaining Man-hours per Unit
- Forecast Remaining Productivity Factor
- Forecast Remaining Cost per Unit

This will set the unit cost and man hour factors. When applied to the remaining qty to deliver and added to the existing actuals this will equal your total forecast amounts.

7.6.3.2 Detailed ETC FC Method

The Detailed ETC (estimate to completion) method lets you modify the crew makeup and production rates that drive the remaining forecast values (based on remaining quantities and hours).

For example, if you started your project and you used apprentices, and now you prefer to use journeymen, you can swap out resources for your forecast resources and use journeymen instead of apprentices.

In Control settings > Project Tracking, you can now enable forecast methods for terminal cost items when the allow-as built is set to all or cost for Detailed ETC. When the Detailed ETC forecast method is enabled, all existing Current Estimate Resources for that cost item are copied to the Forecast Resources tab in the CBS > Cost Item Details slide-out panel.

Terminal cost items

When Allow as-built is set to *All or Cost*
Enable the following Forecast methods for terminal cost items when Allow as-built is set to *All or Cost*

Current estimate	☒	Manual (ETC)	☒
Current budget	☒	Manual (EAC)	☒
Average performance	☒	None	☒
Committed cost	☒	Contract	☒
Detailed ETC	☒		

Default Forecast method for terminal cost items when Allow as-built is set to *All or Cost*

Current estimate

Only enabled selections above are eligible. 'Manual (ETC)' and 'Manual (EAC)' cannot be default options.

When Allow as-built is set to *Quantity*
Enable the following Forecast methods for terminal cost items when Allow as-built is set to *Quantity*

Current estimate	☒	Manual (ETC)	☒
Current budget	☒	Manual (EAC)	☒
Average performance	☒	None	☒

Default Forecast method for terminal cost items when Allow as-built is set to *Quantity*

Current estimate

Only enabled selections above are eligible. 'Manual (ETC)' and 'Manual (EAC)' cannot be default options.


When Allow as-built is set to *None*
Enable the following Forecast methods for terminal cost items when Allow as-built is set to *None*

None	☒
------	-------------------------------------

Default Forecast method for terminal cost items when Allow as-built is set to *None*


None

When the Detailed ETC setting is enabled, a new tab is available in Cost Item Details called Forecast Resources. This new tab is almost identical to the Current Estimate Resources tab, with the major difference being that the Forecast Resources tab contains forecast information. You can edit these resources and values separately from the current estimate resources for a cost item.

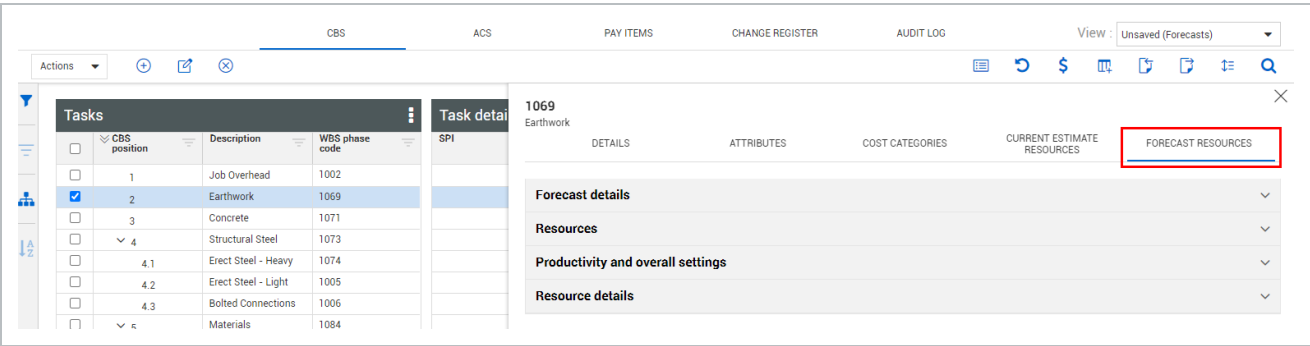

7.7 TIME PHASED FORECASTING


Projects are typically overwhelmed by escalating forecast values as the project progresses. What the business thought they were going to spend doesn't end up being very accurate at the end of a project. One way to mitigate this is to take the forecast and break it down into more consumable, estimate related time blocks/periods, as shown in the screenshot below. This prompts the project engineers to think about what activities, bills, and costs are going to occur in smaller more mentally digestible time periods.

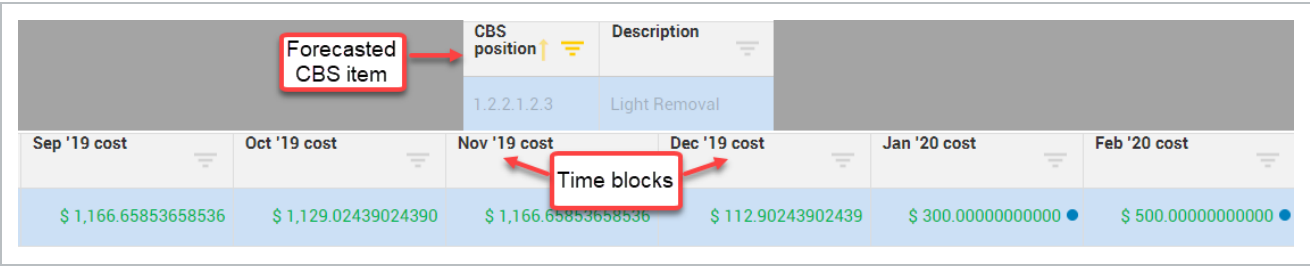

Projects need to spread their estimate by periods to verify forecast accuracy vs. the actuals spent within that period. One of the key goals of time phased forecasting is to see when you are forecasting to spend allocated budget. You can then determine how accurate your forecast was versus the actuals spent within that period. Based on forecast accuracy, this gives you the opportunity to make manual adjustments within the Time phased forecasting register. It also provides the ability to have the system automatically distribute the forecast for you based upon certain criteria.

TPF gives you visibility into when you are going to spend dollars associated to a cost item in monthly time periods. TPF also helps with cash flow, enabling customers to provide more insight into how much money they need to pay employees and other bills.

After selecting a cost item from the CBS, TPF can be accessed from Control > Workspaces > Actions > Time phased forecasting. This is only if the project settings for TPF is enabled under the Forecast section.

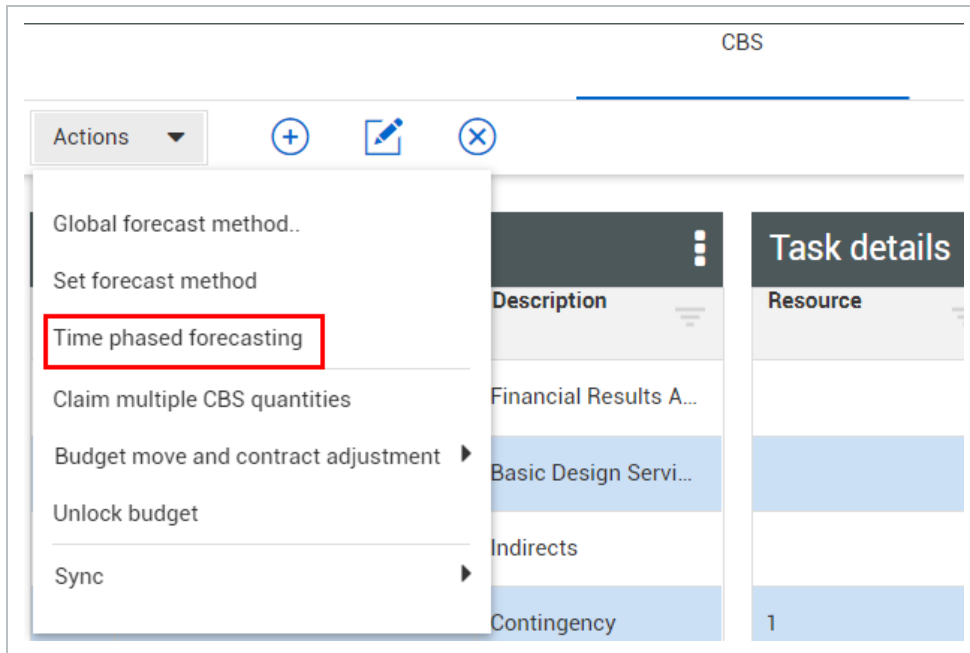

The table below shows the columns from the Time Phased Forecasting page.

Overview - Time phased forecast

	Resource	Description
1	Auto Distribute remaining forecast based on cost curve and start/end dates 	This will automatically distribute remaining forecast based on the cost curve being used, in addition to the Start and Finish dates.
2	CBS position	The CBS position identifier number.
3	Description	The description of the CBS.
4	WBS Phase code	Work Breakdown Structure code number.
5	Start	This is the scheduled start date for the cost item.
6	Finish	This is the scheduled finish date for the cost item.
7	Cost Curve	This is a graph/calculation of the costs of production as a function of total quantity produced. Cost curves can be created, viewed

Overview - Time phased forecast (continued)

	Resource	Description
		and maintained in Settings > Control > Schedule, in the Cost Curves section on the page.
8	Forecast method	Forecast methods include: Current Budget, Current Estimate, Average Performance, Manual (EAC), None, and Rollup.
9	Forecast remaining cost	This is the unsettled balance of forecast. Cost that is projected to still be required to be paid out (varies depending on forecast method).
10	Forecast final cost	Total cost to date + Forecast remaining cost, cost item projected total cost at completion.
11	Phased Forecast Remaining Cost Delta	This is the remaining forecasted cost that has not yet been allocated to a monthly period. It is the difference between the Forecast remaining cost and the sum of forecasted cost currently represented in all remaining months on the TPF window.
12	Load more	This will load additional month columns to view in the TPF window.
13	<date> cost	The forecasted cost projected to be incurred during that individual month.

CBS > Time Phased Foreca...												
	1											
☐	CBS position	Description	WBS phase code	Start	Finish	Cost curve	Forecast method	Forecast remaining cost	Forecast final cost	Phased forecast remaining cost delta	Load m...	Jul '19 cost
☐	1	Financial Results...	1000	06/19/2019	12/31/2019	Linear	Rollup	\$ 15,038,381.26	\$ 15,038,381.26	(\$ 15,038,381.26)		\$ 35,544.88
☐	1.1	Commercial Cost	1025	06/19/2019	12/31/2019	Linear	Rollup	\$ 1,410,506.62	\$ 1,410,506.62	(\$ 1,410,506.62)		\$ 984.78
☐	1.1.1	G & A Expense (7...	1026	06/19/2019	06/19/2019	Linear	Current estimate	\$ 1,090,208.12	\$ 1,090,208.12	(\$ 1,090,208.12)		\$ 0.00
☐	1.1.2	P & P Bond (0.40...	1027	06/19/2019	06/19/2019	Linear	Current estimate	\$ 67,828.91	\$ 67,828.91	(\$ 67,828.91)		\$ 0.00
												Aug '19 cost
												\$ 116,944.26
												\$ 5,507.29
												\$ 0.00
												\$ 0.00
												Aug '19 remaining cost
												\$ 0.00

There is a **Load More** column that exists in the middle/top of the page. When selected, additional monthly time buckets will be added to the page.

Forecast method	Load more	Jan '19 cost
Current estimate		\$ 0.00

7.7.1 TPF Register

The Time phased forecasting register allows you to time phase **auto spread** forecast remaining costs, which are based on cost curves, and start/end dates. You can also **manually override** specific months and change the distribution costs.

For example: you have \$250,000 to spend on a cost item (Forecast remaining cost). You can use Time Phased Forecasting to spread your dollars into monthly allocation buckets. This can be done by automatically spreading the \$250,000 forecast, or by manually overriding the forecast and entering your own values into the monthly buckets.

CBS > Time Phased Foreca...										Auto spread forecast						Manual override					
	CB po	Descript	WE ph co	Start	Finist	Cost cur	Form	Forecast remaining cost	Forecast final cost	Phase remain delta	Sep '19 remaining cost	Oct '19 cost	Nov '19 cost	Dec '19 cost	Jan '20						
	1	Job Overhead	1002	06/11/2019	11/25/2019	Linear	Cur...	\$ 250,000.00	\$ 250,000.00		000.00	\$ 0.00	\$ 60,000.00	\$ 25,000.00	\$ 48,000.00						
	2	Earthwork	1069	11/26/2019	05/11/2020	Linear	Cur...	\$ 800,000.00	\$ 800,000.00		\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	\$ 28,571.43						
	3	Concrete	1071	05/12/2020	10/26/2020	Linear	Cur...	\$ 3,000,000.00	\$ 3,000,000.00		\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00						
	4	Structural Steel	1073	10/27/2020	04/12/2021	Linear	Roll...	\$ 1,050,000.00	\$ 1,050,000.00		\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00						

7.7.2 Auto Distribute

The **Auto distribute** icon allows you to have the system automatically allocate remaining forecast as determined by your **Actual Start** date, **Actual Finish** date, and **Cost Curve**.

CBS

>

Time Phased Foreca...

+ -

+ -

Auto distribute remaining forecast based on
cost curve and start/end dates

	CBS positio								
☒	1.1	Basi...	1001	03/...	09/...	L	Roll...	10,0...	
☒	1.1.1	Indi...	1002	03/...	09/...	L	Roll...	12,1...	
☒	1.1.1.1	Con...	1003	07/...	09/...	L ⚠	Curr...	126,...	
☐	1.1.1.2	Job ...	1009	06/...	09/...	F ⚠	Curr...	USD...	
☐	1.1.1.3	Desi...	1006	07/...	07/...	L ⚠	Curr...	(6,5...	
☐	1.1.1.4	Job ...	1004	03/...	12/...	B	Roll...	(21...	
☐	1.1.1.4.1	Desi...	1005	03/...	08/...	L ⚠	Curr...	30,1...	

Load m...	Jul '19 cost	Aug '19 cost	Aug '19 remaining cost
	1,092,364,798.677	12,310,649,399.471	12,567,815,504.198
	1,092,364,798.677	12,310,649,399.471	12,567,815,504.198
	19,187,552.694	1,641,816.243	102,472,320.000
	USD 21,497,584.087	USD 11,845,050,361.155	USD 12,345,678,901.123
	(136,936.199)	3.116	0.000
	961,605.565	(1,068,557.342)	(1,535,622.827)
	(86,894.355)	(253,032.894)	30,158.730

The Auto distribute icon allows you to automatically distribute dollars into monthly allocation buckets. In this case, the allocating of dollars will begin on the **Start** date of May 2020 and stop allocating on **Finish** date month of October of 2020.

Descript	WBS phase code	Start	Finist	Cos curv	For m	Forec rema cost	Phased forecast remaining...	Sep '20 cost	Oct '20 cost
Concrete	1071	05/12/2020	10/26/2020	Linear 	Curr...	\$ 3,000,00...	\$ 0.00	\$ 553,571.43	\$ 535,714.29

7.7.3 Manual Time Phased Forecast

Using the same example, it's also possible to manually forecast the allotted \$3,000 into your desired monthly buckets. By manually entering in \$400,000.00 into the Oct 2020 bucket, your Phased forecast remaining cost delta changes to \$135,714.29. This represents the remaining amount of dollars to still be forecasted.

Descript	WBS phase code	Start	Finish	Cost curve	Forecast	Forecast remaining	Aug '20 cost	Sep '20 cost	Oct '20 cost
Concrete	1071	05/12/2020	10/26/2020	Linear	Current	\$ 3,000,000	\$ 35,714.29	\$ 553,571.43	\$ 400,000.00

On the right side of the screen, a blue circle displays by the forecast quantity when a manual override to the forecast quantity is performed. If you hover over the blue circle, it shows a description of the manual override.

Sep '19 cost	Oct '19 cost	Nov '19 cost
\$ 238,134.05	\$ 221,910.98	\$ 1,266,...
\$ 10,723.09	\$ 76,254.74	\$ 3,...
\$ 0.00	\$ 500.00	
\$ 0.00		
\$ 0.00		

Manual Override:
Changed by: paul trippi
Change date: 08/05/2019 04:29 PM
Value before: \$ 0.00


On the left side of the screen, a manual override to the forecast amount shows a warning symbol by the cost curve. Hovering over the warning sign shows that the cost item contains a manual change to the time phased months, and thus, the cost curve is no longer accurate.

CBS position	Description	ist	Cost curve	Forec meth	Fore co
1	Financial Results...	31/2019	Linear	Rollup	\$
1.1	Commercial Cost	31/2019	Linear	Rollup	\$
1.1.1	G & A Expense (7...	19/2019	Linear	Current es...	\$
1.1.2	P & P Bond (0.40...	19/2			
1.1.3	Builder's Risk Ins...	10/2019	Linear	Current es...	

Cost item contains manual time phased months


7.7.3.1 Proportional Man Hours and Quantity

In addition to Cost, Man hours and Quantity displays on the Time phased forecast grid. If you manually adjusted the cost for one of the months in the grid, a dialog box appears asking to proportionally adjust Man hours and the Quantity.

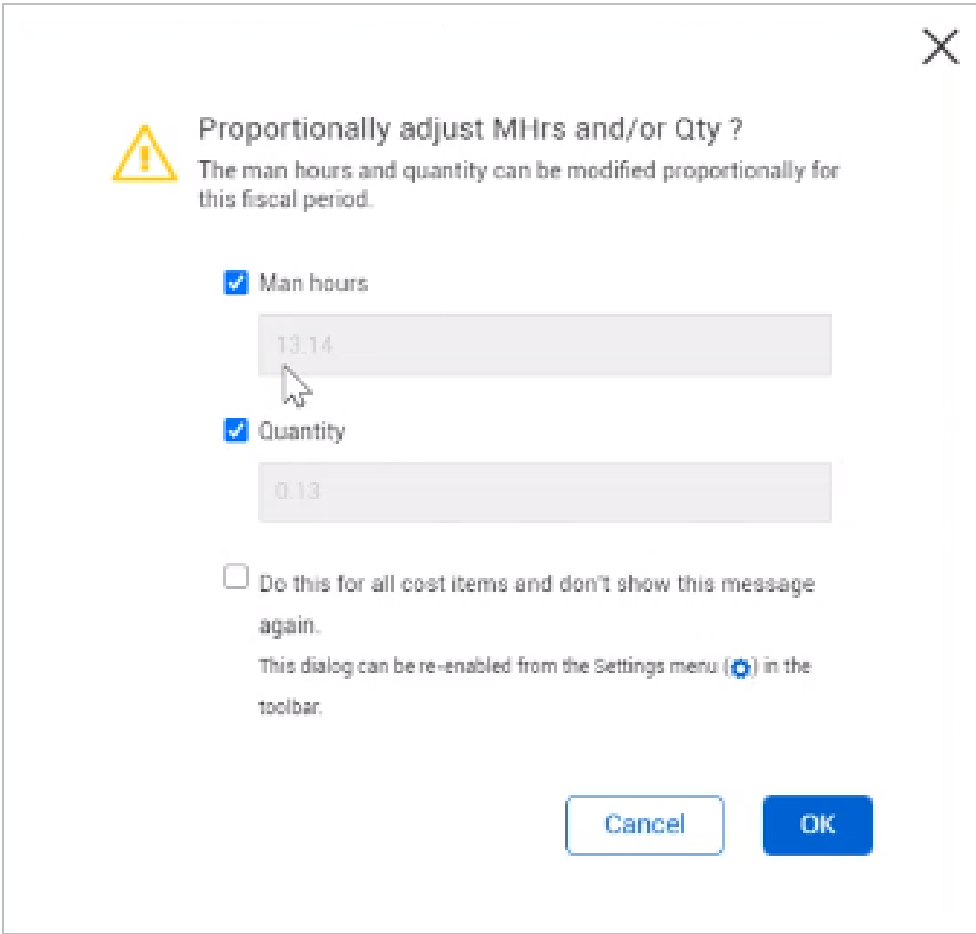

If for example you doubled your cost in the Time phased forecast, it would also proportionally double your Man hours or Quantity. You can view the values that the man hours and quantity would proportionally adjust to in the read only cells.

If you manually adjusted Man hours or Quantity in the Time phased forecast grid, a dialog box appears asking to proportionally adjust cost and man hours .

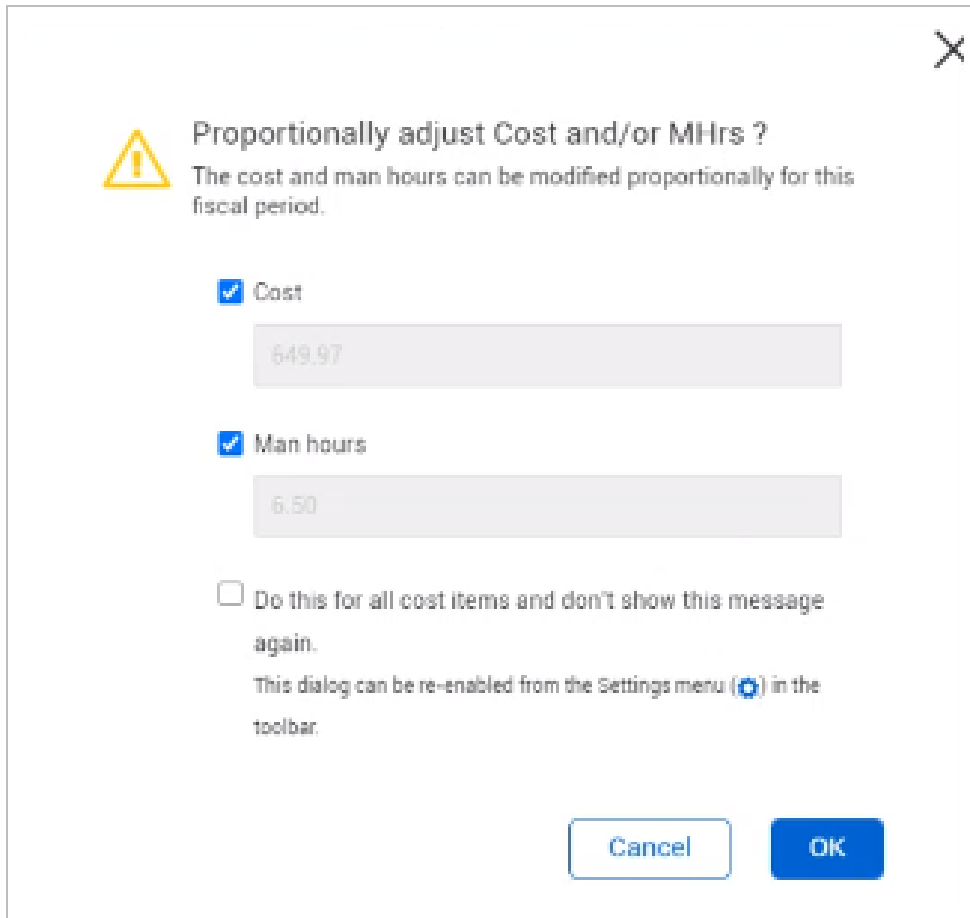

A dialog box with a yellow warning icon and a close button (X) in the top right corner. The title is "Proportionally adjust Cost and/or MHrs ?". The text below the title says "The cost and man hours can be modified proportionally for this fiscal period." There are two checked checkboxes: "Cost" and "Man hours". Below "Cost" is a text field containing "649.97". Below "Man hours" is a text field containing "6.50". There is an unchecked checkbox labeled "Do this for all cost items and don't show this message again." Below this checkbox is a note: "This dialog can be re-enabled from the Settings menu (⚙️) in the toolbar." At the bottom are "Cancel" and "OK" buttons.

Proportionally adjust Cost and/or MHrs ?

The cost and man hours can be modified proportionally for this fiscal period.

☒ Cost

649.97

☒ Man hours


6.50

☐ Do this for all cost items and don't show this message again.


This dialog can be re-enabled from the Settings menu (⚙️) in the toolbar.

Cancel OK

Both dialog boxes have the option to adjust proportionally without showing the message again. If you selected this option and want to revert settings back to see the dialog again, in the Time phased forecast grid, go to the Settings icon and select **Enable dialogs**.

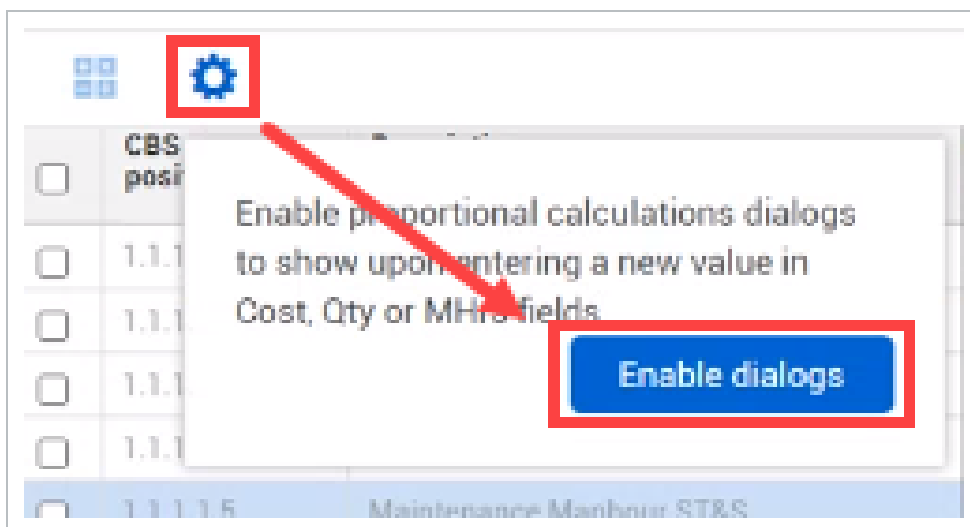


In the Time phase forecast grid, you can also select to export to Excel.

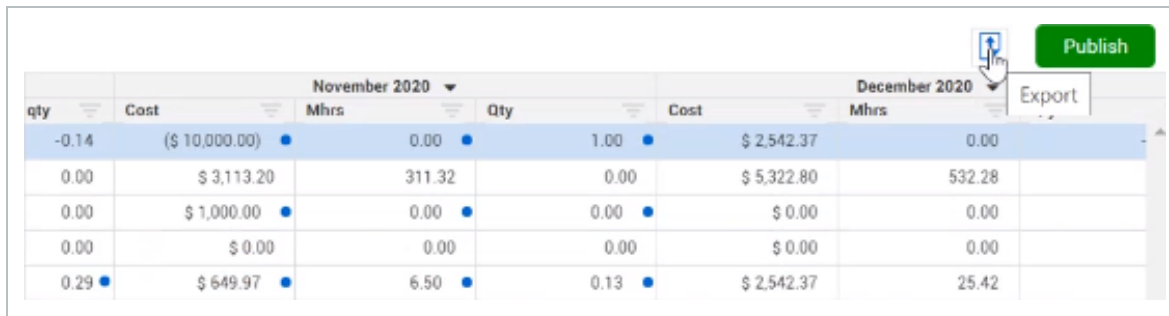

November 2020			December 2020		
Qty	Cost	Mhrs	Qty	Cost	Mhrs
-0.14	(\$ 10,000.00)	0.00	1.00	\$ 2,542.37	0.00
0.00	\$ 3,113.20	311.32	0.00	\$ 5,322.80	532.28
0.00	\$ 1,000.00	0.00	0.00	\$ 0.00	0.00
0.00	\$ 0.00	0.00	0.00	\$ 0.00	0.00
0.29	\$ 649.97	6.50	0.13	\$ 2,542.37	25.42

Selecting this exports everything that is in your view to an Excel spreadsheet.




A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S
CBS posit	Descriptio	WBS phas	Start	Finish	Forecast n	Cost curve	Forecast r	Forecast r	Qty remai	Phased fo	Phased fo	Phased fo	March 20	March 20	March 20	April 2020	April 2020	April 2020
1.1.1.1.1	MAINTAIN	1348	#####	#####	Manual (E Linear	10000	100	-1	-12627.1	-100	1.262712		0	0	0	0	0	0
1.1.1.1.2	FUEL AND	1017	#####	#####	Manual (E Bell Shape	10000	100	-99	0.001005	900	99		0	0	0	0	0	0
1.1.1.1.3	GAS & DIE	1018	#####	#####	Manual (E Front Load	10000	100	-220	1000	-100	220		0	0	0	0	0	0
1.1.1.1.4	FUEL HOSI	1474	#####	#####	Manual (E Back Load	10000	100	1	-1.7E-05	-100	0		0	0	0	0	0	0
1.1.1.1.5	Maintenai	1476	#####	#####	Manual (E Linear	10000	100	1	-535.826	-5.35826	0.01142		0	0	0	0	0	0

7.7.4 Static manual time phased forecasting (TPF)

Static manual TPF lets you distribute a time phased forecast in the future without causing a redistribution. All values entered in the TPF are constant, and any deltas based on current month actuals that do not equal what was forecasted for that month, must be spread manually.

To enable the static manual forecast method, the Forecasting and Push time phased forecast to Live forecast toggles must be set to *On* in Settings > Control > **Forecast**.

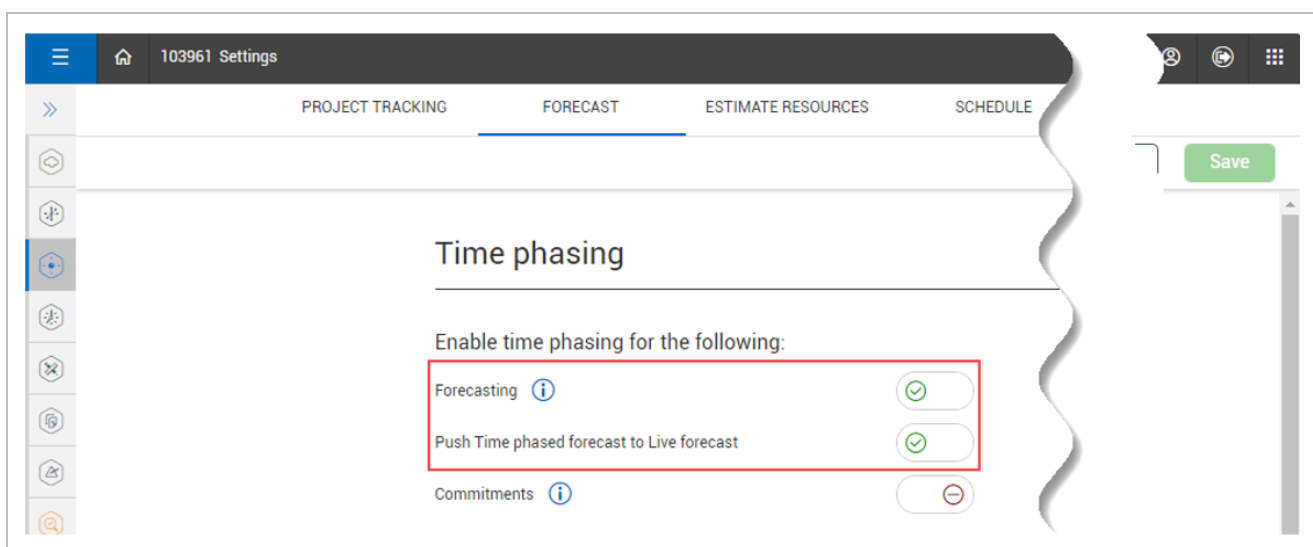

103961 Settings

PROJECT TRACKING FORECAST ESTIMATE RESOURCES SCHEDULE

Time phasing

Enable time phasing for the following:


Forecasting  

Push Time phased forecast to Live forecast 

Commitments  

Save

The static manual forecast can be enabled on the Time phased forecasting page by first making a change to any of the distribution fields. After you click the **Publish** button, the Push these values to the Live forecast dialog box opens. When the Do not redistribute manual spread check box is selected, the values entered in whole months remain as-entered and are not automatically redistributed when actuals are incurred or months close.

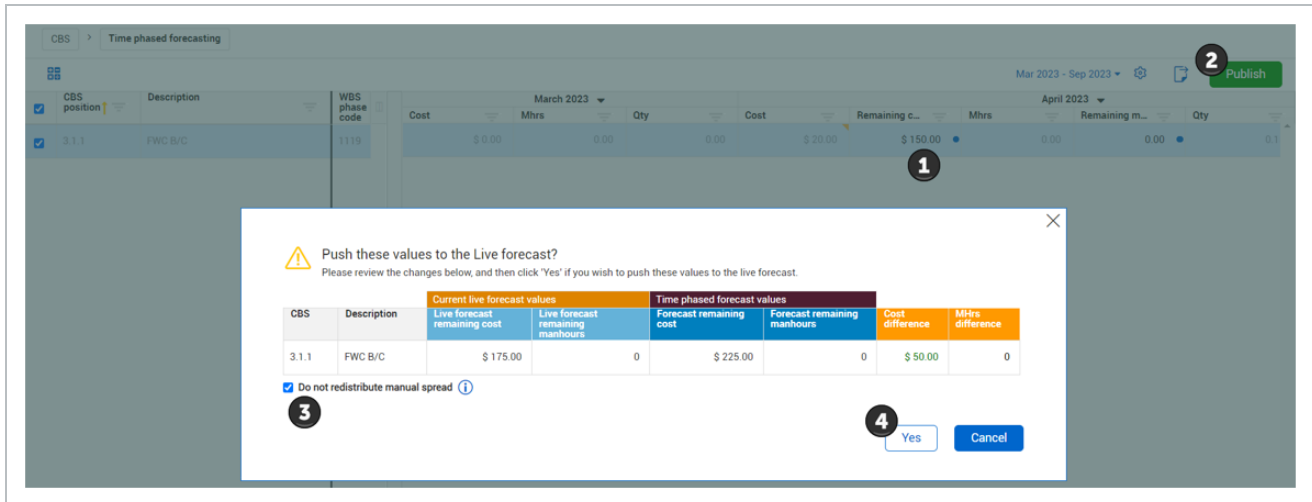

The forecast method for the CBS record automatically changes to static manual TPF, and the forecast remaining cost and forecast total cost changes based on the distribution amount adjusted in TPF.

Tasks			Live forecast  Current live forecast 					04/11/2023 	
☐	CBS position	Description	Forecast remaining cost	Forecast total cost	Forecast remaining Mhrs	Forecast remaining unit cost	Forecast method		
☐	3.1	Misc. Rev External	\$ 2,375.00	\$ 245,042.96	75.00	\$ 9,500.00	Rollup		
☒	3.1.1	FWC B/C	\$ 225.00	\$ 325.00	0.00	\$ 450.00	Static manual TPF ...	Static Manual TPF (estimate at completion)	

If costs are claimed for the CBS item, the forecast total cost remains the same, but the forecast remaining cost is reduced from the claimed actual quantity.

Tasks

	CBS position	Description
☐	3.1	Misc. Rev External
☒	3.1.1	FWC B/C
☐	3.1.2	Vantage Dewateri...
☐	3.1.2.1	Craft Labor
☐	3.1.2.2	Equipment

CLAIM ACTUALS ACTUALS HISTORY COMMITMENTS

CE total cost

\$ 100.00

Actual cost (to date)

\$ 100.00

Claimed cost

50

Cost category

333333

Posted date

04/21/2023

Tasks

	CBS position	Description
☐	3.1	Misc. Rev External
☒	3.1.1	FWC B/C

Live forecast Current live

	Forecast remaining cost	Forecast total cost
	\$ 2,325.00	\$ 245,042.96
	\$ 175.00	\$ 325.00

In TPF, the claimed amount now shows the phased forecast remaining cost, which represents the remaining amount that still needs to be spread. The phased forecast remaining cost now must be deducted somewhere from the TPF distribution.

	CBS position	Description	Forecast remain... cost	Forecast remaining Mhrs	Remaining qty	Phased forecast remaining cost
☐	3.1.1	FWC B/C	\$ 175.00	0.00	0.50	\$ 50.00

	CBS position	Description	WBS phase code	Start	Cost	Remaining c...
☒	3.1.1	FWC B/C	1119	04/01/2023	\$ 0.00	-50

7.7.5 Time Phased Forecast Settings

Time phased forecast can be turned on in Settings > Control > **Project Settings**, in the Forecast section of the page.

If the setting is turned off, you will not see the Time phased forecasting option in the Actions drop-down, CBS tab, in the Control > Workspaces page.

7.7.5.2 Enable Time Phased Forecasting

Time phasing

Enable time phasing for the following:

Forecasting ⓘ

✓

Push Time phased forecast to Live forecast

⊖

Time phased forecasting provides the ability to spread forecast remaining values into the projects fiscal periods. Navigate to Project details to set the Start and End dates which define the earliest and latest project periods.

7.7.5.3 Cost Curves


Cost curves determine the proportion of money to be expended in a certain period of time. In the case of Time phased forecasting, the type of cost curve being used determines how forecast will be spread across the monthly forecasting buckets.

In addition, the fiscal calendar also influences how the forecast is spread.

Cost Curves are found in Settings > Control > Schedule, in the Cost Curves section of the page.

Cost curves																	
Customize cost curve tables																	
+ ⏮ ⏭ × <table> <tr> <th>☐</th><th>Description</th><th>Data points</th></tr> <tr> <td>☐</td><td>Linear</td><td>20</td></tr> <tr> <td>☐</td><td>Front Loaded</td><td>2</td></tr> <tr> <td>☐</td><td>Back Loaded</td><td>2</td></tr> <tr> <td>☐</td><td>Bell Shaped</td><td>21</td></tr> </table>			☐	Description	Data points	☐	Linear	20	☐	Front Loaded	2	☐	Back Loaded	2	☐	Bell Shaped	21
☐	Description	Data points															
☐	Linear	20															
☐	Front Loaded	2															
☐	Back Loaded	2															
☐	Bell Shaped	21															

By selecting a Cost Curve and selecting the View icon, you can view its default distribution.

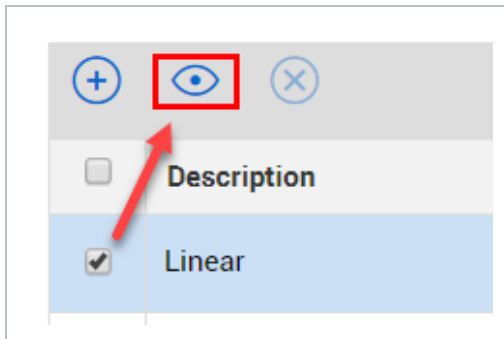

In this case, the Linear Cost Curve settings displays the cost curve durations and values.

Description		Number of points
Linear		20
From duration %	To duration %	Value %
0.00%	5.00%	5.00%
5.00%	10.00%	5.00%
10.00%	15.00%	5.00%
15.00%	20.00%	5.00%
20.00%	25.00%	5.00%
Total		100.00%

For example, using a **Linear Cost curve**, with a Start Date of 05/12/2020, the Forecast Remaining cost is \$3,000,000.00, with a Phased forecast remaining cost delta of \$0. This means that you are forecasting to spend \$3,000,000.00, and your Phased Forecast Remaining Delta is zero because your Time Phased Forecast is now fully met (you have fully forecasted \$3,000.000.00).

CE po	Descript	WE ph: col	Start	Finish	Cost curve	Forecast	Forecast remaining cost	Forecast final cost	Phased forecast remaining cost delta
3	Concrete	1071	05/12/2020	10/26/2020	Linear	Curr...	\$ 3,000,000.00	\$ 3,000,000.00	\$ 0.00

Since your scheduled **Start** date is 05/12/2020, the system will start forecasting money on this cost item in May. Based on the Linear Cost curve and the fiscal calendar it will stop forecasting money in October 2020. This is based off your scheduled **Finish** date of 10/26/2020. Over the period of 6 months, your spend is totaling 3,000.000.00.

May '20 cost	Jun '20 cost	Jul '20 cost	Aug '20 cost	Sep '20 cost	Oct '20 cost
\$ 339,285.71	\$ 500,000.00	\$ 500,000.00	\$ 625,000.00	\$ 500,000.00	\$ 535,714.29

7.7.6 Time Phased Forecast Prerequisites

There are certain **requirements** for a cost item to be eligible for time phased forecasting.

1. The Schedule data block must have a Start and Finish date.
2. The Schedule data block must have a Cost curve association.

7.7.7 Time Phased Forecast View

You may want to create a View in your Control Workspace similar to this one showing a Time Phased Forecast in comparison with the Live forecast. This shows the hours you are forecasting to spend money (TPF) vs. the Live forecast.

Tasks				TPF					Live forecast					This Month	
CB pos	Descrip	WBS phase code		Start	Finish	Cost curve	Forecast remaining cost	★ Phased forecast remaining co...	Forecas method	Forecast final cost	Forecast final man hours/Unit	Forecast final MHrs	Forecast final productiv...	Forecast final unit cost	
1	Job Overh...	1002		06/11/2019	11/25/2019	Linear	\$ 250,000.00	(\$ 0.00)	Current esti...	\$ 250,000.00	0.00	0.00	0.00	\$ 250,000.00	
2	Earthwork	1069		11/26/2019	05/11/2020	Linear	\$ 800,000.00	(\$ 0.00)	Current esti...	\$ 800,000.00	1.60	16,000.00	1.00	\$ 80.00	
3	Concrete	1071		05/12/2020	10/26/2020	Linear	\$ 3,000,000.00	\$ 320,000.00	Current esti...	\$ 3,000,000.00	6.00	60,000.00	1.00	\$ 300.00	
4	Structural ...	1073		10/27/2020	04/12/2021	Linear	\$ 1,050,000.00	(\$ 1,050,000.00)	Rollup	\$ 1,050,000.00	21.00	21,000.00	1.00	\$ 1,050.00	
	Erect Steel...	1074				Linear	\$ 800,000.00	(\$ 800,000.00)	Current esti...	\$ 800,000.00	20.00	16,000.00	1.00	\$ 1,000.00	
	Erect Steel...	1005				Linear	\$ 200,000.00	(\$ 200,000.00)	Current esti...	\$ 200,000.00	20.00	4,000.00	1.00	\$ 1,000.00	
	Bolted Con...	1006				Linear	\$ 50,000.00	(\$ 50,000.00)	Current esti...	\$ 50,000.00	0.50	1,000.00	1.00	\$ 25.00	
5	Materials	1084				Linear	\$ 1,750,000.00	(\$ 1,750,000.00)	Rollup	\$ 1,750,000.00	0.00	0.00	0.00	\$ 1,750,000.00	
	Earthwork ...	1085				Linear	\$ 250,000.00	(\$ 250,000.00)	Current esti...	\$ 250,000.00	0.00	0.00	0.00	\$ 25.00	
	Concrete ...	1086				Linear	\$ 1,000,000.00	(\$ 1,000,000.00)	Current esti...	\$ 1,000,000.00	0.00	0.00	0.00	\$ 100.00	
	Structure ...	1087				Linear	\$ 500,000.00	(\$ 500,000.00)	Current esti...	\$ 500,000.00	0.00	0.00	0.00	\$ 500.00	
Subtotals 11							\$ 6,850,000.00			\$ 6,850,000.00		97,000.00			

The following steps walk you through how to plan Time phased forecasting.

Time Phased Forecast Planning

1. To start time phased forecasting, on the CBS tab, select your pre-determined **CBS items** as shown below.

Tasks			Schedule			
	CBS position	Description	Scheduled	Schedule ID	Schedule plug days	Plug days
☒	1	Job Overhead	☒	HD 0000003	☐	0.00
☒	2	Earthwork	☒	HD 0000019	☐	90.91
☒	3	Concrete	☒	HD 0000044	☐	375.00
☒	4	Structural Steel	☒	HD 0000046	☒	262.50
☒	4.1	Erect Steel - Heavy	☐	HD 0000064	☐	200.00
☒	4.2	Erect Steel - Light	☐	HD 0000105	☐	50.00

2. Select **Time phased forecasting** from the Actions menu.

Actions

Global forecast method..

Set forecast method

Time phased forecasting

Claim multiple CBS quantities

Budget move and contract adjustment

Unlock budget

Sync

Fiscal calendar settings have been

Description
Job Overhead
Earthwork
Concrete


- This action opens the **Time Phased Forecast** window, where you can see the CBS on the left side of the screen, and its associated forecasting monthly allocation cost buckets on the right

CBS > Time Phased Foreca...												Publish				
	CE po	Descript	Wl ph co	St	Finish	Co cur	Fo mi	Forecast remaining cost	Forecast final cost	Phased remain delta	Load m	Jul '19 cost	Aug '19 cost	Aug '19 remaining cost	Sep '19 cost	Oct '19 cost
☐	1	Job Overhead	1002	06/...	11/25/2019	Lin...	Curr...	\$ 250,000.00	\$ 250,000.00			\$ 0.00	\$ 18,000.00	\$ 18,000.00	\$ 62,000.00	
☐	2	Earthwork	1069	11/...	05/11/2020	Lin...	Curr...	\$ 800,000.00	\$ 800,000.00			\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	
☐	3	Concrete	1071	05/...	10/26/2020	Lin...	Curr...	\$ 3,000,000.00	\$ 3,000,000.00			\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	
☐	4.1	Erect Steel - ...	1074			Lin...	Curr...	\$ 800,000.00	\$ 800,000.00			\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	
☐	4.2	Erect Steel - ...	1005			Lin...	Curr...	\$ 200,000.00	\$ 200,000.00			\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	
☐	4	Structural St...	1073	10/...	04/12/2021	Lin...	Roll...	\$ 1,050,000.00	\$ 1,050,000.00			\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	

3. For one of your cost items, type in **\$500** in one of the monthly bucket fields.

	Feb '20 cost	Mar '20 cost	Apr '20 cost
\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00
147,619.05	\$ 147,619.05	\$ 138,095.24	\$ 147,619.05
\$ 0.00	\$ 0.00	\$ 500.00	\$ 0.00
\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00

- Notice how the field now has a blue circle next to the \$500.00. If you hover over it, you see the value before, after, and the date the change was made

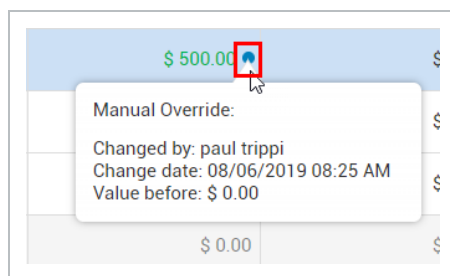


- Because of the manual adjustment, a warning sign appears on the Cost curve for this cost item. The cost curve is not being changed to manual, but the system records that this cost item is no longer linear, because it has been overridden

CE po	Descript	Wl ph co	St	Finish	Cost curve
1	Job Overhead	1002	06/...	11/25/2019	Linear
2	Earthwork	1069	11/...	05/11/2020	Linear
3	Concrete	1071	05/...	10/26/2020	Linear

- The override made to this cost item is no longer needed, and you now decide you want to **revert** to its original setting, and have the system Auto distribute the forecast

4. Make sure your cost item is checked, then select the **Auto distribute** icon.




- This action will revert the time phase values back to the same numbers as they were prior to any manual adjustments, plus:
 - a. It will erase any manual adjustments
 - b. It will distribute the remaining forecast values based on cost curve and start/end dates of that specific cost item, as determined by the fiscal calendar
- The result of selecting the Auto distribute icon starts its forecasting spread on the cost item's **Start** date of 05/12/20, and will **Finish** its schedule on 10/26/20

The screenshot shows a table with columns: Descript, WBS phase code, Start, Finish, Cos' curv, Fo mi, Forec rema cost, Phased forecast remaining..., ig '20 cost, Sep '20 cost, and Oct '20 cost. The first row shows: Concrete, 1071, 05/12/2020, 10/26/2020, Linear, Curr..., \$ 3,000,00..., \$ 0.00, \$ 553,571.43, \$ 553,571.43, \$ 535,714.29. A red box highlights the 'Auto distribute' icon, and a red arrow points from it to the 'Phased forecast remaining...' column.

It is important to remember the purpose of utilizing Time Phase Forecasting is to see how you are forecasting to spend money over a period of time. The expectation is to get the forecast adjusted to where it should be, and update costs as needed.

7.7.8 Time Phased Forecast Microsoft Excel import

You can import a Microsoft Excel file to update the values in Time Phased Forecast by selecting **Import** on the Time Phased Forecast page to download the time phased template. To import time phased forecast values, you can download a template as shown in number 2 in the image below to use as a guide to import your new time phased forecast values. The same format provided in the download template is required for the import to be successful.

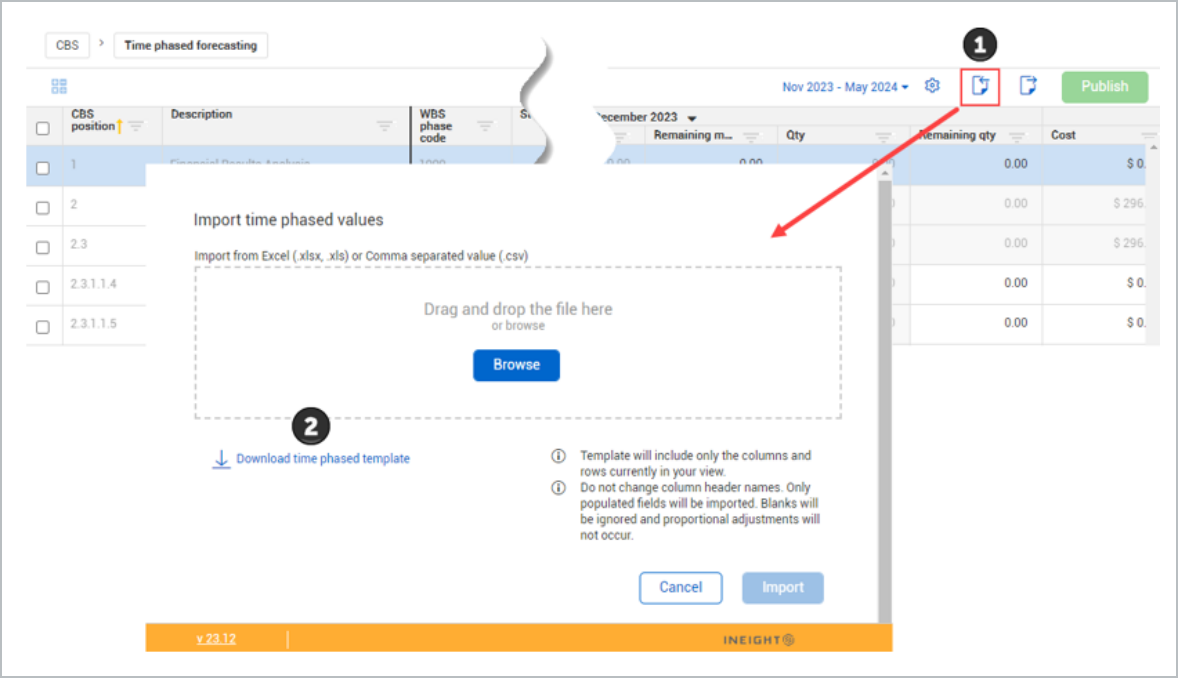

The Excel file includes the cost items that are in your current Time Phased Forecast view. Columns in orange are required, columns in yellow are optional to change, and columns in grey are ignored and cannot be changed. When you are finished making your Excel changes, you can then import the Excel file into Control to update the Time Phased Forecast with your new values. Column header names are ignored if changed.

	A	B	C	D	E		L	M	N	O
1	Orange	Required								
2	Yellow	Optional								
3	Gray	Ignored								
4										
5	CBS position	Description	WBS phase code	Start	Finish		Phased forecast rema	Phased forecast rema	November	November
6	1	Financial Results Analysis	1000			CL	0	-1	0	0
7	2	Misc. Rev Internal	1103	1/1/2024	3/31/2024	Re	0	-0.000956353	0	0
8	2.3	Directs	1001	1/1/2024	3/31/2024		56	9.1E-09	0	0
9	2.3.1.1.4	Type D Excavation LD/PL/CP to Embankm	1007			W	0	0	0	0
10	2.3.1.1.5	Road Subgrade Prep/Place/Finish (1600 m	1008			Cu	0	0	0	0
11	2.3.1.1.8	Sump Excavation & Backfill (CONDITIONA	1011				0	0	0	0


Updates are made when you select **Publish**. Excel imports are shown in the Import History Audit Log, where you can download the Excel file to see a list of errors if the process fails.

Time phased forecast Microsoft Excel import

- 1. To start time phased forecasting, on the CBS tab, select your pre-determined **CBS items** as shown below.

Tasks			Task details		
☐	CBS position	Description	Forecast (T/O) qty	UoM	Actual Mhrs (to date)
☒	1	Financial Results ...	1.00	PLS	0.00
☒	2	Misc. Rev Internal	1.00	PLS	7,030.50
☒	2.1	Misc. Rev Internal	1.00	PLS	0.00
☒	2.3	Directs	1.00	PLS	3,821.00
☒	2.3.1	Direct Labour	1.00	PLS	3,067.00

- 2. Select **Time phased forecasting** from the Actions menu.

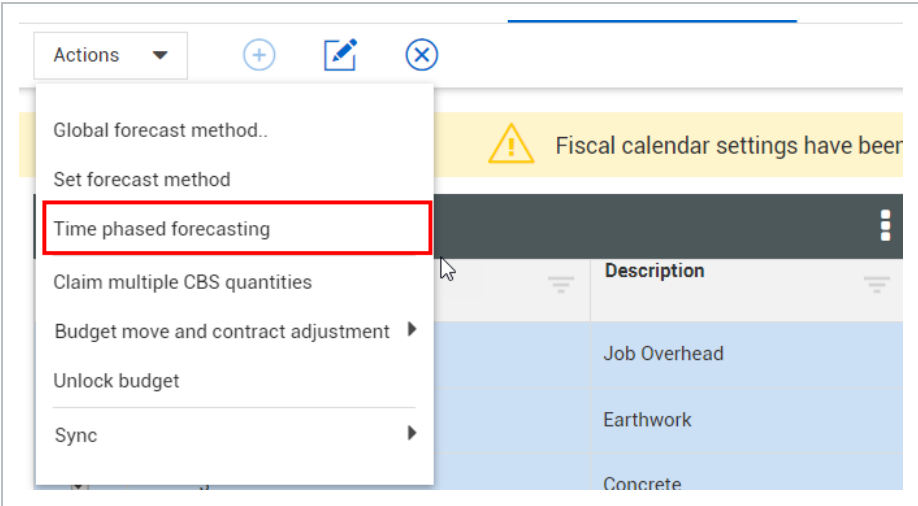

3. Select the **Import** icon.

CBS > Time phased forecasting

☐

CBS position

Description

WBS phase code

☐

1

Financial Results Analysis

1000

☐

2

Misc. Rev Internal

1103

☐

2.1

Misc. Rev Internal

1104

☐

2.3

DIRECTS

1001

☐

2.3.1

Direct Labour

1002

Dec 2023 - Jun 2024

Import icon

Export icon

Publish

February 2024

Mhrs

Qty

Cost

\$ 0.00

0.00

0.00

\$ 0.00

\$ 13.63

10.00

0.00

\$ 12.00

\$ 0.00

0.00

0.00

\$ 0.00

\$ 13.63

10.00

0.00

\$ 12.00

\$ 13.63

10.00

0.00

\$ 12.00

4. Click **Download time phased template**.

Import time phased values

Import from Excel (.xlsx, .xls) or Comma separated value (.csv)

Drag and drop the file here or browse

Browse

Download time phased template

Template will include only the columns and rows currently in your view.

Do not change column header names. Only populated fields will be imported. Blanks will be ignored and proportional adjustments will not occur.


Cancel

Import


5. Adjustment any of the fields under the **yellow columns**. For example, for CBS position 2.3, change the February 2024 Cost from 13.62637329 to 9, then **save** your changes.

T1									
	A	B	S	T	U	V	W	X	Y
1	Orange	Required							
2	Yellow	Optional							
3	Gray	Ignored							
4									
5	CBS position	Description	January 20	February 2024 Cost	February 2024 Mhrs	February 2024 Qty	March 2024 Cost	March 2024 Mhrs	March 2024 Qty
6	1	Financial Results Analysis	0	0	0	0	0	0	0
7	2	Misc. Rev Internal	0	13.62637329	10	0.000614656	12.74725243	10	0.000575001
8	2.1	Misc. Rev Internal	0	0	0	0	0	0	0
9	2.3	Directs	0.001413	13.62637329	10	0.001990392	12.74725243	10	0.00186198
10	2.3.1	Direct Labour	0	13.62637329	10	0	12.74725243	10	0
	CBS position	Description	January 20	February 2024 Cost					
	1	Financial Results Analysis	0	0					
	2	Misc. Rev Internal	0	13.62637329					
	2.1	Misc. Rev Internal	0	0					
	2.3	Directs	0.001413						
	2.3.1	Direct Labour	0	13.62637329					

6. Select the **Import** icon again.



7. Select **Browse**, and then navigate to the Excel file you just saved, then select **Open**.

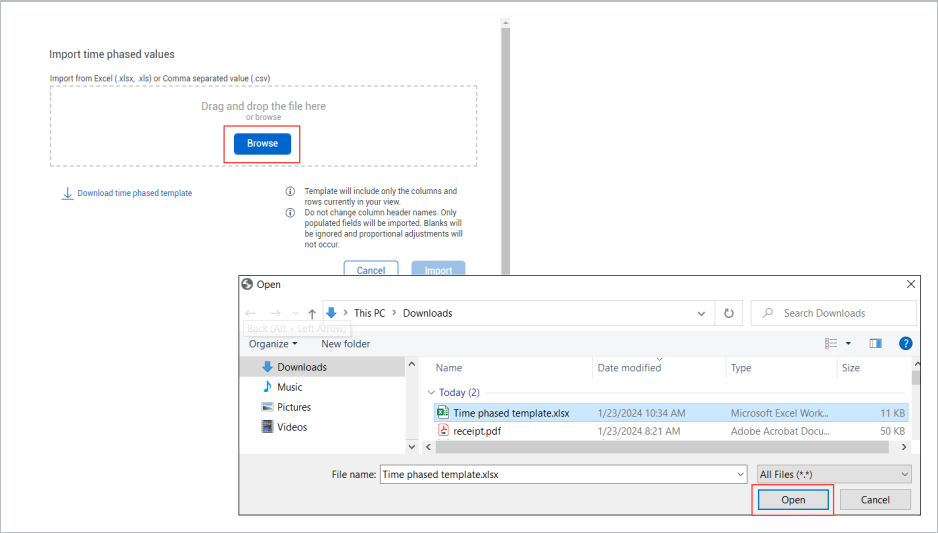

8. Select **Import**.

Import time phased values - Time phased template.xlsx

Import from Excel (.xlsx, .xls) or Comma separated value (.csv)

Drag and drop the file here
or browse

Browse

Download time phased template

ⓘ

Template will include only the columns and rows currently in your view.

ⓘ

Do not change column header names. Only populated fields will be imported. Blanks will be ignored and proportional adjustments will not occur.

Cancel

Import

7.7.9 Column Chooser

When you open the Time phase forecast, a column chooser has been added to the grid.

Column options

Available columns

Search...

Account code

Actual finish

Actual start

Allow as-built

As-built lock

CBS contribute quantity

CBS tag 1

CBS tag 10

CBS tag 11

CBS tag 12

Selected columns

Search...

CBS position

Description

WBS phase code

Start

Finish

Forecast method

Cost curve

Forecast remaining cost

Forecast remaining man hour

Qty remaining

Cancel


Save

After you choose which columns to show, the left side of the grid updates with your selection.

Page 328 of 639

InEight Inc. | Release 26.7

On the right of the grid, you can also adjust your view for each month's Cost, Man hours, and Quantity. This can be done using the drop down next to the month and deselecting the options you do not want to see on your grid.

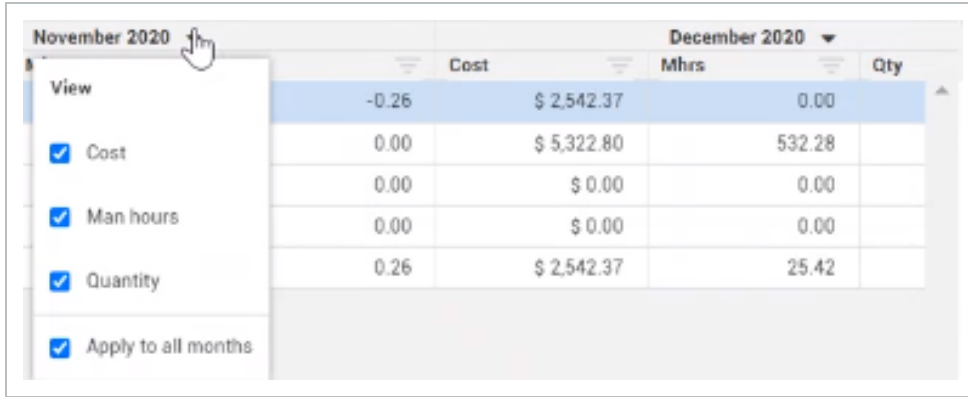

November 2020	Cost	December 2020	Mhrs	Qty
-0.26	\$ 2,542.37	0.00		
0.00	\$ 5,322.80	532.28		
0.00	\$ 0.00	0.00		
0.00	\$ 0.00	0.00		
0.26	\$ 2,542.37	25.42		

If you select cost from past dates, the data is read only.

7.7.10 Audit Log

All changes made within TPF are captured in the Audit log within Control Workspaces. The Audit log captures changes based on any changes made to a forecasted CBS item.

In the example, it shows that a forecasting value was changed on 08/13/19 for Audit ID 232. The forecasting value had been changed from 89.36 to 100.00 for the Aug '10 remaining cost time period.

CBS	Audit ID	Data type	Item type	Description	WBS	Attribute	Change by	Changed date	Value before	Value after
ACS	232	Time phased forecast	Cost item	Job Overhead	1002	Aug '19 remaining cost	Paul trippi	08/13/2019 0...	89.36	100.00
Pay items	225	Current Estimate	Estimate r...	C01.04-Concr...		Resource employed	Paul trippi	08/13/2019 1...		Resource e...
Integration	224	Current Estimate	Estimate r...	E.01.05-Earth...		Resource employed	Paul trippi	08/13/2019 1...		Resource e...
Import history	223	Current Estimate	Estimate r...	C01.04-Concr...		Resource employed	Paul trippi	08/13/2019 1...		Resource e...

7.8 PUSH TO LIVE FORECASTS

As mentioned above, the Live Forecast is the official forecast used for financial reporting and shared with all members of the project.

You can push forecasts entered in the Forecast data block to the Live Forecast either individually or by selection. This allows you to send only the items that you choose from your forecast to the Live Forecast.

The Live Forecast can only be updated if the user is assigned the appropriate role with the associated permissions. Project Admin or Power User can edit the Live Forecast directly.

Forecast changes made in the Forecast data block WILL NOT be pushed to the Live Forecast without an additional action detailed in the Step by Step below.

Changes made to your Forecast are only seen by you, unless you share them with someone else (see topic 9.4 Forecast Management) or update them to the Live Forecast.

Push Live Forecast by Selection in the CBS Tab

1. From the CBS tab with the Forecast data block in the view, select a group of cost items, by clicking the row header check boxes.
2. Click on the **drop-down arrow** in the center of the Forecast data block.
3. Select **Push to Live Forecast**.

The Push to Live Forecast option is disabled until you select one or more cost items.

4. After review, select **Yes** and your forecast values will push to the Live Forecast.

7.8.1 Time phased forecast push to live

The time phased forecast feature lets you make edits in your time phased forecast. You are then able to push those edits to your live forecast.

You can edit your total forecast remaining cost and forecast remaining hour values in the Time phased forecast window. It would then override your forecast remaining cost and your forecast remaining man hour if there is a change.

The Time phasing Forecasting option must be enabled first in order to have the Push Time phased forecast to Live option available to be enabled. Enabling only the Forecasting option does not automatically enable both.

Time phasing

Enable time phasing for the following:

Forecasting ⓘ

☒

Budget ⓘ

☒

Push Time phased forecast to Live forecast

☒

Forecast

% Complete value at which delta from straight line calculation utilizes average performance

The Time phasing section can be located in the Project Settings of Control under the Project tracking tab.

When you have enabled both options under the Time phasing section click save. Then go back to the CBS tab.

Follow these step by steps to use a time phased forecast push to live.

Time phased forecast push to live forecast

1. Select cost items from the CBS tab with a **Forecast remaining cost** to use in the push to live feature.

Make sure the cost items you selected have start and end dates. Otherwise you cannot edit them in the Time phased forecasting window.

2. From Control's CBS tab, select the Actions tab. Then select the **Time phased forecasting** option.
3. In the third data block where it has the Month and Year, scroll to the Remaining cost. Now move the scroll bar over to January of 2021.

CBS > Time phased forecasting										
☐ CBS position	Description	Forecast remain cost	Forecast remaining man hour	Qty remaining	Phased forecast remaining	Remaining c...	Mhrs	Remaining m...	Qty	Remaining qty
☐ 1.2	Fiber optic cable-1	\$ 5,000.00	0.00	10,000.00		\$ 5,000.00	0.00	0.00	0.00	10,000.00
☐ 1.4	CCTV devices	\$ 1,500.00	0.00	6.00		\$ 318.77	0.00	0.00	0.00	1.28

January 2021							February
Remaining qty	Cost	Mhrs	Qty	Cost	Mhrs		
10,000.00		0.00	0.00	\$ 0.00			
1.28	\$ 366.00	0.00	1.46	\$ 402.01			

4. If you believe the line item could take up more time and money, you can adjust the Cost and Man hours for the following month. These changes will then be added to the phased forecast remaining columns once you push to live.

CBS > Time phased forecasting										
☐ CBS position	Description	Forecast remain cost	Forecast remaining man hour	Qty remaining	Phased forecast remaining	Remaining c...	Mhrs	Remaining m...	Qty	Remaining qty
☐ 1.2	Fiber optic cable-1	\$ 5,000.00	0.00	10,000.00		\$ 5,000.00	0.00	0.00	0.00	10,000.00
☐ 1.4	CCTV devices	\$ 1,500.00	0.00	6.00		\$ 318.77	0.00	0.00	0.00	1.28

Quantity will show as changed with a delta next to the column. Currently, you cannot push quantity updates to live.

5. When you have made all the changes you need, select the cost items you want to push to live. You can either select one or all.

CBS > Time phased forecasting										
☐ CBS position	Description	Forecast remain cost	Forecast remaining man hour	Qty remaining	Phased forecast remaining	Remaining c...	Mhrs	Remaining m...	Qty	Remaining qty
☐ 1.2	Fiber optic cable-1	\$ 5,000.00	0.00	10,000.00		\$ 5,000.00	0.00	0.00	0.00	10,000.00
☒ 1.4	CCTV devices	\$ 1,500.00	0.00	6.00		\$ 318.77	0.00	0.00	0.00	1.28

6. Dialog appears asking if you want to push these values to the Live forecast. Select **Yes** to continue. The Cost and Man hours difference shows in the orange columns.

 Push these values to the Live forecast?
Please review the changes below, and then click 'Yes' if you wish to push these values to the live forecast.

CBS	Description	Current live forecast values		Time phased forecast values		Cost difference	Mhrs difference
		Live forecast remaining cost	Live forecast remaining manhours	Forecast remaining cost	Forecast remaining manhours		
1.2	Fiber optic cable-1	\$ 5,000.00	0.00	\$ 6,000.00	100.00	\$ 1,000.00	100.00
1.4	CCTV devices	\$ 1,500.00	0.00	\$ 1,200.00	0.00	(\$ 300.00)	0.00

7. When this is pushed to live, your Forecast remaining cost and Forecast remaining man hour should update in the Live forecast. Your Forecast Method will then change to **Manual ETC**. Manual ETC will have a green dot indicator that states it was pushed from Time phased forecast when you hover over the item.

Live forecast						Live forecast
						12/09/2020
★ Forecast remaining cost	★ Forecast remaining man hour	★ Forecast remaining man hour/Unit	★ Forecast remaining productivity	★ Forecast remaining unit cost	★ Forecast method	
\$ 36,975.68	500.00	500.00	0.80	\$ 36,975.68	Rollup	
\$ 25,000.00	300.00	0.03	1.00	\$ 2.50	Current estimate	
\$ 6,000.00	100.00	0.01	0.01	\$ 0.25	Current estimate	Updated by push from Time phased forecast
\$ 5,000.00	100.00	0.01	1.00	\$ 0.25	Current estimate	
\$ 975.68	0.00	0.00	0.00	\$ 162.61	Manual (ETC)	

The Forecast remaining cost and Forecast remaining man hour columns will have an orange wedge indicator that shows you which values have been updated manually changed when you hover over the indicator.

Tasks					Live forecast							Live forecast 12/9/2020	
☐ CBS position	Description	WBS phase code	Total committed cost		★ Forecast remaining cost	★ Forecast remaining man hour	★ Forecast remaining man hour/Unit	★ Forecast remaining productivity	★ Forecast remaining unit cost	★ Forecast method			
☐	1	Electrical devices	1000	500.00	\$ 5,000.00								
☐	1.1	Install conduit	1002	250.00	\$ 150.00								
☐	1.2	Fiber optic cable-1	1001.1	250.00	\$ 150.00	\$ 36,975.68	500.00	500.00	0.80	\$ 36,975.68	Rollup		
☐	1.3				\$ 25,000.00	300.00	0.03	1.00	\$ 2.50	Current estimate			
☐	1.4				\$ 6,000.00	100.00	0.01	0.00	\$ 0.60	Manual (ETC)			
Most recent change to this item:													
☐	1.5	CBS	Column	Previous value	New value	Previous Forecast final	Forecast final cost new	Previous Forecast final	New Forecast final MH	Changed by	Changed date		
☐	1.6	1.2 - Fiber optic cable-1	ForecastRemainingMa	100.000000000000	200.000000000000	\$ 6,000.00	\$ 7,000.00	100.00	200.00	Danielle Shovel	12/9/2020		
☐	2												

7.9 LIVE FORECAST SNAPSHOT


A Live Forecast Snapshot captures the forecast values for a project at a specific point in time. Snapshots can be used for reporting and historical comparison. Each month, a snapshot is created

either manually, by syncing the live forecast on a specific date, or automatically at the end of the plus-days period. The most recent sync for the month becomes the snapshot for that month.

Snapshots contain all live forecast values at the time of capture, along with actuals for the current month. If actuals are posted during plus days with a posting date within the current period, they are included in the snapshot. However, actuals posted with next-period dates do not show until plus days are complete.

7.9.1 Snapshot settings

You can configure snapshot settings in Project settings > Control > **Project tracking**.

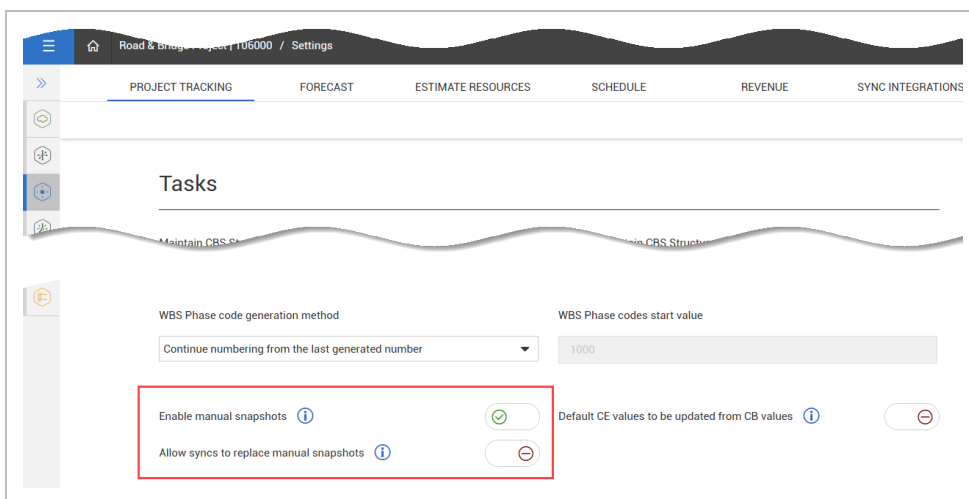


- **Enable manual snapshots** - When enabled, snapshots are captured only when a user with permission takes a monthly snapshot. When disabled, snapshots are captured automatically when *Push to Live Forecast* and *Push Forecast Revenue* syncs are run.
- **Allow Syncs to Replace Manual Snapshots** - When enabled, a manual snapshot is replaced if *Push to Live Forecast* or *Push Forecast Revenue* is synced. When disabled, syncs do not overwrite manual snapshots.

7.9.2 Manage snapshots

You can manage your snapshots from the drop-down menu in the Live forecast data block.

If manual snapshots are enabled, click **Take live snapshot** to capture a snapshot of the current Live forecast values.

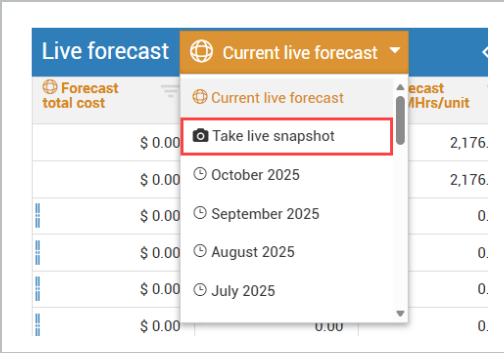

Select a previous snapshot to view read-only values from that month.

Live forecast 🕒 September 2025 ⚠️ < ● ● ● >			
🕒 Forecast total cost	🕒 Forecast total Mhrs	🕒 Forecast total Mhrs/unit	🕒 Forecast total productivity
\$ 250,000.00	0.00	0.00	0.00
\$ 406,300.00	8,310.00	0.83	0.96
\$ 1,499,250.00	29,805.00	2.98	1.01
\$ 1,150,300.00	23,100.00	23.10	0.91


You can also load snapshots in the Forecast delta data block.

Forecast delta ⚠️ 🕒 Sep.. ↔️ 🌐 Liv... < ● ● ● >			
Forecast total cost	Forecast total Mhrs	Forecast total Mhrs/unit	Forecast total productivity factor
\$ 0.00	0.00	0.00	0.00
\$ 0.00	0.00	0.00	0.00
\$ 0.00	0.00	0.00	0.00
\$ 93,700.00	1,874.00	1.87	-0.08
\$ 96,000.00	1,920.00	0.01	-0.11

Snapshots only capture Live forecast values. If you add a column to your view that does not relate to Live forecast values (such as *Committed remaining cost* and *Committed total cost*), those columns show as blank and disabled.

CHAPTER 8 – CHANGE MANAGEMENT


8.1 CHANGE MANAGEMENT WORKFLOW

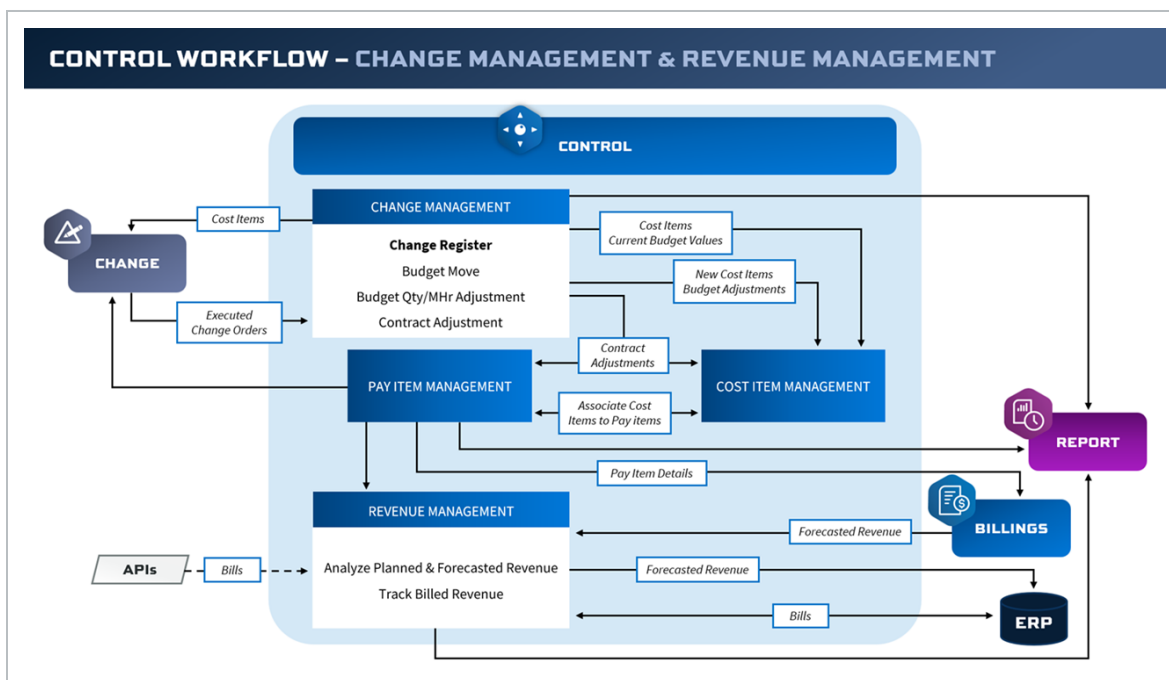

8.2 CHANGE MANAGEMENT OVERVIEW

During any phase of a project there are multiple ways you can manage changes to items such as quantities, design, schedule, and cost. In Control, you can manage changes to quantities, man-hours, and costs through a controlled approval process. You can make records of items such as budget moves, quantity and man-hour adjustments, and change orders by filling out forms.

You can access these change management forms from the Actions menu.

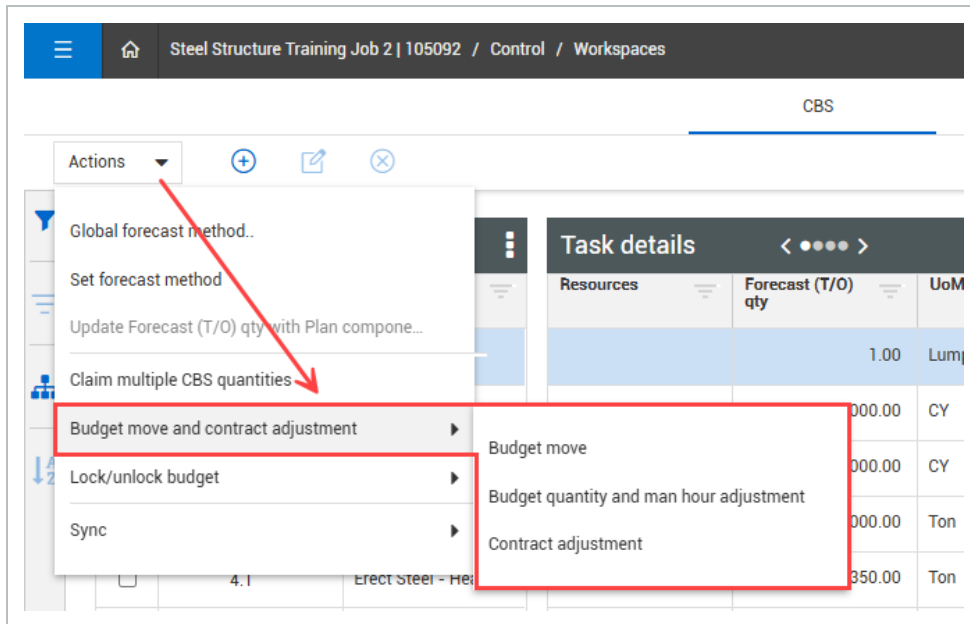

After you fill out and save the applicable changes, Control stores these changes in the Change Register tab, where the project budget is managed.

ACS PAY ITEMS CHANGE REGISTER AUDIT LOG												
ID	Description	CCO	Cre... date	Issue #	Last cha... by	Last changed on	Notes	Status	Total budget cost	Total budget MH	Total contract price	Type
22.0	Contingency Draw - Buildi...	CD-001	01/12/2023		AJ Waters	03/19/2023	1	✓ Approved	\$ 0.00	0.00	\$ 0.00	Budget rr
21.0	Fiber Office Connections	CO220831	08/31/2022	13	AJ Waters	08/31/2022	1	✓ CCO-Approved	\$ 55,000.00	0.00	\$ 57,200.00	Contract
20.0	New Cabinet Hardware	CCO-0015	09/21/2020	9	Jordan Ca...	10/22/2020		✓ CCO-Approved	\$ 3,500.00	0.00	\$ 3,500.00	Contract
19.0	Flooding and material was...	CCO-004	02/10/2020	6	Austin Wil...	03/10/2023		✓ CCO-Approved	\$ 0.00	0.00	\$ 10,000.00	Contract
18.0	Extra Surveying	0019A	02/10/2020	19-1	Chris Hohl...	04/21/2021		🔄 Draft	\$ 15,000.00	0.00	\$ 19,500.00	Contract
17.0	Increase in Scope	002	01/18/2020	002	Mike Paul	02/05/2020		✓ Approved	\$ 22,000.00	0.00	\$ 50,000.00	Contract
16.0	Change in Scope	C01	01/18/2020	001	Paul Benni...	04/24/2020		✓ Approved	\$ 0.00	0.00	\$ 0.00	Budget Q
15.0			11/13/2019		John Upton	04/12/2022		✓ Approved	\$ 0.00	0.00	\$ 0.00	Budget rr
14.0	traslado de dinero dentro ...		10/21/2019	011	Elia Burgu...	03/19/2023		🔄 Pending	\$ 0.00	50.00	\$ 0.00	Budget rr
13.0	Traslado de dinero dentro ...		09/16/2019	013	Elia Burgu...	03/19/2023		🔄 Pending	\$ 0.00	0.00	\$ 0.00	Budget rr
12.0		CCO0002	09/15/2019	003	Mike Paul	03/19/2023		🔄 Pending	\$ 0.00	0.00	\$ 0.00	Budget rr
11.1	Flood control on haul road	CCO-0002	03/22/2021	4	Chris Hohl...	03/22/2021		🔄 CCO-Draft	\$ 9,000.00	0.00	\$ 0.00	Contract
Subtotals									\$ 12,115,309...	64,222.00	\$ 290,200.00	

In the Change Register you can review each change individually and approve changes as needed. When a change is approved, it updates the current budget values in the CBS and is given a status of *Approved* in the Change Register. Otherwise, the change is only documented in the Change Register with a status of *Draft* or *Pending* and has no effect on the current budget.

To manage changes, you must have applicable permissions.

The table below provides a brief description of the three types of changes you can record in Control.

Change type	Description
Budget move	Reallocate costs from one area of the budget to another. When making a budget move, the result must be net zero, neither adding nor removing costs from the budget. The move can include reallocation of man-hours and quantities as well.
Budget quantity and man hour adjustment	Make modifications to budgeted man-hours and/or quantities without making changes to overall budgeted costs.
Contract adjustment	Make a change to the scope of your budget and contract, via the addition or revision of cost items and pay items, which results in a change to the project's budgeted costs and pricing. Also commonly referred to as a change order.

When you perform a budget move, contract adjustment, or budget quantity and man-hour adjustment, you can select a maximum total of 250 cost items or 100 pay items. When you exceed the maximum, the Budget move and contract adjustment option in the Actions menu drop-down becomes unavailable. This improves the speed, reliability, and performance of the change order.

8.2.1 Managing changes using the InEight Suite

For a more holistic approach to managing changes within your organization, your company might choose to follow a change management process that integrates with other InEight applications that can include:

- InEight Change
- InEight Document
- InEight Schedule
- InEight Progress

For more information on how to use the InEight suite of applications to manage change orders, see [Change Order Management](#).

8.2.2 InEight Change integration with Control

The InEight Change application is designed to manage project changes through a detailed, organized process, tracking changes from issue to executed change order. When executed in InEight Change, change orders can automatically become contract adjustments within InEight Control via an integration between the two applications. If your company is using both Change and Control for managing change orders, consult the [Contract adjustment from InEight Change overview](#) topic for more information on this process.

Budget moves can also be initiated in InEight Change and integrate with InEight Control to show up in the Control Change Register. For more information about managing budget moves using Change and Control, see [Budget Moves](#) in InEight Change.

8.3 ASSOCIATED BUDGET MOVE

During a project, you might need to move costs from one area of the budget to another to account for project changes, without changing the total budget amount. In Control, you can manage budget moves via a controlled approval process.

To launch a budget move in Control, from the CBS tab of the Workspaces module, select Actions > Budget move & contract adjustment > **Budget move**. This opens a Budget move record with the option to fill out the record following one of two workflows.

The following table provides information about each budget move workflow.

Budget move workflow	Description	Pros	Cons
Associated	Links each	• Clear audit trail –	• More steps required –


Budget move workflow	Description	Pros	Cons
	source cost item to a target cost item as a single transfer transaction.	Shows both the source and destination of the funds in a single transaction, improving transparency. • Traceability – Easily see where the budget came from and where it went. • Reporting clarity – Helps financial and project controls teams track budget changes as purposeful reallocations rather than isolated changes.	Typically involves selecting both a “from” and “to” item, with extra steps for assigning amounts and adjusting cost categories, which can be more time-consuming than a non-associated move. • Requires clear planning – You must know both ends of the move when performing it, which might not always be the case.
Non-associated	Treats each adjustment (debit or credit) as a standalone action, without explicitly linking the source and destination.	Flexibility – Can make quick, one-sided adjustments without needing to define where the funds are coming from or going to. Faster entry – Useful when you're adjusting budgets over time and the counterbalance to the move is handled later or separately. Auto-calculate – Only non-associated budget moves contain the feature to automatically generate	Lack of traceability – Harder to tell where money came from or where it went, which complicates reviews and audits. Potential for confusion – Can lead to misunderstanding or misreporting of why certain budget changes occurred. Reduced accountability – Without links, it's easier to lose the rationale for the budget changes, especially over a long project timeline.

Budget move workflow	Description	Pros	Cons
		CB budget adjustments from CE values and CE values from CB budget adjustments.	

- The following are considerations when performing a budget move using the Associated workflow option:
- Current Budget cost and man-hours are only maintained at the terminal level. You cannot move cost to or from a parent cost item.
 - You can move costs between multiple cost items at the same time.
 - You can automatically update Current Estimate (CE) values from Current Budget (CB) values only in a non-associated budget move or a contract adjustment.

Perform an associated budget move

1. Select Actions > Budget move & contract adjustment > **Budget move**.

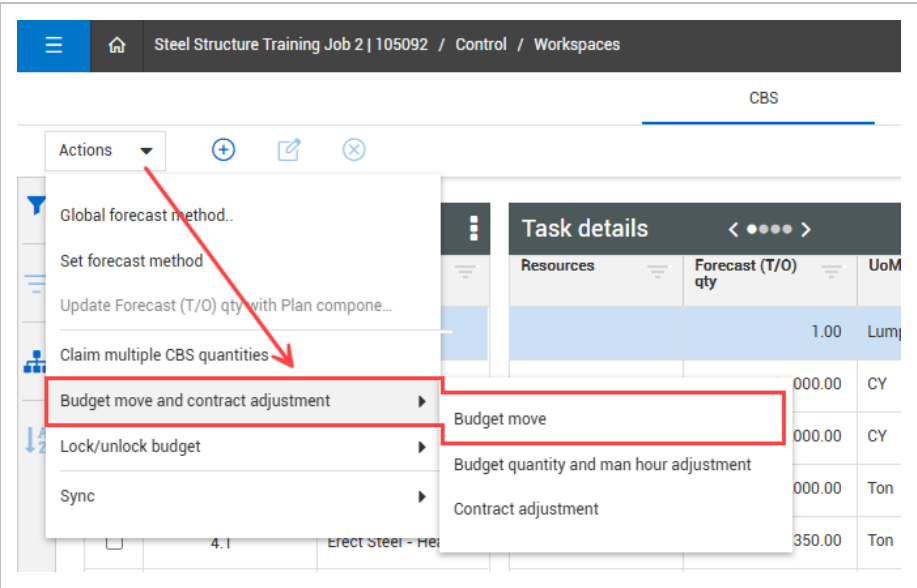

- The Budget Move wizard opens to the step 1, **Details**.
2. Select the **Associated** option and add budget move details as needed, and then click **Next**.

1

Details

2

Select from & to items

3

Define relationships

4

Assign amounts

5

Adjust cost categories

6

Summary

Choose your Budget move workflow

☒

Associated

Define budget moves with a From and To process to provide ultimate traceability of budget moves.

☐

Non-Associated

Define budget moves freely to provide the most flexibility.

Budget move details

Description

453

Move budget from light steel erection to heavy.

CCO

60

CCO

Issue #

57

056

Discipline

484

Structural Steel

The Budget move wizard opens step 2, **Select from & to items**.

3.
- From the **From** section on the left, select the cost items you need to move budget from and from the To (for net zero moves) section on the right, select the cost items you need to move budget to.

Change register > Budget Move

1 Details

2 Select from & to items

3 Define relationships

4 Assign amounts

5 Adjust cost categories

6 Summary

From :

☐	CBS position	Description	WBS phase code
☐	3.1.8	Building N&O - Scrape...	1099
☐	▼ 4	Structural Steel	1073
☐	4.1	Erect Steel - Heavy	1074
☒	4.2	Erect Steel - Light	1005
☐	4.3	Bolted Connections	1006
☐	4.4	Labor	1088
☐	4.5	Equipment	1089
☐	4.6	3rd Party	1090
☐	▼ 5	Materials	1084
☐	5.1	Earthwork - Materials	1085
☐	5.2	Concrete - Materials	1086
☐	5.3	Structure Steel - Mate...	1087

1 items selected

To (for net zero moves):

☐	CBS position	Description	WBS phase code
☐	3.1.8	Building N&O - Scrape...	1099
☐	▼ 4	Structural Steel	1073
☒	4.1	Erect Steel - Heavy	1074
☐	4.2	Erect Steel - Light	1005
☒	4.3	Bolted Connections	1006
☐	4.4	Labor	1088
☐	4.5	Equipment	1089
☐	4.6	3rd Party	1090
☐	▼ 5	Materials	1084
☐	5.1	Earthwork - Materials	1085
☐	5.2	Concrete - Materials	1086
☐	5.3	Structure Steel - Mate...	1087

2 items selected

Cancel

Draft

Back

Next

4. Click **Next**. The Budget move wizard opens to step 3, **Define relationships**.
5. For each cost item listed under the From section, select Define to do one of the following:
 - Select **Cost category, Qty or MHR adjustment only** to modify only the cost category, quantity or man-hours of the cost item (not the cost item's cost).
 - Select the cost item or items to move budget to that includes costs. You can click **Select All**

to select all the listed cost items.

The screenshot shows the 'Define relationships' step of the Budget Move wizard. The 'From' section contains a table with the following data:

	CB total cost	Pending budget cost	CB total MHrs	CB total quantity
4.2 [1005] Erect Steel - Light	\$ 200,000.00	\$ 0.00	4,000	

The 'To' section shows two items: 4.1 [1074] Erect Steel - Heavy and 4.3 [1006] Bolted Connections. A 'Define' dialog box is open, showing the following options:

- ☐ Cost category, Qty or Mhr adjustment only
- ☒ Budget move with Cost category, Qty or Mhr adjustment to:
- ☒ 4.1 [1074] Erect Steel - Heavy
- ☒ 4.3 [1006] Bolted Connections
- [Select All](#)
- [OK](#)

At the bottom of the wizard, there are buttons for 'Cancel', 'Draft', 'Back', and 'Next'.

6. Click **OK** to close the Define window. Now, for each cost item under the To section, it shows the cost items you associate to it from the From section.
7. Click **Next**. The Budget move wizard opens to step 4, **Assign amounts**.
8. In Assign amounts, you can move costs, quantities, and man-hours.
 - You can move costs and man-hours by entering values in the CB total cost and CB total MHrs fields under the To section. This automatically deducts the amounts from the assigned cost items under the From section.

1 Details2 Select from & to items3 Define relationships4 Assign amounts5 Adjust cost categories6 Summary

From:

To:

4.2 [1005] Erect Steel - Light

	CB total cost	Pending budget cost	CB total MHrs	CB total quantity
1	\$ 200,000.00	\$ 0.00	4,000.00	200.00
	\$ 11,000.00		-200.00	0.00
=	\$ 189,000.00		3,800.00	200.00

4.1 [1074] Erect Steel - Heavy

	CB total cost	CB total MHrs	CB total quantity
1	\$ 800,000.00	16,000.00	800.00
	10000.00	200.00	0
=	\$ 810,000.00	16,200.00	800.00

4.3 [1006] Bolted Connections

	CB total cost	CB total MHrs	CB total quantity
1	\$ 50,000.00	1,000.00	2,000.00
	1000.00	0	0

Advanced options

CancelDraftBackNext

- You can enter CB Total Quantity values on the To section. They do not automatically deduct from the From section because you could be moving between cost items with differing units of measure.
- You may need to add more or fewer man-hours than you deduct. To allow this, select **Advanced options** and switch the **Adjust MHrs (not net zero)** to *On*. The CB total MHrs of your From cost items will no longer automatically deduct when you make adjustments to your To cost items.

9. Click **Next**. The Budget move wizard opens to step 5, **Adjust cost categories**.

10. In Adjust cost categories, you can assign your pending budget changes to existing and new cost categories of your cost item. For each cost item under the To section, click the **Add cost category** button to reassign costs to different cost categories.

1 Details2 Select from & to items3 Define relationships4 Assign amounts5 Adjust cost categories6 Summary

From:

To:

4.2 [1005] Erect Steel - Light

	CB total cost	Available:	
		Pending	New total
1	Labor: \$ 200,000.00	\$ 11,000.00	\$ 189,000.00
=	Totals \$ 200,000.00	\$ 11,000.00	\$ 189,000.00

4.1 [1074] Erect Steel - Heavy

	CB total cost	Available:	
		Pending	New total
Labor:	\$ 800,000.00	\$ 8,000.00	\$ 808,000.00
Materials:	\$ 0.00	\$ 2,000.00	\$ 2,000.00
=	Totals \$ 800,000.00	\$ 10,000.00	\$ 810,000.00

Add cost category

4.3 [1006] Bolted Connections

	CB total cost	Available:	
		Pending	New total
Labor:	\$ 50,000.00	\$ 1,000.00	\$ 51,000.00
=	Totals \$ 50,000.00	\$ 1,000.00	\$ 51,000.00

Add cost category

11. On the **Add cost categories** window, select a cost category, then click **OK**.

Add cost categories

Total :2 Selected

☒ Labor

☐ Construction Equipment

☐ FOM Rented Equipment

☐ Supplies

☒ Materials

☐ Subcontract

☐ Fees

☐ Allowance

☐ G & A

☐ Undefined

Cancel

OK

12. In the **Pending** fields, adjust the cost category amounts as needed.

To:

4.1 [1074] Erect Steel - Heavy		Available:	\$ 0.00
	CB total cost	Pending	New total
Labor:	\$ 800,000.00	8,000.00	\$ 808,000.00
Materials:	\$ 0.00	2,000.00	\$ 2,000.00
=	Totals	\$ 800,000.00	\$ 10,000.00
+ Add cost category			

After making your adjustments, the Available amount should equal \$0.00.

13. Click **Next**. The Budget move wizard opens to step 4, **Summary**.

14. In Summary, review your proposed changes, and then click **Submit** to send the budget move for approval.

Change Register > Budget Move

1 Details

2 Select From & To Items

3 Define Relationships

4 Assign Amounts

5 Adjust Cost Categories

6 Summary

From: → To:

4.2 Erect Steel - Light

	CB total cost	CB total MHrs	CB total quantity
Before:	\$ 200,000.00	4,000.00	200.00
Pending:	(\$ 10,000.00)	-100.00	-20.00
	\$ 190,000.00	3,900.00	180.00

4.4 Modluel 01 - Erect Steel Heavy

	CB total cost	CB total MHrs	CB total quantity
Before:	\$ 0.00	0.00	0.00
Pending:	\$ 10,000.00	100.00	20.00
	\$ 10,000.00	100.00	20.00

Cancel

Draft

Back

Submit


Select **Draft** if the budget move is not ready to be submitted and needs to be saved for later.

8.3.1 Associated Budget Move - Single Cost Item

At times, you might encounter changes that require you to make budget changes within the cost categories of a single cost item. For example, you may find that some items that you estimated to be self-performed work may be faster and cheaper if they were subcontracted out. Therefore, you can perform a budget move for a single cost item to redistribute the budgeted cost between different cost categories.

Perform an associated budget move within a single cost item

- 1. Select Actions > Budget move & contract adjustment > **Budget move**.

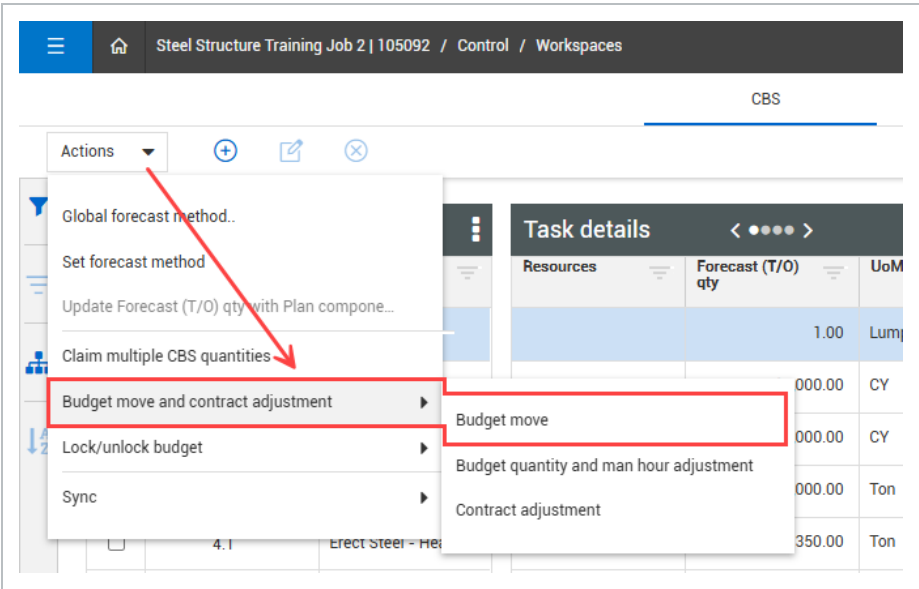

The Budget Move wizard opens to the step 1, **Details**.

- 2. In Details, select the **Associated** option and add budget move details as needed, and then click **Next**.

1 Details2 Select from & to items3 Define relationships4 Assign amounts5 Adjust cost categories6 Summary

Choose your Budget move workflow

☒ Associated
Define budget moves with a From and To process to provide ultimate traceability of budget moves.

☐ Non-Associated
Define budget moves freely to provide the most flexibility.

Budget move details

Description453

Move budget from light steel erection to heavy.

CCO60

CCO

Issue #57

056

Discipline484

Structural Steel

The Budget move wizard opens step 2, **Select from & to items**.

3. In Select from & to items, select the same cost item under both the From and To sections, and then click **Next**.

Change Register > Budget Move

1 Details2 Select From & To Items3 Define Relationships4 Assign Amounts5 Adjust Cost Categories6 Summary

From :

	CBS position	Description	WBS phase code
☐	1	Job Overhead	1002
☐	2	Earthwork	1069
☐	3	Concrete	1071
☐	4	Structural Steel	1073
☐	4.1	Erect Steel - Heavy	1074
☐	4.2	Erect Steel - Light	1005
☒	4.3	Bolted Connections	1006
☐	4.4	Moduel 01 - Erect Steel Heavy	1087
☐	5	Materials	1084
☐	5.1	Earthwork - Materials	1085

1 items selected

To (for net zero moves):

	CBS position	Description	WBS phase code
☐	1	Job Overhead	1002
☐	2	Earthwork	1069
☐	3	Concrete	1071
☐	4	Structural Steel	1073
☐	4.1	Erect Steel - Heavy	1074
☐	4.2	Erect Steel - Light	1005
☒	4.3	Bolted Connections	1006
☐	4.4	Moduel 01 - Erect Steel Heavy	1087
☐	5	Materials	1084
☐	5.1	Earthwork - Materials	1085

1 items selected

Cancel

Draft

Back

Next

The Budget Move wizard opens to the step 3, **Define relationships**.

- 4. In Define relationships, click the **Define** button, and then select **Cost category, Qty, or MHR adjustment only**.

Change Register > Budget Move

1 Details2 Select From & To Items3 Define relationships4 Assign Amounts5 Adjust Cost Categories6 Summary

From:

4.3 Bolted Connections

CB total cost

Pending change

\$ 50,000.00

\$ 0.00

Define

☒ Cost category, Qty or MHR adjustment only

OK

To:

4.3 Bolted Connections

4.3 Adjust only

Selecting the Cost category, Qty, or MHR adjustment only option lets you move budgeted cost category values within a single cost item.

- 5. Click **OK** to close the Define window, and then **Next**. The Budget move wizard opens to step 4, **Assign amounts**.
- 6. In Assign amounts, click **Next** to skip the Assign amounts step because we are not changing the man-hours or quantities. The Budget move wizard opens to step 5, **Adjust cost categories**.
- 7. Click the **Add cost category** button to assign your pending budget changes to existing and new cost categories of your cost item.

Change Register > Budget Move

1 Details2 Select From & To Items3 Define Relationships4 Assign Amounts5 Adjust Cost Categories6 Summary

From:

To:

4.3 Bolted Connections

	CB total cost	Pending	New total
Labor	\$ 50,000.00	0.00	\$ 50,000.00
Totals	\$ 50,000.00	\$ 0.00	\$ 50,000.00

Available:

\$ 0.00

+

 Add cost category

Cancel

Draft

Back

Next

8. On the Add cost categories window, select the cost categories to include in the adjustment, and then click **OK**.

9. Make adjustments in the cost category Pending fields as needed.

- The values shown in the Available and New total fields will automatically adjust based on the values entered in the To Pending fields
- The amount in the Available field must be \$0.00 to proceed to the next step.

4.3 Bolted Connections		Available:	\$ 0.00
	CB total cost	Pending	New total
Labor:	\$ 50,000.00	-50,000.00	\$ 0.00
Subcontract:	\$ 0.00	50,000.00	\$ 50,000.00
= Totals	\$ 50,000.00	\$ 0.00	\$ 50,000.00


10. Click **Next**. The Budget move wizard opens to step 4, **Summary**.
11. In Summary, review your proposed changes, then click **Submit** to send the budget move for approval.

The budget move will now be listed in the project's Change Register with a status of *Pending*.

8.4 NON-ASSOCIATED BUDGET MOVE

During a project, you might need to move costs from one area of the budget to another to account for project changes, without changing the total budget amount. In Control, you can manage budget moves via a controlled approval process.

To launch a budget move in Control, from the CBS tab of the Workspaces module, select Actions > Budget move & contract adjustment > **Budget move**. This opens a Budget move record with the option to fill out the record following one of two workflows.

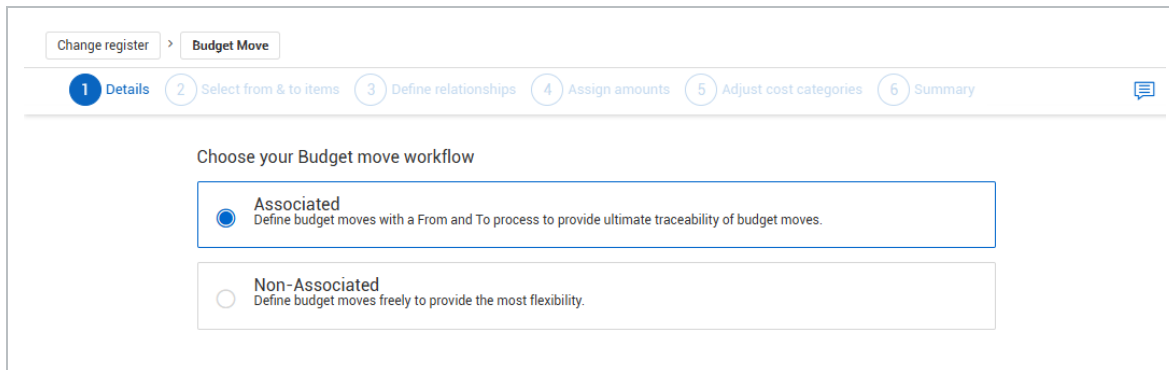

Change register > Budget Move

1 Details 2 Select from & to items 3 Define relationships 4 Assign amounts 5 Adjust cost categories 6 Summary

Choose your Budget move workflow

☒ **Associated**
Define budget moves with a From and To process to provide ultimate traceability of budget moves.

☐ **Non-Associated**
Define budget moves freely to provide the most flexibility.

The following table provides information about each budget move workflow.

Budget move workflow	Description	Pros	Cons
Associated	Links each source cost item to a target cost item as a single transfer transaction.	• Clear audit trail – Shows both the source and destination of the funds in a single transaction, improving transparency. • Traceability – Easily see where the budget came from and where it went. • Reporting clarity – Helps financial and project controls teams track budget changes as purposeful reallocations rather than isolated changes.	• More steps required – Typically involves selecting both a “from” and “to” item, with extra steps for assigning amounts and adjusting cost categories, which can be more time-consuming than a non-associated move. • Requires clear planning – You must know both ends of the move when performing it, which might not always be the case.

Budget move workflow	Description	Pros	Cons
Non-associated	Treats each adjustment (debit or credit) as a standalone action, without explicitly linking the source and destination.	Flexibility – Can make quick, one-sided adjustments without needing to define where the funds are coming from or going to. Faster entry – Useful when you're adjusting budgets over time and the counterbalance to the move is handled later or separately. Auto-calculate – Only non-associated budget moves contain the feature to automatically generate CB budget adjustments from CE values and CE values from CB budget adjustments.	Lack of traceability – Harder to tell where money came from or where it went, which complicates reviews and audits. Potential for confusion – Can lead to misunderstanding or misreporting of why certain budget changes occurred. Reduced accountability – Without links, it's easier to lose the rationale for the budget changes, especially over a long project timeline.

Performing a non-associated move makes cost adjustments at the total cost and cost category levels. In addition to cost adjustments, adjustments to man-hours and quantities can also be made.


With the applicable permissions, you can approve budget moves. When you approve a budget move, a message shows confirming the budget move is approved.



Change order # 1.0 approved. successfully.

Perform a non-associated budget move

- 1. Select Actions > Budget move & contract adjustment > **Budget move**.

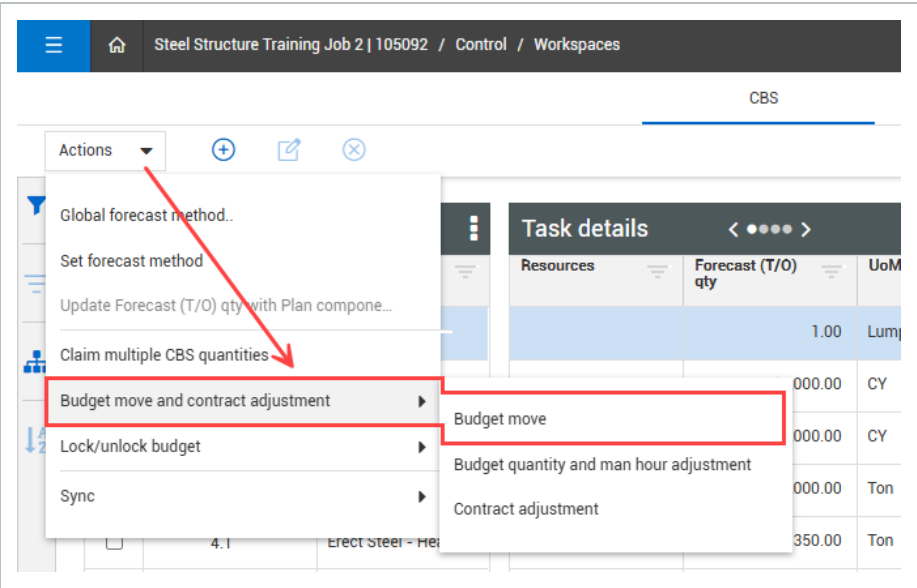

The Budget Move wizard opens to step 1, **Details**.

- 2. In Details, select the Non-Associated option and add budget move details as needed, and then click **Next**.

1 Details2 Select from & to items3 Define relationships4 Assign amounts5 Adjust cost categories6 Summary

Choose your Budget move workflow

☐ Associated
Define budget moves with a From and To process to provide ultimate traceability of budget moves.

☒ Non-Associated
Define budget moves freely to provide the most flexibility.

Budget move details

Description453

Move budget from light steel erection to heavy.

CCO60

CCO

Issue #57

056

Discipline484

Structural Steel

The Budget move wizard opens step 2, Select **Assign amounts**.

3. In Assign amounts, click the **Add cost item** icon to select the applicable cost items.

Change register > Budget Move

1 Details2 Assign amounts

CBS positionDescriptionWBS phase codeCB total costAdjusted CB costCB total MhrsAdjusted CB MhrsCB total quantityAdjusted CB qty

No cost items selected
Click the add icon above to add cost items

No results found

Subtotals 0

\$ 0.00\$ 0.000.000.00

Approve

CancelDraftBackSubmit

4. Select the cost items, and then click **Add**.

Page 356 of 639

InEight Inc. | Release 26.7

Change register > Budget Move > Select cost items

CBS position

Description

WBS phase code

1

Job Overhead

1002

2

Earthwork

1069

3

Concrete

1071

4

Structural Steel

1073

4.1

Erect Steel - Heavy

1074

4.2

Erect Steel - Light

1005

4.3

Bolted Connections

1006

5

Materials

1084

5.1

Earthwork - Materials

1085

Subtotals 32 (3 items selected)

Cancel

Add

5. Enter adjustment amounts for each cost item. You can enter positive or negative adjustments into any of the fields labeled *Adjusted*, including *Adjusted CB cost*, *Adjusted CB MHrs*, and *Adjusted CB qty*. See the following adjustment examples:

- Moving from one cost item to another:

Change register > Budget Move

1 Details

2 Assign amounts

CBS position	Description	WBS phase code	CB total cost	Adjusted CB cost	CB total MHrs	Adjusted CB MHrs	CB total quantity	Adjusted CB qty
4.1	Erect Steel - Heavy	1074	\$ 800,000.00	(\$ 5,000.00)	16,000.00	-200.00	800.00	0.00
4.2	Erect Steel - Light	1005	\$ 200,000.00	\$ 5,000.00	4,000.00	200.00	200.00	0.00
4.3	Bolted Connections	1006	\$ 50,000.00	\$ 0.00	1,000.00	0.00	2,000.00	0.00
Subtotals 3			\$ 1,050,000.00	\$ 0.00	21,000.00	0.00		

Approve

Cancel

Draft

Back

Submit

- Moving one cost item to multiple cost items:

InEight Inc. | Release 26.7

Page 357 of 639

Change register > Budget Move

1 Details 2 Assign amounts

CBS position	Description	WBS phase code	CB total cost	Adjusted CB cost	CB total MHrs	Adjusted CB MHrs	CB total quantity	Adjusted CB qty
4.1	Erect Steel - Heavy	1074	\$ 800,000.00	(\$ 5,000.00)	16,000.00	-200.00	800.00	0.00
4.2	Erect Steel - Light	1005	\$ 200,000.00	\$ 4,000.00	4,000.00	200.00	200.00	0.00
4.3	Bolted Connections	1006	\$ 50,000.00	\$ 1,000.00	1,000.00	0.00	2,000.00	0.00
Subtotals 3			\$ 1,050,000.00	\$ 0.00	21,000.00	0.00		

Approve Cancel Draft Back Submit

- Make cost adjustments at the CB cost category level using any of the Adjusted CB cost category columns:

1 Details 2 Assign amounts

Description	WBS phase code	CB labor total cost	Adjusted CB labor cost	CB construction equipment to...	Adjusted CB construction equipment c...	CB FOM rented equipment total cost	Adjusted CB FOM rented equipment c...
Erect Steel - Heavy	1074	\$ 800,000.00	(\$ 4,000.00)	\$ 0.00	(\$ 1,000.00)	\$ 0.00	(\$ 500.00)
Erect Steel - Light	1005	\$ 200,000.00	\$ 3,000.00	\$ 0.00	\$ 1,000.00	\$ 0.00	\$ 500.00
Bolted Connections	1006	\$ 50,000.00	\$ 1,000.00	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00

- The Adjusted CB total cost must equal zero to submit.
 - The Adjusted CB cost will automatically calculate as the total of all cost category values.
 - Costs entered directly in the Adjusted CB cost field are automatically allocated to the appropriate CB cost categories (for example, Adjusted CB labor cost, Adjusted CB material cost) based on where costs were originally allocated on the cost item.
- Assign amounts at the cost category level by right-clicking on the cost item, and then selecting **Cost category**.

Change register > Budget Move

+

×

+

−

↔

☐	CBS position	Description	WBS phase code
☐	4.1	Erect Steel - Heavy	1074
☒	4.2	Erect Steel - Light	1005
☐	4.3	Bolted Connectio	

Cost category

This gives you a view that makes it easy to see the pending adjustments of all your categories in a slide-out register and how they contribute to the total.

After making adjustments, click the **Close** icon at the top right corner to close the Cost category slide-out.

1 Details

2 Assign amounts

\$

⌵

📄

✕

1005

4.2 Erect Steel - Light

CB total cost

Pending budget cost

CB total MHrs

CB total quantity

\$ 200,000.00

(\$ 10,000.00)

4,000.00

200.00

Cost category	CB total cost	Pending
^ Total	\$ 200,000.00	(\$ 1,000.00)
Labor	\$ 200,000.00	\$ 0.00
Construction Equipment	\$ 0.00	\$ 0.00
FOM Rented Equipment	\$ 0.00	\$ 0.00
Supplies	\$ 0.00	\$ 0.00
Materials	\$ 0.00	(\$ 1,000.00)
Subcontract	\$ 0.00	\$ 0.00
Fees	\$ 0.00	\$ 0.00
Allowance	\$ 0.00	\$ 0.00
G & A	\$ 0.00	\$ 0.00
Undefined	\$ 0.00	\$ 0.00

The Adjusted CB cost subtotal must equal zero to submit. In other words, the cost adjustments must be net-zero to proceed.

6. Review your proposed changes, and then click **Submit** to send the budget move for approval. Click **Draft** if the budget move is not ready to be submitted and needs to be saved for later.

The hours and quantities subtotals do not need to equal zero to submit.

8.4.1 Auto-Calculate budget move values

Non-Associated budget moves include a time-saving feature that auto-calculates values when performing the following tasks:

- **Update CB from CE** – Automatically generates CB adjustments in the non-associated budget move record to match existing current estimate values of the cost items selected.
- **Update CE from CB** - When approved, automatically updates current estimate values in the CBS based on adjustment values defined on the non-associated budget move.

8.4.1.1 Update current budget (CB) adjustments from current estimate (CE)

Prior to generating a budget move record for approval, a common best practice to help you work through project changes and have traceability should questions arise, is to make your budget move adjustments directly in the CE fields of your cost items on the CBS tab.


When the time comes to get approval, you can create a non-associated budget move and use the Auto-calculate feature to generate the CB adjustments on your budget move record automatically.

Perform a budget move using Auto-calculate > Update CB from CE

These steps assume budget move adjustments have already been made in the Current Estimate.

1. Select Actions > Budget move & contract adjustment > **Budget move**. The Budget Move wizard opens to step 1, **Details**.
2. In Details, select the **Non-Associated** option and add budget move details as needed, and then click **Next**. The Budget Move wizard opens to step 2, **Assign amounts**.

3. In Assign amounts, click the **Add** button to select the cost items that are part of the budget move.
4. Click the **Auto-calculate** icon, and then select **Update CB from CE**.
5. . Select the values to auto-calculate, and then click **Apply**.

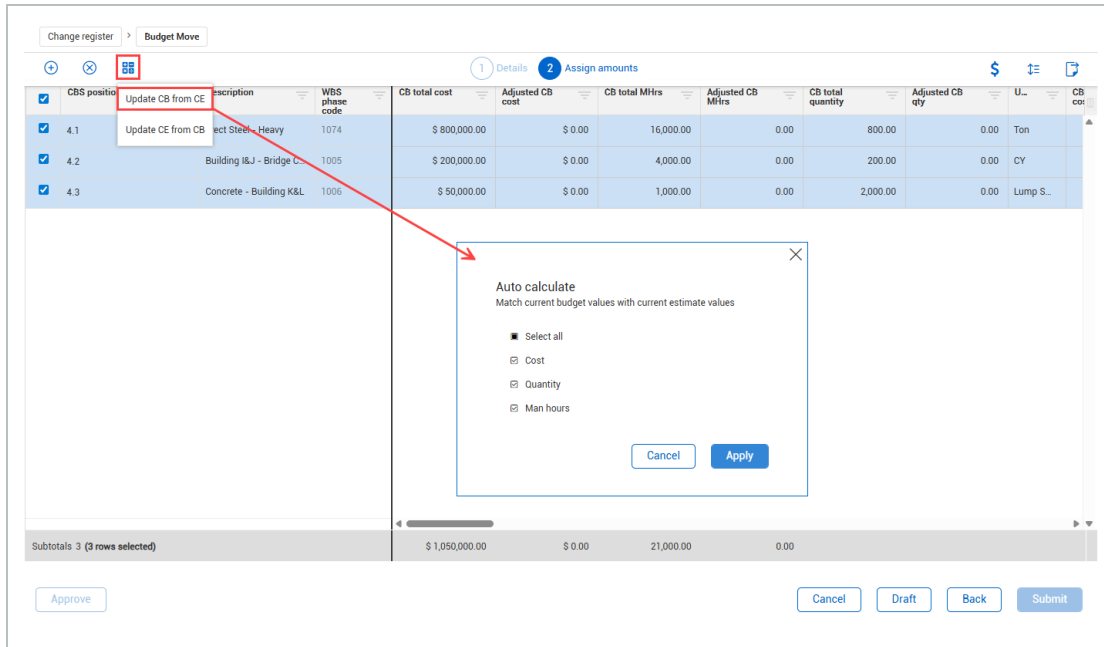

6. Click **Yes** when prompted to confirm.
7. Click **Submit** to submit the budget move for approval. Click **Draft** if the budget move is not ready to be submitted and needs to be saved for later.

8.4.1.2 Update Current Estimate from Adjusted Current Budget

You can update your current estimate values based on the adjusted current budget values for contract non-associated budget moves.

To view adjusted current budget values in relation to current estimate values, add the following columns to your view:

- Cost source
- Update CE total cost
- Update CE total MHrs
- Update forecast (T/O) qty
- CE total cost

- CE total MHrs
- Forecast T/O qty
- New CE total cost
- New CE total MHrs
- New forecast (T/O) qty

To add these columns, initiate a non-associated budget move, go to the **Assign Amounts** step, click the **Column chooser** icon, and then select your columns.

The screenshot shows the 'Assign amounts' step in a software interface. The interface includes a table with the following columns: CB total cost, Adjusted CB cost, CB total MHrs, Adjusted CB MHrs, CB total quantity, Adjusted CB qty, U..., and CB cost. A red box highlights the 'Column chooser' icon in the top right corner. A dropdown menu is open, showing a list of columns with checkboxes. The first three items are checked: CE total cost, CE total MHrs, and Forecast T/O qty. The last five items are also checked: Cost source, Update CE total cost, Update CE total MHrs, Update forecast (T/O) qty, and New CE total cost. The other items are unchecked.

Column	Selected
CE total cost	Yes
CE total MHrs	Yes
Forecast T/O qty	Yes
CE labor total cost	No
CE construction equipment total cost	No
CE rented equipment total cost	No
CE supplies total cost	No
CE materials total cost	No
CE subcontract total cost	No
CE fees total cost	No
CE contingency total cost	No
CE general and admin total cost	No
CE undefined total cost	No
New CB total cost	No
New CB total MHrs	No
New CB total qty	No
Cost source	Yes
Update CE total cost	Yes
Update CE total MHrs	Yes
Update forecast (T/O) qty	Yes
New CE total cost	Yes
New CE total MHrs	Yes
New forecast (T/O) qty	Yes

8.4.1.3 Select cost items to update

The check boxes under the Update CE total cost, Update CE total MHrs, and Update forecast (T/O) qty allows you to update the current estimate based on what is adjusted in the current budget after the budget move is approved.

CBS position		Cost source	Update CE total cost	Update CE total MHrs	Update forecast (T/O) qty
Unassigned cost items			☒	☒	☒
☐	1.1.1.7	Detail	☐	☐	☒
☐	1.1.1.8	Plug	☒	☒	☒
☐	1.1.1.9	Plug	☒	☒	☒
☒	1.1.1.10	Plug	☒	☒	☒
Subtotals 4					

The Update CE total cost and Update CE total MHrs check boxes are active for plug cost source only. The Update CE total cost and Update CE total MHrs check boxes cannot be edited for Detail cost items because cost is driven by your associated resources.

For example, if the Update CE total cost box is checked, the Adjust CB cost is added to the CE total cost after the contract adjustment is approved. You can preview the results in the New CE total cost, New CE total MHrs, and New forecast (T/O) qty columns.

Cost Item	Cost Source	Update CE total cost	Update CE total MHrs	Update forecast (T/O) qty	New CE total cost	New CE total MHrs	New forecast (T/O) qty
1.1.1.10	Plug	☒	☒	☒	1,000.00	1,000.00	1,000.00

8.4.1.4 Select automatic updates for multiple cost items

You can select automatic updates for multiple cost items to save you time from selecting check boxes manually for each cost item.

The Auto-calculate tool automatically checks the adjustment boxes for all the cost items that you select.

To use the Auto-calculate feature select the cost items you wish to update. Click the **Auto-calculate** icon, and then select **Update CE from CB**. In the Auto calculate dialog box, select whether to update Cost, Quantity, Man hours, or Select all for the selected cost items, and then click **Apply**.

Change register > Budget Move

1 Details

2 Assign amounts

	CBS position	Description	WBS phase code	CB total cost	Adjusted CB cost	CB total Mhrs	Adjusted CB Mhrs	Cl	q
☒		Update CB from CE							
☒	4.1	Update CE from CB	ect Steel - Heavy	1074	\$ 800,000.00	\$ 0.00	16,000.00	0.00	
☒	4.2		Building I&J - Bridge C	1005	\$ 200,000.00	\$ 0.00	4,000.00	0.00	
☒	4.3		Concrete - Building K&L	1006	\$ 50,000.00	\$ 0.00	1,000.00	0.00	

Auto calculate

Match current budget values with current estimate values

☒ Select all

☒ Cost

☒ Quantity

☒ Man hours

Cancel

Apply

The applicable check boxes are now automatically selected to adjust your current estimate values for the selected cost items.

8.4.1.5 Set setting for default current estimate update

You can have the current estimate cost, man-hours, and quantity check boxes selected by default to be updated with adjusted current budget cost, man-hours, and quantity values when doing change orders.

In Settings > Control > **Project Tracking**, you can switch the **Default CE values to be updated from CB values** toggle to *ON*. When enabled, all applicable check boxes are selected by default. This is a quick way to keep CE and CB values in sync without having to double enter values.

The screenshot shows the 'Tasks' configuration page within the 'PROJECT TRACKING' tab. The 'Default CE values to be updated from CB values' toggle is turned on and is highlighted with a red rectangular box. Other visible settings include 'Generate WBS phase code automatically' set to 'Yes' and 'WBS Phase codes start value' set to '1000'.

For more information, see the **Default CE values to be updated from CB values** section in Project Tracking, [Tasks](#) settings.

8.5 BUDGET MOVE FROM INEIGHT CHANGE

You can initiate a budget move in InEight Change, which ultimately creates a budget move in InEight Control.

8.5.1 Budget move in Change

A budget move in Change is made by indicating the cost items and their cost adjustments on the Pricing tab of an issue record.

Steel Structure Training Job 2 | 105092 / Change

Change management > Issue > 3-Cracked weld

Current value
\$ 800.00

Cost
\$ 800.00

Billing markup
\$ 0.00

Markup
\$ 0.00

Markup %
0.00%

Deductions
\$ 0.00

Net value
\$ 800.00

Issue status
In Review

Pricing status
In process

Proposal status
Submitted to ...

Actions

DETAILSPRICINGPRICING SUMMARYSUPPORTING DOCUMENTS

CancelSave

Cost item description

WBS phase code

Adjusted CB Qty

Adjusted MHRs

Pay item

Adjusted billable amou...

Adjusted cost

Bil

☐

Erect Steel - Light

1005

10.00

200.00

003 - Steel - Labor & ...

\$ 10,600.00

\$ 10,600.00

☐

Erect Steel - Heavy

1074

-10.00

-200.00

003 - Steel - Labor & ...

(\$ 10,600.00)

(\$ 10,600.00)

For more information about managing budget moves in Change, see [Budget Moves](#).

8.5.2 Budget Move Integration Between Change and Control

When you create a budget move in Change, Change directs you to the Change Register in Control, where a new budget move record is automatically created with a status of *Issue-Draft*.

Steel Structure Training Job 2 | 105092 / Control / Workspaces

<

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LO

Actions

ID	Description	CCO	Crea... date	Issue #	Last cha... by	Last cha... on	Notes	Status
7.0	Cracked weld		06/26/2025	3	Paul benni...	06/26/2025		Issue-Draft
6.0	Steel alignment issue	000-000	06/26/2025	1	Paul benni...	06/26/2025		000-Draft

After the record is created in Control, the budget move can be reviewed, revised, and submitted just like any other budget move in Control.

8.6 BUDGET QUANTITY / MAN-HOUR ADJUSTMENT


During the course of a project, it is typical to have scope modifications that warrant changes to quantities or labor hours.

It is important to remember that changing man-hours or quantities will affect budgeted values of MH/QTY, QTY/MH, and Unit-Costs, but will not change the overall dollar value of your budget.

Within InEight Control, you can perform budget quantity and man-hour adjustments using a controlled approval process.

Perform a Budget Quantity / Man-Hour Adjustment

- 1. Select Actions > Budget move & contract adjustment > **Budget quantity and man hour adjustment.**

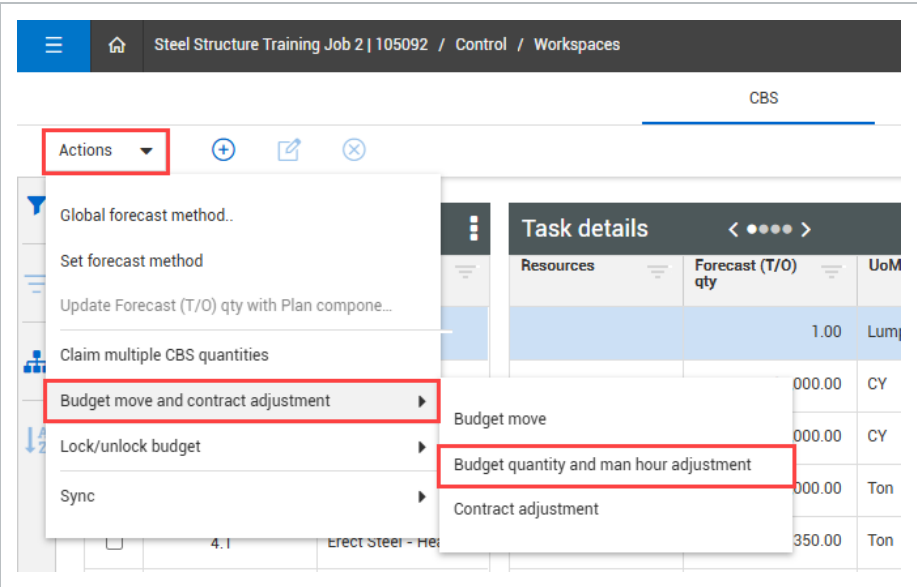

The budget adjustment wizard opens to step 1, **Details**.

- 2. In Details, add details as needed, and then click **Next**.

Change Register > Budget quantity and ...

1 Details

2 Select Items

3 Assign Amounts

4 Summary

Issue #

002XX

CCO

002XX

Description

Tonnage increase due to material change

211

Discipline

500

Change Management tag 1

Change Management tag 2

Change Management tag 3

Cancel

Draft

Next

The budget adjustment wizard opens to step 2, **Select Items**.

3. In Select Items, select a cost item from the list.

Change Register > Budget quantity and ...

1 Details

2 Select Items

3 Assign Amounts

4 Summary

CBS position	Description	WBS phase code
☐ 3	Concrete	1071
☐ 4	Structural Steel	1073
☐ 4.1	Erect Steel - Heavy	1074
☐ 4.2	Erect Steel - Light	1005
☐ 4.3	Bolted Connections	1006
☒ 4.4	Module 01 - Erect Steel Heavy	1087

You can select more than one cost item to adjust; however, these changes will be grouped as a single line item in the Change Register.

4. Click **Next**. The budget adjustment wizard opens to step 3, **Assign amounts**.
5. In Assign Amounts, enter the change to the man-hours or quantities into the applicable field, and then click **Next**.

Change Register > Budget quantity and ...

1 Details

2 Select Items

3 Assign Amounts

4 Summary

4.4 Module 01 - Erect Steel Heavy

	MHrs	Quantity
Original:	0.00	0.00
Pending:		5,000.00
New total:	0.00	5,000.00

The budget adjustment wizard opens to step 4, **Summary**.

- 6. In Summary, review your proposed changes, and then click **Submit** to send the budget move for approval.

Change Register > Budget quantity and ...

1 Details

2 Select Items

3 Assign Amounts

4 Summary

4.4 Module 01 - Erect Steel Heavy

	MHrs	Quantity
Before:	0.00	0.00
Pending:	0.00	5,000.00
After:	No change	5,000.00

Cancel

Draft

Back

Submit

You can select **Draft** if the budget move is not ready to be submitted and needs to be saved for later. With applicable permissions, you can select **Approve** to approve the budget move.

8.7 CONTRACT ADJUSTMENT – CONTROL

8.8 CONTRACT ADJUSTMENT IN CONTROL OVERVIEW

A contract adjustment, often referred to as a change order, represents a change to the scope of the contract that results in a change to the project's budgeted costs, man-hours, and contract price. These adjustments typically involve adding or revising cost and pay items to accurately estimate the financial and labor impacts of the change.

A contract adjustment, often referred to as a Change Order, represents a change to the total project budget. If you are a contractor this also results in a change to total contract price.


8.8.1 Pay Item vs. Cost Item

Contract adjustments involve changes to both your contract price (pay items) and your budget (cost items). The following table reviews the purpose and function of pay items and cost items.

Term	Function
Pay Item	For contractors, a pay item represents a project deliverable, including the pay quantity defined by the owner and the contracted unit price you will be paid for completion of the work. Pay item prices include your overhead and profit. For owners, a pay item can be used in a variety of ways or may even be ignored. One way it can be used is to represent funding sources and total funded amounts. It can also be used to bill internal or external partners.
Cost Item	The individual cost-related activities required to complete the deliverables of the project. Cost items represent the costs your budget needs to complete the work and therefore do not include profit.

8.8.2 Contract adjustment options

In Control, you can initiate a contract adjustment in the Workspaces module, by creating a new contract adjustment record. Go to Actions > Budget move and contract adjustment > **Contract adjustment**.

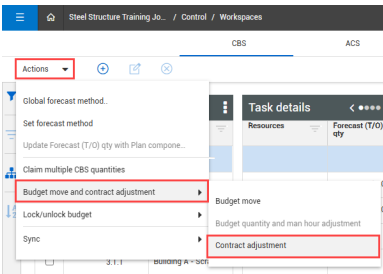

The contract adjustment record progresses through various steps that walk you through creating the adjustment. The steps to complete the contract adjustment depend on the workflow you select. You can start the workflow by selecting cost items or pay items.

Change register > Contract adjustment

Net budget change	Net quantity change	Net man hour change	Markup	Fee	Net contract change	Approval probability
\$ 0.00	No	0.00	\$ 0.00	\$ 0.00	\$ 0.00	

1 Details

2 Cost items

3 Pay items

4 Summary

Choose your Contract adjustment workflow

☒ Start with Cost items
Enter markup and fees on cost items to generate pay item price

☐ Start with Pay items
Adjust pay item price before adjusting cost item budgets

The contract adjustment in InEight Control can be performed using the multiple options for a controlled approval process, including:

- Start with cost items
- Start with pay items
- Auto-calculate

8.8.3 Contract adjustment header

For cost item and pay item contract adjustment workflows, as you progress through the adjustments, the record’s header provides a summary of the contract adjustment’s net budget (cost) and contract (price) change amounts, and the net man-hour change. The Start with Cost items workflow also includes a summary of the markup and fee for the adjustment as well.

Net budget change	Net quantity change	Net man hour change	Markup	Fee	Net contract change	Approval probability
\$ 225,000.00	No	2,900.00	\$ 20,900.00	\$ 5,000.00	\$ 250,900.00	

Both workflows include an option to define the contract adjustment’s approval probability. For more information on this feature, see [Revenue Forecast Probability](#).

8.9 START WITH COST ITEMS CONTRACT ADJUSTMENT

The Start with Cost items workflow lets you begin by entering cost items with their adjustments and clearly defining a separate markup and fee. Through the assignment of your cost items to pay items, these adjustments, markups, and fees then roll up to the pricing of your pay items.

This workflow of starting with costs and markups to build up to the change in contract price is typically the preferred approach and recommended best practice, because of the visibility and ease of use it provides in working out the adjustment.

Contract adjustment starting with cost items

1. Click Actions > Budget and contract adjustment > **Contract adjustment**. The Contract adjustment wizard opens to step 1, **Details**.
2. On Details, select the **Start with Cost items** workflow option, and then add contract adjustment details as needed.

Change register > Contract adjustment

Net budget change	Net quantity change	Net man hour change	Markup	Fee	Net contract change	Approval probability
\$ 0.00	No	0.00	\$ 0.00	\$ 0.00	\$ 0.00	

1 Details

2 Cost items

3 Pay items

4 Summary

Start with Cost items

Enter markup and fees on cost items to generate pay item price

Start with Pay items

Adjust pay item price before adjusting cost item budgets

Contract adjustment details

Description

Description

CCO

CCO

Issue #

Issue #

Discipline

Discipline

Change management tag 1

Change management tag 2

Change management tag 3

Change management user defined 1

Change management user defined 2

Change management user defined 3

Cancel

Draft

Next

3. Click **Next**. The Contract adjustment wizard opens to step 2, **Cost items**. On Cost items, add the cost items involved in the contract adjustment and enter their adjustment amounts. Click the **Add cost item** icon to add cost items. To remove a cost item, click the **Remove cost item** icon.

4. On Cost items, add the cost items involved in the contract adjustment and enter their adjustment amounts. Click the **Add cost item** icon to add cost items. To remove a cost item, click the **Remove cost item** icon.

Change register > Contract adjustment

	Net budget change	Net quantity change	Net man hour change	M
	\$ 0.00	No	0.00	\$

1 Details

2 Cost items

+

×

Assign cost to

	CBS position	Description	WBS phase code	CB total cost

InEight Inc. | Release 26.7

Page 373 of 639

5. Click **Add cost item**. The **Select cost items list** opens. Select the cost items related to the contract adjustment, and then click **Add**.

CBS position	Description	WBS phase code
☐ 4	Structural Steel	1073
☒ 4.1	Erect Steel - Heavy	1074
☒ 4.2	Erect Steel - Light	1005
☒ 4.3	Bolted Connections	1006
☐ 5	Materials	1084
☐ 5.1	Earthwork - Materials	1085
☐ 5.2	Concrete - Materials	1086
☐ 5.3	Structure Steel - Materials	1087
☒ 6	Merrill Iron & Steel - Steel Mater...	1088

Subtotals 32 (4 items selected)

Cancel Add

If the contract adjustment requires a new cost item to be added to the budget, this must be added to the Cost Breakdown Structure on the Workspaces CBS tab before creating the contract adjustment.

In the example above, a new cost item was added in the CBS for additional steel material (Merrill Iron & Steel – Steel Material) prior to creating the contract adjustment, so it is available to select.

When adding a new cost item to your locked budget, it will initially be unlocked and will therefore not be part of the Current Budget. A common practice is to keep the new change order-related cost item unlocked while working through the contract adjustment. If the contract adjustment becomes approved, the cost item will automatically become locked, and its costs and man-hours will become part of the Current Budget.

After your cost items are added to the page, you can enter adjustment values (positive or negative) to any of the following columns:

- Adjusted CB cost
- Adjusted CB MHrs
- Adjusted CB qty

- Any of the Adjusted CB cost categories (for example, labor, construction equipment, supplies, subcontract, etc.)

Contract adjustment with adjustment amounts added - The following image is an example of a contract adjustment with adjustment amounts added.

Change register > Contract adjustment

Net budget change

\$ 225,000.00

Net quantity change

No

Net man hour change

2,900.00

Markup

\$ 0.00

Fee

\$ 0.00

Net contract change

\$ 145,000.00

Approval probability

1 Details

2 Cost items

3 Pay items

4 Summary

Assign cost to

CB position	Description	WBS phase code	CB total cost	Adjusted CB cost	New CB total cost	Billing rate markup	Markup %	Markup	Fee	CB total Mhrs	Adjusted CB Mhrs
Unassigned cost items											
6	Merrill Iron & Steel - Steel M...	1088	\$ 0.00	\$ 80,000.00	\$ 80,000.00					0.00	
Pay item 003 - Steel - Labor & Material			Adjusted current price: \$ 145,000.00	\$ 145,000.00		\$ 0.00	Override Marku...		\$ 0.00	Pay item Fee	
4.1	Erect Steel - Heavy	1074	\$ 800,000.00	\$ 100,000.00	\$ 900,000.00					16,000.00	2,000.00
4.2	Erect Steel - Light	1005	\$ 200,000.00	\$ 40,000.00	\$ 240,000.00					4,000.00	800.00
4.3	Bolted Connections	1006	\$ 50,000.00	\$ 5,000.00	\$ 55,000.00					1,000.00	100.00

Assigning costs to pay items depends on the circumstances of your adjustment. There are multiple scenarios for assigning cost items to pay items.

- a. **Cost item already assigned to pay item scenario** - If the contract adjustment affects cost items that already exist in your budget, they will likely already be assigned to pay items. As you adjust the cost items, including adding markup and fees, the record will calculate the adjusted current price for the pay items the cost items are assigned to.

In the example below, costs are being adjusted on three existing cost items that are already assigned to the Steel – Labor & Material pay item. The Adjusted current price reflects the cost adjustments and markups of the assigned cost items, although a markup and fee have not yet been added.

Assign cost to ▾										
☐	CB position	Description	WBS phase code	CB total cost	Adjusted CB cost	New CB total cost	Billing rate markup	Markup %	Markup	Fee
Unassigned cost items										
☐	6	 Merrill Iron & Steel - Steel M...	1088	\$ 0.00	\$ 80,000.00	\$ 80,000.00				
☒	Pay item 003 - Steel - Labor & Material			Adjusted current price: \$ 145,000.00		\$ 145,000.00	\$ 0.00	Override Marku...	\$ 0.00	Pay item Fee
☐	4.1	Erect Steel - Heavy	1074	\$ 800,000.00	\$ 100,000.00	\$ 900,000.00				
☐	4.2	Erect Steel - Light	1005	\$ 200,000.00	\$ 40,000.00	\$ 240,000.00				
☐	4.3	Bolted Connections	1006	\$ 50,000.00	\$ 5,000.00	\$ 55,000.00				

- b. **Unassigned Cost Assigned to New Pay Item scenario** - If the change order requires a significant scope change, the owner may want to delineate it as a new pay item in the contract. Within the budget, the contractor will likely add a new cost item to

represent the new work and assign it to the new pay item. This assignment can be made prior to the contract adjustment but can also be done within the contract adjustment record.

Assigning a pay item within a contract adjustment is temporary. It will not update the Pay item assignment in the CBS. It is used in the contract adjustment only to help drive the adjusted price for that contract adjustment only.

In the example below, the additional steel material is not yet assigned to a pay item.

Assign cost to						
	CBS position	Description	WBS phase code	CB total cost	Adjusted CB cost	New CB total cost
Unassigned cost items						
☐	6	Merrill Iron & Steel - Steel M...	1088	\$ 0.00	\$ 80,000.00	\$ 80,000.00
Pay item 003 - Steel - Labor & Material				Adjusted current price: \$ 145,000.00		
☐	4.1	Erect Steel - Heavy	1074	\$ 800,000.00	\$ 100,000.00	\$ 900,000.00

To assign an unassigned cost item to a new pay item, select the cost item, then select Assign cost to > **Assign to new pay item**.

Assign cost to						
	CBS position	Description	WBS phase code	CB total cost	Adjusted CB cost	New CB total cost
Unassigned cost items						
☒	6	Merrill Iron & Steel - Steel M...	1088	\$ 0.00	\$ 80,000.00	\$ 80,000.00
Pay item 003 - Steel - Labor & Material				Adjusted current price: \$ 145,000.00		

Assign to new pay item

Assign to existing pay item

Unassign from pay item

The Create new pay item window opens. Add pay item details as needed. In this case, the adjusted cost amount is added in the Current price field, since markup and fees have not yet been considered.

Create new pay item

*Pay item number [?](#)

4

Line number

4

Sales order

Description

Additional steel work

479

*UoM (Unit of measure)

Ton

*Current billing method

Unit price

Current forecast (T/O) qty

100

Current price

\$80,000.00

Current pay qty

100.00

Current unit price

\$800.00


Click **Apply** when finished. The new cost item is now assigned to the new pay item. The Adjusted current price is currently the amount you entered in the pay item details.

				Net budget change	Net quantity change	Net man hour change	Markup	Fee	Net contract change
				\$ 225,000.00	No	2,900.00	\$ 0.00	\$ 0.00	\$ 225,000.00
				1 Details2 Cost items3 Pay items4 Summary					
				Assign cost to					
	☐	CBS position	Description	WBS phase code	CB total cost	Adjusted CB cost	New CB total cost		
Pay item 003 - Steel - Labor & Material					Adjusted current price: \$ 145,000.00		\$ 145,000.00		
	☐	4.1	Erect Steel - Heavy	1074	\$ 800,000.00	\$ 100,000.00	\$ 900,000.00		
	☐	4.2	Erect Steel - Light	1005	\$ 200,000.00	\$ 40,000.00	\$ 240,000.00		
	☐	4.3	Bolted Connections	1006	\$ 50,000.00	\$ 5,000.00	\$ 55,000.00		
Pay item 4 - Additional steel work					Adjusted current p... \$ 80,000.00		\$ 80,000.00		
	☐	6	Merrill Iron & Steel - Steel M...	1088	\$ 0.00	\$ 80,000.00	\$ 80,000.00		

The unlocked icons indicate the pay item and cost item are currently unlocked (not yet part of the Current Budget).

- c. **Unassigned cost assigned to existing pay item scenario** - There may be times when the change order requires a new cost item for the budget, but that cost item will pertain to an existing pay item. For those cases, you can select Assign cost to >

Assign to existing pay item.



You can add individual markup percentages for each cost item assigned to a pay item.

	CBS position	Description	WBS phase code	CB total cost	Adjusted CB cost	New CB total cost	Billing rate markup	Markup %	Markup
^	Pay item 003 - Steel - Labor & Material			Adjusted current price: \$157,750.00		\$145,000.00	\$0.00	Override Marku...	\$12,750.00
☐	4.1	Erect Steel - Heavy	1074	\$800,000.00	\$100,000.00	\$900,000.00		8.00 %	\$8,000.00
☐	4.2	Erect Steel - Light	1005	\$200,000.00	\$40,000.00	\$240,000.00		10.00 %	\$4,000.00
☐	4.3	Bolted Connections	1006	\$50,000.00	\$5,000.00	\$55,000.00		15.00 %	\$750.00

Alternatively, you can add markup at the pay item level, and it will override the markup for all the assigned cost items.

	CBS position	Description	WBS phase code	CB total cost	Adjusted CB cost	New CB total cost	Billing rate markup	Markup %	Markup
^	Pay item 003 - Steel - Labor & Material			Adjusted current price: \$159,500.00		\$145,000.00	\$0.00	10.00 %	\$14,500.00
☐	4.1	Erect Steel - Heavy	1074	\$800,000.00	\$100,000.00	\$900,000.00		10.00 %	\$10,000.00
☐	4.2	Erect Steel - Light	1005	\$200,000.00	\$40,000.00	\$240,000.00		10.00 %	\$4,000.00
☐	4.3	Bolted Connections	1006	\$50,000.00	\$5,000.00	\$55,000.00		10.00 %	\$500.00

You can also add a flat fee (for example, for permits, extra administration, or supervision). Fees are added only at the pay item level. The sum of your markup and fee is your planned profit.

	CBS position	Description	WBS phase code	CB total cost	Adjusted CB cost	New CB total cost	Billing rate markup	Markup %	Markup	Fee
^	Pay item 003 - Steel - Labor & Material			Adjusted current price: \$164,500.00		\$145,000.00	\$0.00	10.00 %	\$14,500.00	\$5,000.00
☐	4.1	Erect Steel - Heavy	1074	\$800,000.00	\$100,000.00	\$900,000.00		10.00 %	\$10,000.00	
☐	4.2	Erect Steel - Light	1005	\$200,000.00	\$40,000.00	\$240,000.00		10.00 %	\$4,000.00	
☐	4.3	Bolted Connections	1006	\$50,000.00	\$5,000.00	\$55,000.00		10.00 %	\$500.00	

- 6. After adjustments, markup and fees are added, and pay item assignments made, click **Next**. The Contract adjustment wizard opens to step 3, **Pay items**. On Pay items, you can review the pay items related to the contract adjustment and make further adjustments to the current price and quantities as needed.

1 2 3 Details Cost items Pay items					
Pay item number	Description	Adjusted current price	Current price	Adjusted current unit price	
4	Additional steel work	\$ 80,000.00	\$ 0.00	\$ 800.00	
003	Steel - Labor & Material	\$ 164,500.00	\$ 1,821,092.28	\$ 0.00	

Adjusted current price indicators show next to the values in the Adjusted current price column. A colored dot indicates the source of your adjusted current price values.

- Green dot - Indicates the Adjusted current price was calculated automatically from the Adjusted current cost + total markup + total fee. You can view the calculation when you hover over the dot.

Description	Adjusted current price	Current price	Adjusted current unit price	Current unit price
Additional steel work	\$ 80,000.00	\$ 0.00	\$ 800.00	\$ 0.00
Steel - Labor & Material	\$ 164,500.00			

System-generated value

Adjusted current price = adjusted budget + total markup + total fee

- Blue dot - Indicates the value was manually overridden. You can hover over the dot to view what the value was before.

Description	Adjusted current price	Current price	Adjusted current unit price
Additional steel work	\$ 80,000.00		
Steel - Labor & Material	\$ 164,500.00	\$ 1,821,092.28	

Manual override

Value before: \$ 86,400.00

This example shows that because the cost item was assigned to a new pay item, the current price was added manually when filling out the new pay item's details.

- Click the **Auto-calculate** button to adjust costs, markup, and fees after selecting the applicable pay items.

1 Details 2 Cost items 3 Pay items						
☐	Pay item number	Description	Adjusted current price	Current price	Adjusted current unit price	
☒	4	Additional steel work	\$ 80,000.00	\$ 0.00	\$ 800.00	
☐	003	Steel - Labor & Material	\$ 164,500.00	\$ 1,821,092.28	\$ 0.00	

When prompted, if you are sure you want to revert back to system-generated values, select **Yes**. The Adjusted current price updates to the current pricing information calculated by the system from the Cost items step.

1				
☐	Pay item number	Description	Adjusted current price	
☒	4	Additional steel work	\$ 86,400.00	
☐	003	Steel - Labor & Material	\$ 164,500.00	

8. After making any necessary adjustments, click **Next**. The Contract adjustment wizard opens to step 4, **Summary**.
9. In Summary, you can review the cost items and pay items summary involved in the contract adjustment with their adjusted values for a final review. Click **Submit** to send it to the Change Register for review and approval. With the applicable permissions, you can approve the contract adjustment directly from the record's Summary step by clicking the **Approve** button.

Change register > 3.0 - Contract adjust...

Net budget change	Net quantity change	Net man hour change	Markup	Fee	Net contract change	Approval probability
\$ 225,000.00	No	2,900.00	\$ 20,900.00	\$ 5,000.00	\$ 250,900.00	

1 Details 2 Cost items 3 Pay items 4 Summary

Cost items

CBS position	Description	WBS phase code	Adjusted CB cost	Adjusted CB Mhrs	Adjusted CB qty	Adjusted CB labor cost	Adjusted CB construction equipment cost	Adjusted CB FOM rented equipment...	Adjusted CB supplies cost	Adjusted CB materials cost
4.1	Erect Steel - Heavy	1074	\$ 100,000.00	2,000.00		\$ 100,000.00				
4.2	Erect Steel - Light	1005	\$ 40,000.00	800.00		\$ 40,000.00				
4.3	Bolted Connections	1006	\$ 5,000.00	100.00		\$ 5,000.00				
6	Merrill Iron & Steel - Steel M...	1088	\$ 80,000.00							
Subtotals 4			\$ 225,000.00	2,900.00		\$ 145,000.00	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00

Pay items

Pay item number	Description	Adjusted current price	Current price	Adjusted current unit price	Current unit price	Adjusted current pay qty	Current pay qty	Current forecast (T/O) qty	U...	Current billing method	Sales order
4	Additional steel work	\$ 86,400.00	\$ 0.00	\$ 800.00	\$ 0.00	108.00	0.00	100.00	Ton	Unit price	
003	Steel - Labor & Material	\$ 164,500.00	\$ 1,821,092.28	\$ 0.00	\$ 1,821,092.28	0.09	1.00	1.00	Each	Unit price	SO-003
Subtotals 2		\$ 250,900.00	\$ 1,821,092.28	\$ 800.00	\$ 1,821,092.28						

At any time during the development of the contract adjustment you can use any of the following buttons:

- **Back** - Use this button to move back a step in the contract adjustment workflow.
- **Draft** - If the contract adjustment is not yet complete or ready for review, select **Draft** to save it for later. This will save the adjustment as a draft in the Change Register. At any time, you can edit the adjustment by selecting the **Edit** icon for the record on the Change Register.

CBSACS

PAY ITEMSCHANGE REGISTER

Actions

ID	Description	CCO	Crea... date	Issue #	Last cha... by	Last cha... on	Notes	Status	Cha... man... tag 1	Cha... man... tag 2
3.0	Additional Steel Work		06/25/2025	079	Paul benni...	06/25/2025		Draft		

- **Cancel** - Select to close the contract adjustment without saving any changes.

8.10 START WITH PAY ITEMS CONTRACT ADJUSTMENT

While less commonly used, if you prefer to begin your calculation of a contract change by adjusting pay items and then the related cost items, you can select the Start with Pay items workflow.

Keep in mind that when using this workflow, you will need to know in advance the pending prices you plan to adjust to for your pay items, including markup and fees, since there is no step to define costs, markups and fees before pay item pricing.

Starting with pay items contract adjustment

1. Click Actions > Budget and contract adjustment > **Contract adjustment**. The Contract adjustment wizard opens to step 1, **Details**.
2. On Details, select the **Start with Pay items** workflow option, and then add contract adjustment details as needed.

Change register > Contract adjustment

Net budget change	Net quantity change	Net man hour change	Net contract change	Approval probability
\$ 0.00	No	0.00	\$ 0.00	

1 Details 2 Select Pay items 3 Adjust pay item 4 Select CBS items 5 Assign amounts 6 Adjust cost categories 7 Summary

Choose your Contract adjustment workflow

☐ Start with Cost items
Enter markup and fees on cost items to generate pay item price

☒ Start with Pay items
Adjust pay item price before adjusting cost item budgets

Contract adjustment details

Description 500
Description

CCO 60
CCO

Issue # 60
Issue #

Discipline 500
Discipline

Change management tag 1
Change management tag 2
Change management tag 3

Change management user defined 1
Change management user defined 2
Change management user defined 3

Cancel Draft Next

3. Click **Next**. The Contract adjustment wizard opens to step 2, **Select Pay items**. On this step, a list is provided of pay items already under the project's contract.

Change register > Contract adjustment

Net budget change
\$ 0.00

Net quantity change
No

Net man hour change
0.00

Net contract change
\$ 1,000.00

Approval probability

1 Details

2 Select Pay items

3 Adjust pay item

4 Select CBS items

5 Assign amounts

6 Adjust cost categories

7 Summary

Search

☐	Pay item number	Description	Current pay qty	UoM	Current unit price	Is billed
☒	001	Earthwork - Labor & Material	1.00	Each	759,887.01	☐
☐	002	Concrete - Labor & Material	1.00	Each	2,919,020.71	☐
☐	003	Steel - Labor & Material	1.00	Each	1,821,092.28	☐

Add pay item

1 items selected

Cancel

Draft

Back

Next

If you need to add a new pay item to the contract for the change order, select **Add pay item** at the bottom left of the list of pay items.

4. You can select existing pay items from the list, and then click **Next.** to go to Step 3, **Adjust pay item.** If you need to add new pay items click **Add pay item** at the bottom left of the list of pay items. This open a new Add pay item workflow which becomes step 2, and the Select pay items step becomes step 3. In Add pay item, add the details of the new pay item.

Change register > Contract adjustment

Net budget change
\$ 0.00

Net quantity change
No

Net man hour change
0.00

Net contract change
\$ 0.00

Approval probability

1 Details

2 Add pay item

3 Select Pay items

4 Adjust pay item

5 Select CBS items

6 Assign amounts

7 Adjust cost categories

8 Summary

+Pay item number [?](#)

5

Line number

5

Row number

4

Description

Additional steel work

479

+UoM (unit of measure)

Ton

+Current billing method

Unit price

Current forecast (T/O) qty

0

Proposal details

Enter any two values and the third will auto-calculate. bnnn3

Current price

\$800,000.00

-

Current unit price

\$800.00

x

Current pay qty

1,000.00

Cancel

Draft

Back

Next

- a. In the Proposal details section, enter Current price and Current unit price. The Current pay qty is auto-calculated.
- b. Click **Next**. The Contract adjustment wizard opens to step 3, **Select Pay items**. The new pay item shows in Select Pay items.

Change register > 4.0 - Contract adjust...

Net budget change
\$ 0.00

Net quantity change
No

Net man hour change
0.00

Net contract change
\$ 1,600,000.00

Approval probability
▼

< 1 Details

2 Add pay item

3 Select Pay items

4 Adjust pay item

5 Select CBS items

6 Assign amounts

7 Adjust cost categories

8 Summe >

Search

☐	Pay item number	Description	Current pay qty	UoM	Current unit price	Is billed
☒	6	Additional steel work	0.00	Ton	0.00	☐
☒	5	Additional steel work	0.00	Ton	0.00	☐
☒	001	Earthwork - Labor & Material	1.00	Each	759,887.01	☒
☐	002	Concrete - Labor & Material	1.00	Each	2,919,020.71	☒
☐	003	Steel - Labor & Material	1.00	Ea	1,821,092.28	☐

Add pay item

3 items selected

Cancel

Draft

Back

Next

The pay item is unlocked, and the quantity and price are zero when the contract adjustment has not been approved. When the contract adjustment is approved, the pay item will lock and officially become part of the contract price.

5. After selecting or adding pay items in Select Pay items, click **Next**. The Contract adjustment wizard opens to step 4, Adjust pay item. On Adjust pay item, for each pay item, you can enter the adjustment amounts under Current price and Current pay qty fields in the Pending row.

003 - Steel -

The locked cell auto-calculates based on the formula:
Current price = Current unit price * Current pay qty
To edit cell, click on the lock and choose a new field to lock.

		Current unit price	Current pay qty
		\$ 1,821,092.28	1.00
4	Pending	164,000.00	0
	New value	\$ 1,985,092.28	1.00

You may need to change which field to lock in order to calculate your unit price and quantities correctly.

6. Click **Next** after defining pending prices of your pay items. The Contract adjustment wizard opens to step 5, Select **CBS items**. On Select CBS items, select the cost items that pertain to the

contract adjustment from the list.

1 Details2 Add pay item3 Select Pay items4 Adjust pay item5 Select CBS items

☐	CBS position	Description
☐	▼ 4	Structural Steel
☒	4.1	Erect Steel - Heavy
☒	4.2	Erect Steel - Light
☒	4.3	Bolted Connections
☐	▼ 5	Materials
☐	5.1	Earthwork - Materials
☐	5.2	Concrete - Materials
☐	5.3	Structure Steel - Materials
☒	6	Merrill Iron & Steel - Steel Material

Similar to a contract adjustment that starts with cost items, if the contract adjustment requires a new cost item to be added to the budget, this must be added to the Cost Breakdown Structure on the Workspaces CBS tab before creating the contract adjustment.

In this example, a new cost item was added in the CBS for additional steel material (Merrill Iron & Steel – Steel Material) prior to creating the contract adjustment, so it is available to select.

7. Click **Next** after selecting CBS items. The Contract adjustment wizard opens to step 6, **Assign amounts**. On Assign amounts, add the adjustment amounts for current budget, man-hours and quantities in the applicable pending fields.

Net budget change\$ 225,000.00Net quantity changeYesNet man hour change2,900.00Net contract change\$ 244,000.00Approval probability

1 Details2 Add pay item3 Select Pay items4 Adjust pay item5 Select CBS items6 Assign amounts7 Adjust cost categories8 Summary

4.1 Erect Steel - Heavy

	Current budget	MHrs	Total quantity
Original	\$ 800,000.00	16,000.00	800.00
Pending	100,000.00	2,000.00	100.00
New total:	\$ 900,000.00	18,000.00	900.00

4.2 Erect Steel - Light

	Current budget	MHrs	Total quantity
Original	\$ 200,000.00	4,000.00	200.00
Pending	40,000.00	800.00	40.00
New total:	\$ 240,000.00	4,800.00	240.00

4.3 Bolted Connections

	Current budget	MHrs	Total quantity
--	----------------	------	----------------

8. Click **Next** after making your adjustments. The Contract adjustment wizard opens to step 8, **Summary**. On Summary, you can do a final review the cost items and pay items involved in the contract adjustment with their adjusted values. Click **Submit** to send it to the Change Register for review and approval.

1 Details 2 Add pay item 3 Select Pay items 4 Adjust pay item 5 Select CBS items 6 Assign amounts 7 Adjust cost categories 8 Summary							
Pay Items							Net contract change: \$ 244,000.00
5 - Additional steel work							
		Current price	Current unit price	Current pay qty	Current forecast (T/O) qty	UoM	Current billing method
1	Original	\$ 0.00	\$ 0.00	0.00	0.00	Ton	Unit price
	Pending	\$ 80,000.00	\$ 800.00	100.00	100.00	Ton	Unit price
	New value	\$ 80,000.00	\$ 800.00	100.00	100.00	No change	No change
003 - Steel - Labor & Material							
		Current price	Current unit price	Current pay qty	Current forecast (T/O) qty	UoM	Current billing method
4	Original	\$ 1,821,092.28	\$ 1,821,092.28	1.00	1.00	Each	Unit price
	Pending	\$ 164,000.00	\$ 164,000.00	0.00	0.00	Each	Unit price
	New value	\$ 1,985,092.28	\$ 1,985,092.28	1.00	1.00	No change	No change

Unlike the Start with Cost items workflow, in the Start with Pay items workflow, the adjusted (pending) values defined for your cost items have no direct influence on your pay items' pending values. In the Start with Cost items workflow, the system directly calculates the adjusted current price from the assigned cost items automatically. In the Start with Pay items workflow this is not the case. Instead, the pending current prices are manually determined, independent from the pending values you enter for the related cost items.

At any time during the development of the contract adjustment you can use any of the following buttons:

- **Back** - Use this button to move back a step in the contract adjustment workflow.
- **Draft** - If the contract adjustment is not yet complete or ready for review, select Draft to save it for later. This will save the adjustment as a draft in the Change Register. At any time, you can edit the adjustment by selecting the **Edit** icon for the record on the Change Register.

CBS

ACS

PAY ITEMS

CHANGE REGISTER

Actions

ID	Description	CCO	Crea... date	Issue #	Last cha... by	Last cha... on	Notes	Status	Cha... man... tag 1	Cha... man... tag 2
3.0	Additional Steel Work		06/25/2025	079	Paul benni...	06/25/2025		 Draft		

- **Cancel** - Select to close the contract adjustment without saving any changes.

8.11 AUTO-CALCULATE CONTRACT ADJUSTMENT VALUES

When managing project changes, as best practice, your organization might want to keep the current estimate (CE) up to date with potential changes so the project team can include those potential changes in their forecast even before the changes have been approved. The following sections cover two ways the system can help you keep the current estimate in sync with the latest pending changes.


8.11.1 Update Current Budget (CB) Adjustments from Current Estimate (CE)

When project issues arise and changes are considered, the CE can be used to estimate the scope and impact of changes before they are approved and added to the CB. As mentioned above, the CE changes can be used by the project team in their forecasts to forecast the project more accurately.

Your organization might prefer to add or revise cost items in the CE with changes as they arise, even before creating contract adjustments, so that they can be part of the project forecast right away. For this approach, when you create contract adjustments for those cost items, you can have the system automatically update the CB adjustment fields (costs, man-hours, quantities) with your CE values. This saves you the work of manually rethinking and reentering the changes on the contract adjustment that were already defined in the CE.

8.11.1.1 Auto-calculate current budget adjustments on the Start with Cost items workflow

When using the Start with Cost items workflow on a contract adjustment record, you can automatically update your CB adjustment values from the Cost items step. From step 2, **Cost items** window, click **Auto-calculate**, then select **Update CB from CE**.

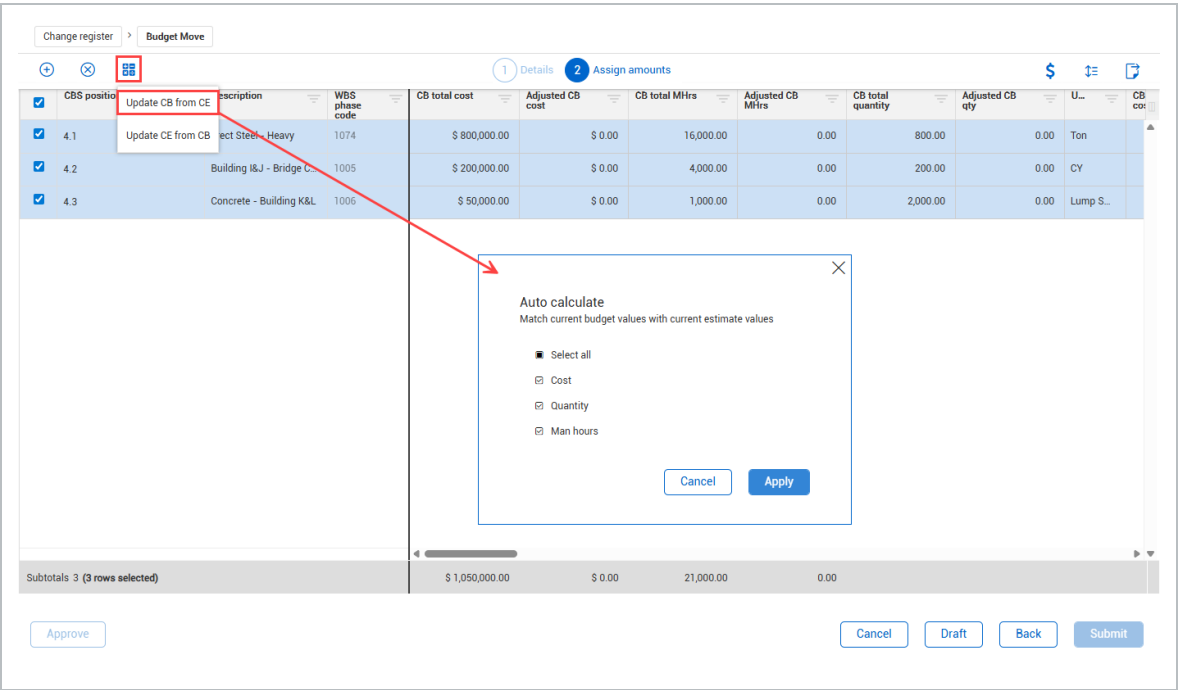

On the Auto-calculate dialog box, you can select which values you want to update (costs, quantities, man-hours, or all).

Click **Apply** after selecting your values. Your Adjusted CB fields update automatically with your CE values.

1 Details 2 Cost items 3 Pay items 4 Summ						
Assign cost to						
	CBS position	Description	WBS phase code	CB total cost	Adjusted CB cost	
Pay item 003 - Steel - Labor & Material				Adjusted current price: \$ 164,500.00	\$ 145,000.00	
☐	4.1	Erect Steel - Heavy	1074	\$ 800,000.00	\$ 100,000.00	
☐	4.2	Erect Steel - Light	1005	\$ 200,000.00	\$ 40,000.00	
☐	4.3	Bolted Connections	1006	\$ 50,000.00	\$ 5,000.00	

8.11.1.2 Auto-Calculate Current Budget Adjustments on the Start with Pay Items Workflow

Similarly, when making a contract adjustment using the Start with Pay items workflow, you can auto-calculate the pending Current Budget values. This is done from the Assign amounts step, by selecting **Advanced options**.

1 Details 2 Select Pay items 3 Adjust pay item 4 Select CBS items 5 Assign amounts

4.1 Erect Steel - Heavy

		Current budget	MHrs
1	Original	\$ 800,000.00	
	Pending	0.00	
	New total:	\$ 800,000.00	

4.2 Erect Steel - Light

		Current budget	MHrs
	Original	\$ 200,000.00	

Advanced options

On the Auto calculate dialog box, select which values to update (costs, quantities, man-hours, or all). Once selected, click **Apply**.

The Pending fields under Current budget, Mhrs, and Total quantity update with your Current Estimate values.

1 Details 2 Select Pay items 3 Adjust pay item 4 Select CBS items 5 Assign amounts 6 Adjust cost categories 7 Summary

4.1 Erect Steel - Heavy

		Current budget	MHrs	Total quantity
1	Original	\$ 800,000.00	16,000.00	800.00
	Pending	100,000.00	2,000.00	100.00
	New total:	\$ 900,000.00	18,000.00	900.00

4.2 Erect Steel - Light

		Current budget	MHrs	Total quantity
2	Original	\$ 200,000.00	4,000.00	200.00
	Pending	40,000.00	200.00	40.00
	New total:	\$ 240,000.00	4,200.00	240.00

8.11.2 Update Current Estimate from Adjusted Current Budget

In some instances, you may not be able to forecast a change in the CE until you know the change will be approved. Or your organization may prefer to handle changes exclusively via contract adjustment records until changes are approved. When approved, the CE will then update with the changes automatically. In any case, if CB adjustments are first recorded on a contract adjustment record, you can use auto-calculate to update the CE with those adjustments.

The Update CE from CB auto-calculate feature is only available on the Start with Cost items workflow.

When a contract adjustment is revised, the Current Estimate values do not get updated or backed out.

When doing a contract adjustment using the Start with Cost items workflow, on the Cost items step, you can add the following columns from the Column chooser that show how the Current Estimate values are based on the adjusted current budget values:

- Cost source
- Update CE total cost
- Update CE total MHrs
- Update forecast (T/O) qty
- CE total cost
- CE total MHrs
- Forecast T/O qty
- New CE total cost
- New CE total MHrs
- New forecast (T/O) qty

The check boxes under the Update CE total cost, Update CE total MHrs, and Update forecast (T/O) qty lets you select to update the CE based on what is adjusted in the CB after the contract adjustment is approved.

The screenshot shows the 'Contract adjustment' screen in the 'Cost items' tab. The table below is a representation of the data shown in the screenshot:

Change register	Contract adjustment	Net budget change	Net quantity change	Net man hour change	Markup	Fee	Net contract change	Approval probability
		\$ 0.00	No	0.00	\$ 0.00	\$ 0.00	\$ 0.00	

Navigation: 1 Details 2 Cost items 3 Pay items 4 Summary

CBIS position	Description	WBS phase code	Adjusted CB fees	Cost source	Update CE total cost	Update CE total MHrs	Update forecast (T/O) qty	CB allowance total cost	Adj allo
Pay item 002 - Concrete - Labor & Material			Adjusted current price: \$ 0.00		☒	☒	☒		
3	Concrete	1071		Plug	☒	☒	☒	\$ 0.00	
Subtotals 2								\$ 0.00	

In other words, when the contract adjustment is approved, the adjustment values update the CB, and the values that are checked also update the CE.


In a contract adjustment, the Update CE total cost and Update CE total MHrs check boxes are active for Plug cost source only. They cannot be edited for Detail cost items because cost is driven by your associated resources.

8.11.2.3 Select automatic updates for multiple cost items

You can select automatic updates for multiple cost items to save you time from selecting check boxes manually for each cost item.

The Auto-calculate tool automatically checks the adjustment boxes for all the cost items that you select.

To use the Auto-calculate feature select the cost items you wish to update. Click the **Auto-calculate** icon, and then select **Update CE from CB**. In the Auto calculate dialog box, select whether to update Cost, Qty, Man hours, or Select all for the selected cost items, and then click **Apply**.

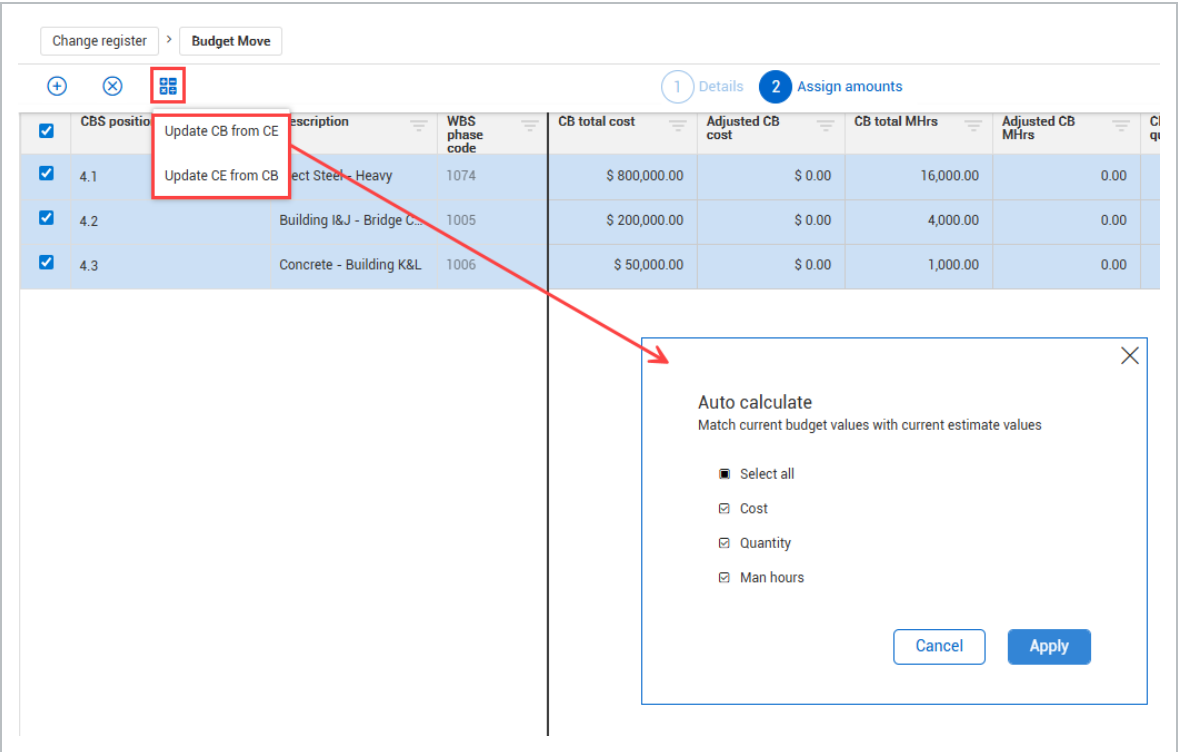

The applicable check boxes are now automatically selected to adjust your current estimate values for the selected cost items.

8.11.2.4 Set setting for default current estimate update

You can have the current estimate cost, man-hours, and quantity check boxes selected by default to be updated with adjusted current budget cost, man-hours, and quantity values when doing change orders.

In Settings > Control > **Project Tracking**, you can switch the **Default CE values to be updated from CB values** toggle to **ON**. When enabled, all applicable check boxes are selected by default. This is a quick way to keep CE and CB values in sync without having to double enter values.

For more information, see the **Default CE values to be updated from CB values** section in Project Tracking, [Tasks](#) settings.

8.12 CONTRACT ADJUSTMENT – INEIGHT CHANGE

8.13 CONTRACT ADJUSTMENT FROM INEIGHT CHANGE OVERVIEW

A contract adjustment, often referred to as a change order, represents a change to the scope of the contract that results in a change to the project's budgeted costs, man-hours, and contract price. These adjustments typically involve adding or revising cost and pay items to accurately estimate the financial and labor impacts of the change.

When you integrate InEight Change with InEight Control, you can track project changes using a more robust, transparent, and auditable process than using just the Control application.

8.14 CONTRACT ADJUSTMENT FROM INEIGHT CHANGE OVERVIEW

A contract adjustment, often referred to as a change order, represents a change to the scope of the contract that results in a change to the project's budgeted costs, man-hours, and contract price. These adjustments typically involve adding or revising cost and pay items to accurately estimate the financial and labor impacts of the change.

When you integrate InEight Change with InEight Control, you can track project changes using a more robust, transparent, and auditable process than using just the Control application.

8.15 MANAGING CHANGES IN INEIGHT CHANGE

The Change application provides a streamlined process for logging issues and managing their development as they progress through the change management process to become potential and possibly executed change orders. This includes producing detailed records for collecting relevant information, determining pricing, and managing correspondence with external stakeholders. It also includes configurable workflows for multi-level review and approval of change orders. For more information on using InEight Change for managing changes, see [Change Order Management](#) and [InEight Change Knowledge Library home page](#).

8.15.1 InEight Change Integration with InEight Control

Contract adjustments can be made within the Change application and are visible in the Change Register of the Control application. After an Issue is created in Change, and becomes an executed change order, it appears as a pending contract adjustment in Control with a status of CCO-Draft.

ACS PAY ITEMS CHANGE REGISTER AUDIT LOG											
Actions											
ID	Description	CCO	Cre... date	Issue #	Last cha... by	Last cha... on	Notes	Status	Total budget cost adjustment	Total budget MH adjustment	Total contract price adjustment
5.0	Additional steel work	CCO-001	06/26/2025	4	Paul benni...	06/26/2025		CCO-Draft	\$ 317,500.00	11,000.00	\$ 112,500.00

For more information on executing the change order in Change, see [Execute the Change Order](#).

On the CCO-Draft contract adjustment register, the cost items with their quantity, cost, and man-hour adjustments, along with any associated pay items show up on the adjustment record.

Steel Structure Training Job 2 | 1... / Control / Workspaces

Change register

>

1.1 - Contract adjust...

CCO total budget	CCO unassigned budget	Net budget change	Net quantity change	Net man hour change	Billing rate markup	CCO markup	CCO unassigned	Fee	Net contract change	CCO agreed price	CCO un...
\$ 160,000.00	\$ 0.00	\$ 160,000.00	Yes	2,000.00	\$ 0.00	\$ 26,319.38	(\$ 0.63)	\$ 0.00	\$ 186,319.38	\$ 186,319.38	\$ 0.00

1

Details

2

Cost items

3

Pay items

4

Summary

Assign cost to

☐	CBS position	Description	WBS phase code	CB total cost	Adjusted CB cost	New CB total cost	Billing rate markup	CCO markup %	CCO markup
Pay item 003 - Steel - Labor & Material					\$ 105,000.00		\$ 0.00	16.45 %	\$ 17,272.50
☐	4.1	Erect Steel - Heavy	1074	\$ 800,000.00	\$ 105,000.00	\$ 905,000.00		16.45 %	\$ 17,272.50
Pay item CCO-001 - Additional Steel Work					\$ 55,000.00		\$ 0.00	16.45 %	\$ 9,047.50
☐	6	Merrill Iron & Steel - Steel m...	1088	\$ 0.00	\$ 50,000.00	\$ 50,000.00		16.45 %	\$ 8,225.00
☐	4.4	Crane Rental	1089	\$ 0.00	\$ 5,000.00	\$ 5,000.00		16.45 %	\$ 822.50

8.15.2 Creating new cost items from Change executed change orders

When adding pricing to an issue in Change, this can include adding new cost items that are not yet part of the budget.

Steel Structure Training Job 2 | 105092 / Change

Change management > Issue > 1-Steel alignment issue

Current value	Cost	Billing markup	Markup	Markup %	Deduc
\$ 1,000.00	\$ 1,000.00	\$ 0.00	\$ 0.00	0.00%	\$ 0.00

Actions

+

✕

+

+

+

+

+

+

Add existing cost items

Add new cost item

Add from template

Add Unassigned pricing item

DETAILS

PRICING

WBS phase code	Adjusted CB Qty	Adjusted MHrs
1074		1.00

Depending on the nature and timing of the issue, the scope and details of the cost item may already be known, or the new cost item can be added as a placeholder until further information becomes available.

Actions

DETAILS

PRICING

PRICING SUMMARY

SUPPORTING DOCUMENTS

Clear all filters

☐	Cost item description	WBS phase code	Adjusted CB Qty	Adjusted MHrs	Adjusted billable amou...
☐					
☐	Erect Steel - Heavy	1074	1.00	20.00	\$ 1,000.00
☐	New Cost Item	New	1.00	0.00	\$ 10,000.00

When the issue becomes an executed change order and triggers a new CCO-Draft contract adjustment in Control, details can be added to the cost item as the contract adjustment is reviewed and revised.

Change register > 18.0 - Contract adj...

CCO total budget	CCO unassigned budget	Net budget change	Net quantity change	Net man hour change	Billing rate markup	CCO markup	CCO unassigned markup	Fee	Net contract change	CCO agreed price	CCO unassigned price	Approval probability
\$ 702.09	\$ 0.00	\$ 702.09	Yes	14.21	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00	\$ 702.09	\$ 702.09	100.00% - Execute...

1 Details

2 Cost items

3 Time phased budget

4 Play items

5 Summary

Assign cost to

CBS position	Description	WBS phase code	CB total cost	Adjusted CB cost	New CB total cost	Billing rate markup	CCO markup %	CCO markup	Fee	CB total MHrs	Adjusted CB MHrs	New CB total MHrs	CB total quantity	Adjusti...
Unassigned cost items														
☐	New cost item		\$ 3,374.33	\$ 1.35	\$ 3,375.68					60.00	0.02	60.02	2,500.00	
☐	2.3.1.2 Maintain A		\$ 700.74	\$ 8,408.83						156.00	14.18	170.18	12.00	

Prior to this step, an executed CCO was created in Change with a new cost item.

This includes being able to specify within the contract adjustment under which parent to place the newly created cost item upon approval. Otherwise, the cost item is added as the last record in the Cost Breakdown Structure on the Workspaces CBS tab.

Tasks			Task details			Actuals	
☐	CBS position	Description	Resources	Forecast (T/O) qty	UoM	Actual qty (to date)	Actual Mhrs/unit (to date)
☐	4.13.2	Not in Use		1.00	Wk	0.00	
☐	4.13.3	Not in Use		1.00	Wk	0.00	
☐	4.14	Not in Use		1.00	PLS	0.00	
☐	4.15	Not in Use		1.00	Gal	0.00	
☐	4.15.1	Not in Use		1.00	Gal	0.00	
☐	4.15.2	Not in Use		1.00	Gal	0.00	
☐	5	New cost item		1.00	Mile	0.00	
Subtotals 35							

8.15.3 Pay item associations from InEight Change executed change orders

When adding new cost items to price out issues in Change, you can associate a pay item to the cost item.

Actions

DETAILS

PRICING

+

+

	Cost item description	WBS phase code	Pay item	Adjusted CB Qty	Adjusted MHR
☐	Erect Steel - Heavy	1074	003 - Steel - Labor & ...	1.00	
☒	New Cost Item	New	Steel - Labor & Material	1.00	

If the issue becomes an executed change order, this association will carry over when it becomes a contract adjustment in Control, as seen on the Cost items step of the contract adjustment record.

Steel Structure Training J... / Control / Workspaces							
Change register > 6.0 - Contract adjust...							
CCO total budget	CCO unassigned budget	Net budget change	Net quantity change	Net man hour change	Billing rate markup	CCO markup	CCO unassigned markup
\$ 11,000.00	\$ 0.00	\$ 11,000.00	Yes	20.00	\$ 0.00	\$ 0.00	\$ 0.00
1 Details 2 Cost items 3 Pay items 4 Summary							
Assign cost to ▾							
☐	CBS position	Description	WBS phase code	CB total cost	Adjusted CB cost		
^	Pay item 003 - Steel - Labor & Material		Adjusted current price: \$ 11,000.00		\$ 11,000.00		
☐	4.1	Erect Steel - Heavy	1074	\$ 800,000.00	\$ 1,000.00		
☐		New Cost Item		\$ 0.00	\$ 10,000.00		

8.15.4 Markup from InEight Change executed change orders

Markups defined in the executed change order's pricing in Change also carry over to the Draft-CCO contract adjustment in Control. On the contract adjustment record, Billing rate markup, CCO markup, and CCO unassigned markup are all contract adjustment header fields that can help you make more informed decisions on how to adjust the Adjusted current price.

Change register									
Detail	CCO unassigned budget	Net budget change	Net quantity change	Net man hour change	Billing rate markup	CCO markup	CCO unassigned markup	Fee	Probability
	\$ 0.00	\$ 1,060.00	Yes	1,000.00	\$ 0.00	\$ 64.13	\$ 64.13	\$ 0.00	\$ 1
1 Details 2 Cost items 3 Time phased budget 4 Pay items 5 Summary									
☐	Pay item number	Adjusted current price	Current price	Adjusted current unit price	Current unit price	Adjusted current pay qty	Current pay qty	Current forecast qty	
☒	1	\$ 1,060.00	\$ 1,001.00	\$ 0.00	\$ 1.00	1,060.00	1,001.00		

8.15.5 Revising a CCO-Draft contract adjustment

When the status of a Client Change Order (CCO) is changed to Executed and submitted, the change becomes a change record in the Change Register in Control. From the Change Register, the CCO-Draft contract adjustment can be reviewed and submitted for final approval.

For detailed steps on how to revise and submit for approval a contract adjustment that comes from InEight Change, see [Approve Contract Adjustment](#).

8.16 CONTRACT ADJUSTMENT HEADER

When revising a contract adjustment from Change, the contract adjustment’s header provides key information to track the total cost, man-hours, and price of the adjustment.

CCO total budget	CCO unassigned budget	Net budget change	Net quantity change	Net man hour change	Billing rate markup	CCO markup	CCO unassigned markup	Fee	Net contract change	CCO agreed price	CCO unassigned price
\$ 259,000.00	\$ 0.00	\$ 259,000.00	Yes	3,000.00	\$ 0.00	\$ 25,900.00	\$ 25,900.00	\$ 0.00	\$ 259,000.00	\$ 284,900.00	 \$ 25,900.00

In the example below, the contract adjustment header shows budget values prior to making any revisions. Note the following:

CCO total budget	CCO unassigned budget	Net budget change	Net quantity change	Net man hour change
\$ 259,000.00	\$ 0.00	\$ 259,000.00	Yes	3,000.00

Header category	Description
CCO total budget	The total cost adjustment coming from the executed CCO in Change.
CCO unassigned budget	Costs within the change order coming from the CCO in Change that are not already assigned to a cost item.
Net budget change	The total cost adjustment on the contract. In this case, it matches the CCO total budget because the cost items with their adjustments came over from the executed CCO to the contract adjustment record.
Net quantity change	The sum of the Adjusted CB qty column of the contract adjustment in control.
Net man hour change	The sum of the Adjusted CB Mhrs column of the contract adjustment in control.

Billing rate markup	CCO markup	CCO unassigned markup	Fee
\$ 0.00	\$ 25,900.00	\$ 25,900.00	\$ 0.00

Header category	Description
Billing rate markup	The markup amount related to billing rates. This will only have a value if billing rate markups are being used. For more information on billing rates, see Billing methods .
CCO markup	The markup value defined on the executed CCO.
CCO unassigned markup	The markup coming from the executed CCO that has not yet been assigned on the contract adjustment record in Control. In this case, because the markup has not yet been assigned, the Net contract change only reflects the adjusted costs from the contract adjustment cost items.
Fee	The sum of lump sum fee amounts defined at the pay item level of the pay items on the Cost items step of the contract adjustment.

Net contract change	CCO agreed price	 CCO unassigned price
\$ 259,000.00	\$ 284,900.00	\$ 25,900.00

Header category	Description
Net contract change	The total amount assigned to pay items on the contract adjustment record. This must equal the CCO agreed price in order to submit the contract adjustment for approval.
CCO agreed price	The final agreed upon price per the executed CCO.
CCO unassigned price	The amount that still needs to be assigned for the net contract change to equal the CCO agreed price.

Note that after adding a 10% markup on the Cost items step of the contract adjustment, the Net contract change matches the CCO agreed price, and the contract adjustment can be submitted.

Net budget change	Net quantity change	Net man hour change	Billing rate markup	CCO markup	CCO unassigned markup	Fee	Net contract change	CCO agreed price	CCO unassigned price
\$ 259,000.00	Yes	3,000.00	\$ 0.00	\$ 25,900.00	\$ 0.00	\$ 0.00	\$ 284,900.00	\$ 284,900.00	\$ 0.00

1 Details	2 Cost items	3 Pay items	4 Summary
-----------	--------------	-------------	-----------

Description	WBS phase code	CB total cost	Adjusted CB cost	New CB total cost	Billing rate markup	CCO markup %	CCO markup
Material	Adjusted current price: \$ 284,900.00		\$ 259,000.00		\$ 0.00	10.00 %	\$ 25,900.00
Concrete	1071	\$ 1,500,000.00	\$ 159,000.00	\$ 1,659,000.00		10.00 %	\$ 15,900.00
Concrete - Materials	1086	\$ 1,000,000.00	\$ 100,000.00	\$ 1,100,000.00		10.00 %	\$ 10,000.00

8.17 CHANGE APPROVAL PROCESS

After budget moves are submitted, they must be reviewed and approved before their values are added to the current budget. The Change Register allows users with applicable permissions to review the details of contract adjustments, budget moves, and quantity or man-hour adjustments. They can revise, reject, or approve the changes.

To access the Change Register in Control Workspaces, select the Change Register tab.

Steel Structure Training Job 2 1... / Control / Workspaces											
CBS			ACS			PAY ITEMS			CHANGE REGISTER		
ID	Description	CCO	Created date	Issue #	Last changed by	Last changed on	Notes	Status	Total budget cost adjustment	Total budget MH adjustment	Total contract price adjustment
8.0	Concrete issue	CCO-003	07/01/2025	2	Paul benni...	07/01/2025		CCO-Pending	\$ 259,000.00	3,000.00	\$ 284,900.00
7.0	Cracked weld		06/26/2025	3	Paul benni...	07/01/2025		Issue-Draft	\$ 0.00	0.00	\$ 0.00
6.0	Steel alignment issue	CCO-002	06/26/2025	1	Paul benni...	06/30/2025		CCO-Draft	\$ 11,000.00	20.00	\$ 1,000.00
3.1	Additional Steel Work	CCO-001	07/01/2025	079	Paul benni...	07/03/2025		Draft	\$ 225,000.00	2,900.00	\$ 250,900.00
3.0	Additional Steel Work		06/25/2025	079	Paul benni...	07/01/2025		Revised	\$ 225,000.00	2,900.00	\$ 250,900.00
2.0	Structural steel budget move		06/19/2025		Paul benni...	07/01/2025		Approved	\$ 0.00	0.00	\$ 0.00
1.0	Erect steel budget move		06/18/2025		Paul benni...	07/03/2025		Pending	\$ 0.00	0.00	\$ 0.00

The Change Register includes the following columns:

Column name	Description
ID	Auto-assigned by the system to uniquely identify each change entry. When a submitted change is revised, a duplicate record is created with the ID indicating a new version of the original. For example, if the original change has

Column name	Description
	an ID of 2.0, the new revision entry will have an ID of 2.1.
Description	The description entered on the Detail step of the change's record.
CCO	Text field for entering a change order number. Contract adjustments generated from InEight Change will automatically have this filled with the number defined in the executed CCO. This is only editable within the CCO in Change.
Creation date	The date the change record was created in the Change Register.
Issue #	Text field for entering the issue number. Change records generated in InEight Change will automatically contain the number as defined on the issue/PPO/CCO in Change. This is only editable within the CCO in Change.
Last changed by	Indicates the user who last made a change to the record.
Last changed on	Indicates the date when the last change was made.
Notes	Clicking on the icon in this field opens a slide out panel where notes can be entered and reviewed in a "text feed" format.
Status	Indicates the state of the change record (for example draft, pending, approved). More information about statuses is covered in a separate table below.
Total budget cost adjustment	Indicates the total amount of adjusted cost estimated on the change record.
Total budget MH adjustment	Indicates the total adjusted man-hours estimated on the change record.
Total contract price adjustment	Indicates the total contracted price adjustment estimated on the change record.

Column name	Description
Type	Indicates whether the change record is a Budget move, Budget Qty & MH adjustment, or Contract adjustment.

Entries in the Change Register will have different statuses depending on what step of the process they are in and where the change was created (for example, Change or Control). The following table lists the possible statuses and what they indicate.

Status	Description
Draft	A change record that is not yet submitted. This allows a change record to be started and saved for later, until it is ready to submit. A change record that came from Change is indicated as Issue-Draft for budget moves or CCO-Draft for executed change orders.
Pending	A change record that has been submitted but not yet approved. A change record that came from Change is indicated as Issue-Pending for budget moves or CCO-Pending for executed change orders.
Approved	A change record that has been approved by someone with the appropriate permissions. An approved change makes the proposed budget cost and contract price adjustments final, updating the Current Budget accordingly. An approved change record that came from Change is indicated as Issue-Approved for budget moves or CCO-Approved for executed change orders.
Rejected	A change record that has been rejected by someone with the appropriate permissions. Rejecting a change ends the change process and prevents the proposed changes from updating cost items and pay items in the Current Budget. A rejected change record that came from Change is indicated as Issue-Rejected for budget moves or CCO-Rejected for executed change orders.
Revised	An approved change record that has been revised. Revising an approved record results in a new version of the change record with a new version number. For example, if an original change record has an ID of 2.0 and has its status changed to Revised, it results in a new change record being created automatically with an ID of 2.1 and a status of Draft. A revised change record that originally came from Change is indicated as Issue-Revised for budget moves or CCO-Revised for executed change orders.

8.17.1 Managing changes in the Change Register

With the applicable permissions, you can review project changes as they are recorded as entries in the Change Register and either approve, reject, or revise them as needed. The Change Register includes both change records that are in progress (status of Draft) and changes that have been submitted (status of Pending).

To review a change record, click within the row representing the change. A slide-out panel opens that summarizes the details of the change. The options available on the slide-out panel depend on the change record's status.

8.17.1.1 Draft changes review

On the slide-out panel for Draft changes, you can select Review, Delete, or Revise.

The screenshot shows the 'CHANGE REGISTER' tab selected in a software interface. A slide-out panel for change record '3.1 Additional Steel Work' is open. The panel displays the following information:

- Type:** Contract adjustment (Cost item...)
- Status:** Draft (with a blue pencil icon)
- Originated on:** 07/01/2025
- Originated by:** Paul bennion
- Last changed on:** 07/02/2025
- Last changed by:** Paul bennion
- Approved on:** N/A
- Approved by:** N/A
- Approval probability:** N/A

Below this information are two tables:

Pay item details

Pay item number	Description	Current billing method	Adjusted current price	Adjusted current unit price	Adjusted current pay qty	Locked date
003	Steel - Labor & Material	Unit price	\$ 164,500.00	\$ 0.00	0.09	
4	Additional steel work	Unit price	\$ 86,400.00	\$ 800.00	108.00	
			\$ 250,900.00	\$ 800.00		

Cost item details

CBS position	Description	WBS pha...	Adjusted CB cost	Adjusted CB MHrs	Adjusted CB atv	Locked date

At the bottom right of the panel, there are three buttons: 'Review' (outlined in red), 'Delete', and 'Revise' (solid blue).

- **Review** - Opens the change record in a read-only state. All the steps of the change can be reviewed, but no changes can be made. This may be a helpful option to give users permission to review changes without having the access to approve or reject them.
- **Delete** - Permanently deletes the draft. When clicking Delete, a prompt comes up to make sure you want to delete the record.

- **Revise** - Opens the change record with full functionality to edit the record. After editing, if the record is ready for approval, on the Summary step you can click **Submit**. If the record is still not ready, you can select Draft to save it for future editing.

8.17.1.2 Pending changes review

On the slide-out panel for changes with a Pending status, you can select Review, Reject, Revise, or Approve.

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

\$

▼

↓

⌂

📄

⚙️

🔍

1.0

Erect steel budget move

Type

Budget move (Associated)

Status

 Pending

Originated on

06/18/2025

Originated by

Paul bennion

Last changed on

07/03/2025

Last changed by

Paul bennion

Approved on

n/a

Approved by

n/a

From/To	CBS position	Description	W... ph... co...	Adjusted CB cost	Adjusted CB MHrs	Adjusted CB qty	Locked
From	4.2	Erect Steel - Light	1005	(\$ 10,000.00)	-200.00	0.00	
To	4.1	Erect Steel - Heavy	1074	\$ 10,000.00	+200.00	0.00	
From	4.2	Erect Steel - Light	1005	(\$ 1,000.00)	0.00	0.00	
To	4.3	Bolted Connections	1006	\$ 1,000.00	0.00	0.00	

\$ 0.00

Review

Reject

Revise

Approve

- **Reject** - Changes the status of the change record to Rejected, ending the change process and preventing the proposed change from updating cost items or pay items. From that point on, the change record is read-only. Once rejected, the change cannot be revised.
- **Approve** - Changes the status of the change to Approved, making the proposed changes final and updating the Current Budget and contract price with the changes. Once approved, you can review or revise the change.
- **Revise** - Opens the change record with full functionality to edit the record. If you revise a Pending record, you can resubmit maintaining the Pending status, or select Draft to save with a status of Draft.

If you revise an approved record, the status of the record will change to Revised and become read only, and a new draft of the record will be created with a new version number.

2.1	Cracked foundations		07/03/2025		Paul benni...	07/03/2025		 Draft
2.0	Cracked foundations		07/01/2025		Paul benni...	07/03/2025		 Revised

Revising an approved record will back out all approved budget, quantity, man-hour, and pay item amounts from the Current Budget. A revising warning message shows to confirm that you want to proceed.



Revising will back out previously approved amounts from current budget.

All approved budgets, quantities, man hours and pay items will be reverted back to it's original, pre-approved state. Are you sure you want to continue?

OK

Cancel

8.17.2 Group By option

You can activate the Group by icon to show certain change columns in groups of like information. Like the CBS, you can activate the Group By icon to categorize certain columns in the Change Register.

Steel Structure Training Job 2 | 1... / Control / Workspaces

CBS

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

Actions


\$

</

This page intentionally left blank.

CHAPTER 9 – REVENUE MANAGEMENT

9.1 REVENUE MANAGEMENT WORKFLOW

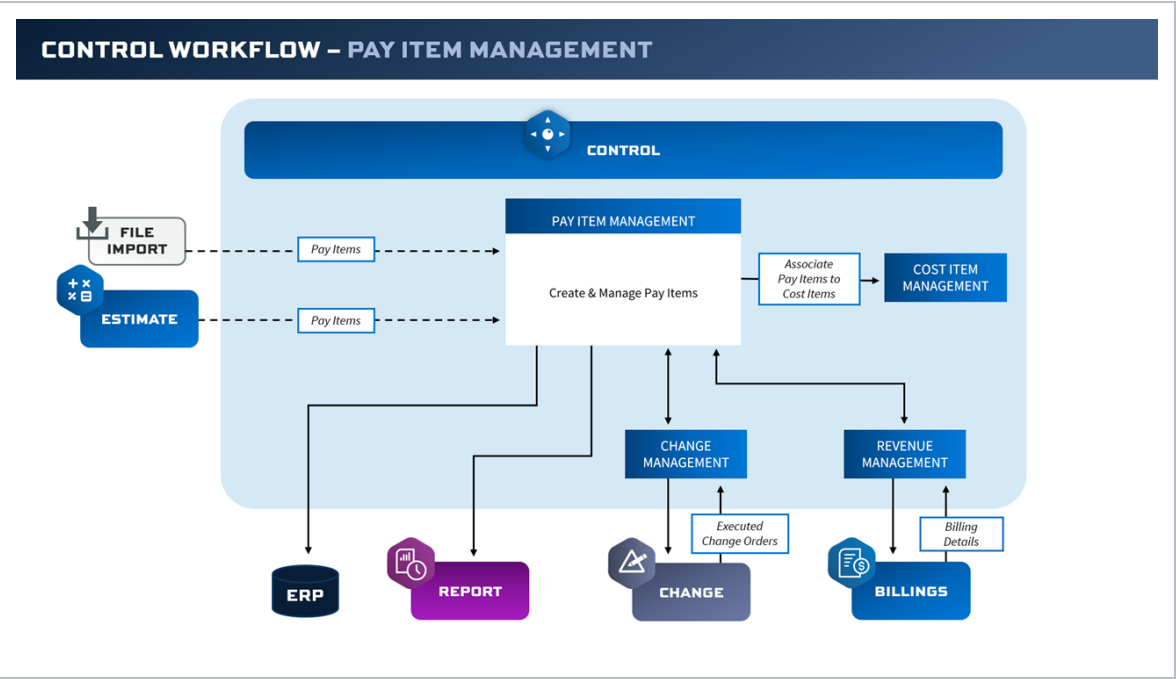


9.2 PAY ITEMS

VIDEO | [Pay Item Details](#)

Pay items distribute the cost calculated in the Cost Breakdown Structure along with all markups, fees and contingencies calculated in the pay items. You can manage pay items on the Pay Items tab. For more information, see [Pay Items registerWorkspaces](#)

9.3 ACCOUNT CODE STRUCTURE WORKFLOW

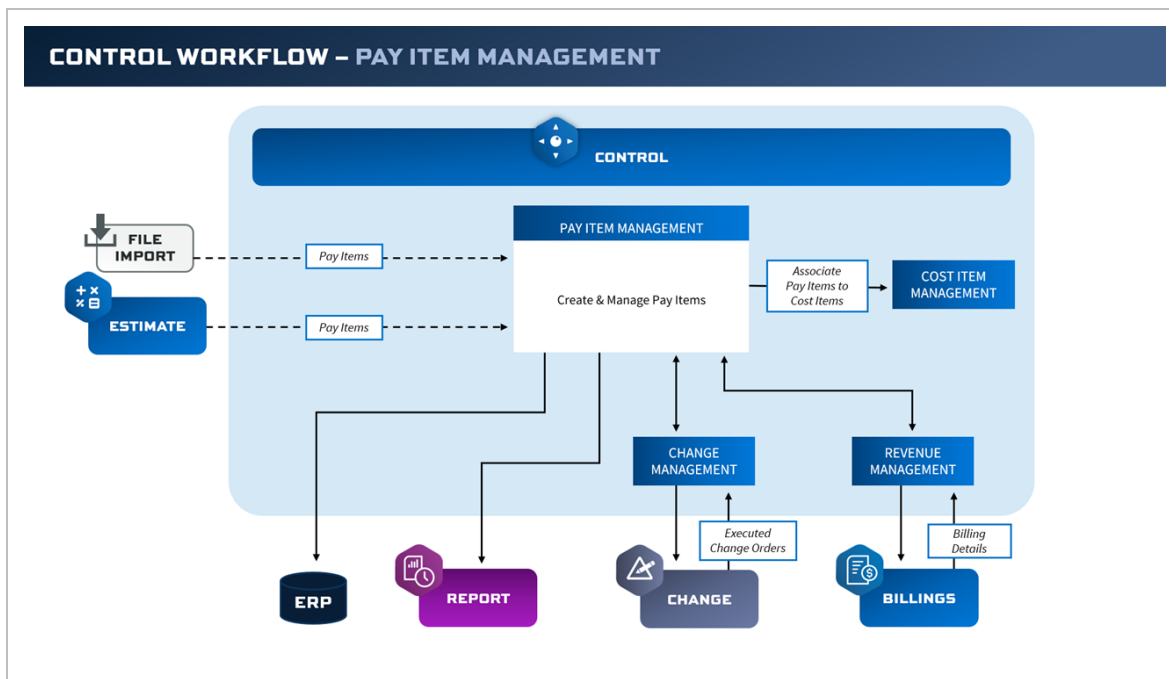


9.4 PAY ITEM DETAILS

Open and manage the details of a pay item by clicking the ellipses next to the pay item description. The pay item options that show are:

- Insert pay item
- Delete pay item(s)
- Pay item details
- Billed revenue details


Click **Pay item details** to open the Pay item details slide-out panel.

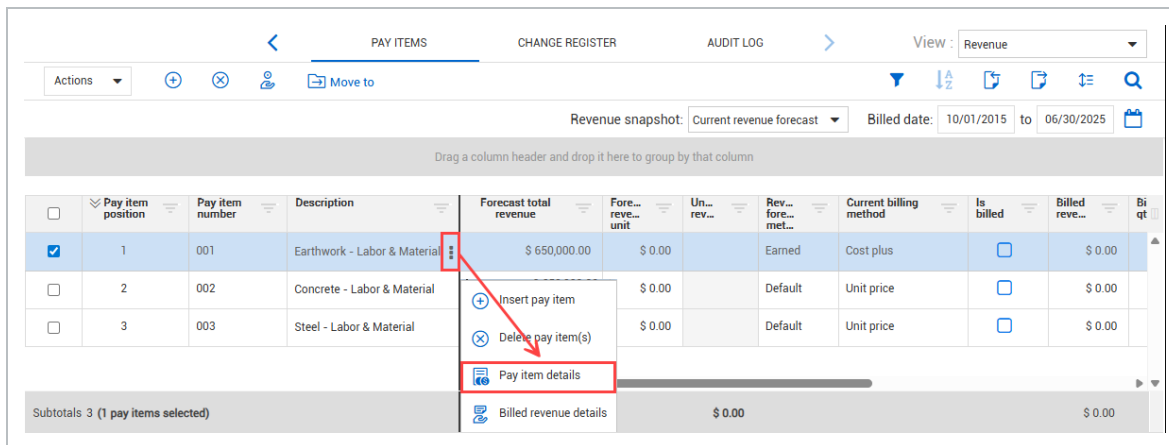

	Pay item position	Pay item number	Description	Forecast total revenue	Fore... reve... unit	Un... rev...	Rev... fore... met...	Current billing method	Is billed	Billed reve...	Bi qt
☒	1	001	Earthwork - Labor & Material	\$ 650,000.00	\$ 0.00		Earned	Cost plus	☐	\$ 0.00	
☐	2	002	Concrete - Labor & Material		\$ 0.00		Default	Unit price	☐	\$ 0.00	
☐	3	003	Steel - Labor & Material		\$ 0.00		Default	Unit price	☐	\$ 0.00	
Subtotals 3 (1 pay items selected)					\$ 0.00					\$ 0.00	

You can also right-click on a pay item to open the slide-out panel to manage the pay item. The pay item's right-click menu includes two additional options:

- Bill multiple pay items
- Actual revenue details

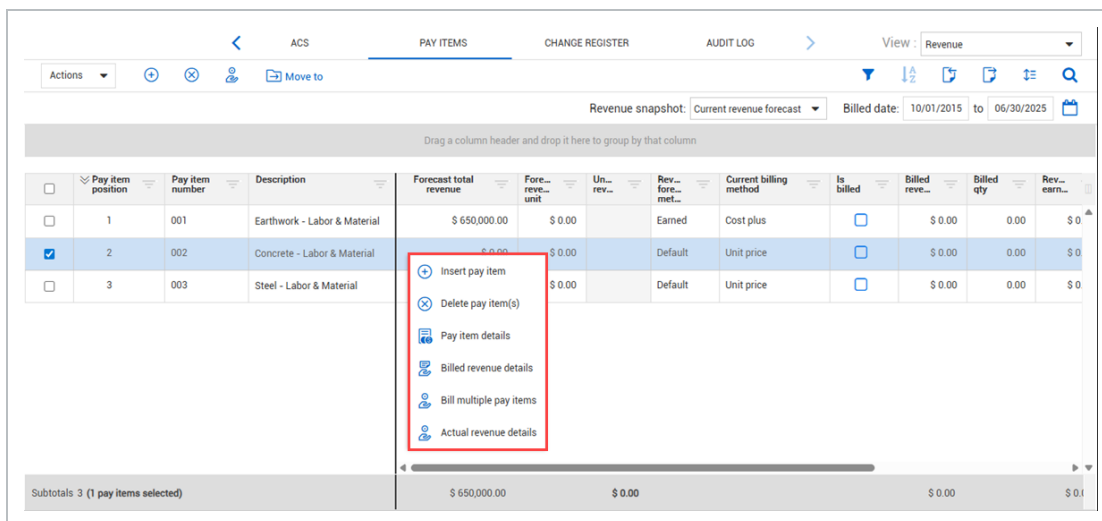

	Pay item position	Pay item number	Description	Forecast total revenue	Fore... reve... unit	Un... rev...	Rev... fore... met...	Current billing method	Is billed	Billed reve...	Billed qty	Rev... earn...
☐	1	001	Earthwork - Labor & Material	\$ 650,000.00	\$ 0.00		Earned	Cost plus	☐	\$ 0.00	0.00	\$ 0
☒	2	002	Concrete - Labor & Material		\$ 0.00		Default	Unit price	☐	\$ 0.00	0.00	\$ 0
☐	3	003	Steel - Labor & Material		\$ 0.00		Default	Unit price	☐	\$ 0.00	0.00	\$ 0
Subtotals 3 (1 pay items selected)				\$ 650,000.00	\$ 0.00					\$ 0.00		\$ 0

Select **Pay item details** to open the pay item slide-out panel.

9.4.1 Pay item details slide-out panel

You can find pay item details in the following tabs:

- Details
- Attributes
- Change orders

- Cost items
- Cost categories

2 - 002

Concrete - Labor & Material

Pay item position	Current price	Current pay qty	Current unit price	Current billing method
2	\$ 2,919,020.71	1.00	\$ 2,919,020.71	Unit price

DETAILS

ATTRIBUTES

CHANGE ORDERS

COST ITEMS

COST CATEGORIES

* Pay Item number

002

Line number

2

Sales order

Description

Concrete - Labor & Material

473

9.4.2 Details Tab

The Details tab is the first tab in the Pay item details. This is where you can view the details for the pay item such as Total Price, Pay Quantity, and Unit Price. You can also make changes to fields, such as Pay Item number, Line number, and Description.

1 - 1

Concrete

Pay item position	Current price	Current pay qty	Current unit price	Current billing method
1	\$ 100,000.00	1.00	\$ 100,000.00	Fixed final price

DETAILS

ATTRIBUTES

CHANGE ORDERS

COST ITEMS

COST CATEGORIES

* Pay Item number

1

Line number

1

Sales order

Description

Concrete

492

Original billing method

Fixed final price

Current billing method

Fixed final price

9.4.3 Attributes Tab

In the Attributes tab, you can associate specific tags to the pay item or define field values. With the applicable permissions, you can change the label names and configure drop-down list values in InEight Platform.

DETAILS

ATTRIBUTES

CHANGE ORDERS

COST ITEMS

COST CATEGORIES

Pay item tag 1	Pay item tag 2	Pay item tag 3
Pay item tag 4	Pay item tag 5	Pay item tag 6
Pay item tag 7	Pay item tag 8	Pay item tag 9
Pay item tag 10	Pay item user defined 1	Pay item user defined 2
Pay item user defined 3	Pay item user defined 4	Pay item user defined 5
Pay item user defined 6	Pay item user defined 7	Pay item user defined 8
Pay item user defined 9	Pay item user defined 10	

To update the label names, go to Main menu > Suite administration > **Custom labels**, and then click inside a field in the Custom label column to rename the label.

Suite administration / Custom labels

Enable custom labels

	Field name ↓	Custom label - EN	Custom label - ES	Custom
☐	Pay item user defined 9	Pay item user defined 9	Pay item user defined 9	Pay ite
☐	Pay item user defined 8	Pay item user defined 8	Pay item user defined 8	Pay ite
☐	Pay item user defined 7	Pay item user defined 7	Pay item user defined 7	Pay ite
☐	Pay item user defined 6	Pay item user defined 6	Pay item user defined 6	Pay ite
☐	Pay item user defined 5	Pay item user defined 5	Pay item user defined 5	Pay ite
☐	Pay item user defined 4	Pay item user defined 4	Pay item user defined 4	Pay ite
☐	Pay item user defined 3	Pay item user defined 3	Pay item user defined 3	Pay ite
☐	Pay item user defined 2	Pay item user defined 2	Pay item user defined 2	Pay ite
☐	Pay item user defined 10	Pay item user defined 10	Pay item user defined 10	Pay ite
☐	Pay item user defined 1	Pay item user defined 1	Pay item user defined 1	Pay ite
☒	Pay item tag 9	Discipline	Pay item tag 9	Pay ite
☐	Pay item tag 8	Pay item tag 8	Pay item tag 8	Pay ite
☐	Pay item tag 7	Pay item tag 7	Pay item tag 7	Pay ite
☐	Pay item tag 6	Pay item tag 6	Pay item tag 6	Pay ite
☐	Pay item tag 5	Pay item tag 5	Pay item tag 5	Pay ite
☐	Pay item tag 4	Pay item tag 4	Pay item tag 4	Pay ite
☐	Pay item tag 3	Pay item tag 3	Pay item tag 3	Pay ite
☐	Pay item tag 2	Pay item tag 2	Pay item tag 2	Pay ite
☐	Pay item tag 10	Pay item tag 10	Pay item tag 10	Pay ite
☐	Pay item tag 1	Pay item tag 1	Pay item tag 1	Pay ite

To update the label values, in the project, go to Settings > **Custom Lists**, and then click the Field values link. In the Field value slide-out panel, enter the custom field values, and then click the **Add** icon.

Steel Structure Training Job 3 | 105093 / Settings

GLOBAL OPTIONSHOME PAGEFISCAL CALENDARFUEL TYPESCUSTOM LISTSMENU OPTIONS

	List name	Label name	Associated entity	Field values	Inherited from parent org
☐	CBS tag 19	CBS tag 19	Cost breakdown structure	None	No
☐	CBS tag 21	CBS tag 21	Cost breakdown structure	None	No
☐	CBS tag 22	CBS tag 22	Cost breakdown structure	None	No
☐	CBS tag 23	CBS tag 23	Cost breakdown structure	None	No
☐	CBS tag 24	CBS tag 24	Cost breakdown structure	None	No
☐	CBS tag 25	CBS tag 25	Cost breakdown structure	None	No
☐	CBS URL 1	CBS URL 1	Cost breakdown structure	URL	No
☐	CBS URL 2	CBS URL 2	Cost breakdown structure	URL	No
☐	CBS URL 3	CBS URL 3	Cost breakdown structure	URL	No
☐	CBS URL 4	CBS URL 4	Cost breakdown structure	URL	No
☐	CBS URL 5	CBS URL 5	Cost breakdown structure	URL	No
☐	CBS URL 6	CBS URL 6	Cost breakdown structure	URL	Yes
☐	CBS URL 7	CBS URL 7	Cost breakdown structure	URL	Yes
☐	CBS URL 8	CBS URL 8	Cost breakdown structure	URL	Yes
☐	CBS tag 13	CBS tag 13	Cost breakdown structure	None	No
☐	CBS tag 14	CBS tag 14	Cost breakdown structure	None	No
☐	CBS tag 3	CBS tag 3	Cost breakdown structure	None	No
☐	Estimating resources ...	Estimating resources ...	Estimating resources	None	No
☐	Estimating resources ...	Estimating resources ...	Estimating resources	None	No
☐	Estimating resources ...	Estimating resources ...	Estimating resources	None	No
☐	Pay item tag 1	Pay item tag 1	Pay item	None	No
☐	Pay item tag 2	Pay item tag 2	Pay item	None	No
☐	Pay item tag 3	Pay item tag 3	Pay item	None	No
☐	Pay item tag 4	Pay item tag 4	Pay item	None	No
☐	Pay item tag 5	Pay item tag 5	Pay item	None	No
☐	Pay item tag 6	Pay item tag 6	Pay item	None	No
☐	Pay item tag 7	Pay item tag 7	Pay item	None	No
☐	Pay item tag 8	Pay item tag 8	Pay item	None	No
☒	Pay item tag 9	Discipline	Pay item	None	No
☐	Pay item tag 10	Pay item tag 10	Pay item	None	No

Pay item tag 9 field values

Description

Concrete

☐ Design engineering

Cancel

Save

Click **Save** to save the list.

9.4.4 Change Orders

The Change Orders tab shows all change orders associated with the selected pay item.

4 - 4
Design

Pay item position

Current price

Current pay qty

Current unit price

Current billing method

4

\$ 44,783,000.00

44,783,000.00

\$ 1.00

Unit price

DETAILS

ATTRIBUTES

CHANGE ORDERS

COST ITEMS

COST CATEGORIES

Change order number	CCO	Issue #	Total price change	Total unit price change	Total pay qty change	Approval probability	Adj for rev
28.1	1184	179	\$ 0.00	\$ 0.00		100.00 %	
28.0	1184	179	\$ 0.00	\$ 0.00		0.00 %	
27.1	1128	89	\$ 0.00	\$ 0.00		100.00 %	
27.0	1128	89	\$ 0.00	\$ 0.00		0.00 %	

9.4.5 Cost Items

The Cost Items tab shows the cost items that are assigned to the selected pay item. In this example there are multiple cost items assigned to the 2-002 Concrete – Labor & Material pay item.

2 - 002

Concrete - Labor & Material

Pay item position

Current price

Current pay qty

Current unit price

Current billing method

2

\$ 2,919,020.71

1.00

\$ 2,919,020.71

Unit price

DETAILS

ATTRIBUTES

CHANGE ORDERS

COST ITEMS

COST CATEGORIES

Earnings amounts based on:

☐ Forecast (T/O) qty
 ☒ CE total cost

Update earning rules

CBS Position	Description	WBS Phase Code	Earning %	Earning Amount (Forecast)
4.1	Erect Steel - Heavy	1074	42.83 %	\$ 0.00
5.2	Concrete - Materials	1086	53.54 %	\$ 0.00
4.3	Bolted Connections	1006	0.00 %	\$ 0.00
3	Concrete	1071	0.00 %	\$ 0.00
3.1.8	Building N&O - Scrape an...	1099	0.00 %	\$ 0.00
3.1.7	Concrete - Building N&O	1098	0.00 %	\$ 0.00

In Cost Items, you can view and update the earning rules for all associated cost items. Click the **Update earning rules** button at the top right of the tab to open the earning rules window. You can adjust the earning rules by Earning % and Earnings Timing. For more information, see [Earning Rules](#).

9.4.6 Cost Categories

The Cost Categories tab shows a cost category-level breakdown of costs for cost items assigned to that pay item, along with related forecast, earned, and billed revenue information. The Cost Categories tab is a quick way to see where you have cost and revenue as well as where you have revenue at the pay item level for the pay item at the cost category level. The different fields represent the different billing methods that are available currently.

	DETAILS	ATTRIBUTES	CHANGE ORDERS	COST ITEMS	COST CATEGORIES
Cost category	Forecast final revenue	Revenue earned	Billed revenue	Markup amount	Total cost (to date)
^ Total	\$ 15,000.00	\$ 7,500.00	\$ 2,000.00	\$ 1,000.00	\$ 900.00
v Labor			\$ 1,000.00		\$ 100.00
v Constructio...			\$ 0.00		\$ 0.00
v FOM Rente...			\$ 0.00		\$ 0.00
v Supplies			\$ 0.00		\$ 0.00
v Materials			\$ 0.00		\$ 0.00
v Subcontract			\$ 0.00		\$ 500.00
v Fees			\$ 0.00		\$ 300.00
v Allowance			\$ 0.00		\$ 0.00
G & A			\$ 0.00		\$ 0.00

Forecast final revenue, Revenue earned, and Markup amount columns only show at the totals level of the cost categories.

Forecast final revenue and Revenue earned columns show the information that is pulled from the pay item's register.

The Total cost (to date) column refers to the costs you incur when you perform the work and breaks down the information from the cost items assigned to the pay based on where you claimed the cost for those items.

The Markup amount column calculates the difference between your total price and your agreed upon current budget cost for those assigned cost items. The markup amount uses the calculation Total price on the pay item - sum of the CB total cost on the assigned cost items.

9.5 CREATING AND LOCKING PAY ITEMS

When setting up your project, you can manually create pay items or quickly import your pay items by uploading them from a Microsoft Excel spreadsheet.

Upload pay items from a Microsoft Excel spreadsheet

1. In the Actions menu, select the **upload** icon to upload the Excel spreadsheet.
2. Drag and drop your Microsoft Excel spreadsheet or select browse to upload it.
3. Select the **New import** option.

4. After the spreadsheet is uploaded, choose the columns you want to see.

9.5.0.1 Adding Pay Item details

Because the project has not started, pricing is unlocked. This means you can:

- Add new pay items
- Enter price and quantity for each item.

When you are done adding details, your pay items show the current values that were entered.

9.5.0.2 Locking in your pricing

After you are done with your list and ready to move forward, lock in your pricing. To lock pricing select Actions > Lock/unlock price > **Lock price**. This saves the changes as the original pricing for the project. If you are not ready to lock all items, you can also select the individual pay items and lock or unlock them from the Actions menu.

After the pricing is locked on a pay item, the pay item's price can only be edited through a contract adjustment.

Partial locking is available. When set, you can add pay items at any time during the project life cycle, and you can lock each pay item individually after you enter the price is entered for that pay item.

9.6 BILLING METHODS

There are three billing methods to choose from:

- Fixed final price
- Unit price
- Cost Plus

Steel

Actions

Pay item

1

2

☒ 3

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

View : Price

Revenue snapshot: Current revenue forecast

Billed date: 10/01/20... to 03/07/20...

3 - 003

Steel - Labor & Material

Pay item position

3

Current price

\$ 1,821,092.28

Current pay qty

1.00

Current unit price

\$ 1,821,092.28

Current billing method

Cost plus

DETAILS

ATTRIBUTES

CHANGE ORDERS

COST ITEMS

COST CATEGORIES

* Pay Item number

003

Line number

3

Sales order

Description

Steel - Labor & Material

476

Original billing method

Unit price

Original price

Original pay qty

Original unit price

Original forecast (T/O) qty

UoM (Unit of measure)

Current billing method

Cost plus

Fixed final price

Unit price

Cost plus

Current pay qty

1.00

Current unit price

\$ 1,821,092.28

Current forecast (T/O) qty

0.00

☐ Is billed

Subtotals 3 (1 pay item)

9.6.1 Fixed final price

The fixed final price method is a lump sum billing method, which is a price agreed upon by a contractor and a client. The fixed final price can change only with a contract change order.

The Forecast total revenue for fixed final price is calculated as *Current Price + [sum of Unapproved changes × Approval probability %]*.

9.6.2 Unit price

The unit price method is the default billing method which bills per unit. The price method multiplies the unit price by the pay quantity to calculate the total price. For example, you can submit an estimate where 44,000 units of an item are needed to complete the job. At the completion of the job, you are paid per unit installed. If only 40,000 units of that item are actually installed, you only get paid for 40,000 units of that item.

The Forecast total revenue for unit price is calculated as *Unit Price × Forecast (T/O) qty*.

9.6.3 Cost Plus

With the cost plus billing method, the contractor is paid based on an hourly billing rate agreed upon with the client, consisting of labor, equipment, or material costs, plus markup. In addition, you can include a markup on top of the billing rate if needed. Cost Plus billing method adds flexibility throughout the project since change orders are not required when you need to change markup, resource rates, quantities, and hours as the job progresses. You do not have a contractual agreement to be paid a certain lump sum.

The InEight Estimate pay items designated with the time and expense pay method become cost plus pay items in Control when the estimate is published to Control.

In the Project library, you can define the billing rate (that includes a markup) and/or a charge rate (that adds an additional markup) to an estimate resource on the Resource Rates tab. The billing and charge rate markup are used only when the Cost Plus billing method is used in a pay item.

Cost Plus pay items are mostly resource driven.

Steel Structure Training Job 3 | 105093 / Control / Project library

ESTIMATE RESOURCES

REVENUE

		Resource code	Description	Default Quanti...	Unit of m...	Utiliza... count	C E-unit cost (Scale...	Cost driver	Account code	Amount per period
Labor										
Construction equipment	☒	1.C.01.1.05	Laborer	0.00	Hour	6,381.82	135.00	Cl Duration		
Rented construction equipment										
Installed material										
Installed equipment										
Supplies										
Unique										

✕

✕

Edit labor estimate resource

• Code

1.C.01.1.05

• Description

Laborer

1000

SETUP

RESOURCE RATES


▼ Allowance	\$ 0.00	\$ 0.00	\$ 0.00
G & A	\$ 0.00	\$ 0.00	\$ 0.00
Undefined	\$ 0.00	\$ 0.00	\$ 0.00
Billing rate	\$ 35.00	\$ 30.00	\$ 40.00
Billing rate markup	\$ 0.00	\$ 0.00	\$ 0.00
Billing rate markup %	0.00 %	0.00 %	0.00 %
Charge rate	\$ 38.50	\$ 30.00	\$ 40.00
Markup amount	\$ 3.50	\$ 0.00	\$ 0.00
Markup %	10.00 %	0.00 %	0.00 %

Cancel

Save

- **Billing rate** - Rates agreed upon with the client.
- **Charge rate** - Add additional markup to your pay items. The charge rates are not visible to the client.

You can setup markup percentage values at the project level in the project settings Markup section of the Revenue tab for Cost categories and Current estimate resources.

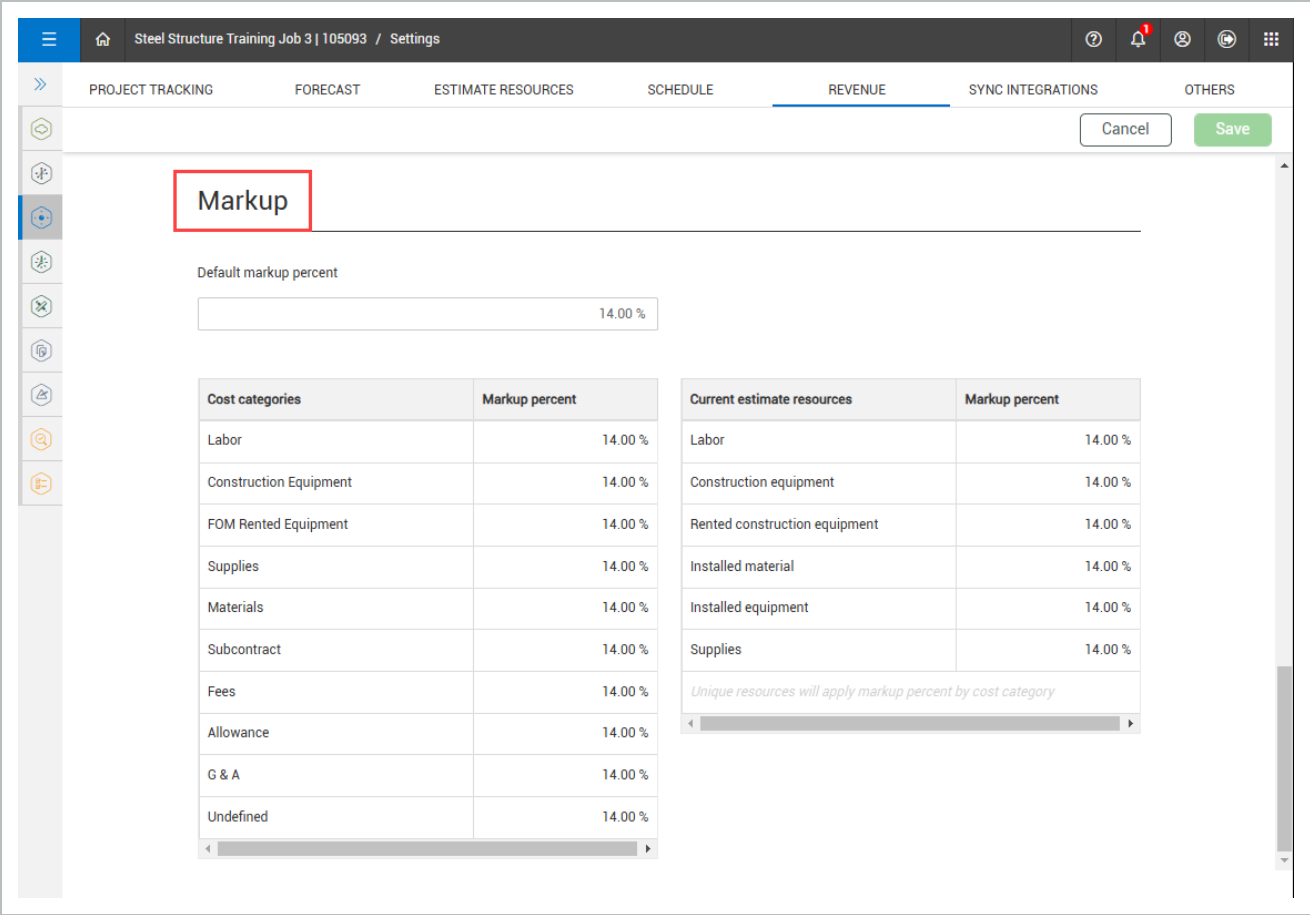

Markups are used only when Cost Plus is selected as the billing method, which drives your revenue. When other billing methods are selected, you only see rates applied to the cost categories that drive your cost.

Markup values are not visible to the client.

You can use the two tables in the Markup section of the **Revenue** tab to enter markup percentages against cost category levels and resource levels. The revenue amounts automatically calculate.

- **Cost category level markups** – These markups are for plug cost items that are not resource driven. You can view and edit the billing rate in the **Cost item details** slide-out, under the **Cost**

categories tab.

1071
Concrete

DETAILS

ATTRIBUTES

COST CATEGORIES

CURRENT ESTIMATE
RESOURCES

FORECAST RESOURCES

% complete

⊕ Live forecast method

Latest actuals in forecast values

100.00 %

Current estimate

🕒 02/28/2025

Total

Per unit

Cost category	Current estimate	Billing rate markup amount	CE billable amount	Markup %	Markup amount	CE revenue amount
^ Total	\$ 1,500,000.00	\$ 0.00	\$ 1,500,000.00	0.00%	\$ 0.00	\$ 1,500,000.00
v Labor	\$ 1,500,000.00	\$ 0.00	\$ 1,500,000.00	0.00%	\$ 0.00	\$ 1,500,000.00
v Construction...	\$ 0.00	\$ 0.00	\$ 0.00	0.00%	\$ 0.00	\$ 0.00
v FOM Rented ...	\$ 0.00	\$ 0.00	\$ 0.00	0.00%	\$ 0.00	\$ 0.00
v Supplies	\$ 0.00	\$ 0.00	\$ 0.00	0.00%	\$ 0.00	\$ 0.00
v Materials	\$ 0.00	\$ 0.00	\$ 0.00	0.00%	\$ 0.00	\$ 0.00
v Subcontract	\$ 0.00	\$ 0.00	\$ 0.00	0.00%	\$ 0.00	\$ 0.00
v Fees	\$ 0.00	\$ 0.00	\$ 0.00	0.00%	\$ 0.00	\$ 0.00
v Allowance	\$ 0.00	\$ 0.00	\$ 0.00	0.00%	\$ 0.00	\$ 0.00
G & A	\$ 0.00	\$ 0.00	\$ 0.00	0.00%	\$ 0.00	\$ 0.00

- **Resource category level markups** – These markups are for cost items with a cost source of Detail. You can view the billing rates in the Cost item details slide-out panel, **Current Estimate Resources** or **Forecast Resources** (depending on your project setup). In the Current estimate

resources section, select a resource, and then open the **Resource details** section.

1091
Bolted Connections

DETAILSATTRIBUTESCOST CATEGORIESCURRENT ESTIMATE RESOURCESFORECAST RESOURCES

When updating the quantity of duration driven labor resources

☒ Proportionally update Units\Man hours
☐ Proportionally update Hours

Resource details

1.C.05.1.04
Ironworker Apprentice

Cost category	Scale 1 unit cost	Scale 2 unit cost	Scale 3 unit cost
▼ Total	\$ 45.00	\$ 45.00	\$ 60.00
Billing rate	\$ 45.00	\$ 45.00	\$ 60.00
Billing rate markup	\$ 0.00	\$ 0.00	\$ 0.00
Billing rate markup %	0.00 %	0.00 %	0.00 %
Charge rate	\$ 45.00	\$ 45.00	\$ 60.00
Markup amount	\$ 0.00	\$ 0.00	\$ 0.00
Markup %	0.00 %	0.00 %	0.00 %

At the pay item level, you can see the total revenue for the pay item, based on the resource billing rates and markup of the cost items that are assigned to each pay item.

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

View : Revenue

Actions

Move to

Revenue snapshot: Current revenue forecast

Billed date: 02/26/2025 to 03/19/2025

Drag a column header and drop it here to group by that column


☐	Pay item position	Pay item number		Forecast total revenue	Forecast revenue unit cost	Unapproved revenue	Revenue forecast method	Current billing method	Is billed	Billed revenue	Billed qty
			U...	\$ 100.000000000000		\$ 100.00					
☐	1	LNT P1 Part 1	L...	\$ 100.000000000000	\$ 100.00	\$ 100.00	Billed	Cost plus	☒	\$ 0.00	0.00000000...
☐	2	005.006		\$ 0.000000000000	\$ 0.00		Default	Fixed final price	☒	\$ 10.00	0.00000000...
☐	3	005.0678		\$ 0.000000000000	\$ 0.00		Default	Fixed final price	☒	\$ 20.00	0.00000000...
☐	4	005.678		\$ 0.000000000000	\$ 0.00		Default	Fixed final price	☒	\$ 30.00	0.00000000...
☐	5	LNT P1 Part 1...	L...	\$ 0.000000000000	\$ 0.00	\$ 0.00	Billed	Cost plus	☐	\$ 0.00	0.00000000...
☐	6	LNT P1 Part 2	L...	\$ 0.000000000000	\$ 0.00	\$ 0.00	Billed	Cost plus	☐	\$ 0.00	0.00000000...
☐	7	4	B...	\$ 100.000000000000	\$ 100.00	\$ 4,253,292.55	Billed	Cost plus	☒	\$ 100.00	0.00000000...
Subtotals 7				\$ 300.000000000000		\$ 4,253,492.55				\$ 160.00	

The rates can be updated in the Cost item details slide-out, in the **Cost categories** tab, and in the **Current Estimate Resources** or **Forecast Resources** (depending on your project setup) in the CBS.

9.7 BULK IMPORT PAY ITEMS

You can import pay items in mass directly into the Pay Item and Proposal register, similar to how cost items can be imported directly into the CBS.

You can access the Excel import feature by clicking on the Import icon on the far right toolbar of Control > Workspaces > Pay Items.

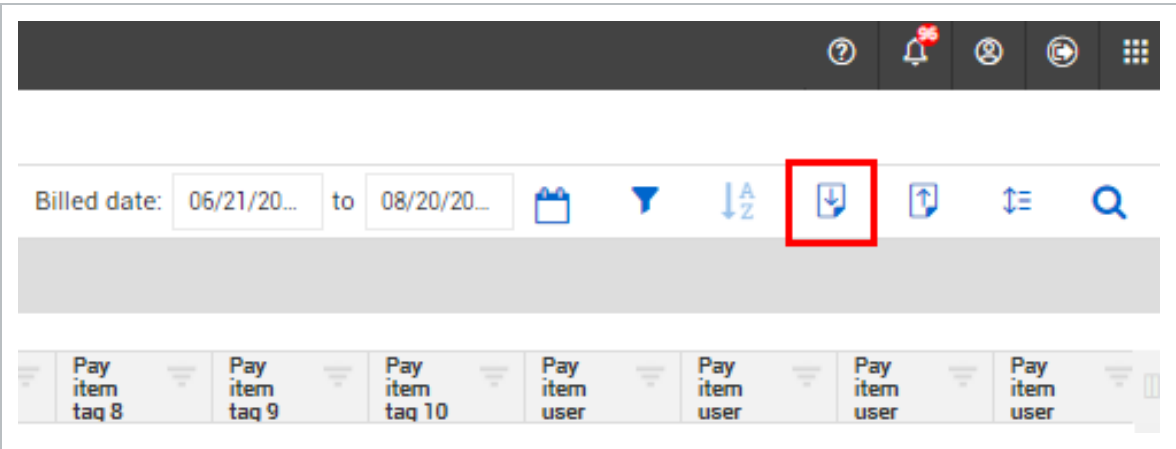

When you click on the Import icon within the Pay Items tab of the Workspaces page, the Import Pay Items window is shown.

Overview - Import Pay Items window

	Title	Description
1	Import from Excel	You can either drag and drop or browse to the file to import. Microsoft Excel files (.xlsx, .xls) and Comma Separated Value (.csv) files can be imported.
2	Import Type	You can add new pay items into the Pay Item and Proposal register.
3	Information message	Explains that once an import file is specified, the next step will allow you to match the columns in your spreadsheet to the appropriate columns in Control.

Import Pay items

1

Import from Excel (.xlsx, .xls) or Comma separated value (.csv)

Drag and drop the file here
or browse

Browse

Options

2

* Import type

Pay Items

☒ New import

3

i The import file is read and field mapping can be specified. Mapping uses row 1 headers from the source document

Cancel

Next

Clicking Next brings you to the Map columns window, where you can map your Excel columns to the applicable column in Control.

Overview - Map Columns Window

Title		Description
1	Template	After you map the import file columns to the Pay Item columns in Control, you can save your settings as a template for future use. This is helpful when you need to make scope changes or updates on a regular basis.
2	Control field	The names of the column headers in Control that you can map your data to.
3	Mapped	A green checkmark indicates the column in your import file is mapped correctly to the Pay Item's column. The Green key indicates the matching code you specified is locked.
4	File columns	The names of the column headers in your import file that you can map to the pay item columns in Control.

Import Pay items - payItems.csv

Map columns

1

Template

Unsaved template

2

Control field

Pay items

Current billing method

Current forecast t/o qty

Current pay qty

Current price

Current unit price

Description

Line number

* Pay item number

Pay item tag 1

3

Mapped

✓

✓

✓

🔍

4

File columns

Blank-do not import

Current forecast (T/O) qty

Blank-do not import

Current price

Blank-do not import

Description

Blank-do not import

Pay item number

Blank-do not import

✎

✖

* Required fields

Reset

Cancel

Back

Next

9.7.1 Spreadsheet Rules

For the import to work correctly, the items in your Excel spreadsheet need to be formatted in a certain way so that Control can recognize them. The following table indicates important spreadsheet rules to follow to make sure your data imports successfully:


Attribute	Rules
Import function	Reads the first worksheet within the referenced workbook. Stops the import process when a blank row is encountered, so consolidating the data to be imported is required.
First row of data	This is the header row of the data. This becomes the titles that are referenced during the mapping process. During import, headers are not read if a blank header cell is encountered.

Attribute	Rules
Numbers	Need to be the actual number, not the summation of cells. Cannot contain the \$ or other currency symbol.

Second row of data This is the first row of data import.

If you make changes in the spreadsheet, you must save the spreadsheet before importing. Only saved data are imported.

After clicking the Next button, the system reads your Excel file and attempts to import pay items. A successful import shows a message stating the number of files to be imported.

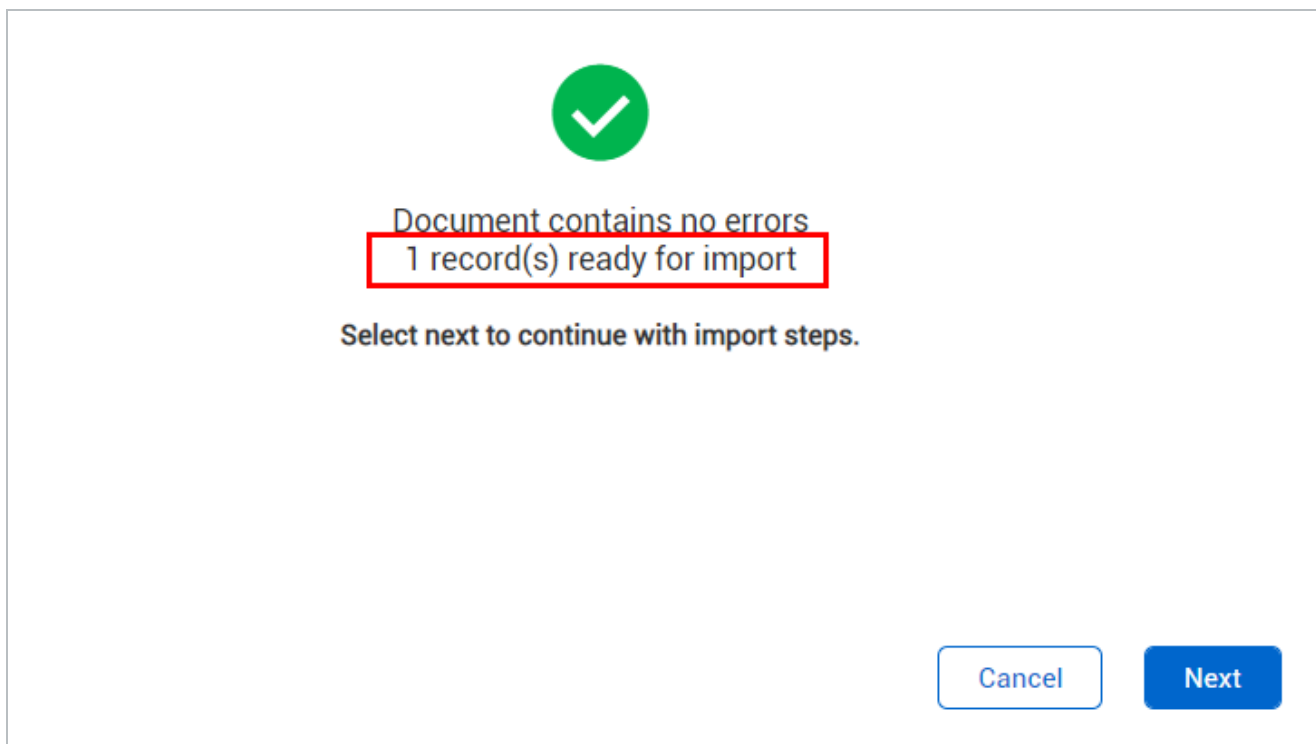

If the import is not successful, a message is shown stating that errors exist. An error file is provided for you to download, review, make corrections to your Excel file, then eventually continue with the pay item import again.



1 of 1 records contain errors

No Pay Items were imported. Multiple errors found in pay item import.

Download the error file to review and resolve errors.
Once all errors have been resolved, reattempt import.

CloseDownload Error File

The import error download file shows exactly where the error(s) exist within the Excel file.

```
|PayItem from External System  
File Import attempted on: 8/20/2021 7:43:46 PM
```

```
The following errors were detected while attempting to import pay item  
values into control.
```

```
Review the errors below, once all the errors have been resolved,  
reattempt the import to Control.
```

```
Error 1: Current unit price must be a numeric value for pay item number  
5. (this error has 1/1 total rows affected)
```

```
Pay Item Number: 5  
Row: 1
```

9.8 MARKUP PERCENT

In your project you can apply markup percentages to current estimate values of specific types of work and have the revenue amount automatically calculated.

There are two tables under the Revenue tab of Control project settings where you can enter the markup percentages against cost categories and Estimate resource types. For more information, see [Markup](#) in Settings.

The markup percent applies a percentage to the current estimate rates to arrive at markup amounts, and the CE revenue amount takes into consideration all markups. Control then calculates an estimated revenue amount for the cost items. This is possible whether that cost item uses resources or plug values to calculate the current estimate values.

The revenue amounts update the Forecast final revenue for Cost plus type pay items. Then, the Cost plus type pay items are used to calculate the values for the following columns in the CBS:


- Forecast total revenue
- Forecast remaining revenue
- Forecast revenue earned
- Forecast revenue unit cost
- Forecast total margin
- Forecast % margin

The pay item calculations are only applicable when the cost items are associated to a Cost Plus type of pay item.

The default markup percentages populate columns in the Estimate resource library and the Control CBS, such as the columns in the following table:

Column location	Column name
Estimate resources	Resource markup %
	Resource markup amount
	Charge rate
CBS - Cost item details slide out - Cost categories tab	Markup %
	Markup amount
	CE revenue amount

You can view this information from Markup columns such as Billing rate markup amount, CE billable amount, Markup %, Markup amount, and CE revenue amount.

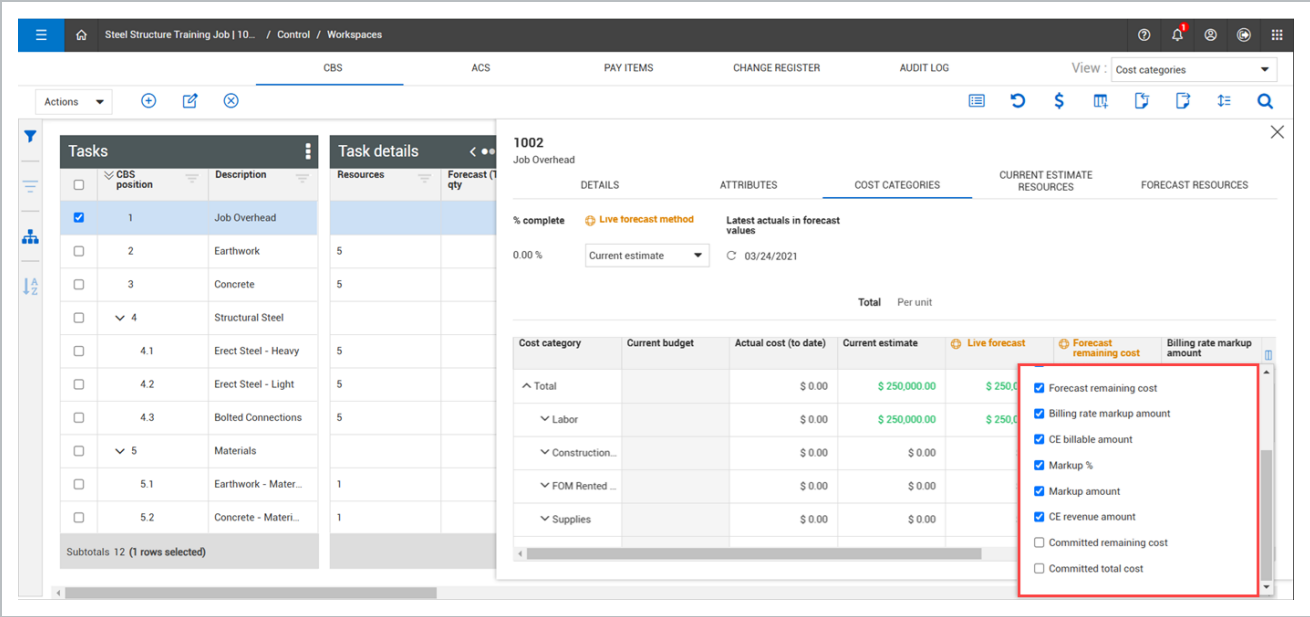

The following table shows markup column information in the Cost categories tab of the Cost item details slide out.

Column	Formula
CE billable amount	Current estimate amount + your Billing rate markup amount = CE billable amount
Markup amount	Markup percent × your current estimate = markup amount - The Billing rate markup amount for plug cost items is always set to zero because you can only have a billing rate on resources. When this is a detailed cost item, this will shows your billing rate markup amount for all those resources.
CE revenue amount	CE billable amount + your Markup amount = CE revenue amount - The CE revenue amount is how much revenue a cost item can have. This is only applicable for cost plus pay items. You can apply markups on cost items, and they do not affect the revenue on those cost items. The markups affect the revenue for cost plus pay items and any cost items that are assigned to cost plus pay items.

9.8.1 Markup % column

The Markup % column is available in the CBS register to quickly manage markup percentages for cost items associated to pay items that use the billing methods Cost plus and Time and Material. In the

Markup % column, you can:

- Enter markup percentages directly into the field.
- Update individual or multiple cost items.
- Copy and paste values across multiple rows.

RELEVANT LINKS

Link 1

Link 2

Link 3

Link 4

Link 5

9.9 EARNING RULES

On the Cost Items tab the **Update earning rules** icon updates the earning rules for all associated cost items. For each cost item associated to a pay item, you can adjust the earning rules by Earning % and Earnings Timing. The Earnings timing indicates when you can earn revenue for a specific cost item associated to a pay item. You can select from the following earnings timing options:

- **Percent complete** – You will earn revenue based on the % complete of the cost item
- **Start** – You will earn all the revenue when the work of the cost item is started (e.g., Mobilization)
- **Finish** – You will not earn any revenue for the cost item until all the work is completed (e.g., QC item)

Pay item ID

002

Description

Concrete - Labor & Material

Total Price

\$2,919,020.71

CBS Position	Description	Earning %	Earning Amount (Forecast)	Earnings Timing	WBS Phase Code
5.2	Concrete - Materials	25.00 %	\$ 729,755.18	Percent complete	1086
3	Concrete	75.00 %	\$ 2,189,265.53		1071
		100.00 %	\$2,919,020.71		

☒ Default Earning Rules

Cancel

Save

In this case for your Structural Steel Project, cost item 3 has an earning rule that equals 75% of the Earning Amount (Forecast) of the pay item's final revenue. Respectively, cost item 5.2 has an earning rule of 25% of the Earning Amount (Forecast).

Since the Total Price of this pay item is \$2,919,020.71, it is expected that cost item 3 will earn 75% of this amount, and cost item 5.2 will earn 25%.

CBS Position	Description	Earning %	Earning Amount (Forecast)	Earnings Timing	WBS Phase Code
5.2	Concrete - Materials	25.00 %	\$ 729,755.18	Percent complete	1086
3	Concrete	75.00 %	\$ 2,189,265.53	Percent complete	1071
		100.00 %	\$2,919,020.71		

☒ Default Earning Rules

Cancel Save

Billing method of Cost plus

When the billing method of the pay item is set to Cost Plus, then the Update earnings rules option will be disabled. Therefore, the associated cost items of the pay item will earn revenue based on the assigned estimate resources' billing rates and the % complete of the cost item.

Adjusting Pay Item Earning Rules

1. On the Pay Items tab, select a pay item.
2. Hover over to the right of the Description and click on the **three black dots**.
3. Select **Pay item details**.
4. Select the **Cost Items** tab.
5. Click the **Update earning rules** icon.
6. Change the Earning % percentages for each associated cost item so the total will equal 100%..
7. Click **Save**.

9.10 BILLED REVENUE

You can track revenue for your cost items in the Billed revenue details panel. The timing and basis for billing revenue varies depending on your contractual agreement. Options include billing by a time period or milestone, or based on a schedule.

The Billed revenue details slide-out panel records and tracks billed revenue.

002

Concrete - Labor & Material

BILLED

RETENTION

BILLED HISTORY

Pending billable qty	Pending billable revenue	Retainage %
0.18	\$ 530,386.06	0.00 %

Billed revenue

\$ 0.00

Retention withheld: \$ 0.00

Net bill: \$ 0.00

Cost category

Undefined

Billed quantity

0.00

* Billed date

07/08/2025

Cost item

Type a CBS position, Description, or Phase code

Change order

Type a Change order ID or Description

Notes

Notes

250

+ Add billed

Cancel

Apply

In the Billed revenue details slide-out panel you can navigate to the following tabs:

- Billed
- Retention

- Billed History

To open the Billed revenue details slide-out panel, from the Pay Items register, click the ellipses next to the pay item description, and then select **Billed revenue details**. The Billed revenue details slide-out panel opens, where you can record and track what you bill to the client.

Steel Structure Training Job 2 | 1050... / Control / Workspaces

CBSACS**PAY ITEMS**CHANGE REGISTERAUDIT LOGView: Unsaved (Revenue)

ActionsMove to

Revenue snapshot: Current revenue forecastBilled date: 10/01/2015 to 07/08/2025

Drag a column header and drop it here to group by that column

☐	Pay item position	Pay item number	Description	Forecast total revenue	Forecast revenue unit cost	Revenue forecast method	Current billing method	Is billed	Billed revenue	Billed qty	Revenue earned	Quantity earned	Pending billable revenue	Pending billable qty	Net billed revenue
☐	1	001	Earthwork - Labor & Material	\$ 799,887.01	\$ 799,887.01	Default	Unit price	☐	\$ 0.00	0.00	\$ 217,444.37	0.29	\$ 217,444.37	0.29	\$ 0.00
☒	2	002	Concrete - Labor & Material	\$ 2,919,020.71	\$ 2,919,020.71	Default	Unit price	☐	\$ 0.00	0.00	\$ 530,386.06	0.18	\$ 530,386.06	0.18	\$ 0.00
☐	3	003	Steel - Labor & Material	01,092.28		Default	Unit price	☐	\$ 0.00	0.00	\$ 321,183.01	0.18	\$ 321,183.01	0.18	\$ 0.00
Subtotals 3 (1 pay items selected)				\$ 5,593,159.69					\$ 0.00		\$ 1,069,013.45		\$ 1,069,013.45		\$ 0.00

Insert pay item

Delete pay item(s)

Pay item details

Billed revenue details

The Billed Revenue Details slide-out panel opens by default to the Billed tab.

9.11 BILLED TAB

On the Billed tab, you can enter information to create a record about what to bill your customer, and view pending billable quantity, and pending billable revenue based on the progress of the cost items associated and their earnings rules. You can also view the retainage percentage associated with the pay item.

002

Concrete - Labor & Material

BILLED

RETENTION

BILLED HISTORY

Pending billable qty	Pending billable revenue	Retainage %
0.18	\$ 530,386.06	0.00 %

Billed revenue

\$ 0.00

☐

Cost category

Undefined

Retention withheld: \$ 0.00

Net bill: \$ 0.00

Billed quantity

0.00

☐

* Billed date

07/08/2025

Cost item

Type a CBS position, Description, or Phase code

Change order

Type a Change order ID or Description

Notes

Notes

250

+ Add billed

Cancel

Apply

9.11.1 Unit price proportional billing

When you bill revenue or quantity for unit price pay items, the billed quantity or revenue automatically adjusts proportionally to the entered billed value to match the unit price.

For example, if the current unit price is \$5,000.00 and the billed quantity is 0.50, then the billed revenue automatically calculates at \$2,500.00.

CBSACS

PAY ITEMSCHANGE REGISTERAUDIT LOG

View: Unsaved (Revenue)

Actions

Revenue snapshot: Current revenue forecastBilled date: 05/14/2025 to 07/09/2025

	Pay item position	Pay item number	Description	Forecast total revenue	Forecast revenue unit cost	Current unit price
☐	362	PS04-033	PS04-033 SOCIAL FPO ...	\$ 0.00	\$ 0.00	\$ 1.00
☒	513	CO-263	CO-263 YARD LIGHTIN...	\$ 0.00	\$ 0.00	\$ 5,000.00
☐	513	CO-263	CO-263 YARD LIGHTIN...	\$ 0.00	\$ 0.00	\$ 5,000.00
☐	417	CO-183	CO-183 M&O FLOORIN...	\$ 0.00	\$ 0.00	\$ 1.00
☐	417	CO-183	CO-183 M&O FLOORIN...	\$ 0.00	\$ 0.00	\$ 1.00
☐	478	CO-233	CO-233 CAT6 ADAPTO...	\$ 0.00	\$ 0.00	\$ 1.00
☐	478	CO-233	CO-233 CAT6 ADAPTO...	\$ 0.00	\$ 0.00	\$ 1.00
☐	488	PS07-045	PS07-045 STRIPING C...	\$ 0.00	\$ 0.00	\$ 1.00
☐	488	PS07-045	PS07-045 STRIPING C...	\$ 0.00	\$ 0.00	\$ 1.00
☐	204	PS07-021	INSTALL AC @ MHS-D...	\$ 0.00	\$ 0.00	\$ 1.00
☐	204	PS07-021	INSTALL AC @ MHS-D...	\$ 0.00	\$ 0.00	\$ 1.00

Subtotals 1068 (1 pay items selected)\$ 4,744,814.75\$ 1

CO-263

CO-263 YARD LIGHTING MATERIAL PROCUREMENT

BILLED

RETENTION

BILLED HISTORY

Pending billable qty

Pending billable revenue

Retainage %

-0.50

(\$ 2,500.00)

0.00 %

Billed revenue

Cost category

\$ 2,500.00

Undefined

Retainage withheld: \$ 0.00

Net bill: \$ 2,500.00

Billed quantity

Billed date

0.50

07/09/2025

Cost item

Change order

Type a CBS position, Description, or Phase code

Type a Change order ID or Description

Cancel

Apply

9.11.1.1 Change Orders

You can associate and view change order cost information on a pay item and additional cost items. When creating a bill in the Billed revenue details slide-out panel or from the Bill multiple pay items option, you can select a change order to assign the billed amount. For more information about using change orders, see [Change orders](#).

Bill for revenue earned

- 1. On the Pay Items tab, click the ellipses next to the pay item description, and then select **Billed revenue details**. The Billed revenue details slide-out opens.
- 2. On the Billed tab, enter any applicable information such as the billed revenue, billed quantity, cost category, cost item, change order, and notes.
- 3. On the Retention tab, select to release withheld retention.

On the Billed History tab, you can review the net billed revenue for the pay item and other pay item history details.

4. Click **Apply**.

You cannot delete a pay item that is billed.

For information about billing multiple pay items, see [Pay item revenue billing in bulk](#).

9.12 RETENTION TAB

On the retention tab, you can release a pay item's full retention amounts. The retention amount shows under Retention withheld at the top of the tab.

The screenshot shows a software window titled "1000 Removal of Underground Storage Tanks" with a close button (X) in the top right corner. The window has three tabs: "BILLED", "RETENTION" (which is selected and highlighted with a red border), and "BILLED HISTORY". Below the tabs, there are two columns of data: "Retention withheld" showing "\$ 937.50" and "Retention released (to date)" showing "\$ 0.00". Below this, there is a section with two input fields: "Retention released" with a value of "\$ 0.00" and a checkbox, and "* Retention released date" with a date of "07/10/2025" and a calendar icon. Below these fields is a "Notes" section with a text area labeled "Notes" and a character count of "250". At the bottom right of the window are two buttons: "Cancel" and "Apply".

To release the retention for a pay item, click the Retention release check box. The retention amount populates automatically in the Retention released field.

1000

Removal of Underground Storage Tanks

BILLED

RETENTION

BILLED HISTORY

Retention withheld

\$ 0.00

Retention released (to date)

\$ 0.00

Retention released

\$ 937.50

☒

* Retention released date

07/10/2025

Notes

Notes

Click to release all retention

250

Cancel

Apply

You can also select a retention release date and add notes about the transaction.

For more information about retention, see [Revenue and cost timing](#) in Control Settings.

9.13 BILLED HISTORY TAB

The Billed History tab shows all billed revenue records for a pay item. You can view billed revenue details such as billed amount, billed date, billed quantity, notes, and change order information under each respective column. You can view, but you cannot edit or delete any information.

Unit price - CE earnings rules

BILLED

RETENTION

BILLED HISTORY

Billed date	Billed qty	Billed	Net billed revenue	Retention withheld	Revenue received
05/14/2025	5.00	\$ 750.00	\$ 500.00	\$ 0.00	
05/14/2025	33.33	\$ 5,000.00	\$ 5,000.00	\$ 0.00	\$
05/14/2025	-33.33	(\$ 5,000.00)	(\$ 5,000.00)	\$ 0.00	

You can also view the same billed history details in the Pay Items register in columns such as Billed revenue, Revenue earned, Billed quantity, and Quantity earned.

9.14 BILLED REVENUE COLUMNS

After you have billed and applied billed revenue and quantities in the Billed revenue details slide-out panel, columns in the Pay Items register are populated with billed revenue values.

The pending amount fields are derived from the quantity earned and revenue earned amounts. Furthermore, the pending amount fields help you identify what has been billed versus what is left to be billed based on what has been completed for your cost items. The Is billed check box shows selected when a pay item has been billed.

You can view the billed revenue data in the following columns:

Steel Structure Training Job 2 | 105092 / Control / Workspaces

ACS PAY ITEMS CHANGE REGISTER AUDIT LOG

View: Unsaved (Revenue)

Revenue snapshot: Current revenue forecast Billed date: 10/01/2015 to 07/09/2025

Drag a column header and drop it here to group by that column

☐	Pay item position	Pay item number	Description	Forecast revenue unit cost	Revenue forecast method	Current billing method	Is billed	Billed qty	Billed revenue	Pending billable qty	Pending billable revenue	Revenue earned	Quantity earned
			Unapproved revenue										
☐	1	001	Earthwork - Labor & M...	\$ 759,887.01	Default	Unit price	☐	0.00	\$ 0.00	0.29	\$ 217,444.37	\$ 217,444.37	0.29
☐	2	002	Concrete - Labor & Mat...	\$ 2,919,020.71	Default	Unit price	☐	0.00	\$ 0.00	0.18	\$ 530,386.06	\$ 530,386.06	0.18
☐	3	003	Steel - Labor & Material	\$ 1,821,092.28	Default	Unit price	☐	0.00	\$ 0.00	0.18	\$ 321,183.01	\$ 321,183.01	0.18
Subtotals 3									\$ 0.00		\$ 1,069,013...	\$ 1,069,013...	

Column	Description
Is billed	When selected, a billing record has been created.
Billed quantity	This value is based on your pay quantities and depends on the unit of measure and how you want to bill the quantity.
Billed revenue	What has been billed to the client.
Pending billable quantity	The quantity that you have earned but has not yet been billed.
Pending billable revenue	The revenue you have earned but has not yet been billed.
Revenue earned	Total earned revenue of all cost items.
Quantity earned	The earned quantity which varies depending on billing method.

The revenue in the CBS is updated after you apply billed revenue against it.

9.15 PAY ITEM REVENUE BILLING IN BULK

Revenue billing often includes multiple pay items. For that reason, Control also lets you claim billed quantities and revenue for multiple pay items at a time using the Pay Items register. This is in lieu of using the Billed revenue details slide-out panel to bill one item at a time.

In the Pay Items register you can select the pay items you want to bill in bulk.

	Pay item number	Description
☒	01.02	FIELD SUPERVISION, ADMIN & MAINTENANCE
☒	01.03	FIELD OFFICES AND SHEDS
☒	11.1	EPOXY COATED STEEL SHEET PILE

In the example below for pay item 11.1, the revenue earned represents the total amount earned to date. Revenue earned is based on the cost items associated with this pay item. As cost items are being claimed, revenue earned is generated. For pay item 11.1, the Revenue earned column shows \$365,924.12 has been earned to date. The Billed revenue column shows that \$20,966.00 has been billed thus far. The difference between the revenue earned and the billed revenue is the pending billable revenue which shows under the Pending billable revenue column as \$344,958.12. This is the amount that you can bill the customer.

Pay item number	Description	Billed quantity	Billed revenue	Pending billable quantity	Pending billable revenue	Quantity earned	Revenue earned
01.02	FIELD SUPERVISION, ADMIN & MAINTENANCE	21,027.00	\$ 26,311.00	-21,004.55	\$ 1,545,122.64	22.45	\$ 1,571,433.64
01.03	FIELD OFFICES AND SHEDS	21,921.00	\$ 21,574.00	-21,909.60	\$ 377,555.84	11.40	\$ 399,129.84
03.04	STRUCTURAL STEEL	21,072.55	\$ 21,061.00	-21,030.66	\$ 355,983.32	41.89	\$ 377,044.32
11.1	EPOXY COATED STEEL SHEET PILE	21,417.00	\$ 20,966.00	161,545.06	\$ 344,958.12	182,962.06	\$ 365,924.12

Typically, when it is time to bill a customer, you can select the pay items with positive values in the Pending billable revenue column.

	Pay item number	Description	Line number	Total price	Unit price	Pay quantity	Forecast T/O Qty	UoM	Is billed	Billing methods	Billed quantity	Billed revenue	Pending billable quantity	Pending billable revenue	Quantity earned	Revenue earned
✓	01.02	FIELD SUPE...	2	\$ 3,220,000.00	\$ 70,000.00	46.00	46.00	Mo	✓	Unit price	21,027.00	\$ 26,311.00	-21,004.55	\$ 1,545,122.64	22.45	\$ 1,571,433.64
✓	01.03	FIELD OFFL...	3	\$ 1,610,000.00	\$ 35,000.00	46.00	46.00	Mo	✓	Unit price	21,921.00	\$ 21,574.00	-21,909.60	\$ 377,555.84	11.40	\$ 399,129.84
✓	03.04	STRUCTUR...	19	\$ 1,737,000.00	\$ 9,000.00	193.00	193.00	Ton	✓	Unit price	21,072.55	\$ 21,061.00	-21,030.66	\$ 355,983.32	41.89	\$ 377,044.32
✓	11.1	EPOXY COA...	72	\$ 1,090,000.00	\$ 2.00	545,000.00	545,000.00	Lb	✓	Unit price	21,417.00	\$ 20,966.00	161,545.06	\$ 344,958.12	182,962.06	\$ 365,924.12

A negative value in the Pending billable quantity or Pending billable revenue fields signifies an over billing to the customer.

When you are ready to bill a customer, select the check box for the pay items. Right-click a selected pay item, and then select **Bill multiple pay items**.

	Pay item number	Description	Line number
☒	01.02	FIELD SUPE...	2
☒	01.03	FIELD OFF...	3
☒	03.04		
☒	11.1		
☐	Danielle test ...		
☐	PAY ITEM 1		
☐	02.01		

- Insert pay item
- Delete pay item(s)
- Pay item details
- Billed revenue details
- Bill multiple pay items

The New Bill Request register shows a list of billing related fields to potentially be billed to the customer.

Pay Item > New Bill Request

Cancel

Submit

Billed date: 02/11/2020

Pay item number	Description	Billing method	Pending billable revenue	Pending billable quantity	Billed revenue	Billed quantity	Unit of meas..	Cost category	Cost item
03 04	STRUCTURAL STEEL	Unit Price	0.00	0.00	355,983.32	-21,030.66	Ton	Undefined	
01 02	FIELD SUPERVISION, ADMIN & MAINTEN..	Unit Price	0.00	0.00	1,545,122.64	-21,004.55	Mo	Undefined	
01 03	FIELD OFFICES AND SHEDS	Unit Price	0.00	0.00	377,555.84	-21,909.60	Mo	Undefined	
11.1	EPOXY COATED STEEL SHEET PILE	Unit Price	0.00	0.00	344,958.12	161,545.06	Lb	Undefined	

The Pending billable quantity and Pending billable revenue columns show zero because their values have been moved to the Billed Revenue and Billed quantity fields, to be billed as part of the overall transaction. The Billed revenue and Billed quantity values in the New bill request register match the Pending billable revenue and Pending billable quantity values in the Pay items tab.

In the New Bill Request, the values in the Billed quantity and Billed revenue fields are the amounts that are to be billed to the customer. The Billed Revenue and Billed Quantity columns show the same amounts that exist in the Pay Item register under the Pending billable quantity and Pending billable revenue columns.

You also have the option to change the Billed Revenue amount in the New Bill Request register. For example, if there's remaining work to be completed, and shows that it is not 100% complete, you can change the Billed revenue to a different amount. Using the example below for Pay item 11.1, you can

partially bill the pending billed revenue of \$344,958.12. By changing the billed revenue amount to \$300,000.00, the remaining \$44,958.00 shows under the Pending billable revenue column.

Now, you can see that if you bill for \$300,000.00, then you still have \$44,958.00 available to bill.

Pay Item >

New Bill Request

Cancel

Submit

Billed date: 02/12/2020

Pay item number	Description	Billing method	Pending billable revenue	Pending billable quantity	Billed revenue	Billed quantity	Unit of meas...	Cost category	Cost item
03.04	STRUCTURAL STEEL	Unit Price	0.000000000000	0.000000000000	355,983.31699820043	-21,030.66092730624	Ton	Undefined	
01.02	FIELD SUPERVISION, ADMIN & MAINTEN...	Unit Price	0.000000000000	0.000000000000	1,545,122.64433237491	-21,004.55094793810	Mo	Undefined	
01.03	FIELD OFFICES AND SHEDS	Unit Price	0.000000000000	0.000000000000	377,555.84256304969	-21,909.59629021248	Mo	Undefined	
11.1	EPOXY COATED STEEL SHEET PILE	Unit Price	\$ 44,958.12199933658	0.000000000000	\$ 300,000.00000000000	161,545.06099966829	Lb	Undefined	

You can assign the bill request to a Cost category and a Cost item. Each billed revenue transaction requires a cost category to be selected. The default value in the Cost category field is Undefined.

Pay Item > New Bill Request

Cancel

Submit

Billed date: 02/12/2020

Pay item number	Description	Pending billable revenue	Pending billable quantity	Billed revenue	Billed quantity	Unit of meas...	Cost category	Cost item	Notes
☐ 03.04	STRUCTURAL STEEL	\$ 0.000000000000	0.000000000000	\$ 355,983.31699820043	-21,030.66092730624	Ton	Undefined		
☐ 01.02	FIELD SUPERVISION, ADMIN & MAINTEN...	\$ 0.000000000000	0.000000000000	\$ 1,545,122.64433237491	-21,004.55094793810	Mo	Undefined		
☐ 01.03	FIELD OFFICES AND SHEDS	\$ 0.000000000000	0.000000000000	\$ 377,555.84256304969	-21,909.59629021248	Mo	Undefined		
☒ 11.1	EPOXY COATED STEEL SHEET PILE	\$ 44,958.12199933658	0.000000000000	\$ 300,000.00000000000	161,545.06099966829	Lb	Installed Materials	1 6.1.1 [1163] Pioneering- Sheet Pile	

In the Notes column, you can select to enter and save any information specific to the bill request. Click the **Notes** icon in the Notes column to open the form field.

BILLED

RETENTION

Cancel

Submit

Billed date: 07/11/20...

Cost category	Cost item	Change order	Notes
Undefined			
Undefined			

Notes

151

Billing customer for \$300,000.00 on 02/11/2025, and will submit the remaining \$44,958.12 in April.

Cancel

Save

After you select the Submit button in the New Bill Request register, the billed transaction shows in the Billed History tab in the Billed Revenue Details slide-out tab.

002

Concrete - Labor & Material

BILLED

RETENTION

BILLED HISTORY

Billed date	Billed qty	Billed	Net billed revenue	Retention withheld	Revenue received
07/11/2025	0.18	\$ 530,386.06	\$ 530,386.06	\$ 0.00	

Notes:

Billing customer for \$300,000.00 on 02/11/2025, and will submit the remaining \$44,958.12 in April.

In the Pay Items register, the following columns are updated:

- Billed revenue
- Billed qty
- Pending billable revenue
- Pending billable qty
- Forecast total revenue and Forecast unit revenue (when Cost plus billing method)

Submitting the new bill request also creates new audit log entries in the Pay Item's audit log. The entries include the pay item that was changed, fields that show before and after values, and the user that made the change.

AUDIT LOG												
Actions	Audit ID	Data type	Item type	Descripti...	Pay item...	Attribute	Changed...	Changed...	Value be...	Value aft...	Current ...	Current ...
CBS	85	Pay Item	Pay Item	Steel - Labor &...	003	Billed quantity	Julio	07/11/2025 12...	0.00	0.16	\$1,821,092.28	\$1,821,092.28
ACS	84	Pay Item	Pay Item	Concrete - Lab...	002	Billed quantity	Julio	07/11/2025 12...	0.00	0.18	\$2,919,020.71	\$2,919,020.71
Pay items	83	Pay Item	Pay Item	Steel - Labor &...	003	Billed revenue	Julio	07/11/2025 12...	0.00	295,859.10	\$1,821,092.28	\$1,821,092.28
Integration	82	Pay Item	Pay Item	Concrete - Lab...	002	Billed revenue	Julio	07/11/2025 12...	0.00	530,386.06	\$2,919,020.71	\$2,919,020.71
Import history	80	Pay Item	Pay Item	Additional stee...	4	Pay item numb...	Paul	07/01/2025 01...	Pending	Approved	\$0.00	\$86,400.00
	79	Pay Item	Pay Item	Steel - Labor &...	003	Pay item numb...	Paul	07/01/2025 01...	Pending	Approved	\$1,821,092.28	\$1,985,592.28
	75	Pay Item	Pay Item	Steel - Labor &...	003	Sales Order	Paul	04/15/2025 01...		SO-003	\$1,821,092.28	\$1,821,092.28
	74	Pay Item	Pay Item	Concrete - Lab...	002	Sales Order	Paul	04/15/2025 01...		SO-002	\$2,919,020.71	\$2,919,020.71
	73	Pay Item	Pay Item	Earthwork - La...	001	Sales Order	Laur	04/15/2025 01...	Sales Order 1	SO-001	\$759,887.01	\$759,887.01
	72	Pay Item	Pay Item	Earthwork - La...	001	Sales Order	Laur	04/08/2025 12...		Sales Order 1	\$759,887.01	\$759,887.01
	71	Pay Item	Pay Item	Earthwork - La...	001	Is billed	Laur	03/31/2025 02...	True	False	\$759,887.01	\$759,887.01
	70	Pay Item	Pay Item	Earthwork - La...	001	Is billed	Paul	03/31/2025 02...	False	True	\$759,887.01	\$759,887.01
	60	Pay Item	Pay Item	Steel - Labor &...	003	Price lock status	Paul	09/02/2022 10...	Price unlocked	Price locked		

Bill for multiple pay items

1. On the Pay Items tab, select multiple pay items.
2. Right-click on a selected pay item, and then select **Bill multiple pay items** from the list.

PAY ITEMS												
Actions	Pay item position	Pay item number	Description	Forecast total revenue	Forecast revenue unit cost	Revenue forecast method	Current billing method	Is billed	Billed qty	Billed revenue		
			Unapproved revenue	\$ 93,159.69								
☒	1	001	Earthwork - Labor & M...	\$ 759,887.01	\$ 759,887.01	Default	Unit price	☐	0.00	\$ 0.00		
☒	2		e - Labor & Mat...	\$ 2,919,020.71	\$ 2,919,020.71	Default	Unit price	☐	0.00	\$ 0.00		
☐	3		Labor & Material	\$ 1,821,092.28	\$ 1,821,092.28	Default	Unit price	☐	0.00	\$ 0.00		
Subtotals 3 (2 pay items are revenue)				\$ 5,593,159.69						\$ 0.00		

The New Bill Request register opens. You can verify that the billed revenue matches the pending billable revenue in the Pay Item register.

Pay Item > New bill request

BILLED

RETENTION

Cancel

Submit

Billed date: 07/10/20...

Pay item number	Description	Billing method	Forecast total revenue	Pending billable qty	Billed revenue	Retention %	Retention withheld	Net bill	Billed qty	Unit	Cost category	Cost item	Change order	Notes
☐ 002	Concrete - Labor & Material	Unit price	\$ 0.00	0.00	\$ 0.00	0.00 %	\$ 0.00	\$ 0.00	0.00	Each	Undefined			
☒ 001	Earthwork - Labor & Material	Cost plus	\$ 0.00		\$ 0.00	0.00 %	\$ 0.00	\$ 0.00	0.00	Each	Undefined			
Subtotals 2 (1 rows selected)			\$ 0.00		\$ 0.00									

In the Retention tab, you can view any retention amounts from previous transactions, such as retention withheld, released (to date), and amount released, similar to the Retention tab in the Billed revenue details slide-out panel.

3. In the Billed revenue column, enter the amount to bill. In the following example, half of the forecasted total revenue is billed, and the other half shows in the Pending billable revenue column.

CBS ACS PAY ITEMS CHANGE REGISTER AUDIT LOG View: Unsaved (Revenue)

Revenue snapshot: Current revenue forecast Billed date: 10/01/2015 to 07/10/2025

Drag a column header and drop it here to group by that column

Pay item position	Pay item number	Description	Forecast total revenue	Forecast revenue unit cost	Revenue forecast method	Current billing method	Is billed	Billed qty	Billed revenue	Pending billable qty	Pending billable revenue	Revenue earned	Quantity earned
☒ 1	001	Earthwork - Labor & M...	\$ 650,000.00	\$ 0.00	Earned	Cost plus	☐	0.00	\$ 0.00		\$ 0.00	\$ 0.00	0.00
☒ 2	002	Concrete - Labor & Mat...	\$ 100,000.00	\$ 0.00	Default	Unit price	☐	0.00	\$ 0.00		\$ 0.00	\$ 0.00	0.00

Control - New pay item request - Google Chrome

Steel Structure Training Job 3 (106993) /

Pay Item > New bill request

BILLED

RETENTION

Cancel

Submit

Billed date: 07/10/20...

Pay item number	Description	Billing method	Pending billable revenue	Pending billable qty	Billed revenue	Retention %	Retention withheld	Net bill	Billed qty	Unit	Cost category
☐ 002	Concrete - Labor & Material	Unit price	(\$ 50,000.00)	0.00	\$ 50,000.00	0.00 %	\$ 0.00	\$ 50,000.00	0.02	Each	Undefined
☒ 001	Earthwork - Labor & Material	Cost plus	(\$ 325,000.00)		\$25000	0.00 %	\$ 0.00	\$ 325,000.00	0.00	Each	Undefined
Subtotals 2 (1 rows selected)			(\$ 375,000.00)		\$ 375,000.00						

4. In the Cost category column, you can assign a cost category to the new bill request.
5. In the Notes column, you can enter a note for each pay item, such as *“Billing half the amount the customer now and will bill the other half when job is complete”*.
6. Click **Submit**.


You can view the entry created for this transaction in the Billed History tab for the pay item just updated.

9.16 SYNC BILLED REVENUE DETAILS

When work is progressed on cost items that are associated to pay items, the quantity earned, revenue earned, pending billable quantity, and pending billable revenue fields are populated with the applicable values. When a bill is processed, the billed quantity and billed revenue fields automatically update, and the pending billable quantity and pending billable revenue fields also update (minus the new billed amounts). The quantity earned and revenue earned columns are not affected by billing.

9.16.1 Sync billed revenue

You can sync billed revenue with your integrated billing system. To update a pay item’s billed revenue to your integrated billing system, go to Actions > **Sync**, and then select **Push Billed revenue**. To update billed revenue in Control, select the **Get Billed revenue** option.

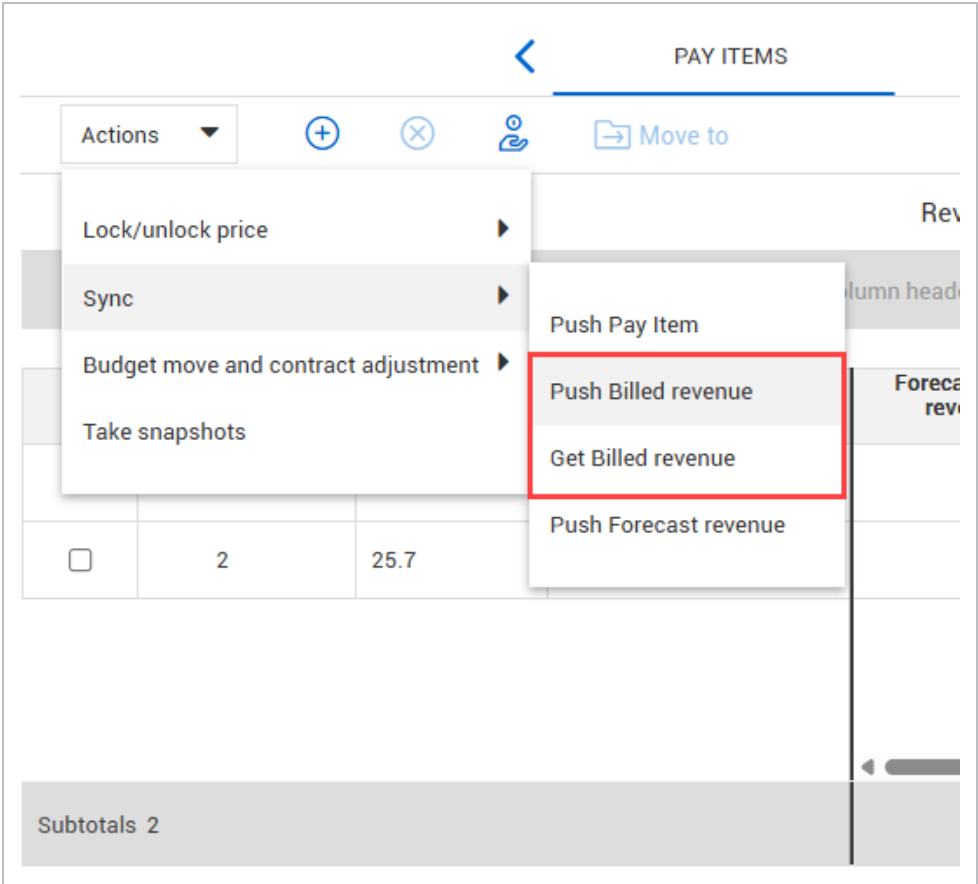

9.17 ACTUALIZING REVENUE

In Pay Items, after a bill is sent to a client, you can log revenue you receive so that you can track received revenue.

In the Pay Items register, when you select the Claim Revenue icon, it shows all transactions for all pay items that contain billed revenue that has not been logged as received.

103961 | Ten Mile Slide - Phase 2 (Carrying) / Control / Workspaces

Actions

+

×

Move to

☐	Pay item position	Pay item number	Descript...	Line num...
☐	1	1	1	1

Alternatively, you can right-click on one or more pay items and select **Actual revenue details**.

103961 | Ten Mile Slide - Phase 2 (Carrying) / Control /

Actions

+

×

Move to

☐	Pay item position	Pay item number	Descript...
☒	1	1	1
☒			2
☐			3
☐			4

+

 Insert pay item

×

 Delete pay item(s)
 Pay item details
 Billed revenue details
 Bill multiple pay items
 Actual revenue details

The Actual revenue details form opens and shows all the selected pay item billed transactions. In the Revenue received column, you can enter the amount of money received by a client. The Revenue received date lets you enter the date the money is received.

Pay item

>

Actual revenue details

Cancel

Submit

⊖

⚙


Default revenue received date: 04/07/2022

📅

📄


☐	Pay item position	Pay item number	Description	Billed date	Billed qty	Billed revenue	Revenue received (to date)	Revenue received	Revenue received date	Cost item	Cost category	Change order	Notes
☐	2	2		04/06/2022	-3.00	\$ 1,000.00	\$ 2,000.00	\$ 0.00	04/07/2022		Undefined		📄
☒	4	4		03/23/2022	50.00	\$ 500.00	\$ 250.00	\$ 150.00	04/07/2022		Undefined Supplies		📄

You can select from the billed transactions, and then click the **Auto Calculate** icon to match the total revenue received values with the billed revenue values (everything that has been billed has been received in total).

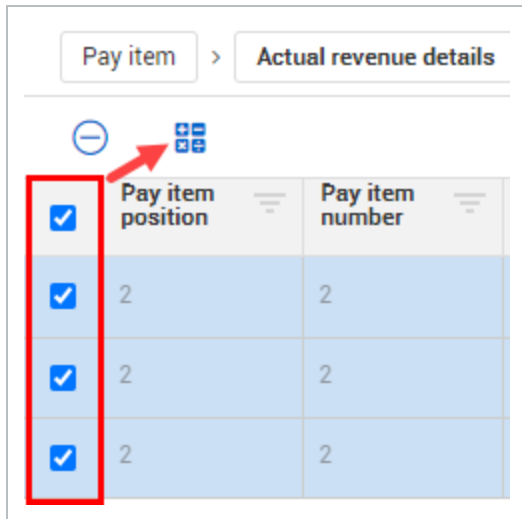

☒	Pay item position	Pay item number
☒	2	2
☒	2	2
☒	2	2

The revenue is also updated on the Billed History tab in Billed Revenue Details, for a pay item.

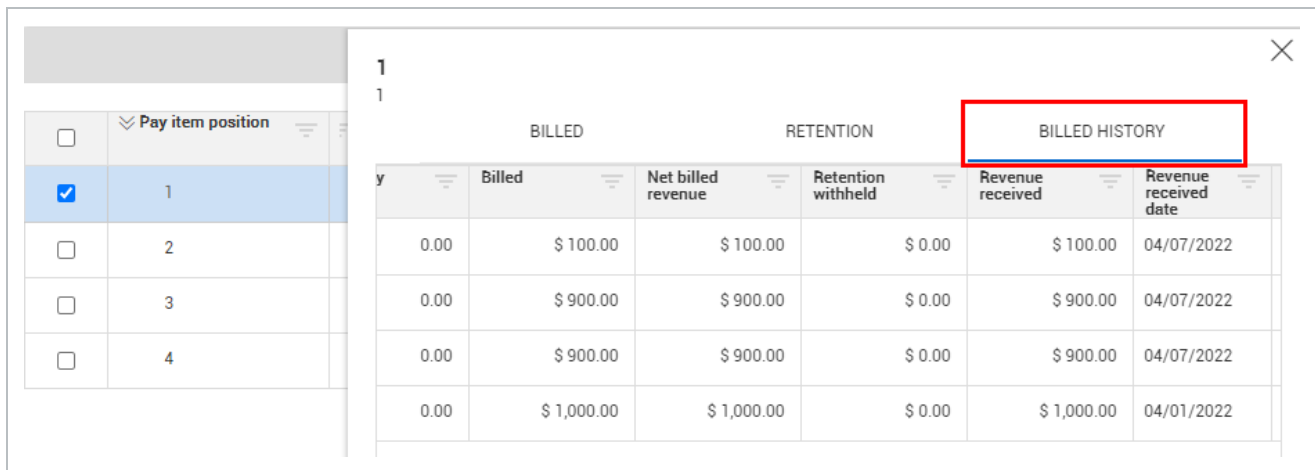

		BILLED		RETENTION	BILLED HISTORY	
		Billed	Net billed revenue	Retention withheld	Revenue received	Revenue received date
☒	1					
☐	2	0.00	\$ 100.00	\$ 100.00	\$ 0.00	\$ 100.00 04/07/2022
☐	3	0.00	\$ 900.00	\$ 900.00	\$ 0.00	\$ 900.00 04/07/2022
☐	4	0.00	\$ 900.00	\$ 900.00	\$ 0.00	\$ 900.00 04/07/2022
		0.00	\$ 1,000.00	\$ 1,000.00	\$ 0.00	\$ 1,000.00 04/01/2022

After the Actual revenue details form is submitted, the Revenue received (to date) column on the Pay Items form shows the pay item amount received.

☒	Pay item position	Pay item number	Descript...	Curr... price	Curr... unit price	Curr... pay qty	Revenue received (to date)
☒	1	1	1	\$ 100,0...	\$ 100,000....	1.00	\$ 2,900.00
☒	2	2	2	\$ 30,00...	\$ 200.00	150.00	\$ 3,200.00
☒	3	3	3	\$ 10,00...	\$ 1,000.00	10.00	\$ 100.00
☒	4	4	4	\$ 2,500...	\$ 2,500.00	1.00	\$ 600.00

9.18 CHANGE ORDERS

You can associate and view change order cost information on a pay item and additional cost items to provide better visibility on the progress of a project and the breakdown of costs.

When creating a bill in the Billed revenue details slide-out panel, or from the Bill multiple pay items option, you can select a change order to assign the billed amount to. This allows you to select which approved change order to assign to the bill.

CBS
ACS
PAY ITEMS
CHANGE REGISTER
AUDIT LOG

Revenue snapshot: Current revenue forecast
Billed date: 02/11/2020 to 12/15/2021

002
Concrete - Labor & Material

BILLED
BILLED HISTORY

Pending billable quantity
-55.00

Pending billable revenue
(\$ 2,500.00)

Billed revenue
\$ 2,500.00

Cost category
Installed Equipment

Billed quantity
55.00

Billed date
12/15/2021

Cost item
3 [1071] Concrete

Change order
758.00

Notes
Associated to change order 758.

Add billed

Cancel
Apply

InEight Inc. | Release 26.7

Page 453 of 639

In the Billed History tab, the selected change order is associated with the bill after the bill is submitted.

PAY ITEMS							
Revenue snapshot: Current revenue forecast Billed date: 11/23/2021 to 11/30/2021							
CO.003 Release 1 and Chang order 4 release 2							
Billed date	Billed quantity	Billed	Cost item	Cost Category	Change order		
11/30/2021	2.0000	\$ 2,555.00		Undefined	22.1		

In the Pay Items register, you can view Change order details in the following columns.

- **Change order** — Shows the Change order number which can be used to associate with the correct change order or contract adjustment.
- **Total change order amount** — Shows the total change order amounts for the pay item. This is a summary of all the approved change orders that are attributed to a pay item.
- **Billed change order amount** — Shows how much money has been billed to the customer against a change order.

Rev... earn...	Quantity earned	Pen... billa... reve...	Pending billable qty	Net billed revenue	Change order	Billed change order	Total change order
\$ 0.00		(\$ 750.00)		\$ 500.00		\$ 0.00	\$ 16,000.00
\$ 0.00		\$ 0.00		\$ 0.00	... (2)	\$ 0.00	\$ 10,060.00
\$ 0.00	0.00	\$ 0.00	0.00	\$ 0.00	... (2)	\$ 0.00	\$ 10,000.00
\$ 0.00	0.00	\$ 0.00	0.00	\$ 0.00	... (12)	\$ 0.00	\$ 2,000.00
\$ 0.00	0.00	\$ 0.00	0.00	\$ 0.00	... (16)	\$ 0.00	\$ 2,000.00
\$ 0.00	0.00	\$ 0.00	0.00	\$ 0.00	... (3)	\$ 0.00	\$ 1,000.00
\$ 0.00	0.00	\$ 0.00	-0.50	\$ 0.00	✓ (1)	\$ 0.00	\$ 1,000.00
\$ 0.00	0.00	\$ 0.00	0.00	\$ 0.00	... (2)	\$ 0.00	\$ 60.00
\$ 0.00	0.00	\$ 0.00	0.00	\$ 0.00	... (1)	\$ 0.00	\$ 60.00
\$ 0.00		(\$ 8,100.00)		\$ 8,100.00		\$ 0.00	\$ 60.00
\$ 60.00		(\$ 8,790.00)		\$ 8,600.00		\$ 0.00	\$ 44,760.00

9.19 REVENUE FORECASTING

Revenue forecasting is used to determine the projected revenue a contractor will receive for completing a project or scope of work. The amount of revenue earned compared to the total cost spent determines how much profit and % margin is made. Therefore, understanding projected revenue is critical to determine the profitability and health of a project.

It is often necessary to compare forecasted cost to expected revenue at a cost item level. Within Control, you can view this comparison using the revenue columns available in the CBS. The revenue fields in the CBS auto calculate based on the billing method of each line item or can be overridden by manually entering a revenue forecast.

9.19.1 Pay Item Position Code Column

The Pay Item tab contains a Pay Item Position column that lets you view, sort, and group pay items in a hierarchical manner much like you can in the CBS. This feature lets you expand and collapse pay items by clicking the down-arrow, while also letting you group scopes of work together into a hierarchy.

☐	Pay item position	Pay item number	Descri...	Line num...	Row num...	Curr... price	Curr... unit price	Curr... pay qty
☐	▼ 1	Pay 1	Pay 1	1	26	\$ 80,20...		
☐	▼ 2	16Pay 2	Pay 2	17	15	\$ 0.000...		
☐	▼ 3	17Pay 3	Pay 3	18	16	\$ 0.000...		
☐	4	Testpay	Set new pay...	37	27	\$ 0.000...	\$ 1.50000...	0.0000000...

Adjusting the pay item position code column lets you see the parent-child rollup relationship between pay items, terminal pay items, and the revenue forecast method, in addition to any other price and revenue columns. This lets you see how the values for the child pay items all roll up to its parent pay item, then see the totals at a parent pay item level.

☐	Pay item position	Pay item number	Descri...	Line num...	Is term...	Row num...	Current price	Revenue forecast method
☐	^ 1	Pay 1	Pay 1	1	☐	26	\$ 80,200.00000000010	Rollup
☐	^ 1.1	Pay 1.1	Pay 1.1	2	☐	1	\$ 79,300.00000000010	Rollup
☐	1.1.1	3Pay 1.1.1	Pay 1.1.1	3	☒	2	\$ 55,300.00000000000	Manual
☐	1.1.2	4Pay 1.1.2	Pay 1.1.2	4	☒	3	\$ 11,000.00000000010	Manual
☐	1.1.3	5Pay 1.1.3	Pay 1.1.3	5	☒	4	\$ 9,000.00000000000	Default
☐	1.1.4	6Pay 1.1.4	Pay 1.1.4	6	☒	5	\$ 1,000.00000000000	Billed
☐	^ 1.1.5	7Pay 1.1.5	Pay 1.1.5	7	☐	6	\$ 3,000.00000000000	Rollup
☐	1.1.5.1	9Pay 1.1.5.1	Pay 1.1.5.1	9	☒	8	\$ 3,000.00000000000	Default
☐	1.1.5.2	10Pay 1.1.5.2	Pay 1.1.5.2	10	☒	9	\$ 0.00000000000	Default
☐	1.1.6	8Pay 1.1.6	Pay 1.1.6	8	☒	7	\$ 0.00000000000	Default
☐	^ 1.2	11Pay 1.2	Pay 1.2	11	☐	10	\$ 900.00000000000	Rollup
☐	1.2.1	14Pay 1.2.1	Pay 1.2.1	15	☒	13	\$ 900.00000000000	Default
☐	1.2.2	15Pay 1.2.2	Pay 1.2.2	16	☒	14	\$ 0.00000000000	Default

9.19.2 Cost Item Revenue View

It's important to see forecasted cost and forecasted revenue side by side, in order to compare the costs and revenue on individual cost items as a subtotal of the overall project.

In Control, you can create a custom revenue data block containing six revenue-related columns. Permissions can be established to limit who may view these Revenue columns. You can view this data block within the same view as a forecasted costs data block for a side-by-side comparison.

Tasks			Task details			Revenue			Pay Item/CB/FC										
☐	CB position	Description	WBS phase code	WBS phase code	Pay item assignment	CB contribution qty	Forecast total cost	Forecast total margin	Forecast total revenue	Forecast % margin	Forecast remaining revenue	Forecast revenue earned	Forecast revenue unit cost	Pay item assignment	Forecast total cost	Actual cost (to date)	% complete	CB total cost	CE total cost
☐	1	Job Overhead	1002	1002			\$ 250,000.00	\$ 0.00	\$ 0.00	0.00 %	\$ 0.00	\$ 0.00	\$ 0.00		\$ 250,000.00	\$ 0.00	0.00 %	\$ 250,000.00	\$ 250,000.00
☐	2	Earthwork	1009	1009	001		\$ 400,000.00	\$ 20,976,402.116.13	\$ 20,976,402.116.13	100.00 %	\$ 20,976,402.116.13	\$ 0.00	\$ 407,622.78	001	\$ 400,000.00	\$ 0.00	0.00 %	\$ 400,000.00	\$ 400,000.00
☐	3	Concrete	1071	1071	002		\$ 0.00	\$ 0.00	\$ 0.00	0.00 %	\$ 0.00	\$ 0.00	\$ 0.00	002	\$ 0.00	\$ 0.00	100.00 %	\$ 1,500,000.00	\$ 1,500,000.00
☐	4	Structural Steel	1073	1073			\$ 1,000,000.00	\$ (847,200.00)	\$ 202,800.00	-17.76 %	\$ 202,800.00	\$ 0.00	\$ 0.00		\$ 1,000,000.00	\$ 0.00	0.00 %	\$ 0.00	\$ 1,000,000.00
☒	4.1	Erect Steel - Heavy	1074	1074	002		\$ 800,000.00	\$ (600,000.00)	\$ 0.00	0.00 %	\$ 0.00	\$ 0.00	\$ 0.00	002	\$ 800,000.00	\$ 0.00	0.00 %	\$ 0.00	\$ 800,000.00
☐	4.2	Erect Steel - Light	1005	1005	003		\$ 200,000.00	\$ 2,800.00	\$ 202,800.00	1.38 %	\$ 202,800.00	\$ 0.00	\$ 0.00	003	\$ 200,000.00	\$ 0.00	0.00 %	\$ 200,000.00	\$ 200,000.00
☐	4.3	Bolted Connections	1006	1006	002		\$ 50,000.00	\$ (50,000.00)	\$ 0.00	0.00 %	\$ 0.00	\$ 0.00	\$ 0.00	002	\$ 50,000.00	\$ 0.00	0.00 %	\$ 50,000.00	\$ 50,000.00
☐	4.4	Labor	1008	1008	001		\$ 0.00	\$ 0.00	\$ 0.00	0.00 %	\$ 0.00	\$ 0.00	\$ 0.00	001	\$ 0.00	\$ 0.00	0.00 %	\$ 0.00	\$ 0.00
☐	4.5	Equipment	1009	1009	001		\$ 0.00	\$ 0.00	\$ 0.00	0.00 %	\$ 0.00	\$ 0.00	\$ 0.00	001	\$ 0.00	\$ 0.00	0.00 %	\$ 0.00	\$ 0.00
☐	4.6	3rd Party	1000	1000			\$ 0.00	\$ 0.00	\$ 0.00	0.00 %	\$ 0.00	\$ 0.00	\$ 0.00		\$ 0.00	\$ 0.00	0.00 %	\$ 0.00	\$ 0.00
☒	5	Materials	1004	1004			\$ 1,750,000.00	\$ 12,896,376.323.87	\$ 12,896,376.323.87	99.99 %	\$ 12,896,376.323.87	\$ 0.00	\$ 0.00		\$ 1,750,000.00	\$ 0.00	0.00 %	\$ 0.00	\$ 1,750,000.00
☐	5.1	Earthwork - Mater...	1005	1005	001		\$ 250,000.00	\$ 12,896,376.323.87	\$ 12,896,376.323.87	100.00 %	\$ 12,896,376.323.87	\$ 0.00	\$ 292,264.23	001	\$ 250,000.00	\$ 0.00	0.00 %	\$ 250,000.00	\$ 250,000.00
☐	5.2	Concrete - Mater...	1006	1006	002		\$ 1,000,000.00	\$ (1,000,000.00)	\$ 0.00	0.00 %	\$ 0.00	\$ 0.00	\$ 0.00	002	\$ 1,000,000.00	\$ 0.00	0.00 %	\$ 1,000,000.00	\$ 1,000,000.00
☐	5.3	Structure Steel - ...	1007	1007	003		\$ 500,000.00	\$ 0.00	\$ 500,000.00	0.00 %	\$ 500,000.00	\$ 0.00	\$ 0.00	003	\$ 500,000.00	\$ 0.00	0.00 %	\$ 500,000.00	\$ 500,000.00
Subtotals 14							\$ 3,450,000.00	\$ 33,402,537,340.00	\$ 33,402,537,340.00	99.99 %	\$ 33,402,537,340.00	\$ 0.00	\$ 0.00		\$ 3,450,000.00	\$ 0.00	0.00 %	\$ 0.00	\$ 3,450,000.00

The Revenue columns can only be populated if the associated cost items have an assigned pay item. In the example below, cost item 1 Job Overhead, does not have a corresponding pay item assignment,

therefore the Revenue columns are not populated. The opposite is true for Cost item 2 which has a corresponding pay item assignment.

Tasks				Task details			Revenue						
☐	CBS position	Description	WBS phase code	WBS phase code	Pay item assignment	CBS contribute qty	Forecast total cost	Forecast total margin	Forecast total revenue	Forecast % margin	Forecast remaining revenue	Forecast revenue earned	Forecast revenue unit cost
☐	1	Job Overhead	1002	1002			\$ 250,000.00	\$ 0.00	\$ 0.00	0.00 %	\$ 0.00	\$ 0.00	\$ 0.00
☐	2	Earthwork	1069	1069	001		\$ 400,000.00	\$ 20,575,002,116.13	\$ 20,575,402,116.13	100.00 %	\$ 20,575,402,116.13	\$ 0.00	\$ 467,622.78

9.19.3 Cost item revenue calculation by allows as-built

For parent cost items where the allow as-built is not equal to *None*, where cost or quantities are being tracked, revenue values are now being calculated at the parent cost item level rather than always rolling up children revenue values to the parent. If the costs or quantities are being tracked at the terminal cost items, then those revenue values are calculated at the terminal cost items and roll up to the parent.

Tasks				Task details			Revenue					
☐	☒ CBS position	De...	WBS phase code	Change status	As-built lock	Allow as-built	Forecast revenue unit cost	Forecast total margin	Forecast total revenue	Forecast remaining revenue	Forecast revenue earned	Forecast % margin
☐	1	Financi...	1000		☒	All	\$ 0.000000000000	\$ 0.000000000000	\$ 0.000000000000	\$ 0.000000000000	\$ 0.000000000000	0.000000000000 %
☐	2	Misc. R...	1103		☐	None		(\$ 43,529.5644980...	\$ 545.695501000000	\$ 0.00083358262	\$ 545.69466741738	-7,976.896349380...
☐	2.1	Misc. R...	1104		☒	All	\$ 0.000000000000	\$ 0.000000000000	\$ 0.000000000000	\$ 0.000000000000	\$ 0.000000000000	0.000000000000 %
☐	2.2	Escalati...	1101		☐	Costs	\$ 0.000000000000	\$ 8.661833000000	\$ 8.661833000000	\$ 0.000000000000	\$ 8.661833000000	100.000000000000 %
☐	2.2.1	General ...	1102		☒	Quantities	\$ 0.000000000000	\$ 454.304498000000	\$ 454.304498000000	\$ 0.000000000000	\$ 454.304498000000	100.000000000000 %
☐	2.3	Directs	1001		☐	None		\$ 0.000000000000	\$ 0.000000000000	\$ 0.000000000000	\$ 0.000000000000	0.000000000000 %

9.20 REVENUE FORECASTING COLUMNS

The revenue forecasting data exists in the CBS and Pay Item registers as shown in the following images:

- CBS register revenue columns:

Revenue						
Forecast total cost	Forecast total margin	Forecast total revenue	Forecast % margin	Forecast remaining revenue	Forecast revenue earned	Forecast revenue unit cost
\$ 250,000.00	\$ 0.00	\$ 0.00	0.00 %	\$ 0.00	\$ 0.00	\$ 0.00
\$ 400,000.00	\$ 20,575,002,116.13	\$ 20,575,402,116.13	100.00 %	\$ 20,575,402,116.13	\$ 0.00	\$ 467,622.78

- Pay Item register revenue columns:

☐	Pay item position	Pay item number	Description	Forecast total revenue	Forecast total cost	Revenue forecast method	Billed revenue	Current billing method	Forecast % margin	Forecast total margin	Forecast revenue unit cost	Revenue earned
☐	1	001	Earthwork - Labor...	\$ 33,435,028,440.00	\$ 650,000.00	Default	\$ 0.00	Unit price	100.00 %	\$ 33,434,378,440.00	\$ 759,887.01	\$ 0.00
☐	2	002	Concrete - Labor ...	\$ 0.00	\$ 1,850,000.00	Default	\$ 0.00	Unit price	0.00 %	(\$ 1,850,000.00)	\$ 0.00	\$ 0.00
☐	3	003	Steel - Labor & M...	\$ 702,800.00	\$ 700,000.00	Earned	\$ 0.00	Cost plus	0.40 %	\$ 2,800.00	\$ 0.00	\$ 0.00

The following table shows an overview of the revenue forecasting columns.

Overview - Revenue Forecasting columns

Columns	Register	Description
Forecast total revenue	CBS and Pay Items	This is your expected final revenue at completion. The calculations vary by assigned billing method. This value is based on the Pay item's final revenue * a percentage that can be earned by the cost item.
Forecast total cost	CBS and Pay Items	Total cost (to date) + Forecast remaining cost.
Revenue forecast method	Pay Items	For Fixed Final Price, you can select Default and Manual. For Cost Plus, you can select from Earned, Billed, and Manual. The roll-up revenue forecast method is automatically assigned for parent pay items, and not editable, as all forecast revenue for child pay items rolls up to the parent pay item.
Billed revenue	Pay Items	Amount billed to the client for a single pay item.
Fixed final price	Pay Items	Lump sum billing method (price agreed upon by a contractor and a client does not change without a contract order).
Forecast % margin	CBS and Pay Items	Forecast final margin / forecast final revenue.
Forecast total margin	CBS and Pay Items	Forecast final revenue - Forecast final cost. This is the total profit you're forecasting to make at completion of the job.
Forecast remaining	CBS	Forecast final revenue - Forecast revenue earned, revenue remaining to earn.

Overview - Revenue Forecasting columns (continued)

Columns	Register	Description
revenue		
Forecast revenue unit cost	CBS and Pay Items	Forecast final revenue / Forecast take-off quantity, amount of revenue earned per quantity.
Forecast revenue earned	CBS	% complete * Forecast final revenue. This is revenue that is earned based on completion of work.

9.21 REVENUE CALCULATIONS

The revenue calculations are based on the following:

- Pay items assigned billing method.
- Pay items assigned revenue forecast method.

Control calculates revenue in the CBS and Pay Item registers based on the billing and revenue forecast methods.

9.21.1 Cost Breakdown Structure (CBS) register revenue Calculations

The following tables show how the different types of revenue are calculated in the CBS.

Forecast total revenue

Billing method	Revenue forecast method	Calculation
Fixed final price Unit price	Default	Earnings % × Assigned pay item's Forecast total revenue.
Unit price	Default	Earnings % × Assigned pay item's Forecast total revenue.
Cost plus	Earned	IF Cost source = <i>Detail</i>

Forecast total revenue (continued)

Billing method	Revenue forecast method	Calculation
	(Current estimate)	THEN Forecast final revenue (labor resource) + Forecast final revenue (construction equipment resource) + Forecast final revenue (all other resources) ELSE Forecast final revenue (plug) WHERE Forecast final revenue (labor resource) = Work hours × Scale 1 % × Scale 1 Charge rate + Work hours × Scale 2 % × Scale 2 Charge rate + Work hours × Scale 3 % × Scale 3 Charge rate. Forecast final revenue (construction equipment resource) = Work hours × Charge rate. Forecast final revenue (all other resources) = Resource quantity × Charge rate Forecast final revenue (plug) = CE revenue amount.
	Earned (Forecast cost)	Forecast remaining revenue + Sum for each cost category [Actual cost category cost (to date) × (1 + Cost category markup % from settings)] IF Forecast method = <i>Rollup</i> THEN Sum (children's Forecast final revenue) ELSE IF Forecast method is <i>disabled</i> THEN 0.
	Billed	IF all of the Billed revenue is assigned to cost item(s) THEN Forecast remaining revenue + Billed Revenue assigned to the cost item ELSE Forecast remaining revenue + (Billed Revenue of the pay item unassigned to a cost item × (CE final cost of the cost item ÷ CE final cost of all cost items assigned to the pay item) + Billed Revenue

Forecast total revenue (continued)

Billing method	Revenue forecast method	Calculation
		assigned to the cost item.
Time & Material	Earned	Forecast total revenue = Pay item forecast total revenue × (Cost item Forecast total cost ÷ sum of all assigned cost items' Forecast total cost excluding Rollup method and disabled forecasts).
	Billed	IF all of the Billed revenue is assigned to cost item(s) THEN Forecast remaining revenue + Billed Revenue assigned to the cost item ELSE Forecast remaining revenue + (Billed Revenue of the pay item unassigned to a cost item × (CE final 202cost of the cost item ÷ CE final cost of all cost items assigned to the pay item) + Billed Revenue assigned to the cost item.
All methods	Manual	Forecast final revenue of the pay item × (CE final cost of the cost item ÷ CE final cost of all cost items assigned to the pay item).

Forecast remaining revenue

Billing method	Revenue forecast method	Calculation
Fixed final price Unit price		Forecast final revenue of the pay item × (CE final cost of the cost item ÷ CE final cost of all cost items assigned to the pay item)
Cost plus	Earned (Current estimate)	Forecast total revenue - Forecast revenue earned.
	Earned (Forecast)	IF Cost source = <i>Detail</i> THEN

Forecast remaining revenue (continued)

Billing method	Revenue forecast method	Calculation
	cost)	Forecast remaining revenue (labor resource) + Forecast remaining revenue (construction equipment resource) + Forecast remaining revenue (all other resources) {Using resources in the Forecast resources tab only} ELSE Forecast remaining revenue (plug) WHERE Forecast remaining revenue (labor resource) = [Remaining work hours × Scale 1 % × Scale 1 Billable rate + Remaining work hours × Scale 2 % × Scale 2 Billable rate + Remaining work hours × Scale 3 % × Scale 3 Billable rate] × [1 + Labor resource markup % from settings] Forecast remaining revenue (construction equipment resource) = Remaining work hours × Billable rate × 41[1 + Construction equipment resource markup % from settings]. Forecast remaining revenue (all other resources) = Resource remaining quantity × Billable rate × [1 + Resource markup % from settings] Forecast remaining revenue (plug) = Sum for each cost category [Forecast cost category remaining cost × (1 + Cost category markup % from settings)] IF Forecast method = <i>Rollup</i> THEN sum (children's Forecast remaining revenue) ELSE IF Forecast method is <i>disabled</i> THEN 0.
	Billed	IF Cost source = <i>Detail</i> THEN Forecast remaining revenue (labor resource) + Forecast remaining revenue (construction equipment resource) + Forecast remaining revenue (all other resources) ELSE

Forecast remaining revenue (continued)

Billing method	Revenue forecast method	Calculation
		Forecast remaining revenue (plug) WHERE Forecast remaining revenue (labor resource) = (1 - % complete) × Work hours × Scale 1 % × Scale 1 Charge rate + (1 - % complete) × Work hours × Scale 2 % × Scale 2 Charge rate + (1 - % complete) × Work hours × Scale 3 % × Scale 3 Charge rate Forecast remaining revenue (construction equipment resource) = (1 - % complete) × Work hours × Charge rate Forecast remaining revenue (all other resources) = (1 - % complete) × Resource quantity × Charge rate Forecast remaining revenue (plug) = (1 - % complete) × CE revenue amount.
Time & Material		IF Cost source = <i>Detail</i> THEN Forecast remaining revenue (labor resource) + Forecast remaining revenue (construction equipment resource) + Forecast remaining revenue (all other resources) {Using resources in the Forecast resources tab only} ELSE Forecast remaining revenue (plug) WHERE Forecast remaining revenue (labor resource) = [Remaining work hours × Scale 1 % × Scale 1 Billable rate + Remaining work hours × Scale 2 % × Scale 2 Billable rate + Remaining work hours × Scale 3 % × Scale 3 Billable rate] × [1 + Labor resource markup % from settings] Forecast remaining revenue (construction equipment resource) = Remaining work hours × Billable rate × [1 + Construction equipment resource markup % from settings] Forecast remaining revenue (all other resources) = Resource remaining quantity × Billable rate × [1 + Resource markup % from settings]

Forecast remaining revenue (continued)

Billing method	Revenue forecast method	Calculation
		Forecast remaining revenue (plug) = Sum for each cost category [Forecast cost category remaining cost × (1 + Cost category markup % from settings)] IF Forecast method = <i>Rollup</i> THEN sum (children's Forecast remaining revenue) ELSE IF Forecast method is disabled THEN 0.
All methods	Manual	Forecast total revenue - Forecast revenue earned.

Forecast revenue earned

Billing method	Revenue forecast method	Calculation
Time & Material	All methods	WHEN the <i>Revenue is considered earned when a LEM is setting</i> is set to <i>Pending</i> THEN Sum of all BillAmount values where BatchType = LEM AND DocumentStatus <> Cancelled ELSE WHEN the <i>Revenue is considered earned when a LEM is setting</i> is set to <i>Approved</i> THEN Sum of all BillAmount values where BatchType = LEM AND DocumentStatus <> <i>Cancelled OR Pending approval</i>.
All other methods	All methods	Forecast total revenue × % complete.

9.21.2 Pay Items register calculations

The following tables show how the different types of revenue are calculated in the Pay Items register.

Forecast total revenue

Billing method	Revenue forecast method	Calculation
Fixed final price	Default	Current price.
Unit price		Current unit price × Current forecast (T/O) qty.
Cost plus	Earned	Sum of assigned cost items' Forecast total revenue excluding Rollup values.
	Billed	Billed revenue + sum of assigned cost items' Forecast remaining revenue.
Time & Material	Billed	Billed revenue + sum for all assigned cost items {(1-% complete) × sum for all cost categories[Forecast total cost × (1+Markup % from cost category settings)]}.
	Earned	IF the <i>Revenue is considered earned when a LEM is setting</i> is set to <i>Pending</i> THEN = Revenue earned + sum for all assigned cost items {(1-% complete) × sum for all cost categories[Forecast total cost × (1+Markup % from cost category settings)]} ELSE IF the <i>Revenue is considered earned when a LEM is setting</i> is set to <i>Approved</i> THEN = Revenue earned + Pending LEMs + sum for all assigned cost items {(1-% complete) × sum for all cost categories [Forecast total cost × (1+Markup % from cost category settings)]} Forecast final margin ÷ forecast final revenue.

Forecast revenue earned

Billing method	Revenue forecast method	Calculation
Time & Material		WHEN the <i>Revenue is considered earned when a LEM is setting</i> is set to <i>Pending</i> THEN sum of 'BillAmount' values where 'BatchType' = LEM AND DocumentStatus <> <i>Cancelled</i> OR <i>Pending removal</i> ELSE WHEN the <i>Revenue is considered earned when a LEM is setting</i> is set to <i>Approved</i> THEN sum of all 'BillAmount' values where 'BatchType' = LEM AND DocumentStatus <> <i>Cancelled</i> OR <i>Pending approval</i> OR <i>Pending removal</i>.
All other methods		Sum of assigned cost items' Forecast revenue earned.

9.22 COST PLUS REVENUE FORECAST METHODS

Another phrase for the Cost plus billing method is **Time and Material** or **Time and Expenses**. Instead of having a contractual agreement of being paid a certain lump sum, you are reimbursed for your time, labor, and equipment hours and any materials that you purchased as well. With Cost plus, a markup value is typically included. You submit time cards each week to get paid for your labor hours, equipment hours, and any materials or supplies that you purchased plus any markup value that had been agreed upon.

The Cost plus Revenue Forecast Methods are only applicable to pay items that have a billing method of Cost plus. These forecast methods include:

- Billed
- Earned
- Manual

The following image and table show details for the revenue forecast methods.

CBS

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

Actions

Billed date: 09/06/2017 to 10/01/202

Drag a column header and drop it here to group by that column

	Pay item number	Description	Total price	Unit price	Pay qua...	Fore... T/O Qty	UoM	Is billed	Billing met...	Cha... order	Rev... fore... met...	Forecast final revenue
☐	Pay 2	Pay 2	\$ 56,566,100.06...	\$ 565,650...	100.00194	0.00000	SB UOM 5...	☒	Unit price	(7)	Default	\$ 0.00000
☐	90909190	909090	\$ 1,234,560.000...	\$ 1,230.00...	1,003.707...	0.00000	-0098765...	☒	Cost plus	(9)	Billed	\$ 47,866.66667
☐	TEST1	Cost plus test1	\$ 100.00000	\$ 10.00000	10.00000	10,000.00...	new_bug1...	☒	Cost plus	(6)	Billed	\$ 21,809.00000
☐	TEST2	Danielle fixed final price...	\$ 100.00000	\$ 100.000...	1.00000	1.00000	PLS	☒	Fixed final	(10)	Default	\$ 100.00000
☐	danielle test 2	cost plus 2	\$ 100.00000	\$ 10.00000	10.00000	1.00000	-00987655	☒	Cost plus	(6)	Billed	\$ 20,950.00000
☐	Pay1		(\$ 60.00000)	\$ 20.00000	-3.00000	2,000.000...	-00987655	☒	Fixed final	(14)	Default	(\$ 60.00000)
☐	1111	1111	\$ 10,000.00000	\$ 10,000.0...	1.00000	100.00000	MP_Test18	☒	Fixed final	(11)	Default	\$ 10,000.00000
☐	1234567890...		\$ 10.00000	\$ 10.00000	1.00000	100.00000	Acre	☒	Unit price	(9)	Default	\$ 1,000.00000
☐	C3333	C33	\$ 360.00000	\$ 220.000...	1.63636	22.00000	TEST SB U...	☒	Unit price	(11)	Default	\$ 4,840.00000
☐	A11	A11	\$ 70.00000	\$ 70.00000	1.00000	7.00000	-0098765...	☒	Unit price	(8)	Default	\$ 490.00000
☐	Pay110	Pay110	\$ 70.00000	\$ 70.00000	1.00000	7.00000	-0098765...	☒	Unit price	(11)	Billed	\$ 606.15000
☐	Pay7878		\$ 70.00000	\$ 70.00000	1.00000	7.00000	-0098765...	☒	Cost plus	(12)	Default	\$ 100.00000
☐	kunal		\$ 20.00000	\$ 10.00000	2.00000	10.00000	-0098765...	☒	Unit price	(10)	Default	\$ 100.00000
☐	33		\$ 23.00000	\$ 3.00000	7.66667	123.00000	Acre	☒	Unit price	(4)	Default	\$ 369.00000
☐	Road #2	Road #2	\$ 400,000.00000	\$ 200.000...	2,000.000...	2,000.000...	Ft	☒	Unit price	(6)	Manual	\$ 400,000.00000
☒	Electrical dev...	Electrical devices	\$ 800,000.00000	\$ 400,000...	2.00000	0.00000	PLS	☐	Cost plus	(3)	Billed	\$ 0.00000

Forecast method	Description
Billed	All of your forecast remaining revenue that is driven off your cost items. Meaning this method's calculation is the following: 1 - % complete x Work Hours x Billing Rate . This gives you your Forecast Remaining revenue which is your Remaining revenue you need to earn on the cost item. For the pay item, the revenue sums up all of those remaining revenues at the cost item level. It then adds anything that has been billed which is the Remaining revenue at the cost item level plus any revenue that has been billed to the pay item.
Earned	Similar to the Billed Revenue except it uses the Forecast remaining revenue. The Earned Revenue calculation is your forecast remaining revenue at the cost item level summed up for all the cost items assigned to that pay item plus your earned revenue. The earned revenue is also driven by the cost items. To summarize, it is the forecast remaining revenue plus anything that you earned. This is also the calculation for your percent complete as well.
Manual	manually forecasts your final revenue on that pay item with you entering in a value.

9.23 PUSH FORECAST REVENUE

The Push Forecast revenue syncs all of your revenue details from the Pay Items tab to an ERP system. In the CBS register, go to Actions > Sync > **Push Forecast revenue** to start the sync.

CBS

Actions

Global forecast method..

Set forecast method

Update Forecast (T/O) qty with Plan compone...

Claim multiple CBS quantities

Budget move and contract adjustment

Lock/unlock budget

Sync

Task details

Resources	Forecast (T/O) qty
	1.00
5	10,000.00
5	10,000.00

☐	4.1	Erect Steel - Hea	
☐	4.2	Erect Steel - Lig	
☐	4.3	Bolted Connecti	
☐	4.4	Labor	
☐	4.5	Equipment	
☐	4.6	3rd Party	
☐	5	Materials	
☐	5.1	Earthwork - Mat	
☐	5.2	Concrete - Mate	

Push CBS structure

Push CBS structure and Budget

Push CBS structure and Live forecast

Push CBS structure and Actual quantities

Push CBS structure, Budget, Live forecast, and ...

Push Pay Item

Push Billed revenue

Push Forecast revenue

Get quantities

Get Actual cost and MHrs


Get Billed revenue

9.23.1 Revenue Snapshots

Revenue snapshots capture pay item information and cost item revenue information using the sync Push Forecast revenue. When a project forecast revenue is pushed, it generates a revenue snapshot.

When the project month rolls over, the last push revenue forecast sync before month-end is recorded. If a sync has not run during the month, then the system automatically takes the revenue forecast snapshot based on the date and time.

After the revenue snapshot has been recorded, you can look at past snapshots to view previous values. For example, in the pay items register you can view current and previous Revenue snapshots using the Revenue snapshots in the drop-down menu.

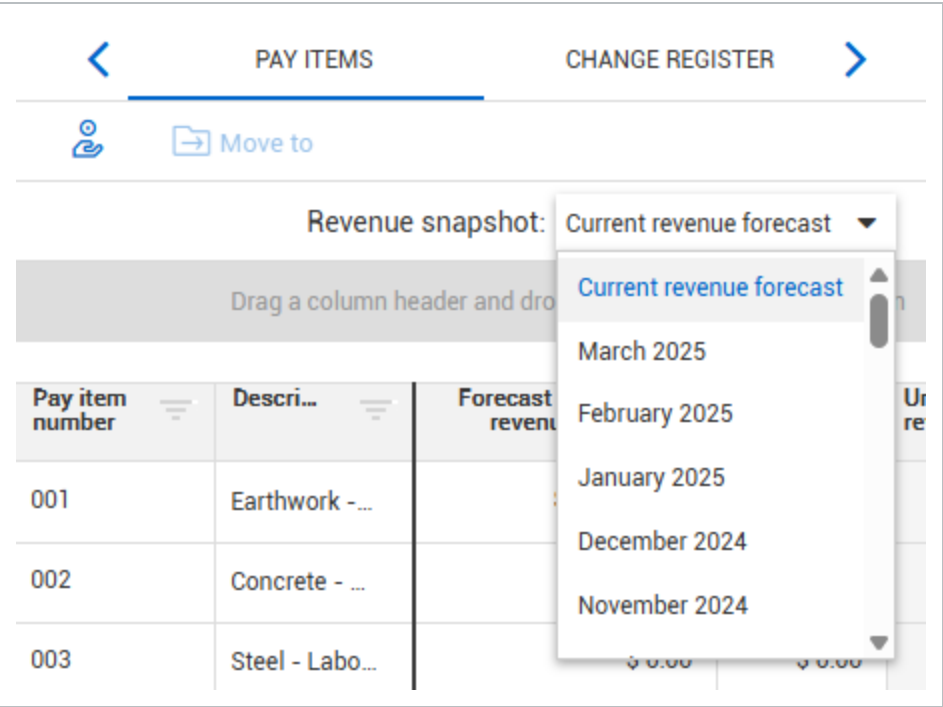

If you view a past snapshot, the data that loads is read-only. You cannot edit any of the fields.

Steel Structure Training J... / Control / Workspaces

CBSACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

View: Revenue

Revenue snapshot: March 2025Billed date: 09/30/2015 to 03/07/2025

Drag a column header and drop it here to group by that column

	Pay item position	Pay item number	Descri...	Forecast total revenue	Fore... reve... unit	Un... rev...	Rev... fore... met...	Curr... billing met...	Is billed	Billed reve...	Billed qty	Rev... earn...	Quantity earned	Pen... billa... reve...	Pending billable qty
	1	001	Earthwork - ...	\$ 650,000.00	\$ 0.00	\$ 0.00	Earned	Cost plus	☐	\$ 0.00		\$ 0.00		\$ 0.00	
	2	002	Concrete - ...	\$ 0.00	\$ 0.00	\$ 0.00	Default	Unit price	☐	\$ 0.00		\$ 0.00	0.00	\$ 0.00	
	3	003	Steel - Labo...	\$ 0.00	\$ 0.00	\$ 0.00	Default	Unit price	☐	\$ 0.00		\$ 0.00	0.00	\$ 0.00	
Subtotals 3				\$ 650,000.00	\$ 0.00					\$ 0.00		\$ 0.00		\$ 0.00	

The billed date shows the earliest build of the project when the snapshot was taken and includes any pay items in the pay item register. The snapshot might not include back-dated bills or newly created pay items. The snapshot might include deleted pay items.

PAY ITEMSCHANGE REGISTERAUDIT LOG

Revenue snapshot may not include back-dated bills or newly created pay items, and it may include deleted pay items

Billed date: 06/18/2019

For example, February has ended and the snapshot was taken it is now March and you backdated a bill, such as billed revenue or billed quantity into February. The backdated bill is not included in February's snapshot because the snapshot had already been taken.

The snapshot is automatically recorded by month and year. Whenever the month ends, the monthly Revenue snapshot shows in the revenue snapshot drop-down list.

The snapshot records the revenue columns for pay items. The columns are the following:

- Forecast final revenue
- Forecast remaining revenue
- Forecast revenue earned
- Forecast unit revenue
- Percent margin
- Forecast final margin

The snapshot records the information automatically based on your fiscal calendar settings.

9.24 REVENUE FORECAST PROBABILITY

Revenue can come from Control or Change. Only Contract Adjustments have revenue. You can also adjust your pay item values in a Contract Adjustment. For example a drop down field called Approval Probability is a drop down of all your revenue categories and their associated probability. This drop down field displays the Approval probability by percentage and associated name.

Follow the steps below to select an approval probability.

Approval Probability

1. Select the **Actions** drop down menu.
2. Hover over **Budget move and contract adjustment**, then click **Contract Adjustment**.
3. In the Approval probability drop down, select the percentage and associated name.
4. In step 3, select the add icon to add either new or existing pay items.
5. Enter a value into the **Adjusted total price** text box.
6. Either save as **Draft** or select the **Submit** button. Now it shows the selected approval probability in the Change Register. It also displays in the line item slideout. This updates automatically based on status changes.

7. If your line item is approved, it has a 100.00% in the Approval Probability column.
8. If a Contract Adjustment has been **revised** or **rejected**, then the line item has a 0.00% in the Approval Probability column.

That Contract Adjustment's revenue is never going to be earned or added to the pay items because a new Contract Adjustment has been created.

9. If your line item is in a **Draft** or **Pending** state, the Approval Probability column displays the approval probability you selected for that line item.

If you don't select an approval probability, the Approval Probability column is blank.

Your Approval Probability drives the price you include in your Forecast Final Revenue. For this next example, we are going to include the Unapproved Revenue into the Forecast Final Revenue. In the Pay Items Register, the Unapproved Revenue column calculates all the Contract Adjustments. The column adds up all Contract Adjustments that include the pay item and the adjusted price that has not yet been approved. The Unapproved Revenue column calculates anything that is in a **Draft** or **Pending** state.

CBS

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

Actions

+

×

Billed date:

06/19/2019

to

10/01/2020

Drag a column header and drop it here to group by that column

	Pay item number	Description	Pay Item User	Forecast final revenue	Fore... unit reve...	% Mar...	Billed reve...	Billed qua...	Rev... fore... met...	Rev... earn...	Quantity earned	Unapproved revenue	Pending billable quantity
☐	1			\$ 212.00	\$ 26.50	100.00 %	\$ 0.00	-1.00	Default	\$ 0.00	0.00		1.00 \$ 0.
☐	001	Pay Item 1		\$ 112,594,397.58	\$ 0.91	100.00 %	\$ 10,020.12	888,910.12	Default	\$ 112,594,...	123,458.77		-765,451.35 \$ 1.
☐	005	Danielle test		\$ 105,062.40	\$ 105.06	-4,278.83 %	\$ 105,062...	822.00	Billed	\$ 875,767...			\$ 7.
☐	123	123		\$ 4,014,854.93	\$ 1,003.71...	100.00 %	\$ 220,485...	219.67	Default	\$ 3,954.88...	3.94		-215.73 (\$.
☒	12345	12345		\$ 3,010.00	\$ 3,010.00	100.00 %	\$ 124.00	1.00	Default	\$ 0.00	0.00	\$ 1,000.00	-1.00 (\$.

In Pay Item Details, the Change Orders, you can view the following details:

- Total price change
- Total unit price change
- Total pay quantity change
- Approval probability
- Adjusted forecast final revenue
- Status

12345						
12345						
Total Price		Pay Quantity		Unit Price		
\$ 3,000.00		1.00		\$ 3,000.00		
DETAILS		ATTRIBUTES		CHANGE ORDERS		COST ITEMS
Issue #	Total price change	Total unit price change	Total pay qty change	Approval probability	Adjusted forecast final revenue	Status
	\$ 1,000.00	\$ 0.00	0.33	1.00 %	\$ 10.00	Draft
	\$ 0.00	(\$ 3,000.00)	0.00	0.00 %	\$ 0.00	Pending
	\$ 0.00	(\$ 3,000.00)	0.00	0.00 %	\$ 0.00	Revised
	\$ 3,000.00	\$ 3,000.00	1.00	100.00 %	\$ 3,000.00	Approved

The Forecast Final Revenue is the sum of all the Adjusted Forecast final revenue. Calculating the Unapproved Revenue with the Forecast Final Revenue provides you with a more accurate look at the revenue you will see when the Contract Adjustment is approved. Nothing is added into the Total Pay Item Price until it is approved.

Approval Probability drop down is only available in the Contract Adjustment. Everywhere else it is read only. To manually adjust the Contract Adjustment, go to the **Change Register**. Then right click the line item you want to change and select **Revise**. The Contract Adjustment can also automatically change based on status changes.

The Revenue Category Name and probability percentage drives the Approval Probability. The Revenue Category Name draws from the Revenue Categories in the Master Data libraries.

English					Español		ES-MX
Revenue category name	Revenue change status name	Probability percentage	State		Revenue category name	Revenue change status name	
☐ ss1	ss		11	Active	ss1	ss	
☐ ss	ss		11	Active	ss	ss	
☐ @222222222	sdsad		111	Active	@222222222sda	sdsad	
☐ New Demo S72 EN1	English1		410	Inactive	New Demo S72 EN1	English1	
☐ New Demo S72 EN	Englishas		10	Active	New Demo S72 EN	English	
☐ 0918	0918		9.18	Active	0918	0918	
☐ HVT_18/09/2020_edit	HVT_18/09/2020		23	Active	HVT_18/09/2020	HVT_18/09/2020	
☐ Count1	Count		10	Active	Count1	Count	
☐ Count	Count		18	Active	Count	Count	
☐ 23ASDA	23ASDA		23	Active	asda	qw	
☐ 123123123123123	123123123123		23	Active	123123123123123	123123123123	
☐ lo	lo		9	Active	lo	lo	
☐ Rev_eng	Rev_eng		99	Active	Rev_eng	Rev_eng	
☐ Check 1_eng	Check 1_eng		100	Active	Check 1_eng	Check 1_eng	

The Revenue Categories show the Revenue category name and probability percentage for only **active** revenue.

9.25 TIME-PHASED BUDGET

Time-phased budget lets you plan out where to spend money in the months of the active fiscal calendar for the project.

The point of being able to time phase your budget is so that you can plan out your budget cost per cost item. You are spreading out your budget over the course of the project for each cost item.

9.25.1 Budget organization setting

The time-phased budget feature includes an organization setting located in the Project tracking tab of the Control settings. The organization setting sets the default for all the projects within that organization.

You can also change the budget setting at the project level. If you are starting new projects in your organization, you need to have Time phasing budget switched on.

By default all the projects that are created under that organization also have the time phased budget enabled. This is the same for when budget is disabled.

Time phasing

Enable time phasing for the following:

Budget ⓘ

☒

Edit past Time phased budget values

☐

9.25.2 Edit Past Time-Phased Budget Values

The Edit past Time phased budget values toggle lets you edit past fiscal period time phased budget values.

Time phasing

Enable time phasing for the following:

Budget 



Edit past Time phased budget values



When this setting is enabled, you can edit your past time phased budget values via a budget move or a contract adjustment in the time phased budget step, with the proper permissions.

Change register

>

Contract adjustment

Net budget change

\$ 0.00

Net quantity change

No

Net man hour change

0.00

Markup

\$ 0.00

Fee

\$ 0.00

Net contract change

\$ 0.00

Approval probability

1 Details

2 Cost items

3 Time phased budget

4 Pay items

5 Summary

	CBS position	Description	WBS phase code	Start	Finish	Cc	January 2022		February 2022	
							Cost	Adjusted cost	Cost	Adjusted cost
	2.3.1.1.1	Resurface Existing Access road	1004	10/16/2022	11/15/2022	Lin	\$ 212.33	(\$ 212.33)	\$ 191.78	\$ 212.33
	2.3.1.1.2	Maintain Access Road	1005	10/16/2022	11/15/2022	Lin	\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00

Selecting the new Rebaseline icon resets the cost item's time-phased budget distribution based on the Start and Finish dates against that cost item. Rebaselining lets you amend your time-phased budget distribution costs for a cost item.


You can also edit any of the Adjusted cost values manually for past months.

☐	CBS position	Description	Start	Finish	April 2022		May 2022	
					Adjusted cost	Cost	Adjusted cost	Cost
☐	2.3.1.1.1	Resurface Existing Access	10/16/2022	11/15/2022	\$ 205.48	\$ 0.00	\$ 212.33	\$ 0.00
☒	2.3.1.1.2	Maintain Access Road	05/01/2022	12/31/2022	\$ 0.00	\$ 471.92	\$ 0.00	\$ 975.31

At the project level, the time-phased budget inherits the organization settings, but still lets you switch the budget setting *On* or *Off* at the project level. For example, you can have time phased budget turned on at the organization level and you can turn it off at the project level.

9.25.3 Switching off time-phasing budget

If the Time phasing budget is switched on, that means there is time-phasing budget data in the database. If you turn it off time phasing budget at the project level, it gives you the following warning message:

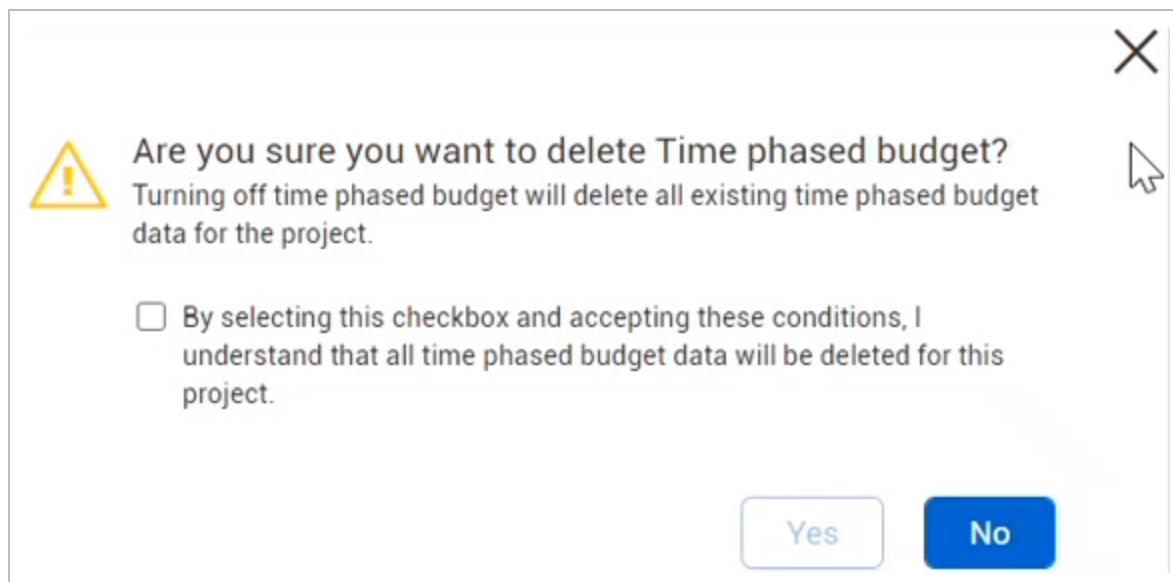

All of your time-phased budget data is going to be deleted if you switch time phased budget off. You must select the check box in the warning dialog acknowledging that you understand and accept these conditions.

If you still want to turn off the time phasing budget, you can select **Yes** and then click **Save**. This will delete the time-phasing budget data from the database.

9.25.4 Switching on the time-phasing budget

If you want to turn on time phased budget, the following dialog box appears if there are any missing start or end dates:

Cost items are missing start and end dates.

How would you like to populate the missing cost item start and end dates?

☒ Default all budget to current fiscal period

☐ Default to project start and end dates

☐ Go back and populate the missing dates

Cancel
Confirm

Every cost item in your project needs the start and finish date entered to use that data in the time-phase budget.

When time-phased budget data is calculated, the calculation is based off of the data in the current budget and total cost for the cost item. Then, the cost is distributed to the cost items start date, finish date, and cost curve.

Time phased budget < • >				
CB total cost	Start	Finish	Cost curve	Pending budget cost
\$ 48,790.00	01/01/2020	03/31/2022	Linear	\$ 150.00
\$ 25,020.00	01/01/2020	07/30/2021	Back Loaded	(\$ 5,060.00)
\$ 5,050.00	12/30/2020	12/31/2020	Front Loaded	\$ 4,640.00
\$ 5,120.00	01/01/2021	05/31/2021	Linear	\$ 540.00
\$ 1,600.00	12/01/2020	03/31/2021	Custom curve 1	\$ 10.00
\$ 1,000.00	12/01/2020	05/15/2021	Bell Shaped	\$ 10.00
\$ 11,000.00	12/01/2020	03/31/2022	Custom curve 2	\$ 10.00

9.25.4.1 Default all budget to current fiscal period

The first option you have is to default all of the budget to the current fiscal period. Then, all cost items that don't have defined start and finish dates have the current budget going to the current fiscal

period.

For example, if you look at WBS phase code 1007, you would have \$100,000 put into December 2020.

Tasks				Time phased budget				
☐	✓ CBS position	Description	WBS phase code	CB total cost	Start	Finish	Cost curve	Pending budget cost
☐	1	Electrical devices	1000	\$ 48,790.00	01/01/2020	03/31/2022	Linear	\$ 150.00
☐	1.1	Install conduit	1002	\$ 25,020.00	01/01/2020	07/30/2021	Back Loaded	(\$ 5,060.00)
☐	1.2	Fiber optic cable-1	1001.1	\$ 5,050.00	12/30/2020	12/31/2020	Front Loaded	\$ 4,640.00
☐	1.3	Pull cable	1003	\$ 5,120.00	01/01/2021	05/31/2021	Linear	\$ 540.00
☐	1.4	CCTV devices	1004	\$ 1,600.00	12/01/2020	03/31/2021	Custom curve 1	\$ 10.00
☐	1.5	Terminations	1005	\$ 1,000.00	12/01/2020	05/15/2021	Bell Shaped	\$ 10.00
☐	1.6	Light poles	1006	\$ 11,000.00	12/01/2020	03/31/2022	Custom curve 2	\$ 10.00
☐	2	Indirects	1008	\$ 305,000.00			Linear	\$ 0.00
☐	2.1	Staff	1010	\$ 305,000.00			Linear	\$ 0.00
☐	2.1.1	PM	1007	\$ 100,000.00			Linear	\$ 0.00
☐	2.1.2	PE	1009	\$ 85,000.00			Linear	\$ 0.00
☐	2.1.3	Super	1011	\$ 120,000.00			Linear	\$ 0.00
☐	3	Staff training	1012	\$ 5,500.00			Linear	\$ 0.00
☐	4	Craft training	1013	\$ 17,500.00			Linear	\$ 0.00
☐	5	ST&S	1014	\$ 45,000.00			Linear	\$ 0.00
Subtotals 64				\$ 431,790.00				\$ 150.00

9.25.4.2 Default to project start and end dates

The next option is to default to the start and end dates. On the project details page you define all the project start and end dates. After those are defined, then we can default all of those missing start and end dates to just the project start and end dates.

9.25.4.3 Populate missing dates manually

You can also return to the Time phased budget step and manually populate the missing dates. If you choose this option, the budget setting turns off again (if it wasn't already turned off and on again in previous sections). You then have to go into the CBS and manually enter all the start and finish dates. Then, you could turn the budget setting back on and it should distribute the budget.

Time-phased budget data currently can only be seen in the CBS contract adjustment.


For more information about settings for time phasing budget, see [Time-phasing](#).

9.25.5 Time-phased budget in contract adjustment

From the CBS, select cost items to adjust in the contract adjustment.

Tasks				Time phased budget				
☐	CBS position	Description	WBS phase code	CB total cost	Start	Finish	Cost curve	Pending budget cost
☐	1	Electrical devices	1000	\$ 48,790.00	01/01/2020	03/31/2022	Linear	\$ 150.00
☒	1.1	Install conduit	1002	\$ 25,020.00	01/01/2020	07/30/2021	Back Loaded	(\$ 5,060.00)
☒	1.2	Fiber optic cable-1	1001.1	\$ 5,050.00	12/30/2020	12/31/2020	Front Loaded	\$ 4,640.00
☒	1.3	Pull cable	1003	\$ 5,120.00	01/01/2021	05/31/2021	Linear	\$ 540.00
☐	1.4	CCTV devices	1004	\$ 1,600.00	12/01/2020	03/31/2021	Custom curve 1	\$ 10.00

Then select the **Actions** drop-down, hover over the **budget move and contract adjustment** and then select **Contract adjustment**.

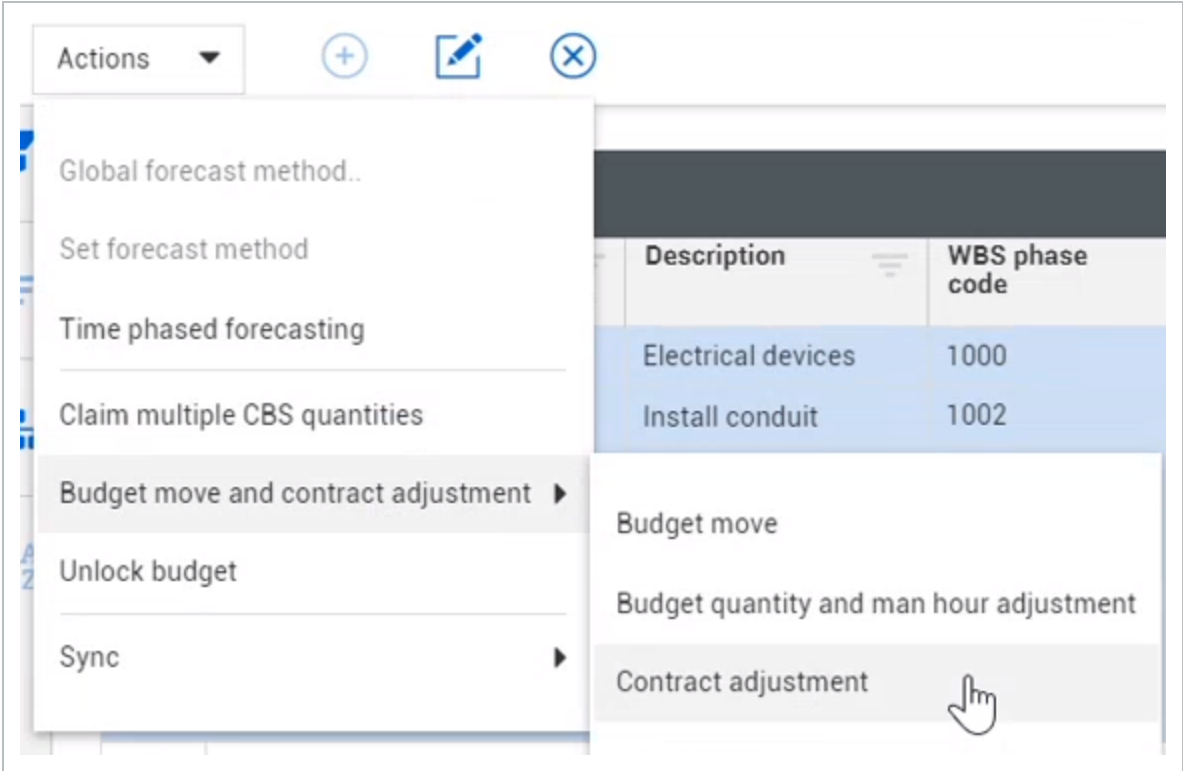

In the contract adjustment, there is an area called Change order attributes. This area lets you set your change orders/contract adjustment to the following:

- Start date
- Finish date
- Cost curve

1 Details2 Cost items3 Time phased budget4 Pay items5 Summary

Choose your Contract adjustment workflow

☒ Start with Cost items
Enter markup and fees on cost items to generate pay item price

☐ Start with Pay items
Adjust pay item price before adjusting cost item budgets

Change order attributes

Start date

2020 ▼

December ▼

Finish date

2020 ▼

December ▼

Cost curve


Linear ▼

Contract adjustment details

Issue #

CCO

Cost Curve can be adjusted in many ways. If you select **Bell Shaped** the cost adjustments increase during the summer months and then decreases in the winter months.

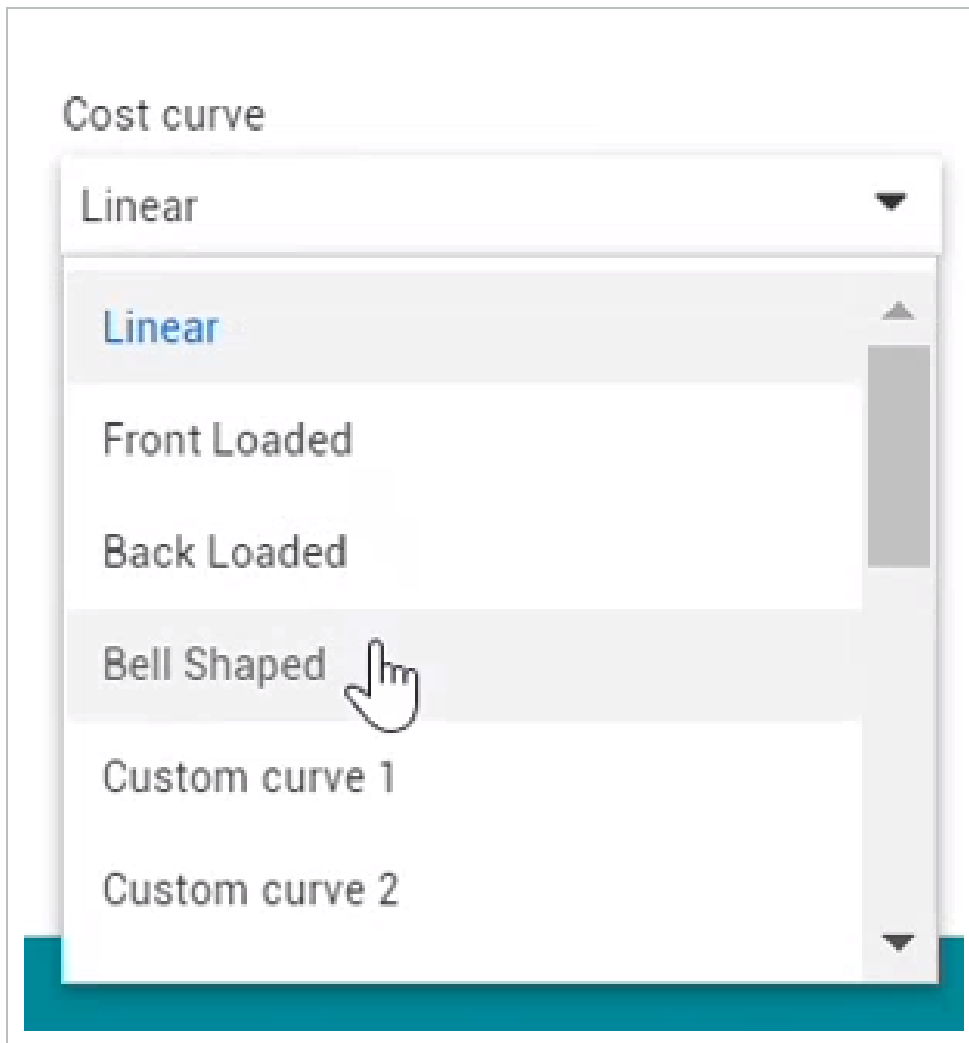

In step 3 of the contract adjustment, the Time phased budget step can be used for both Start with Cost items work flow and the Start with Pay items work flow. You can adjust your time phased budget in either contract adjustment work flow.

The only time your time-phased budget should change is when you get change orders and you have to change your overall budget amount.

For the Start dates, you cannot put budget in the past. If you try to select a month that has already passed, you will get an error stating Start date must be in an open fiscal period.

Change order attributes

Start date: 2020 January Finish date: 2021 December Cost curve: Linear

Start date must be in an open fiscal period

Finish date has to be greater than your start date otherwise you get the following error.

Finish date: 2020 December Cost curve: Linear

Finish date cannot be earlier than start date

Move onto step 2 Cost Items. You can add Adjusted CB total cost. In this example we are adding \$100 to each cost item.

1 Details 2 Cost items 3 Time phased budget

Assign cost to

	CBS position	Description	WBS phase code	CB total cost	Adjusted CB total cost	Markup %
Unassigned cost items						
☐	1.2	Fiber optic cable-1	1001.1	\$ 5,050.00	\$ 100.00	
☐	1.1	Install conduit	1002	\$ 25,020.00	\$ 100.00	
☐	1.3	Pull cable	1003	\$ 5,120.00	\$ 100.00	
☐	1.4	CCTV devices	1004	\$ 1,600.00	\$ 100.00	
☐	1.5	Terminations	1005	\$ 1,000.00	\$ 100.00	
☒	1.6	Light poles	1006	\$ 11,000.00	\$ 100.00	

In the Time phased budget step, the 100 dollars now has to be distributed. Scroll over to the Distribution type column.

In step 3, only terminal cost items are brought into that grid. Non-terminal cost items do not show on the Cost items grid of the contract adjustment.

[illegible]

There are three different Distribution types:

- Change order (default setting)
- Cost Item
- Manual

When Distribution type is set to **Change order**, it means it is pulling in the start date, finish date, and cost curve from the details step of your change order.

The changes to the Adjusted total cost column are then distributed throughout the start and finish date and shows in the Adjusted Cost column.

If your cost curve was set to **linear**, roughly the same amount of cost goes into the same fiscal period. Since some months are longer than others, they will have additional cost.

1

Details

2

Cost items

3

Time phased budget

4

Pay items

5

Summary

\$ 0.00

Dec 2020 - Dec 2021

View Cost column

☐	CBS position	Description	WBS phase code	Start	Finish	Cost curve	Distribution type	October 2021		November 2021		December 2021	
								Cost	Adjusted cost	Cost	Adjusted cost	Cost	Adjusted cost
☐	1.1	Install conduit	1002	12/27/2020	12/25/2021	Linear	Change order	\$ 0.00	\$ 9.62	\$ 0.00	\$ 7.69	\$ 0.00	\$ 7.69
☐	1.2	Fiber optic cable-1	1001.1	12/27/2020	12/25/2021	Linear	Change order	\$ 0.00	\$ 9.62	\$ 0.00	\$ 7.69	\$ 0.00	\$ 7.69
☐	1.3	Pull cable	1003	12/27/2020	12/25/2021	Linear	Change order	\$ 0.00	\$ 9.62	\$ 0.00	\$ 7.69	\$ 0.00	\$ 7.69
☐	1.4	CCTV devices	1004	12/27/2020	12/25/2021	Linear	Change order	\$ 0.00	\$ 9.62	\$ 0.00	\$ 7.69	\$ 0.00	\$ 7.69
☐	1.5	Terminations	1005	12/27/2020	12/25/2021	Linear	Change order	\$ 0.00	\$ 9.62	\$ 0.00	\$ 7.69	\$ 0.00	\$ 7.69
☐	1.6	Light poles	1006	12/27/2020	12/25/2021	Linear	Change order	\$ 792.18	\$ 9.62	\$ 633.74	\$ 7.69	\$ 633.74	\$ 7.69

9.25.6 Time-phased budget at the budget move

Time-phased budget is included for both the non-associated and associated budget move.

The total adjusted CB total cost must be zero before you can move budget. This shows as a net zero budget adjustment when you are moving budget from cost items to other cost items. You can also move the time-phased budget.

You can set the start date, finish date, and cost curve for the budget move change orders.

1 Details

2 Assign amounts

3 Time phased budget

4 Summary

Choose your Budget move workflow

☐ **Associated**
 Define budget moves with a From and To process to provide ultimate traceability of budget moves.

☒ **Non-Associated**
 Define budget moves freely to provide the most flexibility.

Change order attributes

Start date
 2021 ▼ April ▼

Finish date
 2021 ▼ December ▼

Cost curve
 Linear ▼

Budget move details

Issue #

CCO

Description

500

The Time phased budget step is similar to the Time phased budget step for Contract adjustment. The distribution type on this step is where you can select to distribute by the change order attributes or the cost item attributes. You can also manually adjust your cost.

Change register

Budget Move

1 Details

2 Assign amounts

3 Time phased budget

4 Summary

\$ 0.00

Feb 2021 - Aug 2021

View Cost column

	CBS position	Description	WBS phase code	Start	Finish	Cost curve	Distril type	February 2021	March 2021	April 2021			
								Cost	Cost	Adjusted cost	Cost	Adjusted cost	Cost
☒	41	Cost item 1	01	05/01/2021	12/31/2021	Linear	Cost R	\$ 0.00	\$ 1,500.00	\$ 0.00	\$ 0.00	\$ 0.00	
☒	42	Cost item 2	02	05/01/2021	05/01/2022	Front Loaded	Cost R	\$ 0.00	\$ 200.00		\$ 0.00	\$ 0.00	

Cancel

Draft

Back

Next

When you adjust the budgeted cost either through a contract adjustment or a budget move, you can adjust the cost over the different fiscal periods and decide where to place the adjusted cost.

9.25.7 Time-phased budget grids

In the left side grid, you have many of the cost item details in columns. This includes the following columns:

- CBS position
- Description
- WBS phase code
- Start
- Finish
- Cost curve
- Distribution type
- CB total cost
- Adjusted CB total cost
- Pending budget cost: any outstanding budget cost that has not yet been approved. For example, if you have another pending contract adjustment, it adds those values in this column.
- Phased budget cost delta

☐	CBS position	Description	CB total cost	Adjusted CB total cost	Pending budget cost	Phased budget cost delta
☐	1.1	Install conduit	\$ 25,020.00	\$ 100.00	(\$ 5,060.00)	\$ 0.00
☐	1.2	Fiber optic cable-1	\$ 5,050.00	\$ 100.00	\$ 4,640.00	\$ 0.00
☐	1.3	Pull cable	\$ 5,120.00	\$ 100.00	\$ 540.00	\$ 0.00
☐	1.4	CCTV devices	\$ 1,600.00	\$ 100.00	\$ 10.00	\$ 0.00
☐	1.5	Terminations	\$ 1,000.00	\$ 100.00	\$ 10.00	\$ 0.00
☐	1.6	Light poles	\$ 11,000.00	\$ 100.00	\$ 10.00	\$ 0.00

You can adjust the amount of columns you see using the slider to move between the left side grid and the right side grid.

The right side grid shows your cost and adjusted cost columns. Your cost columns show current cost that has been approved.


For example, in the **CB total cost** column, if you have \$1,000 approved, the cost columns for each month distributes that cost throughout each month.

1 Details 2 Cost items 3 Time phased budget 4 Pay items 5 Summary \$ 0.00 Dec 2020 - Dec 2021 View Cost column													
CBS position	Description	CB total cost	Adjusted CB total cost	December 2020		January 2021		February 2021		March 2021			
				Cost	Adjusted cost	Cost	Adjusted cost	Cost	Adjusted cost	Cost	Adjusted cost		
☐	1.1 Install conduit	\$ 25,020.00	\$ 100.00	\$ 0.00	\$ 0.00	\$ 0.00	\$ 9.62	\$ 0.00	\$ 7.69	\$ 0.00	\$ 0.00		\$
☐	1.2 Fiber optic cable-1	\$ 5,050.00	\$ 100.00	\$ 0.00	\$ 0.00	\$ 5,050.00	\$ 9.62	\$ 0.00	\$ 7.69	\$ 0.00	\$ 0.00		\$
☐	1.3 Pull cable	\$ 5,120.00	\$ 100.00	\$ 0.00	\$ 0.00	\$ 1,017.22	\$ 9.62	\$ 949.40	\$ 7.69	\$ 949.40			\$
☐	1.4 CCTV devices	\$ 1,600.00	\$ 100.00	\$ 327.43	\$ 0.00	\$ 440.77	\$ 9.62	\$ 352.62	\$ 7.69	\$ 428.81			\$
☒	1.5 Terminations	\$ 1,000.00	\$ 100.00	\$ 14.43	\$ 0.00	\$ 187.96	\$ 9.62	\$ 387.76	\$ 7.69	\$ 312.69			\$
☐	1.6 Light poles	\$ 11,000.00	\$ 100.00	\$ 588.48	\$ 0.00	\$ 792.18	\$ 9.62	\$ 633.74	\$ 7.69	\$ 633.74			\$

9.25.8 Changing Distribution type to cost item

You can change the auto distribute type to Cost item if you want your adjusted budget to use attributes from the CBS.

To do this, you can select one, many, or all of your cost items in the left side grid, and then click on the **auto distribute** icon. Then select **Cost item**.

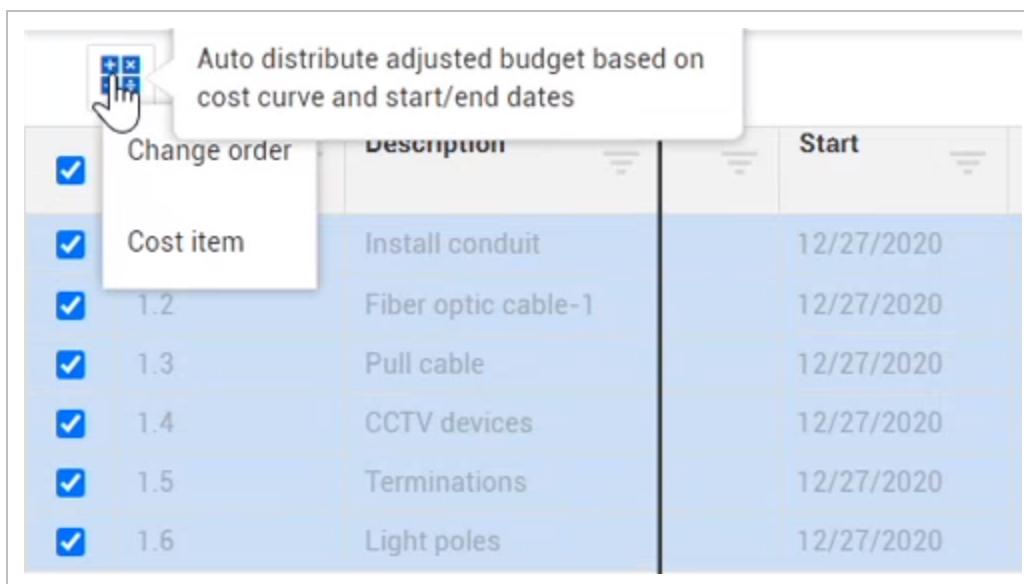

Your Distribution type has changed to cost item. You are now distributing your adjusted budget based on the cost item attributes that are pulling in from the CBS.

☐	CBS position	Description		Finish	Cost curve	Distribution type	CB total cost
☒	1.1	Install conduit	020	07/30/2021	Back L...	Cost item	\$ 25,020
☒	1.2	Fiber optic cable-1	020	12/31/2020	Front ...	Cost item	\$ 5,050
☒	1.3	Pull cable	021	05/31/2021	Linear	Cost item	\$ 5,120
☒	1.4	CCTV devices	020	03/31/2021	Custo...	Cost item	\$ 1,600
☒	1.5	Terminations	020	05/15/2021	Bell Sh...	Cost item	\$ 1,000
☒	1.6	Light poles	020	03/31/2022	Custo...	Cost item	\$ 11,000

This also changes how the Cost curve distributes the adjusted cost. As you can see from the screenshot above, some cost curves have been adjusted.

9.25.9 Manual distribution of cost adjustment


You can change a specific cost item's cost adjustment to zero and then manually redistribute that zeroed cost to other months. If you do not distribute the cost to other months, the following missing amount for the adjustment cost is highlighted in orange.

December 2020		January 2021		February 2021			
Cost	Adjusted cost	Cost	Adjusted cost	Cost	Adjusted cost	Cost	
\$ 0.00	\$ 10.00 ●	\$ 0.00	\$ 50.00 ●	\$ 0.00			
\$ 0.00	\$ 0.00	\$ 5,050.00	\$ 100.00	\$ 0.00	\$ 0.00		
\$ 0.00	\$ 0.00	\$ 1,017.22	\$ 19.87	\$ 949.40	\$ 18.54		
\$ 327.43	\$ 20.46	\$ 440.77	\$ 27.55	\$ 352.62	\$ 22.04		
\$ 14.43	\$ 1.44	\$ 187.96	\$ 18.80	\$ 387.76	\$ 38.78		
\$ 588.48	\$ 5.35	\$ 792.18	\$ 7.20	\$ 633.74	\$ 5.76		

After redistribution, there are some manual indicators showing what the value was before the change.

Start	Finish	Cost curve	Distribution type	December 2020		January 2021		February 2021		Cost
				Cost	Adjusted cost	Cost	Adjusted cost	Cost	Adjusted cost	
01/01/2020	07/30/2021	Back L... 	Manual	\$ 0.00	\$ 10.00	\$ 0.00	\$ 50.00	Value before: \$ 0.00	\$ 0.00	\$ 0.00
12/30/2020	12/31/2020	Front ...	Cost item	\$ 0.00	\$ 0.00	\$ 5,050.00	\$ 100.00	\$ 0.00	\$ 0.00	\$ 0.00
01/01/2021	05/31/2021	Linear	Cost item	\$ 0.00	\$ 0.00	\$ 1,017.22	\$ 19.87	\$ 949.40	\$ 18.54	\$ 18.54
12/01/2020	03/31/2021	Custo...	Cost item	\$ 327.43	\$ 20.46	\$ 440.77	\$ 27.55	\$ 352.62	\$ 22.04	\$ 22.04
12/01/2020	05/15/2021	Bell Sh...	Cost item	\$ 14.43	\$ 1.44	\$ 187.96	\$ 18.80	\$ 387.76	\$ 38.78	\$ 38.78
12/01/2020	03/31/2022	Custo...	Cost item	\$ 588.48	\$ 5.35	\$ 792.18	\$ 7.20	\$ 633.74	\$ 5.76	\$ 5.76

The warning indicator on the cost curve column lets you know that your cost item contains manual time-phased months and is not technically back loaded anymore.

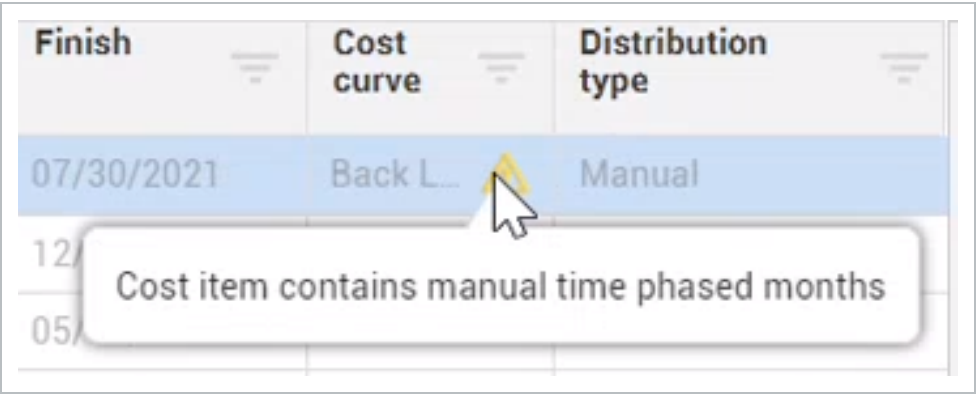

9.25.10 Deltas in a adjusted cost columns

Deltas appear on a contract adjustment when the adjusted cost for a cost item does not match the current budget total cost.

You are not allowed to submit or approve a cost item adjustment that has a delta.


That is where the **phased budget cost delta** column displays any missing or over budgeted costs for any one cost item.

This column sums up all of your adjusted cost in the right side grid and compares it to the Adjust CB total cost.

For example, if you have \$10 not distributed, you need to add it to the adjusted cost in that same cost item before moving onto the next step. If the current budget total cost has \$100, you must spread that total cost amount throughout your months.

			△ \$ 10.00 Dec 2020 - Dec 2021 View Cost column					
Adjusted CB total cost	Pending budget cost	Phased budget cost delta	December 2020		January 2021		February 2021	
			Cost	Adjusted cost	Cost	Adjusted cost	Cost	Adjusted cost
\$ 100.00	(\$ 5,060.00)	\$ 10.00	\$ 0.00	\$ 0.00	\$ 0.00	\$ 50.00	\$ 0.00	\$ 40.00
\$ 100.00	\$ 4,640.00	\$ 0.00	\$ 0.00	\$ 0.00	\$ 5,050.00	\$ 100.00	\$ 0.00	\$ 0.00


Hovering over the delta warning in the right side grid shows where the error in cost is occurring. If you have multiple deltas in different cost items, the delta cost would then sum up all delta costs.

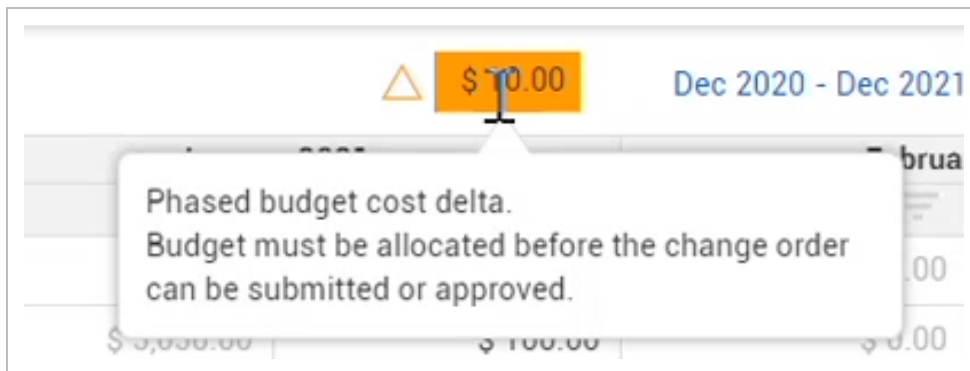

If you attempt to submit or approve the contract adjustment with deltas and you return to the Time phased budget step, the **Phased budget cost delta** column shows which cost items have a delta. You need to resolve the deltas and redistribute the costs in the **Adjusted cost** columns in the right side grid before moving forward.

			△ \$ 20.00					
CBS position	Description	Adjusted CB total cost	Pending budget cost	Phased budget cost delta	December 2020		January 2021	
					Cost	Adjusted cost	Cost	Adjusted cost
1.1	Install conduit	\$ 0.00	\$ 100.00	(\$ 5,060.00)	\$ 10.00	\$ 0.00	\$ 0.00	\$ 50.00
1.2	Fiber optic cable-1	\$ 0.00	\$ 100.00	\$ 4,640.00	\$ 10.00	\$ 10.00	\$ 5,050.00	\$ 100.00
1.3	Pull cable	\$ 0.00	\$ 100.00	\$ 540.00	\$ 0.00	\$ 0.00	\$ 1,017.22	\$ 19.87
1.4	CCTV devices	\$ 0.00	\$ 100.00	\$ 10.00	\$ 0.00	\$ 327.43	\$ 440.77	\$ 27.55

You can also adjust your delta costs using the same Auto distribution button from earlier and selecting **Change order**. Change order always distributes without a delta.

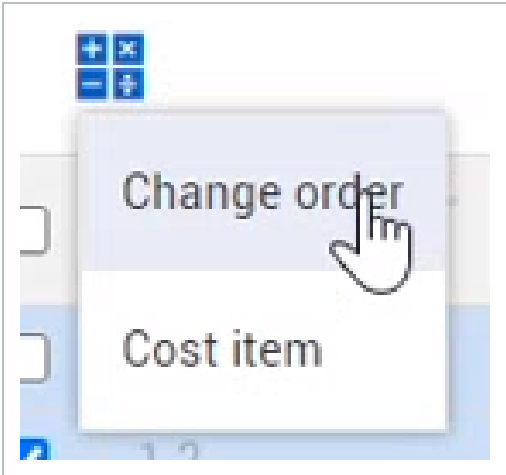

Now you can submit and approve your contract adjustment. All those values are going to be committed into your time-phased budget.

For example, if you sync into your ERP, you can receive all changes made in the contract adjustment right after those changes have been approved.

9.25.11 View cost columns


If you want to view just your adjusted cost columns, select the **View Cost column** slider to turn off your cost columns. Only the adjusted cost columns shows. These columns show what you are adjusting in the active project months for the contract adjustment.

								\$ 0.00	Dec 2020 - Dec 2021	View Cost column ☒
December 2020	January 2021	February 2021	March 2021	April 2021	May 2021	June 2021	July 2021			
Adjusted cost	Adjusted cost	Adjusted cost	Adjusted cost	Adjusted cost	Adjusted cost	Adjusted cost	Adjusted cost			
\$ 0.00	\$ 9.62	\$ 7.69	\$ 7.69	\$ 7.69	\$ 9.62	\$ 7.69	\$			
\$ 0.00	\$ 9.62	\$ 7.69	\$ 7.69	\$ 7.69	\$ 9.62	\$ 7.69	\$			
\$ 0.00	\$ 9.62	\$ 7.69	\$ 7.69	\$ 7.69	\$ 9.62	\$ 7.69	\$			
\$ 0.00	\$ 9.62	\$ 7.69	\$ 7.69	\$ 7.69	\$ 9.62	\$ 7.69	\$			
\$ 0.00	\$ 9.62	\$ 7.69	\$ 7.69	\$ 7.69	\$ 9.62	\$ 7.69	\$			
\$ 0.00	\$ 9.62	\$ 7.69	\$ 7.69	\$ 7.69	\$ 9.62	\$ 7.69	\$			

9.25.12 Date range filter

The date range filter lets you filter the right side grid to show only the months you want to see. You can view the project months based on the following options:

- This month (current fiscal month you are in)
- Next 3 months
- Next 6 months
- Next 12 months
- Through project finish date

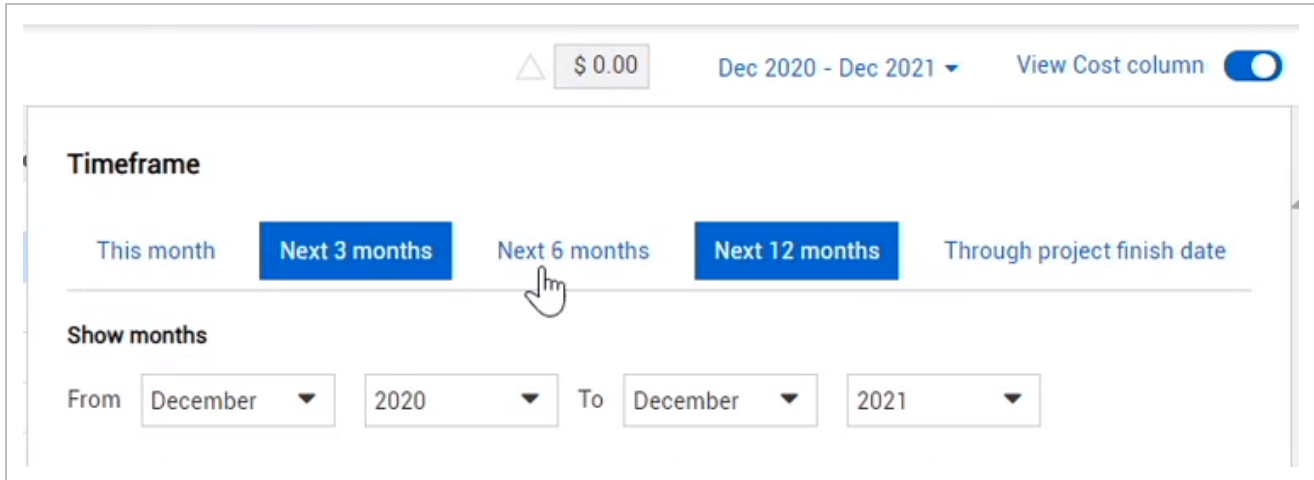

The screenshot shows a software interface for selecting a timeframe. At the top, there is a currency display showing '\$ 0.00' and a date range 'Dec 2020 - Dec 2021'. To the right is a toggle switch labeled 'View Cost column' which is currently turned on. Below this is a section titled 'Timeframe' containing five buttons: 'This month', 'Next 3 months', 'Next 6 months', 'Next 12 months', and 'Through project finish date'. The 'Next 3 months' button is highlighted with a blue background, and a mouse cursor is pointing at the 'Next 6 months' button. Below the timeframe buttons is a section titled 'Show months' with two rows of dropdown menus. The first row is labeled 'From' and contains a month dropdown (set to 'December'), a year dropdown (set to '2020'), and a 'To' label. The second row contains a month dropdown (set to 'December') and a year dropdown (set to '2021').

You can also manually select the months you want to view using the **Show months** drop-down lists.

9.25.13 Approving budget warnings

You can't approve budget set in the past. If you have any adjusted cost set for the current month (December) and the contract adjustment is approved in the next month (January), the approver receives a warning stating *you have budget in past or closed periods*.

The contract adjustment can still be approved, but the adjusted cost from the closed month moves to the following month.

The other option the approver has is to revise the adjusted cost. When revising, the adjusted cost from December has already moved into the adjust cost column for January. If you do not want all of the previous month added into a single month, you can manually move the additional adjusted cost from January into the other open fiscal period months.

9.26 REVENUE CALCULATIONS

The revenue calculations are based on the following:

- Pay items assigned billing method.
- Pay items assigned revenue forecast method.

Control calculates revenue in the CBS and Pay Item registers based on the billing and revenue forecast methods.

9.26.1 Cost Breakdown Structure (CBS) register revenue calculations

The following tables show how the different types of revenue are calculated in the CBS.

Forecast total revenue

Billing method	Revenue forecast method	Calculation
Fixed final price	Default	Earnings % x Assigned pay item's Forecast total revenue.
Unit price	Default	Earnings % x Assigned pay item's Forecast total revenue.
Cost plus	Earned (Current estimate)	IF Cost source = <i>Detail</i> THEN Forecast final revenue (labor resource) + Forecast final revenue (construction equipment resource) + Forecast final revenue (all other resources) ELSE Forecast final revenue (plug) WHERE Forecast final revenue (labor resource) = Work hours x Scale 1 % x Scale 1 Charge rate + Work hours x Scale 2 % x Scale 2 Charge rate + Work hours x Scale 3 % x Scale 3 Charge rate.[MB3.1] Forecast final revenue (construction equipment resource) = Work hours x Charge rate. Forecast final revenue (all other resources) =

Forecast total revenue (continued)

Billing method	Revenue forecast method	Calculation
	Earned (Forecast cost)	Resource quantity x Charge rate Forecast final revenue (plug) = CE revenue amount. Forecast remaining revenue + Sum for each cost category [Actual cost category cost (to date) x (1 + Cost category markup % from settings)] IF Forecast method = <i>Rollup</i> THEN Sum (children's Forecast final revenue) ELSE IF Forecast method is <i>disabled</i> THEN 0.
	Billed	IF All the Billed revenue is assigned to cost item(s) THEN Forecast remaining revenue + Billed Revenue assigned to the cost item ELSE Forecast remaining revenue + (Billed Revenue of the pay item unassigned to a cost item x (CE final cost of the cost item/CE final cost of all cost items assigned to the pay item) + Billed Revenue assigned to the cost item.
Time & Material	Earned	Forecast total revenue = Pay item forecast total revenue x (Cost item Forecast total cost / sum of all assigned cost items' Forecast total cost excluding Rollup method and disabled forecasts).
	Billed	IF All the Billed revenue is assigned to cost item(s) THEN Forecast remaining revenue + Billed Revenue

Forecast total revenue (continued)

Billing method	Revenue forecast method	Calculation
		assigned to the cost item ELSE Forecast remaining revenue + (Billed Revenue of the pay item unassigned to a cost item x (CE final cost of the cost item/CE final cost of all cost items assigned to the pay item) + Billed Revenue assigned to the cost item.
All methods	Manual	Forecast final revenue of the pay item x (CE final cost of the cost item/CE final cost of all cost items assigned to the pay item).

Forecast remaining revenue

Billing method	Revenue forecast method	Calculation
Fixed final price Unit price		Forecast final revenue of the pay item x (CE final cost of the cost item/CE final cost of all cost items assigned to the pay item).
Cost plus	Earned (Current estimate)	Forecast total revenue - Forecast revenue earned.
	Earned (Forecast cost)	IF Cost source = <i>Detail</i> THEN Forecast remaining revenue (labor resource) + Forecast remaining revenue (construction equipment resource) + Forecast remaining revenue (all other resources) {Using resources in the Forecast resources tab only} ELSE Forecast remaining revenue (plug)

Forecast remaining revenue (continued)

Billing method	Revenue forecast method	Calculation
		WHERE Forecast remaining revenue (labor resource) = [Remaining work hours x Scale 1 % x Scale 1 Billable rate + Remaining work hours x Scale 2 % x Scale 2 Billable rate + Remaining work hours x Scale 3 % x Scale 3 Billable rate] x [1 + Labor resource markup % from settings] Forecast remaining revenue (construction equipment resource) = Remaining work hours x Billable rate x [1 + Construction equipment resource markup % from settings] Forecast remaining revenue (all other resources) = Resource remaining quantity x Billable rate x [1 + Resource markup % from settings] Forecast remaining revenue (plug) = Sum for each cost category[Forecast cost category remaining cost x (1 + Cost category markup % from settings)] IF Forecast method = <i>Rollup</i> THEN Sum (children's Forecast remaining revenue) ELSE IF Forecast method is disabled THEN 0.
	Billed	IF

Forecast remaining revenue (continued)

Billing method	Revenue forecast method	Calculation
		Cost source = <i>Detail</i> THEN Forecast remaining revenue (labor resource) + Forecast remaining revenue (construction equipment resource) + Forecast remaining revenue (all other resources) ELSE Forecast remaining revenue (plug) WHERE Forecast remaining revenue (labor resource) = (1 - % complete) x Work hours x Scale 1 % x Scale 1 Charge rate + (1 - % complete) x Work hours x Scale 2 % x Scale 2 Charge rate + (1 - % complete) x Work hours x Scale 3 % x Scale 3 Charge rate Forecast remaining revenue (construction equipment resource) = (1 - % complete) x Work hours x Charge rate Forecast remaining revenue (all other resources) = (1 - % complete) x Resource quantity x Charge rate Forecast remaining revenue (plug) = (1 - % complete) x CE revenue amount.
Time & Material		IF Cost source = <i>Detail</i> THEN Forecast remaining revenue (labor resource) + Forecast remaining revenue (construction equipment resource) + Forecast remaining revenue (all other

Forecast remaining revenue (continued)

Billing method	Revenue forecast method	Calculation
		resources) {Using resources in the Forecast resources tab only} ELSE Forecast remaining revenue (plug) WHERE Forecast remaining revenue (labor resource) = [Remaining work hours x Scale 1 % x Scale 1 Billable rate + Remaining work hours x Scale 2 % x Scale 2 Billable rate + Remaining work hours x Scale 3 % x Scale 3 Billable rate] x [1 + Labor resource markup % from settings] Forecast remaining revenue (construction equipment resource) = Remaining work hours x Billable rate x [1 + Construction equipment resource markup % from settings] Forecast remaining revenue (all other resources) = Resource remaining quantity x Billable rate x [1 + Resource markup % from settings] Forecast remaining revenue (plug) = Sum for each cost category [Forecast cost category remaining cost x (1 + Cost category markup % from settings)] IF Forecast method = <i>Rollup</i> THEN Sum (children's Forecast remaining revenue) ELSE

Forecast remaining revenue (continued)

Billing method	Revenue forecast method	Calculation
		IF Forecast method is disabled THEN 0.
All methods	Manual	Forecast total revenue - Forecast revenue earned.

Forecast revenue earned

Billing method	Revenue forecast method	Calculation
Time & Material	All methods	WHEN The Revenue is considered <i>earned</i> when a LEM's setting is set to <i>Pending</i> THEN Sum of all BillAmount values where BatchType = LEM AND DocumentStatus <> Cancelled ELSE WHEN The Revenue is considered <i>earned</i> when a LEM's setting is set to <i>Approved</i> THEN Sum of all BillAmount values where BatchType = LEM AND DocumentStatus <> Cancelled OR Pending approval.
All other methods	All methods	Forecast total revenue x % complete.

9.26.2 Pay Items register revenue calculations

The following tables show how the different types of revenue are calculated in the Pay Items register:

Forecast total revenue

Billing method	Revenue forecast method	Calculation
Fixed final price	Default	Current price
Unit price	Default	Current unit price x Current forecast (T/O) qty.
Cost plus	Earned	Sum of assigned cost items' Forecast total revenue excluding Rollup values.
	Billed	Billed revenue + sum of assigned cost items' Forecast remaining revenue.
Time & Material	Billed	Billed revenue + sum for all assigned cost items $\{(1-\% \text{ complete}) \times \text{sum for all cost categories [Forecast total cost} \times (1 + \text{Markup \% from cost category settings})]\}$.
	Earned	IF The Revenue is considered <i>earned</i> when a LEM's setting is set to <i>Pending</i> THEN = Revenue earned + sum for all assigned cost items $\{(1-\% \text{ complete}) \times \text{sum for all cost categories [Forecast total cost} \times (1 + \text{Markup \% from cost category settings})]\}$ ELSE IF the Revenue is considered <i>earned</i> when a LEM's setting is set to <i>Approved</i> THEN = Revenue earned + Pending LEMs + sum for all assigned cost items $\{(1-\% \text{ complete}) \times \text{sum for all cost categories [Forecast total cost} \times (1 + \text{Markup \% from cost category settings})]\}$ Forecast final margin/forecast final revenue.

Forecast revenue earned

Billing method	Revenue forecast method	Calculation
Time & Material		WHEN The Revenue is considered <i>earned</i> when a LEM's setting is set to <i>Pending</i> THEN Sum of BillAmount values where BatchType = LEM AND DocumentStatus <> <i>Cancelled</i> OR <i>Pending removal</i> ELSE WHEN The Revenue is considered <i>earned</i> when a LEM's setting is set to <i>Approved</i> THEN Sum of all BillAmount values where BatchType = LEM AND DocumentStatus <> <i>Cancelled</i> OR <i>Pending approval</i> OR <i>Pending removal</i>
All other methods		Sum of assigned cost items Forecast revenue earned.

RELEVANT LINKS

[Link 1](#)[Link 2](#)[Link 3](#)[Link 4](#)[Link 5](#)

CHAPTER 10 – SCHEDULING

10.1 SCHEDULING OVERVIEW

You can use features in Control to track schedule dates at a CBS level. The ability to easily add and modify this information allows you to accurately track your operations planned and completed dates.

The schedule data can either be mass imported through a Microsoft Excel upload, created and modified directly within the CBS, or by way of Primavera schedule integration through and XER file import.

10.2 SCHEDULE DATA BLOCK

The schedule data block is where all information regarding schedule dates is contained. Some of the key fields inside this data block are:

- Schedule ID
- Planned Start Date
- Planned Finish Date
- Early Start Date
- Early Finish Date
- Late Start Date
- Late Finish Date
- Actual Start Date
- Actual Finish Date

You can add and edit this information directly inside the Schedule data block. However, this will only allow you to modify one CBS line item at a time.


The following Step by Step shows you how to add the Schedule data block, save a Scheduling view, and add various dates for a specific CBS item.

Schedule Data Block

- From the Workspaces page of the Steel Structure Job, remove each data block from the page, except for the Tasks and Task Details data blocks, by right clicking on the **context menu**.

Current budget					
CB total quantity	CB total Mhrs	CB total cost	CB Mhrs/Unit	CB Unit/MHr	CB unit cost
1.00	0.00	\$ 250,000.00	0.00	0.00	\$ 250,000.00
10,000.00	0.000.00	\$ 400,000.00	0.00	1.00	\$ 40.00


- For each data block you plan to remove, select **Remove Data Block**

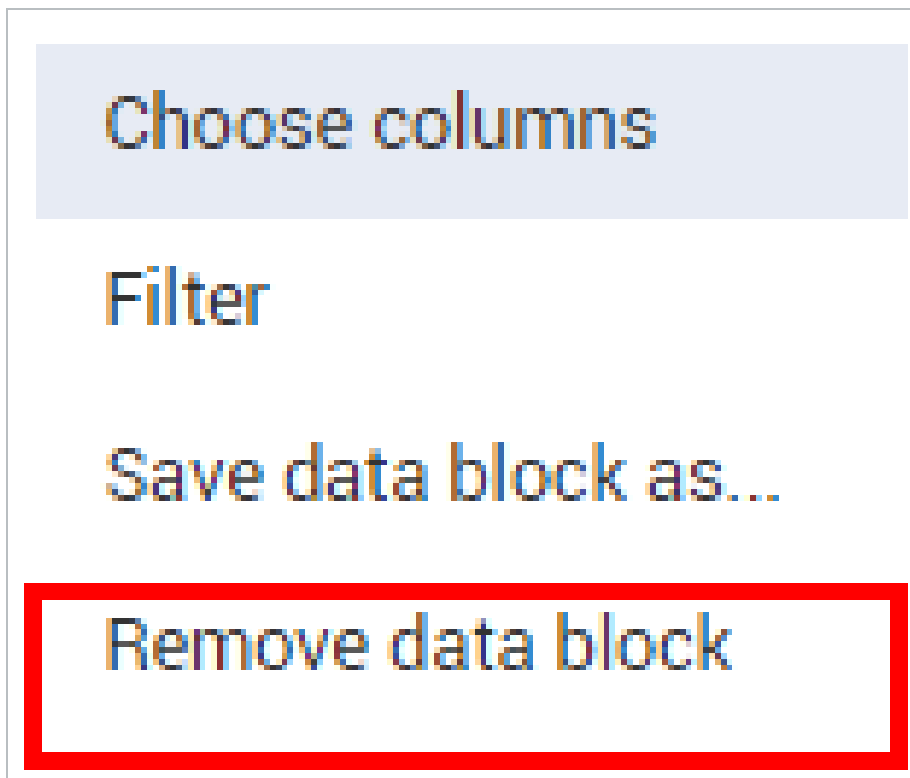


- Once the data blocks are removed, click the **Add Data Block** button.




4. Drag and drop the **Schedule Data Block** to the right of Task Details.

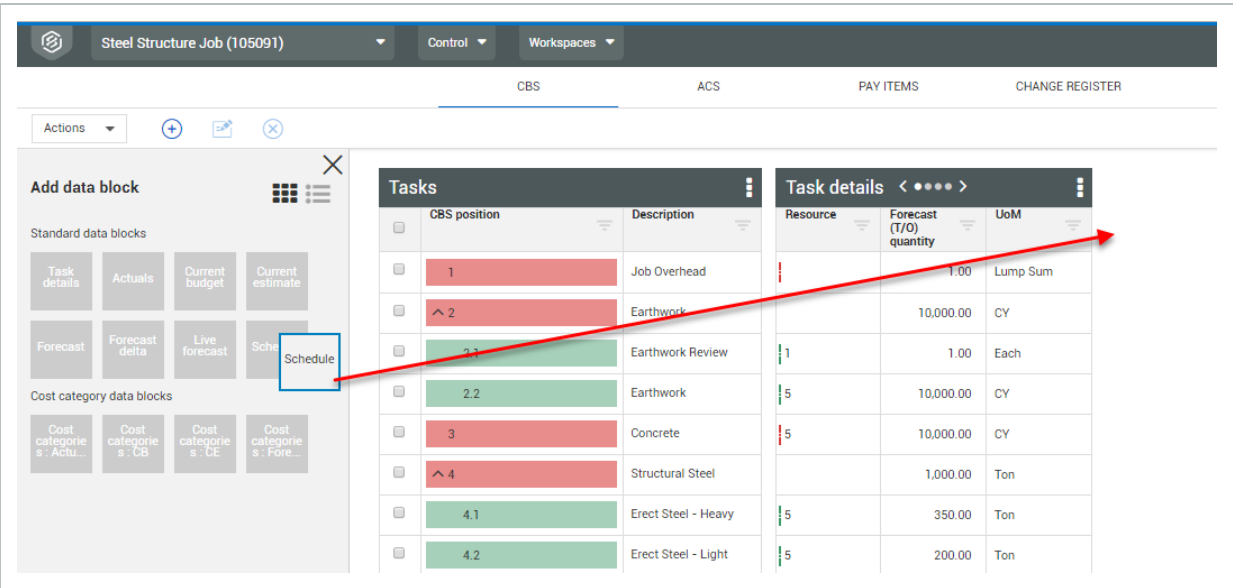

5. Select **Module [your initials] – [description.]**



6. In the schedule data block, type **your Initials.01234** in the Schedule ID field.

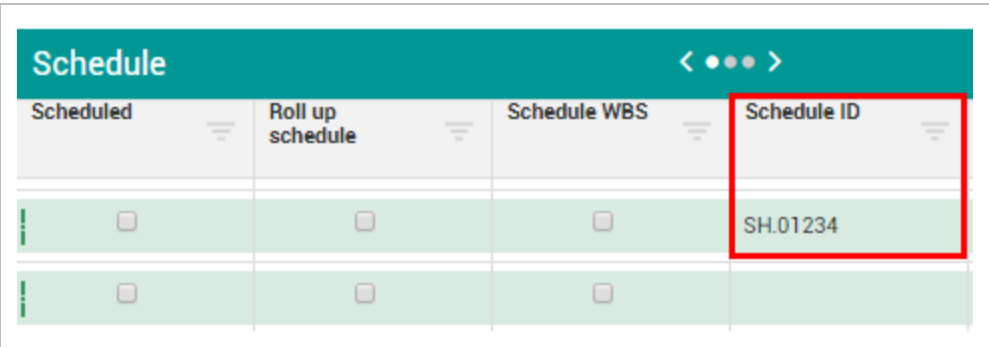

7. Click the **right arrow** to move to next set of columns in the schedule data block.

Scheduled	Roll up schedule	Schedule WBS	Schedule ID
-----------	------------------	--------------	-------------

8. Double click into each field and enter the following:

- Start = **10/05/2020**
- Finish = **10/15/2020**
- Early Start = **10/01/2020**
- Early Finish = **10/15/2020**
- Late Start = **10/07/2020**
- Late Finish = **10/15/2020**

Start	Finish	Early start	Early finish	Late start	Late finish
10/05/2020	10/15/2020	10/01/2020	10/15/2020	10/07/2020	10/15/2020

- Entering dates on any terminal CBS item will auto-populate the parent's dates. If there are multiple terminal items under one parent, any start dates will take the earliest and any finish dates will take the latest
- Once all the initial schedule dates are entered, the schedule data block also allows for the project to track actual dates

9. Click the **Right Arrow** to move to next set of columns in the schedule data block.

- You will leave these columns blank for this Step by Step

Actual start	Actual finish

10.3 SCHEDULE EXCEL IMPORT


The Control application allows for an Excel import to import data into the Schedule data block. This is especially useful when bringing in large sets of data for multiple CBS items.

Excel imports can sometimes 'hang' while attempting to import CBS data. If this happens, it's possible to cancel an Excel import while the system continues the attempt to import the data.

The following Step by Step covers downloading this Excel sheet, entering the necessary data, and importing it back it into Control.


Excel Import

1. From the Workspaces page, using the **Schedule** view on the CBS tab, click the **Export** button, then **CBS as CSV**.

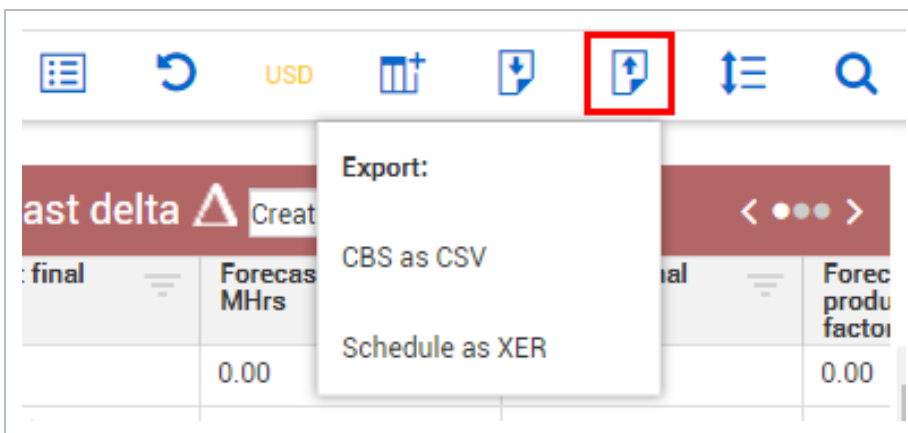

- This creates a CBSDataBlock folder in your Downloads folder

2. Open the **CBSDataBlock.csv** file.



3. Inside the Excel spreadsheet, delete all rows except for **Module [your initials] – [description]**.

	A	B	C	D	E	F	G	H
1	CBS position	Description		Resource	Forecast (T/O) quantity	UoM	Change status	Allow as-bu
2	4.4	Module 01 - Erect Steel Heavy		3	800	Ton		All
3								
4								
5								
6								


4. Enter the following:

- Actual Start = **10/03/2020**
- Actual Finish = **10/12/2020**


AB	AC	AD	AE
Late finish	Actual start	Actual finish	Cost curve
10/14/2020	10/03/2020	10/12/2020	Linear

5. **Save** the file to your computer (as .xlsx, .xls, or .csv).

6. From the Control > Workspaces page, click the **Import** button for Cost Items.

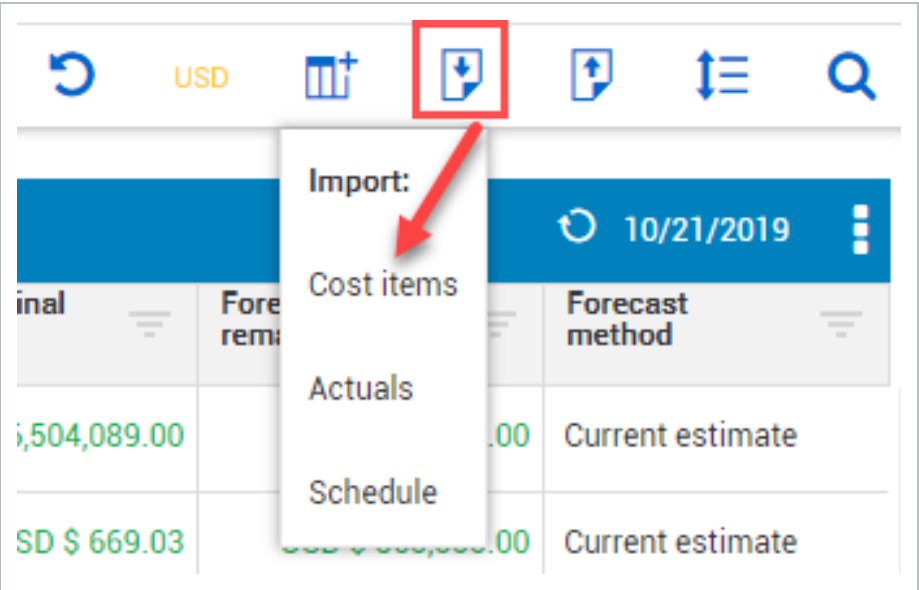

7. Click **Browse** to select your Excel file.

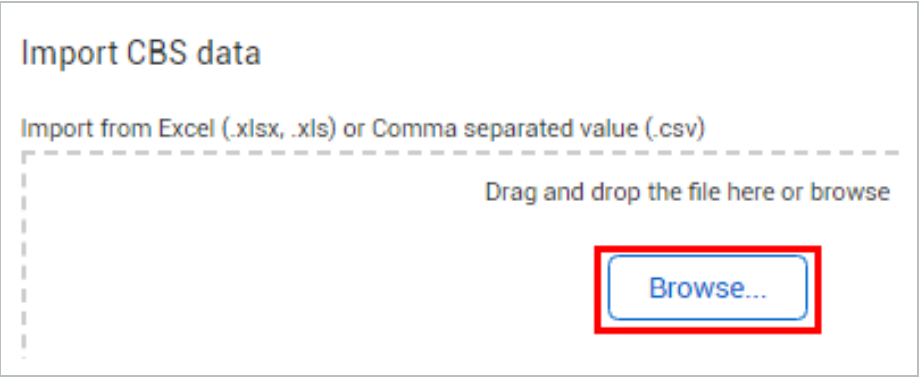

8. Select **Cost Items** and cost item attributes, **Update Existing Items** and **CBS position**.

Options

* Import type

Cost items and cost item attributes ▼

☒ Update existing and new items

Cost item matching criteria

CBS position ▼

☐ Update existing items

☐ New items

9. Click **Next**.

Cancel Next

10. Next, you will map which columns from the Excel sheet get imported to which columns in Control. Click on **CBS Columns** to sort A-Z.

Map columns

Template

Actual Start/Finish

Order	Data type	CBS columns	Mapped	File columns
-------	-----------	-------------	--------	--------------


11. Under **File Columns**, match Actual Finish and Actual Start to the CBS columns description.

CBS columns	Mapped	File columns
Actual finish	✓	Actual finish
Actual start	✓	Actual start

12. Do the same for WBS Phase Code.

CBS columns	Mapped	File columns
User defined 6		Blank-do not import
User defined 7		Blank-do not import
User defined 8		Blank-do not import
WBS client code 1		Blank-do not import
WBS client code 2		Blank-do not import
WBS phase code	🔑	WBS phase code

13. Click **Next**.



- The actual dates you specified import into the Schedule data block

CBS

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

Actions

Tasks

CBS position

1

2

3

4

4.1

4.2

4.3

4.4

Job Overhead

Earthwork

Concrete

Structural Steel

Erect Steel - Heavy

Erect Steel - Light

Bolted Connections

Module 01 - Erect Steel Heavy

Task details

Resource

Forecast (T/O) quantity

UoM

1.00

Lump Sum

5

10,000.00

CY

5

10,000.00

CY

1,000.00

Ton

6

800.00

Ton

5

200.00

Ton

5

2,000.00

Ea

350.00

Ton

Schedule

Actual start

Actual finish

Cost cum

10/03/2020

10/12/2020

Linear

Bell Shap

10/03/2020

10/12/2020

The Excel import can only be accomplished if the Control > Settings > Schedule setting is set to Manual Entry.

PROJECT TRACKING

ESTIMATE RESOURCES

SCHEDULE

Define project schedule

Schedule data source:

Manual entry

Manual entry

XER file type

Duplicate field values for Baseline and Current schedule columns.

10.4 PRIMAVERA SCHEDULE INTEGRATION

The XER (file extension used by Primavera containing project file related data) import functionality allows the milestones and schedule dates (baseline and current) to be integrated into planning activities. Schedule IDs in Control are used to map Primavera Activity IDs to import and export the project information. The status of construction activities and progress are then integrated back into the InEight scheduling tools.

The Primavera schedule integration not only allows for XER file import of schedule dates but is also capable of a cost item bi-directional push and pull between Control and Primavera. XER imports integrate critical milestones and schedule dates into planning activities in the InEight cloud platform.

It's also possible for you to map the existing Control 25 CBS tag fields, and also the existing 15 user defined fields to P6. Conversely, you can create new fields in P6 based on tagging scheme. This allows you to filter Primavera and Control in similar ways, with the same sets of dates within both applications.

You also can push (Physical) % complete to P6. As you are progressing in Plan or Progress, and as quantities drive the percent complete in Control, it's possible to push the percent complete back to the associate activity in P6.

10.4.1 Primavera Schedule Integration Settings

The setting to change the schedule data source to Manual entry or an **XER file type** is in Settings > Control > Schedule > Define project schedule.

Under the Schedule data source, it's possible to manually enter schedule dates, or you can utilize the XER file type.

Define project schedule

Schedule data source:

XER file type

Manual entry → Option 1

XER file type → Option 2

After selecting your Schedule data source, you will have the option of making sure that your schedule IDs are similar across your baseline and current schedule.

Duplicate field values for Baseline and Current schedule columns:

- ☒ Schedule ID and Baseline schedule ID
- ☒ Scheduled and Baseline Scheduled
- ☒ Schedule WBS and Baseline schedule WBS
- ☒ Roll up schedule and Baseline roll up schedule

If you uncheck one of these options, and then check it back, you will be given the option to copy existing Schedule ID column values to Baseline schedule ID column, and vice versa. This is a way to ensure that data consistencies remain in check for both baseline and current monthly schedule.

**Select one:**

- ☒ Copy existing Schedule ID column values to Baseline schedule ID column
- ☐ Copy existing Baseline schedule ID column values to Schedule ID column

CloseOK

Under Percent complete, you can either update the XER file with physical percent complete from Control, or not.

Under the second dropdown for Update XER activities, you have the option to update XER with tags and user defined fields from Control, or not to.

Percent complete:	Update XER activities with cost item tags and user defined fields from Control:
Do not update percent complete Update XER with physical percent complete from Control Do not update percent complete	Do not update tags or user defined fields Update XER with tags and user defined fields from Control Do not update tags or user defined fields

If you choose to update XER with tags and user defined fields, the Define tags and user defined export rules table appears. The 3 options to choose from are to match using Control field name, match using external system field name, or do not export.

If you choose to map to an external system field (as shown below using Tag 15 for the second record), you will need to manually type in the name of the field first. Because this is not an API, the system is not aware the existing fields within P6. Therefore, you need to self-determine which Control values you want to populate in P6.

Percent complete: Do not update percent complete

Update XER activities with cost item tags and user defined fields from Control: Update XER with tags and user defined fields from Control

Define XER tags and user defined export rules:

Column names in external scheduling system must be an exact match. If the specified name does not have a match with the external system, then a new column will be added at the project level.

	Match using External system field name	Match using Control field name	Match using External system field name	Do not export
	Export Rule	*External system field		
☐ EN_CBS tag 8(CBS tag 8)	Match using External system field name	Tag 15		
☐ EN_CBS tag 17(CBS tag 17)	Match using Control field name	EN_CBS tag 17(CBS tag 17)		
☐ EN_CBS tag 19(CBS tag 19)	Do not export			
☐ EN_CBS tag 25(CBS tag 25)	Do not export			
☐ EN_CBS user defined 6(CBS user defined 6)	Do not export			
☐ EN_CBS user defined 12(CBS user defined 12)	Do not export			
☐ EN_CBS tag 4(CBS tag 4)	Do not export			
☐ EN_CBS tag 10(CBS tag 10)	Do not export			
☐ EN_CBS tag 15(CBS tag 15)	Do not export			

* Required fields

10.4.1.1 Primavera XER Schedule Integration Prerequisites

1. XER file type or manual entry must be selected in Settings > Control > Schedule, in the Schedule data source section.

PROJECT TRACKING
ESTIMATE RESOURCES
SCHEDULE
OTHERS

Define project schedule

Schedule data source:

XER file type
Manual entry
XER file type

- On the Schedule data block, the **Scheduled column** must be checked prior to importing a schedule.

Schedule < ● ● ● >					
Scheduled	Schedule ID	Sched plug days	Plug days	Start	Finish
☒	PS.1	☒	21,682.50	07/18/2019	07/18/2019
☒	PS.2	☒	0.00	07/18/2019	07/18/2019
☒	XYZ	☐	0.00	07/18/2019	07/18/2019


- The **Schedule ID** in Control must match the **Activity ID** in the XER file.

Schedule < ● ● ● >					
Scheduled	Schedule ID	Sched plug days	Plug days	Start	Finish
☒	PS.1	☒	21,682.50	07/18/2019	07/18/2019
☒	PS.2	☒	0.00	07/18/2019	07/18/2019
☒	XYZ	☐	0.00	07/18/2019	07/18/2019


The following steps walk you through how to import a Primavera .XER file into Control.

Schedule Integration Import

1. From the CBS tab of the Control Workspaces page, select the **Import icon** on the top right menu bar, then click **Schedule**.

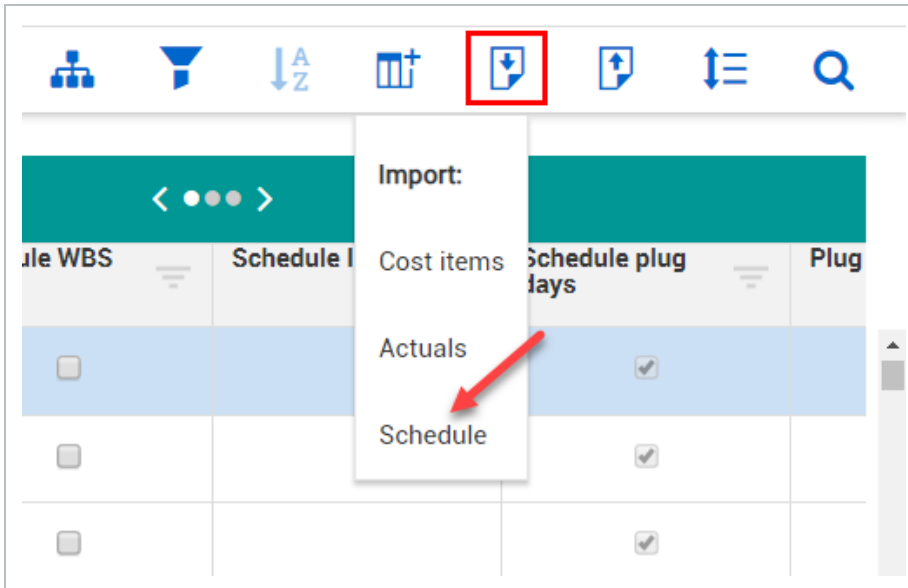

2. A warning message appears asking if the XER Activity IDs and Control IDs match. Click **Yes** if both IDs match before continuing.

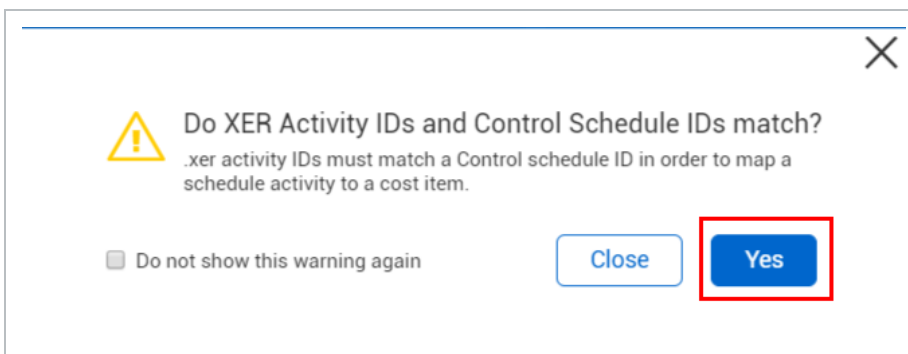

3. In the Import schedule data window, click on the **Browse** icon in the Drag and drop file portion of the screen.

Import schedule data

Import from schedule (.xer)

Drag and drop the file here
or Browse

Browse

Maximum upload file size: 50 MB

Options

☐ **Baseline schedule**
A fixed project schedule that is the standard by which project performance is measured, and a reflection of all formally authorized scope and schedule changes. After importing a baseline, you can import a current schedule and derive some key performance indicators (KPI's).

☒ **Current schedule**
A schedule update, which reflects progress to date, plus forecast progress going forward and is used for monitoring. Schedule data can be mapped to domain data such as Control cost items to derive cost based schedules, and time phasing, for example.

4. In the Import schedule data window, click on the **Browse** icon in the Drag and drop file portion of the screen.
5. Select the desired **.XER** file that was generated in Primavera.
 - Once the .XER file is uploaded, the Browse box turns green

Import schedule data - Activity ID file.xer

Import from schedule (.xer)

Drag and drop the file here
or Browse

Browse

Maximum upload file size: 50 MB

6. In **Options**, select either the Baseline schedule or Current schedule for the schedule type that you want to import.

Options

☐ **Baseline schedule**
A fixed project schedule that is the standard by which project performance is measured, and a reflection of all formally authorized scope and schedule changes. After importing a baseline, you can import a current schedule and derive some key performance indicators (KPI's).

☒ **Current schedule**
A schedule update, which reflects progress to date, plus forecast progress going forward and is used for monitoring. Schedule data can be mapped to domain data such as Control cost items to derive cost based schedules, and time phasing, for example.

7. Select **Next**.
8. Select **Import** after reviewing the Schedule summary.

Import schedule data - Activity ID file.xer

Schedule summary

Schedule name

WSFN Shoreline Protection

Schedule type

Current schedule

Total schedule records	
Schedule WBS	107
Schedule activities	306

Import may take some time. You may continue to make changes to your project while the import is processing.

Cancel

Import

- The **Importing data** process screen displays the current status for each step of the .XER data import.

Processing schedule data import - Activity ID file.xer ("3058" OPG WSFN Shoreline Protection-A00131-1)

Importing data

Step	Status
Step 1: Preparing data to be sent	Complete
Step 2: Placing data in queue	Processing - 1mins
Step 3: Writing data to master library	
Step 4: Sending data to project	
Step 5: Mapping master data to project data	
Step 6: Inserting data to project tables	

This may take some time. You may continue to make changes to your project while the import is processing.

Status update is also available in the Import history

- If there are errors in any of the steps, you can click on the **Pending unmapped items found** link to make the corrections

Importing data	
Step	Status
Step 1: Preparing data to be sent	✓ Complete
Step 2: Placing data in queue	✓ Complete
Step 3: Writing data to master library	✓ Complete
Step 4: Sending data to project	✓ Complete
Step 5: Mapping master data to project data	⚠ Pending, unmapped items found
Step 6: Inserting data to project tables	

- You can also navigate to Audit Log > Import history to view the import status, which includes the **Total line items** imported

File name	Status	Processing Details	Total line items	Errors	Total imported	Added estimate resources	Added pay items	Created by	Created date
NEWPROJ.xer (D...	✓ Complete	All steps	18	0	19	0	0	Asmita Ray	08/02/2019 10:0...

- If there are corrections to be made, once completed, you can select **Import** to re-import the data.

Audit log > Import history > Activity ID file.xer ("..."									
Cancel Import									
Status details				Schedule details		Cost item details			
Map status	XER activity ID	Control schedule ID	Description	CBS position	Description	WBS phase code	Scheduled		
⚠ No match found		HD.0000003		1	Job Overhead	1002			
⚠ No match found		HD.0000019		2	Earthwork	1069			
⚠ No match found		HD.0000044		3	Concrete	1071			

- When the import is successful, select the **Close** button.

Processing schedule data import - NEWPROJ.xer (Duplicate-NEWPROJ)

Importing data

Step	Status
Step 1: Preparing data to be sent	✔ Complete
Step 2: Placing data in queue	✔ Complete
Step 3: Writing data to master library	✔ Complete
Step 4: Sending data to project	✔ Complete
Step 5: Mapping master data to project data	✔ Complete
Step 6: Inserting data to project tables	✔ Complete

This may take some time. You may continue to make changes to your project while the import is processing.

Status update is also available in the Import history

✔ Job ended successfully

Close

- Check the Control: **Schedule block** for newly imported **scheduled dates**
- This is a quick audit to make sure that the desired Primavera dates imported successfully into Control

Tasks			Schedule					
	CBS position	Description	Scheduled	Schedule ID	Schedule plug days	Plug days	Start	Finish
	^ 1	Financial Results A...	✔	PS.1	✔	21,682.50	07/18/2019	07/18/2019
	^ 1.1	10 - Commercial C...	✔	PS.2	✔	0.00	07/18/2019	07/18/2019
	1.1.1	Dependent G&A	✔	XYZ		0.00	07/18/2019	07/18/2019


The following steps walk you through how to export a Primavera .XER file from Control.

Primavera Schedule Integration Export


1. From the CBS tab of the Control Workspaces page, select the **Export icon** on the top right menu bar, then click **Schedule as XER**.

2. Assuming you have Percent Complete and User defined Fields and tags turned on in your settings, click **Export**.

- Depending on what you'd like to export, you can always uncheck undesired options

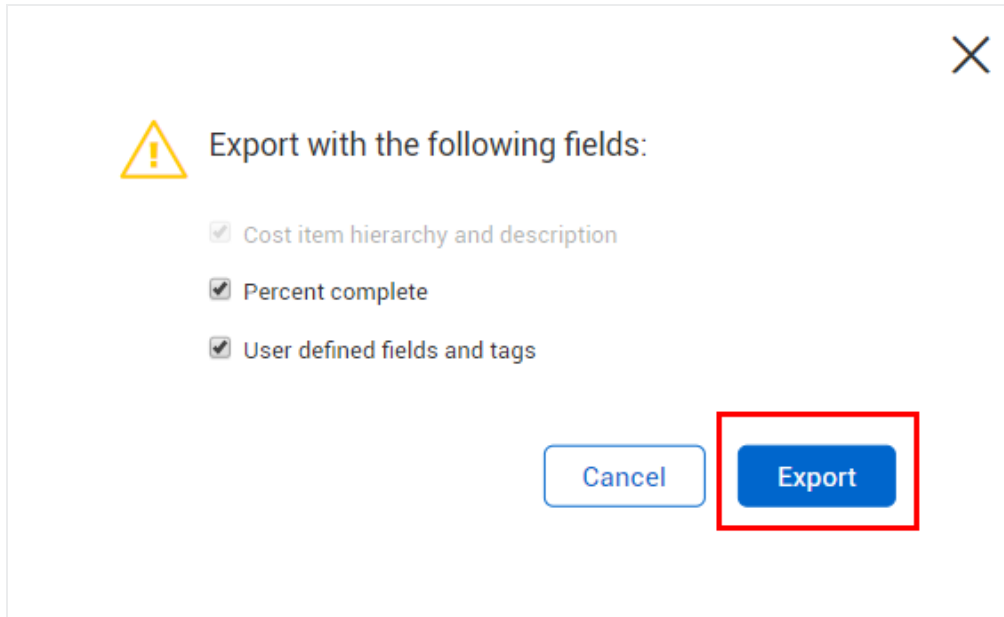

- After selecting Export, an XER file will generate and be placed within your C:/Downloads folder. The file will be named <job name>(Schedule).xer



- At this point you are ready to import the XER file into Primavera

10.4.2 Percent Complete column updates in CBS

If you are progressing your schedule in P6, it's possible to import this progress data directly into Control using the Schedule Integration Import process. The % Complete column records within the CBS can receive updates from the P6 XER file. The XER file can originate from Primavera or InEight Schedule. As long as the % Complete data is captured within the XER file, it will update the CBS with this new schedule information.

Tasks				Actuals 9/2/2019 to 1/12/2020				
	CBS position	Description	WBS phase code	Schedule ID	% Complete	Qty complete (to date)	Start	Finish
	^ 1	Financial Results An...	1000	PS.001	0.45 %	0.00	10/01/2019	08/25/2020
	^ 1.1	INDIRECTS & UNASS...	1001	PS.002	0.76 %	0.01	10/01/2019	08/25/2020
	^ 1.1.1	Commercial Cost	1002	PS.003	2.30 %	0.00	10/01/2019	10/15/2019
	1.1.1.1	Direct Pickup	1016	PS.013	100.00 %	30.50	10/01/2019	11/29/2019

By not using this feature, the % Complete column updates from P6 will not populate the % Complete column within Control. You would need to update the CBS with the % Complete or claimed quantity via other methods for completing progress measurement which are addressed in the [Progress Measurement & Forecasting User Guide](#).

This feature allows for the Schedule Import process to align the P6's schedule % complete with the cost item's % Complete.


After running the Schedule Integration Import process, you can check the CBS and verify the progress results in the % Complete column.

This page intentionally left blank.

CHAPTER 11 – ACCOUNT CODE STRUCTURE (ACS)

11.1 Account code structure workflow	523
11.2 What is an Account Code?	524
11.3 Account code setup	524
11.3.1 Staging vs. Published Account Codes	525
11.3.2 Account code permissions	531
11.4 Measurement types	540
11.5 Cost category label customizations	541

11.1 ACCOUNT CODE STRUCTURE WORKFLOW

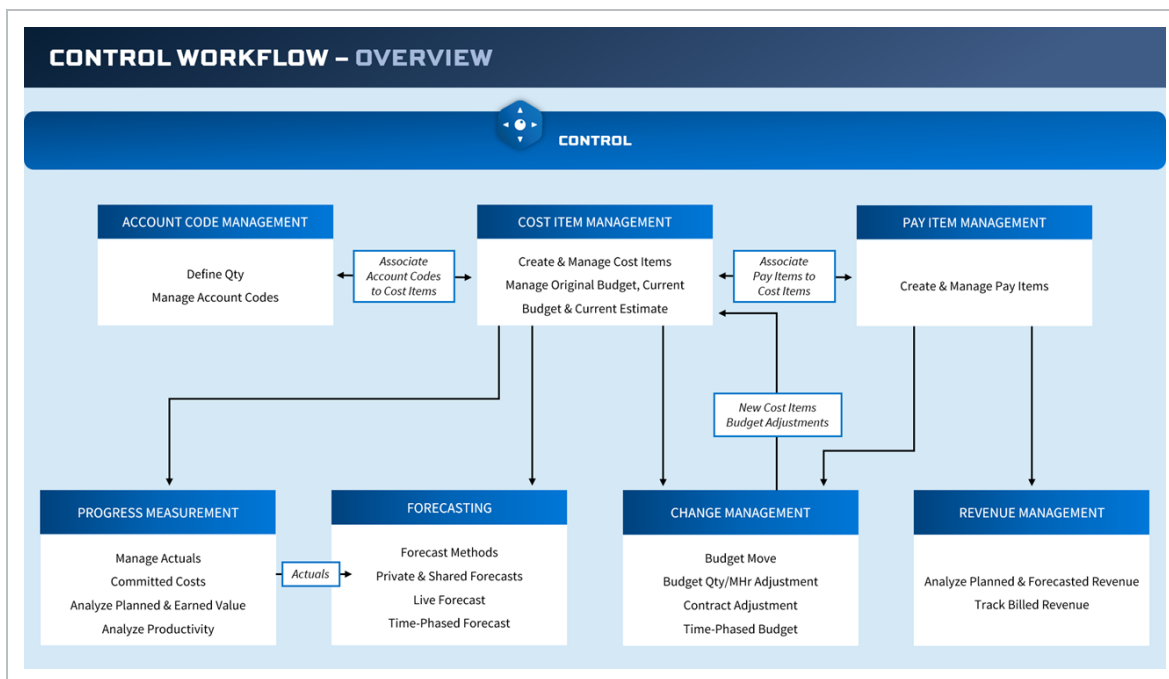


11.2 WHAT IS AN ACCOUNT CODE?

Account Codes serve as a standardized coding system to track like operations across a company, for the purpose of global reporting and benchmarking. Account Codes typically follow a hierarchical structure which allows for summary level reporting rolled up to company standards, but can also be a flat list.

Account Codes are assigned to cost items similar to a tag on a cost item. Once an account code has been assigned to all terminal cost items you can view many project and organization reports organized by the account code structure, rather than individual project cost break down structure which often differs from project to project. Account Codes can also tie back to InEight Estimate where estimators can assign the same standard set of account codes to estimate items, and compare them to active or completed projects for historical benchmarking.


11.3 ACCOUNT CODE SETUP

The master set of account codes is created and stored under Master data libraries > Account Codes.

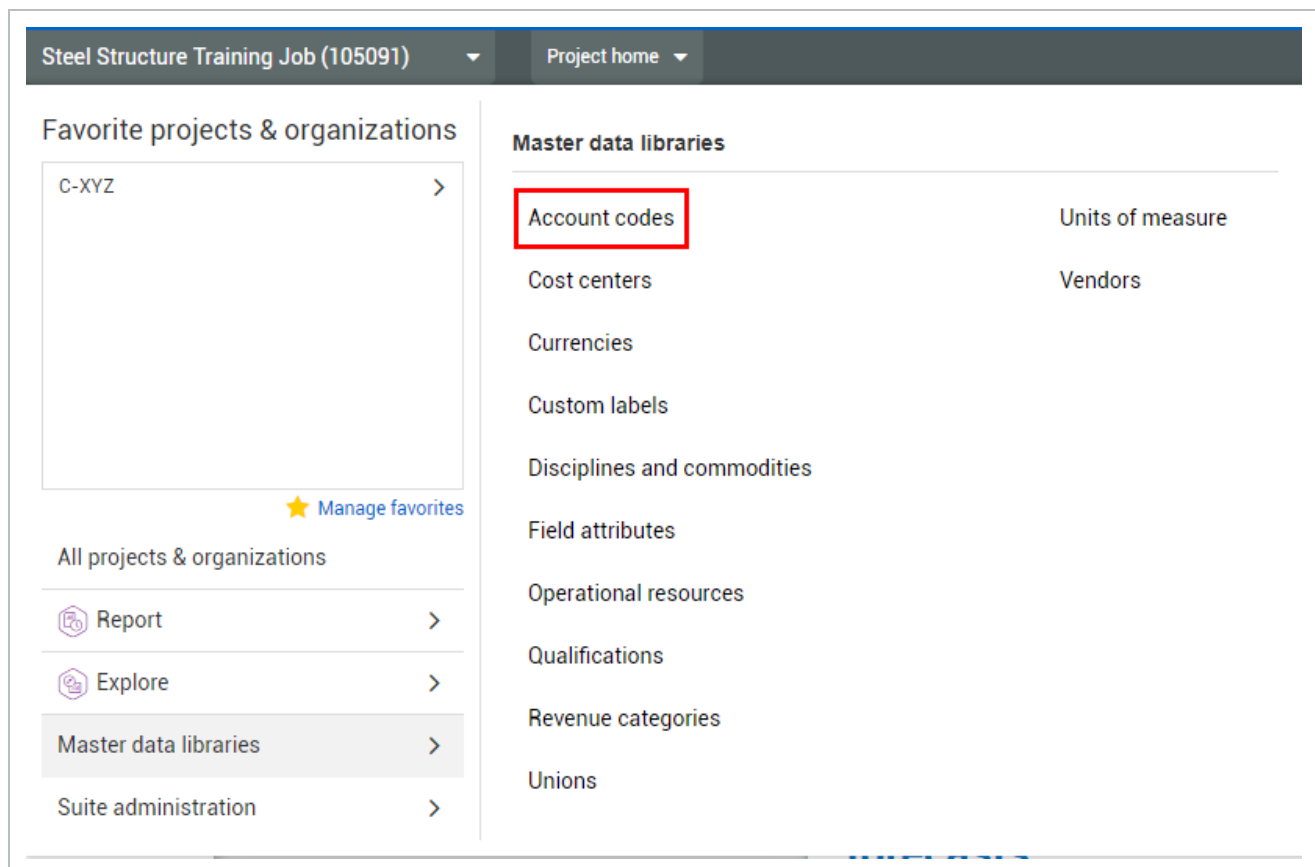


11.3.1 Staging vs. Published Account Codes

The Account Codes master data library contains four tabs: Published, Staging, Audit Log, and Import Log.

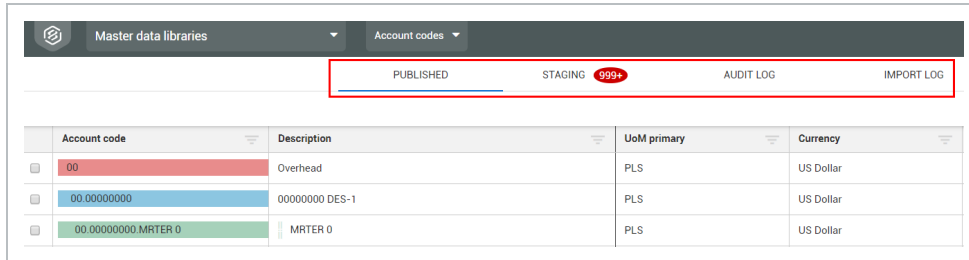

Account code	Description	UoM primary	Currency
00	Overhead	PLS	US Dollar
00.00000000	00000000 DES-1	PLS	US Dollar
00.00000000 MTRER 0	MTRER 0	PLS	US Dollar

- The **Published** tab lists all account codes that have been created and published under the Staging tab.
- Under the **Staging** tab, you create and edit account codes, and then publish them for use. Account codes are not available for use in projects until they are published
- The **Audit Log** tracks changes made to the Account Code Structure, including the value before and after, the changed date, and who made the change
- Under the **Import Log** tab, you can track the status of all the account code import processes.
 - When you hover over the **Failed with errors** imports, a pop-up will provide a brief import status, along with next steps
 - Under the pop-up, there is a down facing blue arrow where you can download a detailed error log

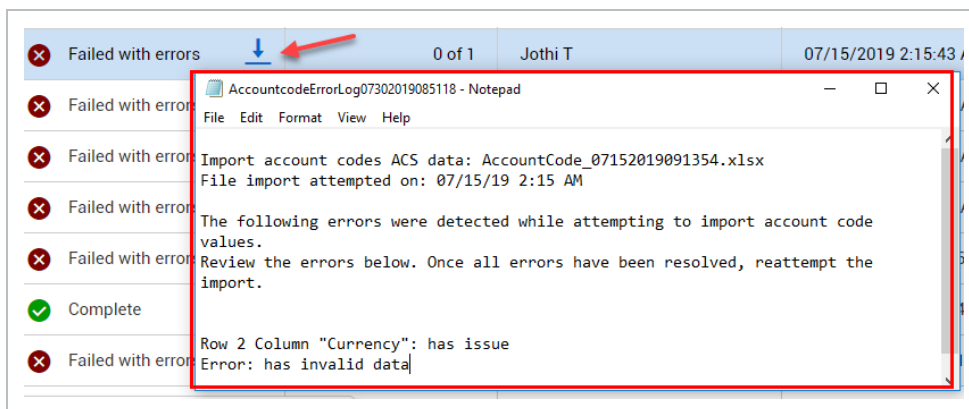

Account codes are typically maintained at an organization administration level to ensure that categories and codes remain consistent with company standards.

The account codes within the Account Code Structure are arranged into a hierarchy of parent-child relationships that can contain varying levels of detail, indicated by color, for each level of the hierarchy.

You can assign account codes to cost items anywhere, from the highest level to the lowest level. The lower the level assigned, the higher the level of detail associated to the account code.


The example below shows a level 3 account code (50.03.04) acting as a parent to two subordinate account codes (50.03.04.002 and 50.03.04.004).

Account code	Description
50.03.02.004.02	Break - Concrete Paving Removal
50.03.02.004.04	Load out - Concrete Paving Removal
50.03.04	Paving Milling and Scarification
50.03.04.002	Paving Milling and Scarification - Asphalt
50.03.04.004	Paving Milling and Scarification - Concrete
50.03.06	Utility Line Removals - Underground
50.03.06.002	Utility Line Removals - Underground (<4' Depth)
50.03.06.002.02	Utility Line Removal (<4' Depth)
50.03.06.002.04	Storm Sewer Removal (<4' Depth)

The following Step by Step walks you through how to create a new account code.


Create an Account Code

1. From the Project home page, select the **1st Level drop-down menu**.
2. Select **Master Data Libraries**.
3. Select **Account Codes**.

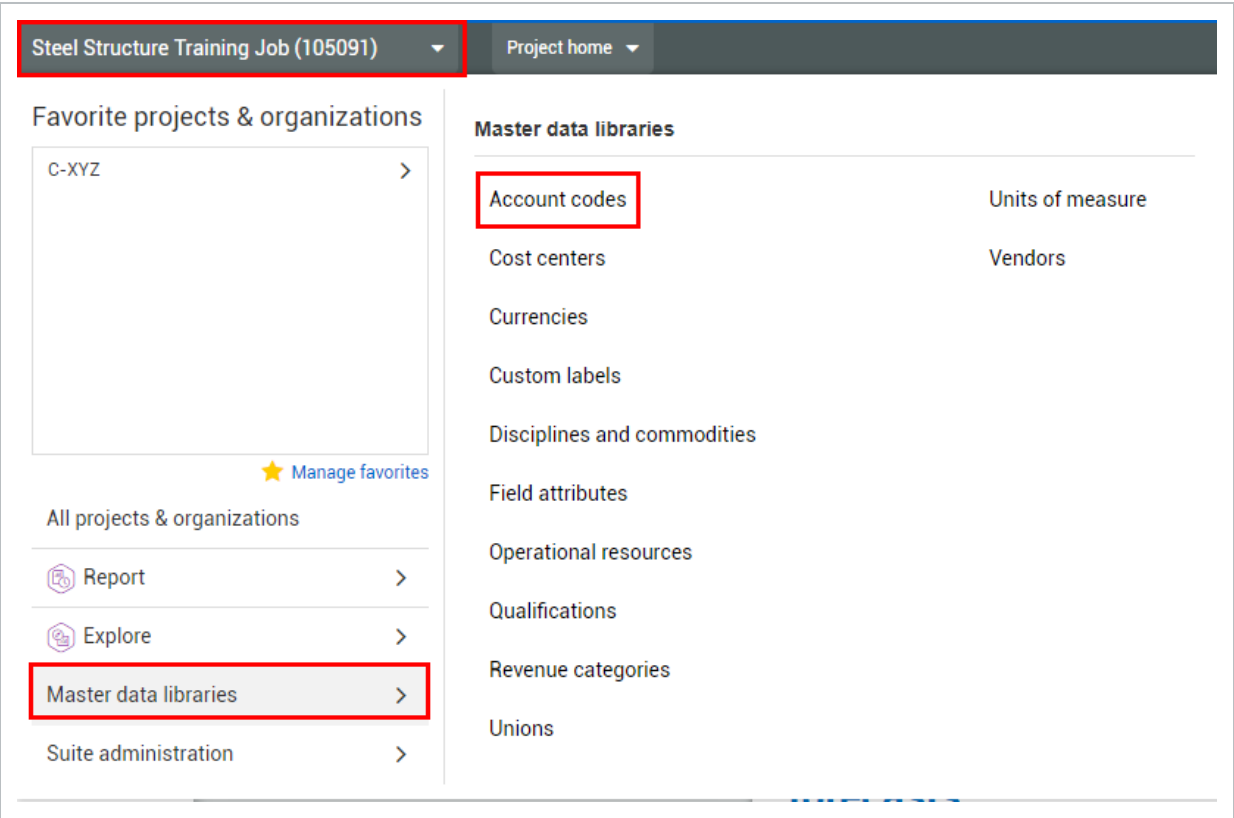


- All the account codes appear on your screen in a hierarchy format

4. Select the **Staging** tab.



5. Click the **check box** next to any of the existing account codes.



6. Click the **Add Account Code** button.

	Account code	Description	UoM
☐	62.03.04.004	Module Assembly - Erect Steel	Ton
☐	62.03.04.004.02	Module Assembly - Erect Steel - Erect Steel - Light (0-19 lb/LF)	Ton
☐	62.03.04.004.04	Module Assembly - Erect Steel - Erect Steel - Medium (20-39 lb/LF)	Ton
☒	62.03.04.004.06	Module Assembly - Erect Steel - Erect Steel - Heavy (40-79 lb/LF)	Ton

- This creates a new account code with the code you selected as the parent
- In the Account code details slide out panel, the following can be assigned:

Item	Function
Parent Account Code	Account Code with lower level “child” account codes below it.
Account Code	The alpha numeric sequence assigned as the code.
Description	Description detailing the account code’s scope.
Currency	The currency assigned to the account code.
UoM Primary	The primary unit of measure for the account code.
UoM Secondary	The secondary unit of measure for the account code.
Auto Quantity Primary/Secondary	Automatically roll up cost item quantities if the cost items and this account code have the same primary/secondary UoMs. It can also be set on a project specific basis.
Parent Roll Up Behavior	Controls whether primary or secondary quantities of account code roll up to the parent account code’s primary or secondary quantity.
Account Code Tag 1-20	Tags that can be associated to account codes to enable them to be categorized.
User Defined Field 1-10	Optional open-text fields you can use to add information related to the account code.

The asterisk (*) at the beginning of a tile indicates it is a required field and it must be populated before the code will be created.

7. Fill in the information below:

- Account code: **Your Initials** (Since a parent was selected when creating this new account code, numbering prior to ‘–Your Initials’ will be the parent’s)
- Description: **Your Initials – Account Code**
- Currency: **US Dollar**
- UoM primary: **Ton**
- Leave all other defaults/blanks

8. When you have filled out all the information, click **Stage** to send the new account code to staging area.

- The new account code now exists in the Account Code Structure on the Staging tab
- The new account code will not be available for use within projects until it is published

9. If you have the permissions to publish account codes, check the box for the account code you created..
10. Click the **Publish** button in the top-right corner of the page.

You can also edit existing account codes within the Account Code Structure, as indicted in the steps below.

Edit Account Code Details

1. From the Account Code – **Staging** tab, select the account code you created.
2. Click the **Edit Account Code** button.

PUBLISHED					
STAGING					
Account code	Description	UoM primary	Currency	UoM second	
62.03.04.004	Module Assembly - Erect Steel	Ton	US Dollar		
62.03.04.004.02	Module Assembly - Erect Steel - Erect Steel - Light (0-19 lb/LF)	Ton	US Dollar		
62.03.04.004.04	Module Assembly - Erect Steel - Erect Steel - Medium (20-39 lb/LF)	Ton	US Dollar		
62.03.04.004.06	Module Assembly - Erect Steel - Erect Steel - Heavy (40-79 lb/LF)	Ton	US Dollar		
62.03.04.004.06-User #	Your Initials - Account Code	Ton	US Dollar		
62.03.04.004.08	Module Assembly - Erect Steel - Erect Steel - Extra Heavy (80-119 lb/LF)	Ton	US Dollar		

- The edit account code page opens where changes can be made

Note that only the description, auto quantity primary, auto quantity secondary, parent roll up behavior, and account code tags can be edited after an account code has been created. All other items are greyed out and read only.

3. Once you are done editing the account code, click **Stage** to update the account code.

Cancel

Stage

Account code details

• Parent account code

62.03.04.004.06-Module Assembly - Erect Steel - ...

Start typing the code or description. i.e. footing

• Account code

62... -User #

• Description

Your Initials - Account Code

• Currency

USD-US Dollar

Start typing the entity, name or code. i.e. USD

• UoM primary

Ton

Start typing the name. i.e. cubic yard

UoM secondary

Start typing the name. i.e. cubic yard

Associated entity roll up behavior

Auto quantity primary

Off ⓘ

Auto quantity secondary

Off ⓘ

Parent roll up behavior

Contribute primary to primary

Off

Contribute primary to secondary

Off

Contribute secondary to secondary

Off

11.3.2 Account code permissions

If you have the required permissions, you can delete, replace, or rename account codes.

The account administrator does not have permissions automatically assigned to approve account codes. Your account administrator must add the permission to approve account codes in the Master data libraries to the administrative account.

11.3.2.1 Deleting account codes

Follow the step-by-step to delete an account code.

If you are deleting a parent account code, all children under the parent are also deleted.

Delete account code

Replacement account code (optional)

Select one

Cancel Next

In the Replacement account code optional text box, you can enter in an existing account code to replace the account code you are deleting.

5. On the Delete account code confirmation page, select **Delete** in the lower-right corner.

Delete account code

Cancel

Stage

Delete account code

Confirm deletion

Are you sure you want to delete this account code? This action cannot be undone.

None:___001

Back

Cancel

Delete

6. Click the **Stage** button.
 - This takes you back to the Staging page.

Approve all [Download] [Upload] [Info] [Search] [Publish]

Approve account codes

Are you sure you want to approve all pending account codes? This action cannot be undone.

Staging notes
Staging notes entered here will be applied to all account codes being approved.

500

Type message here

[Cancel] [Approve]

7. From the Staging page, select **Approve all**, and then select **Approve**.

- You can view your current items and deleted items in the Published tab.

The deleted account code shows the following error code in the Cost Item Details and in the CBS tab.

Task details		
Account code	Hide in plan and progress	Is terminal
	☐	☐
#REF! 	☐	☒
00	☒	☒
	☐	☒
	☐	☒
	☐	☒

11.3.2.2 Replacing deleted account codes

To remove the **#REF!** error in the cost item details slide-out panel and grid, select the error to open the Assign Account Code dialog box. Select another account code from the list, and then click **Assign**. The error on both the CBS tab and the Cost Item Details slide-out panel is replaced with the account code you selected.

✕

Assign account code

Search... 🔍

Sel...	Utilized	Account code	Description	UoM
☒	☐	00	Overhead	PLS
☐	☒	00	DES WD A2k	Hour
☐	☐	00.00000000.Core Functi...	DES - DUTCH	Test123456Test123456Te...
☐	☐	00.0000000000000001	desrption updated_1324	Test1920- Copy
☐	☐	00.0000000000000001.MRT...	DES_P	PLS
☐	☐	00.0000000000000001.MRT...	DES_PDU	TestSep13
☐	☐	00.0000000000000001.nan...	nandy	TestSep13
☐	☐	00.0000000000000001.Nan...	Nandy Test Acs	TestSep13
☐	☐	00.0000000000000001.New...	New nandy May20th	TestSep13
☐	☐	00.0000000000000001.NR_...	00.00000000.NR_050820...	Acre

Clear
Cancel
Assign

11.3.2.3 Renaming account codes

If you have the required permissions, you can rename account codes. Follow the step by step to rename an account code.

Renaming account codes

1. Go to the Master data libraries, and then select **Account codes**.
2. From the Staging tab, select an account code you want to rename.
3. Select the **Edit** icon in the upper-left corner.

Master data libraries		Account codes			
		PUBLISHED	STAGING	AUDIT LOG	IMPORT LOG
		 Staged account code changes and requests may differ from current published codes, refer to Published tab for current information.			
Account code	Description	UoM primary	Currency	UoM secondary	
☒ ___001	___001	Acre	US Dollar		
☐ 00	DES WD A2k	Hour	CFA Franc BCEAO	Hour	
☐ 00.0000000000000001	desrption updated_1324	Test1920- Copy	US Dollar	TestSep13	
☐ 00.0000000000000001 MRTER 0	DES_P	PLS	US Dollar		
☐ 00.0000000000000001 MRTER 0 Core H	DES_PDU	TestSep13	US Dollar	TestSep13	
☐ 00.0000000000000001.nandy kendo	nandy	TestSep13	Unidad de Fomento	TestSep13	
☐ 00.0000000000000001.Nandy test ACS	Nandy Test Acs	TestSep13	US Dollar	TestSep13	
☐ 00.0000000000000001 New nandy May20	New nandy May20th	TestSep13	US Dollar	TestSep13	
☐ 00.0000000000000001 NR_05082019	00.00000000 NR_05082019_DESC	Acre	US Dollar		
☐ 00.0000000000000001 NR1_05082019	00.00000000 NR1_05082019_DESC	Acre	US Dollar	098765	
☐ 00.0000000000000001 NR1_05082019...	NR1_09082019_DESC	Acre	US Dollar		
☐ 00.0000000000000001.PK -Oct-2019	PK -Oct-2019-description	Test01 30-05-2019	US Dollar	TestSep13	

4. On the Edit account code page, enter a new name for your selected account code in the **Description** text box. Then enter a new name for your selected account code.

Account code details

* Parent account code
None - None

* Account code
No... ___001

Start typing the code or description. i.e. footing


* Description
___001

* Currency
USD - US Dollar

* UoM primary
Acre

UoM secondary

5. Click the **Stage** button.
- This takes you back to the Staging page.

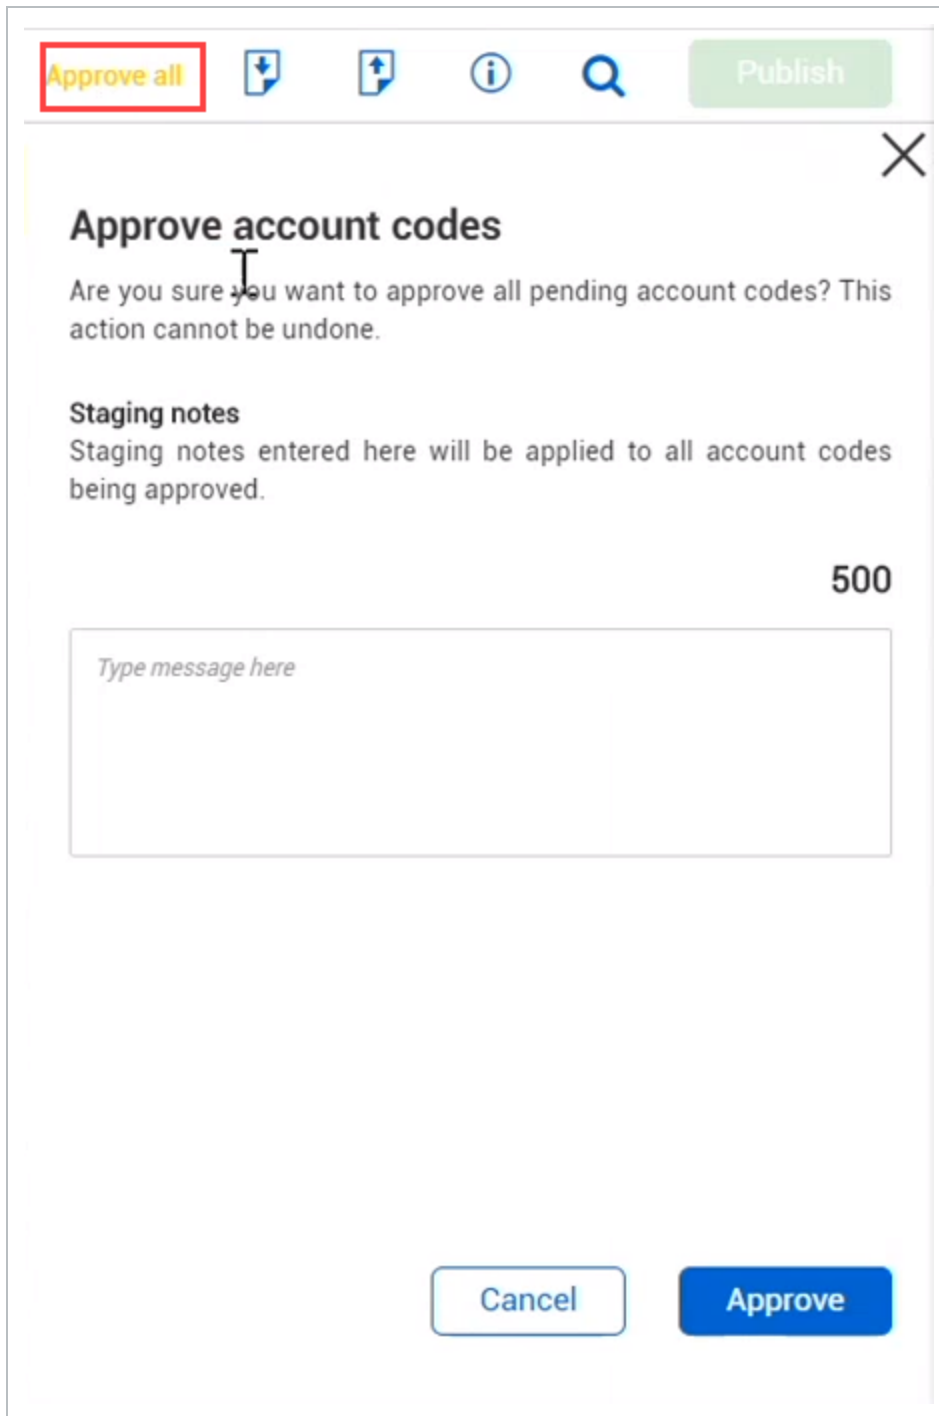

Approve all [Download] [Upload] [Info] [Search] [Publish]

Approve account codes

Are you sure you want to approve all pending account codes? This action cannot be undone.

Staging notes
Staging notes entered here will be applied to all account codes being approved.

500

Type message here

[Cancel] [Approve]

6. From the Staging page, select **Approve all**, and then select **Approve**.
 - You can view your current items and renamed items in the Published tab.

Your renamed account code is viewable through the Account code column, Cost Item Detail tab, and the ACS tab.

11.4 MEASUREMENT TYPES

In master data libraries units of measure, there are two sections. The sections are Units of measure, and Measurement types. Using any two Units of measure that share the same Measurement type (such as area), you are able to do a measurement type conversion in the ACS.

If you have a cost item with a different unit of measure assigned to an account code, but with the same measurement type, that cost item can contribute to the same account code.

Master data libraries		Units of measure		
Units of measure				
Measurement types				
Name	Description	Measurement type		
☐ #NAME?- Copy AE ae	BACKLOGS	Area		
☐ #NAME?- Copy B	DESC	Area		
☐ #NAME?d	DESC	Area		
☐ -0098765- Copy- Copy1- Copy		Area		
☐ -0098765- Copy- Copy1- Copy...	-0098765- Copy- Copy1- Copy...	Area		

You can have a cost item with a measurement type of acre contribute its values to its assigned account code if the account code has a measurement type of square foot. This is Because acre and square foot are both a measurement type of Area.

The column Primary to Primary lets you choose the cost item that contributes quantities of the account code.

Primary Qty

2,460.1999...

Primary UoM

SF

DETAILS

COST CATEGORIES

ACS item details


Primary to Primary

CBS posi... code	Desc...	WBS phase code	Forec... (T/O) quan...	UoM	CE final MHrs	CE total cost	Prim... to Prim...	Prim... to Seco...
1.1.1.1	Permits	1004_	450.00000	Acre	2,323.00000	99.9999950...	☒	☐
1.9.2.1	SOE for fou...	1252	320.00000	SF	64.00000	0.00000000...	☒	☐
1.9.2.2	Excavate fo...	1253	95.00000	CY	57.00000	0.00000000...	☐	☐
1.9.2.3	U&H Steel	1254	2.64600	Ton	5.29200	0.00000000...	☐	☒
1.9.2.4	Set Steel Fr...	1255	35.00000	Each	140.00000	0.00000000...	☐	☐
1.9.2.5	Bolt Up	1256	172.00000	Each	22.36000	0.00000000...	☐	☐
1.9.2.6	Metal Grati...	1257	180.00000	SF	28.00000	4,032.9767...	☒	☐

The items without a check mark, such as Cubic Yards, have a measurement type that is not considered an area, so you cannot select Primary to Primary for Cubic Yards, Ton, and Each.

11.5 COST CATEGORY LABEL CUSTOMIZATIONS

In Master data libraries > Cost categories, there is a **Enable custom labels** toggle. If this toggle is turned on, all of your cost category field names come from the custom columns depending on your language preference in Control. Language preference is located in user settings.



You can overwrite the custom labels if you have the applicable permissions. Depending on where you have cost categories shown in the product, the overwritten labels show with the new custom labels.

These labels can be viewed at the organization level. Every project within that organization can see these labels.

If the organization prefers a different field name, it can be renamed using the cost category custom labels.

Dimmed custom labels cannot be overwritten. For example, the Field name Total.

Field name	Is terminal	Custom label - EN
Total	☐	Total
Labor ⓘ	☐	TEST-12345-94
Labor Base	☒	L-Base

If the custom label for the field name is blank, then the custom label column will use the default name for the field name column.

One way of finding these custom labels in the project is by going to the CBS register. From there, open the Cost Categories slide-out panel. Under the Cost category column, find your custom label. For example, the Labor Base field name can be customized and renamed L-Base.

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

1004_

Permits

DETAILS

ATTRIBUTES

COST CATEGORIES

% Complete

★ Live forecast method

Latest actuals in forecast values

75.55556 %

Manual (EAC)

12/11/2020

Total

Per unit

Cost category	Current budget	Total cost (to date)	Current estimate	★ Live forecast
^ Total	\$ 109.999995000...	\$ 30,559.6000000...	\$ 99.99999500000	\$ 49,999.9999990...
^ Labor	\$ 0.00000000000	\$ 44,111.0000000...	\$ 0.00000000000	\$ 72,352.8918529...
L-Base	L-Base	00000...	\$ 0.00000000000	\$ 183.093332000...

These changes can take a few minutes to fully generate because custom categories span the entire project.

If the Enable custom labels toggle has been shut off, then the category names come from the Field names in the Master data libraries only.

This page intentionally left blank.

CHAPTER 12 – INTERFACES


The InEight cloud platform has multiple options for synchronizing information from one platform to another. This gives you many options to utilize data efficiently between various programs, saving you time and resources.

After the initial import from Estimate, you can use the Push and Get actions to integrate directly with Control. You can use Push actions to send the CBS structure, budget, live forecast, actual quantity, pay item, billed revenue, or forecast revenue from your job. You can use the Get actions to bring in quantities, actual cost, man-hours, and billed revenue from other Platform and external applications.

The table below shows you the high-level functions of platforms to help you better understand how the actions interrelate.

Title	Description
Estimate	Create CBS/ACS/WBS structures Create cost estimates Analyze contractor/supplier quotes Prepare bid proposals Benchmark estimate values
Contract	Create and manage bid packages Set up and manage contracts Create and manage issues and change orders
Control	Edit CBS/ACS/WBS structures Manage budgets and contracts Manage forecasts Record actuals (manual entry, or import from Plan and ERP) Calculate job costs/variances, earned values, contract earnings
Plan	Associate planning components with CBS/ACS/WBS structures Create work plans and packages
Progress	Create work plans and daily plans Record progress and timesheets (as-builts) Approve executed daily plans
ERP	Budget, Payroll, Forecasts, AP/AR, Final Costs

The workflow diagram below shows how programs connect and how data flows between the InEight products.

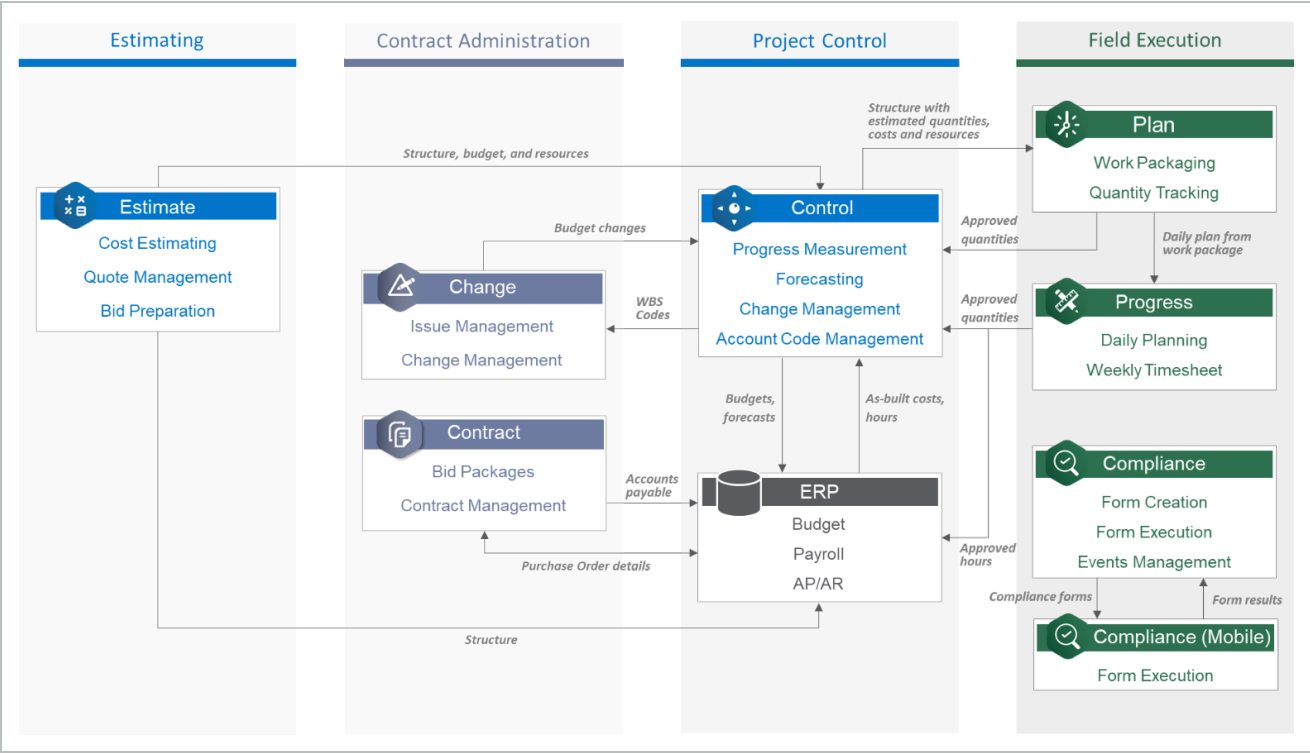

12.1 Push and Get actions 546

12.2 Scheduled syncs 551

 12.2.1 Sync integrations 552


12.3 Audit log - Integration 556

12.1 PUSH AND GET ACTIONS

Control integrations are used to move specific data in to or out of the application. As data is generated or modified in one product, it does not automatically change in other connected products; you must perform a manual sync action, referred to as a *Push* or *Get* action.

- A *Push* sync occurs when you send information to another InEight cloud Platform application or an external application.
- A *Get* sync occurs when you retrieve information from a different InEight cloud Platform application or an external application.

Click the **Actions** menu from the Control main page and hover over the *Sync* option to see the available integration options.

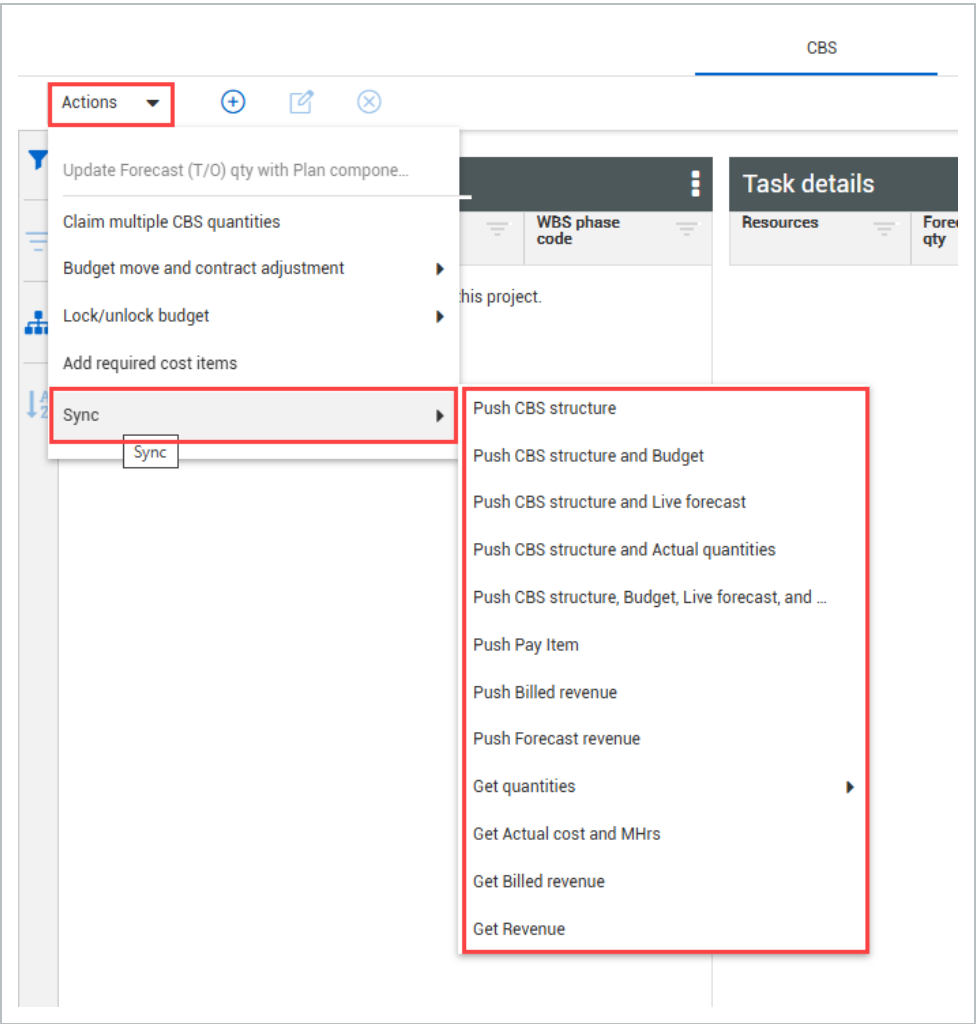


The table below provides a description of the sync type functions.

Sync option	Function
Push CBS structure	Syncs the Control CBS structure to the ERP system.
Push CBS structure and Budget	Syncs the Control CBS structure, budgeted quantities, man-hours, and costs to the ERP system.
Push CBS structure and Live forecast	Syncs the Control CBS structure and Live forecasted quantities, man-hours, and costs to the ERP system.
Push CBS structure and Actual quantities	Syncs the Control CBS structure and job-to-date actual quantities to the ERP system.
Push CBS structure, Budget, Live forecast,	Simultaneously performs all the syncing functions listed above (1-4).


Sync option	Function
and Actual QTY	
Push Pay Item	Syncs the Pay item list and data to the ERP system.
Push Billed revenue	Syncs job to date billed amounts to the ERP system.
Push Forecast revenue	Sync pay item revenue values (billed revenue, earned revenue, forecast revenue).
Get quantities (Through Previous Pay Period or Job To Date)	Retrieves the claimed quantities from InEight applications and incorporates the information to Actual QTY in Control.
Get Actual cost and MHrs	Retrieves actual project costs and man-hours from the ERP system and incorporates the information to Actual costs and Actual man-hours within Control.
Get Billed revenue	Retrieves billed amounts from the ERP system and incorporates the information to Billed revenue within Control
Get Revenue	Retrieves revenue information from Ineight applications and incorporates the information to forecasted revenue. This feature is available with the applicable setup and settings.

Sync Options

- 1. From the Control main page, click the **Actions** menu.

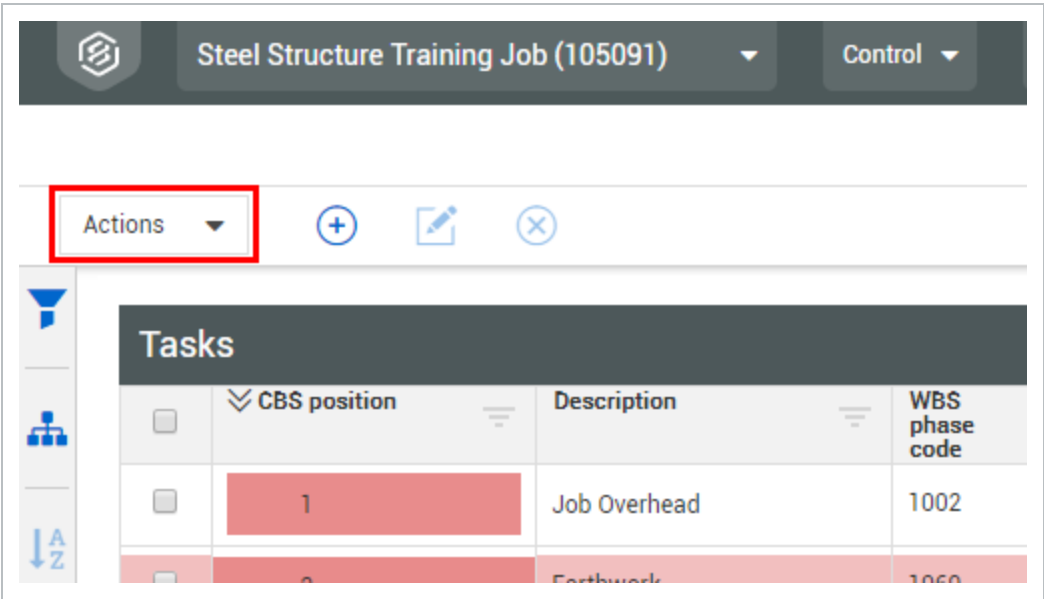

- 2. Select **Sync** from the Actions drop-down.

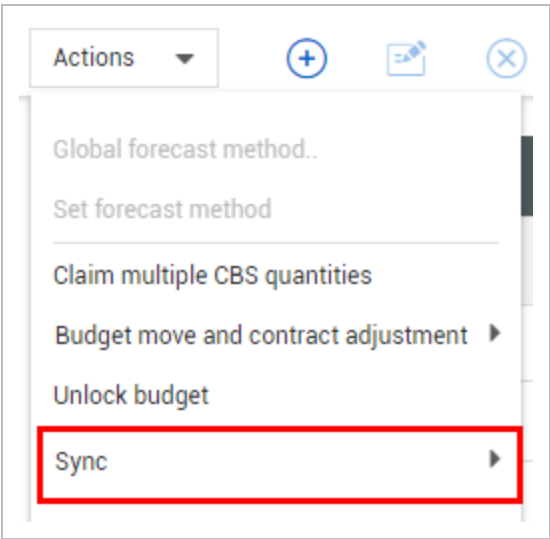

- 3. Select **Push CBS Structure** from the Sync drop-down.

The screenshot shows the 'Actions' menu with the following options:

- Global forecast method..
- Set forecast method
- Claim multiple CBS quantities
- Budget move and contract adjustment ▶
- Unlock budget
- Sync ▶

The 'Sync' sub-menu is open, showing the following options:

- Push CBS structure (highlighted with a red rectangle)
- Push CBS structure and Budget
- Push CBS structure and Live forecast
- Push CBS structure and Actual quantities
- Push CBS structure, Budget, Live forecast, and Act...
- Get Plan quantities ▶
- Get Actual cost and MHrs

The background table 'Task details' has the following data:

Description	Resource	Forecast (T/O) quantity
Earthwork		10,000.00
Earthwork Review	1	1.00
		0,000.00
		0,000.00
		0,000.00
		350.00
		200.00
		0,000.00


- A message shows at the top of the page that shows the process initiated.

The screenshot shows the top navigation bar with the following elements:

- Steel Structure Job (105091)
- Control
- Workspaces
- CBS structure sync initiated** (highlighted with a red rectangle)
- CBS
- ACS
- PAY ITEMS
- CHANGE REGISTER

- You can follow the same steps for selecting the other sync options
- For the Get Plan Quantities option, you must select the **Through Previous Pay Period**

option

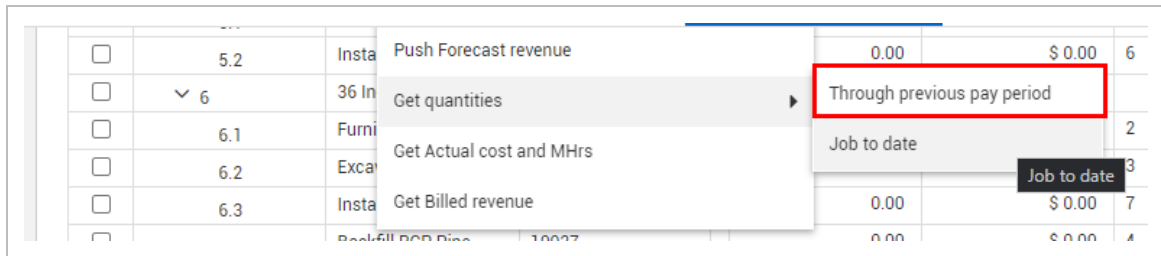

When you want certain types of data to sync automatically, you can schedule syncs. For more information, see [Scheduled syncs](#).

12.2 SCHEDULED SYNCs

Scheduled syncs allow you to set up automatic syncs, so you don't have to manually perform the syncs. You can set a time and date for the type of information you want updated from push or get data sync options. You can do a one-time sync or set up recurring syncs to get up-to-date costs or man-hours.

To use the sync features in Control, you must first select **Control with confirmation** in Global Options. For more information, see [Cost item integration behavior](#).

To schedule syncs, you must first configure them for your organization in Application integrations. You can open Application integrations in Main menu > Suite administration > **Application integrations**.


The available sync types are:

- Push CBS structure
- Push CBS structure and Budget
- Push CBS structure and Live forecast
- Push CBS structure and Actual quantities
- Push CBS structure, Budget, Live forecast and Actual quantities
- Push Pay item
- Push Billed revenue
- Push Forecast revenue
- Get Quantities
- Get Actual cost and MHrs
- Get Billed revenue

For more information about push and get functions, see [Push and Get actions](#).

12.2.1 Sync integrations

To start scheduling syncs, go to the Sync integrations tab in the Control Project settings. You can add syncs by selecting the **Add sync schedule** button. You can schedule all your syncs for the project at one time.

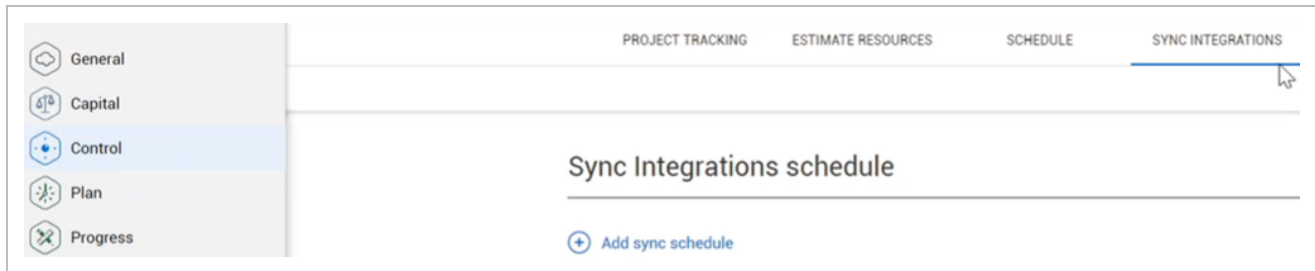

There are five required fields you must fill out in order to schedule a sync.

- Sync type
- Time zone
- Start date
- Time to run sync
- Repeat

Sync types lists all available push and get syncs.

* Sync type

Select one

Select one

Push CBS structure

Push CBS structure and Budget

Push CBS structure and Live forecast

Push CBS structure and Actual quantities

Push CBS structure, Budget, Live forecast and Actual quantities

Push Pay item

Push Billed revenue

Push Forecast revenue

Get Plan quantities

Get Actual cost and Mhrs

Get Billed revenue

* Time zone

(UTC-06:00) Central Time (US & Canada)

* Time to run sync

12:00 AM

Through previous pay period

Job to date

Cancel

The Time zone is where you select which region's time zone you are in.

Start date functions similarly to selecting a start date for a project. You cannot select to start a sync from a day in the past. The scheduled sync starts at the current day by default unless you select otherwise.

Add sync schedule

* Sync type

Select one

* Time zone

(UTC-06:00) Central Time (US & Canada)

* Start Date

02/02/2021

* Time to run sync

12:00 AM

* Repeat

Never

Daily

Weekly

Monthly

Cancel

Add

You can only select start times in 30 minute increments.

The Repeat section is where you select how often a scheduled sync repeats. You can choose to have the sync repeat daily, weekly, monthly, or never depending on your preference. You can end the schedule syncs on a certain date or end after a number of occurrences.

For daily syncs, select how often you want to repeat the sync or when you want the reoccurring syncs to end.

* Repeat

Never

Daily

Weekly

Monthly

* End

☒ After

1

Occurrence(s)

☐ On

02/03/2021

Cancel

Add

For weekly syncs, select which days the sync repeats on as well as when you want the sync to end.

* Repeat

Never Daily Weekly Monthly

* End

☒ After 1 Occurrence(s)

☐ On 02/03/2021

* Repeat on All None

☐ S ☐ M ☐ T ☐ W ☐ T ☐ F ☐ S

For monthly syncs, select what day in the month the sync repeats and when you want the sync to end.

* Repeat

Never Daily Weekly Monthly

* End

☒ After 1 Occurrence(s)

☐ On 02/03/2021

* Repeat on

☐ Day 1

☒ First

First

Second

Third

Fourth

Last

Sunday

Cancel Add

After you click **Add**, the sync shows in the Sync Integrations tab.

Sync Integrations schedule

+ Add sync schedule

Scheduled syncs

Push Billed revenue Sync type: Push Billed revenue Time to run sync: 12:00 PM CST Repeat: Weekly	Start date: 02/01/2021 Repeat on: Fri End: 12/31/2021	 
Get Plan quantities Sync type: Get Plan quantities - Job to date Time to run sync: 1:00 PM CST Repeat: Monthly	Start date: 02/08/2021 Repeat on: Last - Saturday End: 12/31/2021	 


You can edit syncs or delete them using the Edit and Delete buttons on the right of the sync data box. When you want to perform manual syncs for certain type of data, you can use the *Push* or *Get* action. For more information, see [Push and Get actions](#).

12.3 AUDIT LOG - INTEGRATION


As you utilize the sync option, you have the option to go back and audit the status of the actions taken. The Audit Log Integration section shows all sync processes that have been initiated and their status. The Integration section captures whether the sync process between InEight Control and the ERP system was completed successfully. You can also view how long the sync process took to complete and who requested the sync.

Sync Audit Log

1. From the Control Workspaces page, click the **Audit Log** tab.



2. On the left side bar menu, click **Integration**.

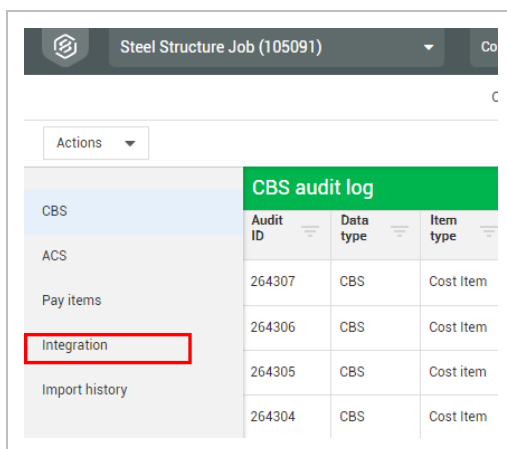

The log displays the current sync status

CHAPTER 13 – INEIGHT PLATFORM SETTINGS

To manage a project successfully in Control, the correct project details must be added before project initiation.

You can view project details in the All projects & organizations page of the InEight cloud platform.

Every new project launch has its own particularities, and the setup and initialization of these projects depends on multiple factors, such as:

- Project organizational structure
- Staff and resources assigned
- Location of the project
- Units of measurement
- Currencies
- Financial reporting period

These settings are set up and configured in InEight Platform.

13.1 ORGANIZATIONAL BREAKDOWN STRUCTURE

The Organizational Breakdown Structure (OBS) represents the hierarchical company structure. It is the way your company is structured and divided, such as departments, districts, sectors, etc. Roles and permissions can be added at different levels in your OBS, so users with district level access would have access to all the projects under that district's umbrella. For more information, see [Organizational breakdown structure](#) in Platform.

To access the OBS, from the main menu click **All projects & organizations**, and then select the **Organizations** tab.

All projects & organizations	
PROJECTS ORGANIZATIONS	
Organization	Description
☐ C-XYZ	Company XYZ
☐ C-XYZ : C-XYZ-ND	Company XYZ - North Division
☐ C-XYZ : C-XYZ-ND : C-XYZ-ND-HC	Company XYZ - North Division - Heavy Civil
☐ C-XYZ : C-XYZ-ND : C-XYZ-ND-BC	Company XYZ - North Division - Building Construction
☐ C-XYZ : C-XYZ-ND : C-XYZ-ND-M	Company XYZ - North Division - Mining
☐ C-XYZ : C-XYZ-SD	Company XYZ - South Division
☐ C-XYZ : C-XYZ-SD : C-XYZ-SD-M	Company XYZ - South Division - Mining
☐ C-XYZ : C-XYZ-SD : C-XYZ-SD-P	Company XYZ - South Division - Power
☐ C-XYZ : C-XYZ-OSD	Company XYZ - Over Seas Division
☐ C-XYZ : C-XYZ-OSD : C-XYZ-OSD-M	Company XYZ - Over Seas Division - Mining
☐ C-XYZ : C-XYZ-OSD : C-XYZ-SD-HC	Company XYZ - South Division - Heavy Civil

13.1.1 Unique budget code segments

You can populate budget segments in Workspaces to show a unique code label. Unique budget code segments contain additional options to identify a cost item using four independent fields that are separated by periods. Budget codes can be configured at the organization level and are primarily used with Time Center.

All projects & organizations

Edit organization

Budget code

The segments are combined to create a single unique budget code separated by periods. They cannot be changed once a project has been added.

Using unique budget code? ☒

* Unique budget code

Segment 1

Segment 2

Segment 3

Segment 4

Project

Cost center

Other (String)

Phase code


Please specify name

Cost Code

Tasks

	CBS position	Description	Budget Segment 1	Budget Segment 2	Budget Segment 3	Budget Segment 4	Forecast method
☐	1	Financial Results ..	103961		1000		Average performan..
☐	2	Misc. Rev Internal	103961		1103		Rollup
☐	2.1	Misc. Rev Internal	103961		1104		Manual (EAC)
☐	2.2	Escalation/Contin..	103961		1101		Rollup
☐	2.2.1	General Project Ri..	103961		1102		Current estimate
☐	2.3	Directs	103961		1001		Rollup
Subtotals 163							

When the edit WBS phase codes and budget segments permission is assigned to a role in Suite administration > Roles and permissions > **Control**, users are allowed to populate the WBS phase codes and budget segments in the CBS workspace. This permission only applies based on configurations set for the WBS phase code and the budget segments. The edit WBS phase codes and budget segments permission must be selected to allow users to edit WBS phase codes and budget segments.

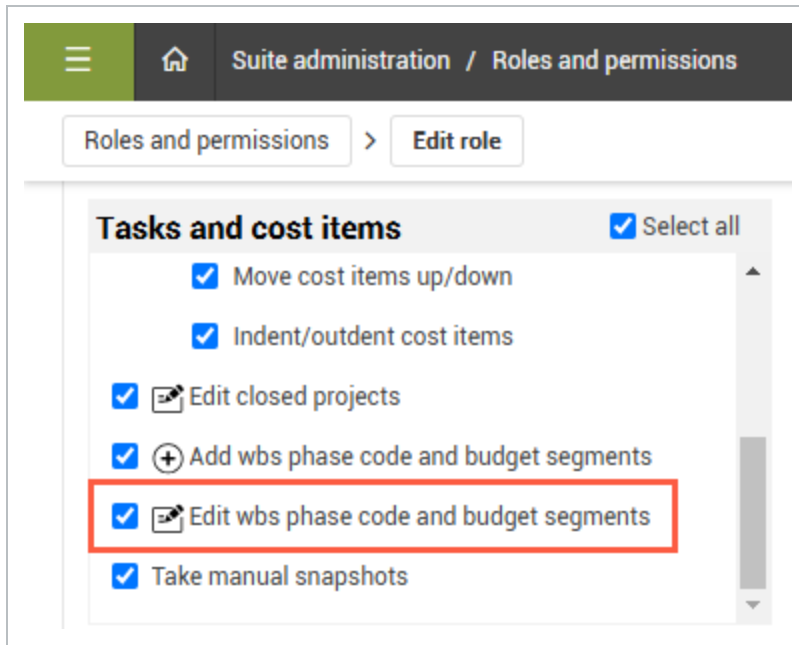

When only the Add wbs phase code and budget segments permission is assigned, users are only allowed to import WBS phase code and budget segments, and not to edit them.

When importing, users who have only been assigned the Add wbs phase code and budget segments permission must use the **New items** option in the Import CBS data dialog box.

Import CBS data

Import from Excel (.xlsx, .xls) or Comma separated value (.csv)

Drag and drop the file here
or browse

Browse

Options

* Import type

Cost items and cost item attributes ▼

☐ Update existing and new items

☐ Update existing items

☒ New items

↓ Cost categories list

① The import file is read and field mapping can be specified. Mapping uses row 1 headers from the source document

For new cost items, if the CBS position field is mapped then the position specified is where the cost item will be placed in the hierarchy. If the CBS position field is not mapped then the new cost item will be inserted at the bottom of the CBS hierarchy.

Cancel

Next

Open Project Details

1. From the All projects & organizations page, right-click on **your job**.
2. Select **Edit Project**, or click the **Edit** icon.

13.2 PROJECT PAGE

The Edit Project page is where general project setup information is edited and stored, including the following settings:

- Project Details
- Location
- Project Dates
- Prime Contact and Project contacts

- Currency and Markets

Steel Structure Training Job | 105091 / Project details

All projects & organizations > Edit project
DETAILS INFORMATION ATTRIBUTES
Project settings Cancel Save

Project details

Add project image
Minimum of 540px x 360px

* Project ID
105091

* External project ID ⓘ
105091

Notes

* Name
Steel Structure Training Job

* Status
Active

* Phase ⓘ
Execution

* Organization
C-XYZ

Location

Country / Region
United States Of America

Address 1

Address 2

City
Denver

State
Colorado

Postal / Zip code

Latitude

Longitude

* Time zone
(UTC-06:00) Central Time (US & Canada)

Project dates

Project start date
10/01/2015

Project end date
04/12/9999

Forecast start date
month/day/year

Duration ⓘ

Forecast completion date ⓘ
month/day/year

Hint: Notice to proceed date or ...

Hint: forecast time duration in c...

Forecast extensions/reductions

Forecast revised duration

Forecast revised completion date
month/day/year

Prime contract

Company legal name

Owner legal name

Tax id

Original contract amount

Contract number

Contract date
month/day/year

Hint: Business name

Hint: Client or Designer project ...

Hint: Date original contract sign...

Contract start date
month/day/year

Duration ⓘ

Contract completion date ⓘ
month/day/year

Certificate of substantial completion(expected)
month/day/year

Certificate of substantial completion(awarded)
month/day/year

Hint: Notice to proceed date or ...

Hint: Contract time duration in c...

Contract extensions/reductions

Contract revised duration

Contract revised completion date
month/day/year

Certificate of final completion(expected)
month/day/year

Certificate of final completion(awarded)
month/day/year

Currency ⚠

* Base currency
USD - US Dollar

Hint: type the entity, name or code i.e. USD

Add another currency

Project contacts

Owner

Designer

Contact 1

Contact 2

Contact 3

Contact 4

Markets

Market

Hint: type the market name or description

Add another market

Business case

For more information, see [Project initiation](#) in Platform.

13.3 MANAGE USERS

As an administrator, you can manage users and set up the correct roles and permissions in InEight Platform to manage and organize the application successfully.

13.3.1 User Management

The User Management page provides a list of users inside your organization. You can view any user's project access, roles, and permissions within your organization. Users with applicable administrative permissions can edit and grant permissions to other users, up to the equivalent level of access they have been granted. For more information, see [User Management](#) in Platform.

13.3.2 Roles and permissions

A role in InEight Platform is defined as the function that a user occupies inside an organization or project. A role contains a set of predetermined authorizations and permissions. When a role is assigned to a user, they acquire all the permissions of that role in the project or organization that you can assign to users or project staff.

With sufficient rights and permissions, you can add or remove a role and all access it provides from the user. The Roles and Permissions section is where you can view what permissions each role has. For more information, see [Roles and Permissions](#) in Platform.

Control has permissions that control important functions within the program as shown in the image below.

Suite administration / Roles and permissions

Roles and permissions > **Edit role** Cancel Save

Control Select all


Category	Sub-category	Permissions
Tasks and cost items	View tasks	☒ ☐
	Add cost items	☒ ☐
	Edit tasks	☒ ☐
	Edit cost items	☒ ☐
	Delete cost items	☒ ☐
	Delete sync'd cost items	☒ ☐
Change management	View everyone's change orders	☒ ☐
	View everyone's draft change orders	☒ ☐
	Edit any draft change order	☒ ☐
	Delete draft change orders	☒ ☐
	Approve/reject change orders	☒ ☐
	Create change orders	☒ ☐
Integrations	View integrations	☒ ☐
	Push CBS structure	☒ ☐
	Push CBS structure and budget	☒ ☐
	Push CBS structure and live forecast	☒ ☐
	Push CBS structure and actual qty	☒ ☐
	Push CBS structure, budget, live forecast, and actual qty	☒ ☐
Audit log	View audit log	☒ ☐
	View CBS audit log	☒ ☐
	View ACS audit log	☒ ☐
	View pay item audit log	☒ ☐
	View sync audit log	☒ ☐
	View import history	☒ ☐
Revenue	View billed revenue	☒ ☐
	Edit billed revenue	☒ ☐
	View revenue	☒ ☐
	Edit revenue forecast	☒ ☐
	View revenue library	☒ ☐
	Edit revenue library	☒ ☐
View sets	View personal view sets	☒ ☐
	Add personal view sets	☒ ☐
	Edit personal view sets	☒ ☐
	Delete personal view sets	☒ ☐
	Send personal view sets	☒ ☐
	Send personal views to all users in a project	☒ ☐
Actuals	View actuals	☒ ☐
	Edit open period quantities	☒ ☐
	Edit open period costs	☒ ☐
	Edit open period man-hours	☒ ☐
	Edit open period equip-hours	☒ ☐
	Edit any period quantities	☒ ☐
Pay items	View pay items	☒ ☐
	Create pay items	☒ ☐
	Edit pay items	☒ ☐
	Delete pay items	☒ ☐
	View project library resources	☒ ☐
	Edit project library resources	☒ ☐
Budgets	View original budget	☒ ☐
	View original budget cost categories	☒ ☐
	View current budget	☒ ☐
	View current budget cost categories	☒ ☐
	View current estimate	☒ ☐
	Edit current estimate	☒ ☐
Forecasting	View private forecasts	☒ ☐
	Edit private forecasts	☒ ☐
	Push to shared forecasts	☒ ☐
	View shared forecasts	☒ ☐
	Edit shared forecasts	☒ ☐
	View forecast delta data block	☒ ☐
Account codes	Edit forecasts	☒ ☐
	View live forecast in the ACS	☒ ☐
	Push to live forecast in the ACS	☒ ☐
	Edit live forecast in the ACS	☒ ☐
	View original budget	☒ ☐
	View current budget	☒ ☐
Schedule	View schedule data block	☒ ☐
	Edit schedule data	☒ ☐

13.3.3 Considerations

Establishing roles and permissions is an administrative function. As such, access to these settings may not be available to you, as the setup of these settings may not be within the scope of your daily tasks.

13.4 ORGANIZATION GENERAL SETTINGS

The organization settings page contains general setup information for all the InEight products, including Control. The left ribbon menu lets you navigate to the appropriate settings for each application, including Control.

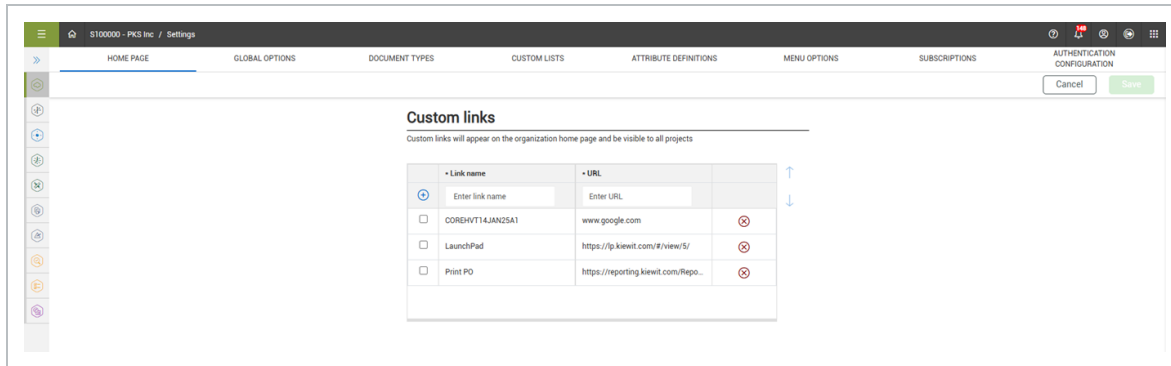


The general settings are the following:

- Home Page
- Global Options
- Fiscal Calendar
- Document Types
- Custom Lists
- Attribute Definitions
- Menu Options

13.5 HOME PAGE

In the Home Page tab, you can configure custom URL links that show on the organization and project level home pages.

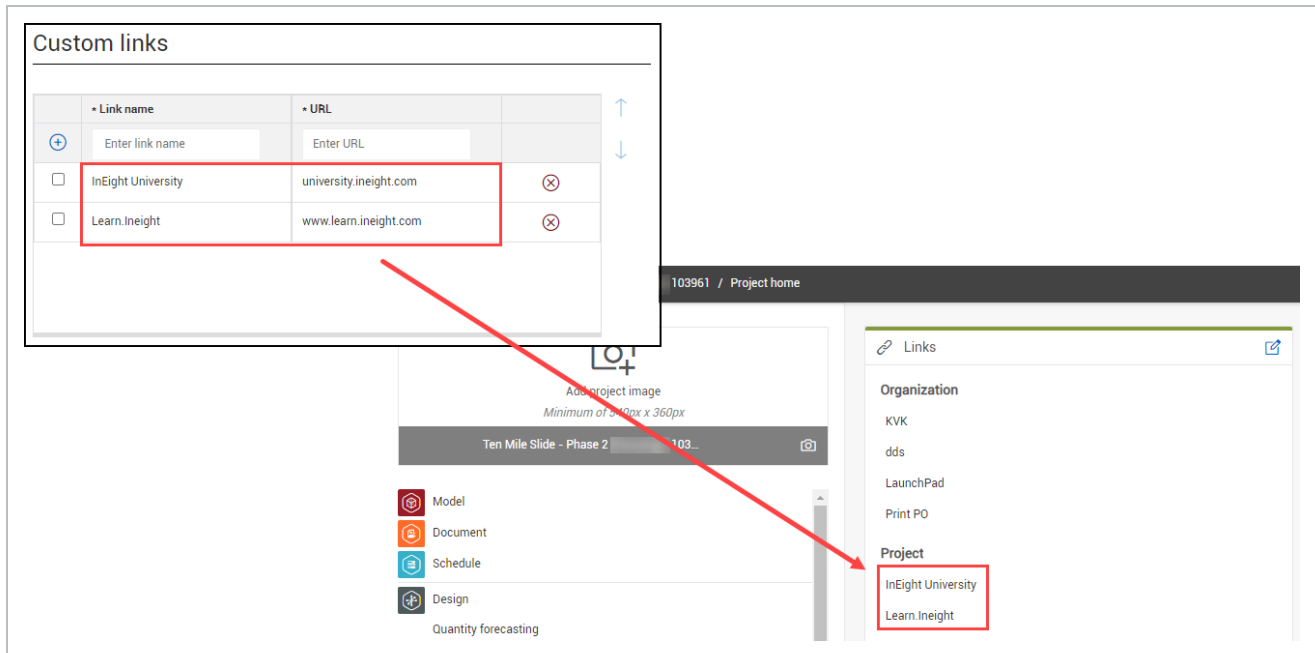

To go to the Home page, click Main menu > <organization> > **Settings**.

13.6 GLOBAL OPTIONS


In Global Options, you can configure the following settings:

- Master data libraries
- Role Assignment
- Project display in primary navigation
- Cost item integration behavior
- Email preferences
- Environment indicator
- Session timeout
- Landing page default view
- Organization/Project images
- Product integrations

13.6.1 Master data libraries

You can switch the Validate equipment to project currency toggle to *On* if you want to validate equipment resources to the project currency. When turned *Off*, there is no equipment to the project currency validation. You can assign an equipment resource with a currency that is different (mismatched) than the project currency or alternate currencies.


When turned *On*, equipment is checked against the project currency. If the equipment currency is different than the project currency, you are unable to use that equipment on the project unless the equipment or project currency are changed to match.



The setting is irrelevant if all equipment and the project use the same currency.

13.6.2 Role Assignment

You can switch the Allow users to self-assign roles toggle to *ON* to let users self-assign their own roles.



13.6.3 Project display in primary navigation

You can select to:

- Show the project name first which may truncate the Project ID if name are long.
- Show the project ID first which may truncate the project name.

Project display in primary navigation

☒ Project name first | may truncate Project ID if name...
 ☐ Project ID first | may truncate Project name

Sample:

Core Bank Corporate Headquarters | 123456

Truncated:

Core Bank Corporate Headquarters | 1...

Sample:

123456 | Core Bank Corporate Headquarters

Truncated:

123456 | Core Bank Corporate Headq...

13.6.4 Cost item integration behavior

Provides flexibility in how to configure Control with and without a direct tie to an ERP system. There is also an option to pass cost items directly from other sources to applications. You can select from the following options:

- **Control with confirmation** — Use this option if you use Control and an ERP. To sync cost items between Control and other applications, you must confirm using the sync options in the Actions menu in Control or set up a sync schedule in Sync Integrations. For more information about sync integrations, see [Scheduled syncs](#).
- **Control without confirmation** — Use this option if you use Control but not an ERP. Cost items sync automatically between Control and other applications.
- **Without Control without confirmation** — Use this option if you do not use Control. Cost items pass directly from other sources to applications.

Cost item integration behavior

☒ **Control with confirmation**
 Control with confirmation: Use this option if you use Control and an ERP. To sync cost items between Control and other applications, you must confirm using the sync options in the Actions menu in Control.

☐ **Control without confirmation**
 Control without confirmation: Use this option if you use Control but not an ERP. Cost items sync automatically between Control and other applications.

☐ **Without control without confirmation**
 Without control without confirmation: Use this option if you do not use Control. Cost items pass directly from other sources to applications.


When using a direct integration between InEight Control and your ERP, InEight Control will serve as the project controls interface for setting up and maintaining the project budget and cost structure. Every cost item created in InEight Control also needs to exist in your ERP system so actual costs can be recorded correctly. Your ERP system remains the system of record for all cost transactions, making it imperative that it remains in sync with

any budget or structure changes. Your organization will need to consider what frequency is best for running each sync.

13.6.5 Email preferences

You can enable the following email options:


- Use image in email notifications.
- Send email to user when there is a role change
- Send email to user where there is an email change.



The screenshot shows the 'Email preferences' panel. It has a title 'Email preferences' with a horizontal line below it. There are three toggle switches, each with a green checkmark icon to its left, indicating they are turned on. The first toggle is labeled 'Use image in email notifications?'. The second is labeled 'Send email to user on role change'. The third is labeled 'Send email to user on email change'. To the right of these toggles is a preview area showing a circular image of a globe with a golden eagle perched on top, which is the organization's logo. A small gray square with a white close icon is in the bottom right corner of the preview area.

13.6.6 Environment indicator

You can enable indicators and options for header badge display, header badge color, and footer color. You can also select the option to *Include environment indicator in email subject line*.



The screenshot shows the 'Environment indicator' panel. It has a title 'Environment indicator' with a horizontal line below it. There are three sections: 'Header badge display' with a toggle switch (checked) and a text input field containing 'QA-Main-T01'; 'Header badge color' with a toggle switch (checked) and a purple color selection box; and 'Footer color' with a toggle switch (checked) and an orange color selection box. At the bottom, there is a checkbox labeled 'Include environment indicator in email subject line' which is checked.

13.6.7 Session timeout

You can enable and configure session timeout options.

Session timeout

Enable session timeout

☒

Force signout time

999 MIN

☒ Warn the user 10 min prior to signout

13.6.8 Landing page default view

Select the default landing page view for all users. The default landing page views you can select from are:

- Owner
- Contractor
- Sub-contractor
- Vendor

Landing page default view

Select a landing page view to be used as a default for all users

Contractor ▼

13.6.9 Organization/Project images


You can enable the *Inherit root organization image when creating new projects/sub organizations* toggle to inherit the root organization image when creating new projects or sub-organizations.

Organization/Project images

☒ Inherit root organization image when creating new projects/sub organizations

13.6.10 Product integrations

Enable product settings for all projects created. When a project has a product enabled, the project is available in the selected product.



13.7 FISCAL CALENDAR

13.7.1 Fiscal calendar

The settings in the Fiscal Calendar can be set at the organization and project levels. These settings specify:

- Week ending day
- Financial year start month
- Period end options of month end day, last weekday, financial period closing day, month end plus days, financial period closing time, and closing time zone.
- Project fiscal calendar settings (Organizational level only)

It is important to know the different cut-off dates, especially when you pull the current period actual quantities to compare them to prior periods, or when you synchronize your quantities with the other applications.

Changes to a project level fiscal calendar only impact the project, while changes to the organization level fiscal calendar impact all projects that do not have fiscal calendar modifications. If there are no changes at the project level, and the project matches the organization fiscal calendar settings, the project inherits the organization-level settings.

Any changes to the project fiscal calendar impact read-only snapshots, which are captured at the closure of month-end plus days, for the period month being closed. Changes also influence the monthly time buckets in time-phase forecasting and budgeting and to the time periods in which claims can or cannot be posted.

HOME PAGE GLOBAL OPTIONS **FISCAL CALENDAR** DOCUMENT TYPES CUSTOM LIS

Cancel Save

• Week ending day
Saturday

• Financial year start month
January

Period end

• Month end day
Last day of the month

Last weekday

• Financial period closing day
Same as Month End Plus Days

• Month end plus days
7

• Financial period closing time
23:30

• Closing time zone
(UTC-06:00) Central Time (US and Canada)

Project fiscal calendar settings

☐ Enable project level editing

13.8 DOCUMENT TYPES

You can assign a document type to InEight applications. This lets you filter the payload of Document Types for visibility and use in the assigned application.

English					Español		ES-MX
Name	Description	Product(s)	System managed	Name	Description		
☒ Diagram	Diagram	Model, Document, Estimate, Control, Pla...	Yes	☒ Diagrama	Diagrama		
☐ Photo	Photo	Model, Document, Estimate, Control, Pla...	Yes	☐ Imagen	Imagen		
☐ Design	Design	Model, Document, Estimate, Control, Pla...	Yes	☐ Design	Design		
☐ Executed contract	Executed contract	Model, Document, Estimate, Control, Pla...	Yes	☐ Contrato ejecutado	Contrato ejecutado		
☐ Executed change order	Executed change order	Model, Document, Estimate, Control, Pla...	Yes	☐ Orden de cambio ejecutada	Orden de cambio ejecutada		
☐ Permit	Permit	Model, Document, Estimate, Control, Pla...	Yes	☐ Permiso	Permiso		
☐ Transmittal	Transmittal	Model, Document, Estimate, Control, Pla...	Yes	☐ Transmisión	Transmisión		
☐ Request for information	Request for information	Model, Document, Estimate, Control, Pla...	Yes	☐ Solicitud de información	Solicitud de información		
☐ Submittal	Submittal	Model, Document, Estimate, Control, Pla...	Yes	☐ Envío	Envío		
☐ Other	Other	Model, Document, Estimate, Control, Pla...	Yes	☐ Otros	Otros		
☐ Checklist	Checklist	Model, Document, Estimate, Control, Pla...	Yes	☐ Lista de verificación	Lista de verificación		
☐ Correspondence	Correspondence	Model, Document, Estimate, Control, Pla...	Yes	☐ Correspondencia	Correspondencia		

13.8.1 Considerations

The Document Types settings is available at the organization level only.

13.9 CUSTOM LISTS

Similar to the tag feature in InEight Estimate, you can enter your tags and their values to use later for categorizing your cost items as you manage your project in Control.

Many of the tag fields are validated fields, meaning you can choose from options in a drop-down list. You define both the names of the tags and their drop-down values here.

The field names associated with Cost breakdown structure and Account codes, are tags defined and editable at the organizational level; you cannot edit them at the project level, as indicated by the statement *Inherited from parent organization*.

The screenshot shows the 'CUSTOM LISTS' tab in the application. A table lists various tags with columns: List name, Label name, Associated entity, Field values, and Inherited from parent org. The 'ACS tag 3' row is selected, and a modal titled 'ACS tag 3 field values' is open. The modal shows a description of the tag and a checkbox for 'Inherited from parent organization' which is checked. A red box highlights the 'Multiple' value in the 'Field values' column of the table and the 'Inherited from parent organization' checkbox in the modal.

List name	Label name	Associated entity	Field values	Inherited from parent org
ACS tag 1	ACS tag 1	Account code	Multiple	Yes
ACS tag 2	ACS tag 2	Account code	Multiple	Yes
✓ ACS tag 3	ACS tag 3	Account code	Multiple	Yes
ACS tag 4	ACS tag 4	Account code	None	Yes
ACS tag 5	ACS tag 5	Account code	None	Yes
ACS tag 6	ACS tag 6	Account code	None	Yes
ACS tag 7	ACS tag 7	Account code	None	Yes
Change management ...	Change management ...	Change management	None	No
Change management ...	Change management ...	Change management	None	No
Change management ...	Change management ...	Change management	None	No
CBS tag 1	CBS tag 1	Cost breakdown structure	None	No
CBS tag 11	CBS tag 11	Cost breakdown structure	None	Yes

13.9.1 CBS URL columns

You can create direct links to URL addresses outside of Project Suite under Custom Lists. In the URL Field values you can define a URL with associated criteria to be used as an attribute for a cost item in the CBS.

In the URL Builder enter a URL that you want associated with your list name, along with any other dynamic attributes such as Project ID and CBS position code. Paste your URL and highlight the section you want to reference with another field. First highlight an attribute in the URL string, and then click the [T] reference icon to select which field to connect with.

The screenshot shows the 'CUSTOM LISTS' tab with a table of CBS URLs. The 'CBS URL 1' row is selected, and a modal titled 'URL builder' is open. The modal shows the URL 'www.google.com/[Project ID]/[CBS position]' and a dropdown menu for selecting a field to reference. A red arrow points from the '[CBS position]' part of the URL to the dropdown menu. The dropdown menu lists: Project ID, Control CBS, WBS phase code, CBS position, and Account code.

List name	Label name	Associated entity	Field values	Inherited from parent org
CBS tag 25	CBS tag 25	Cost breakdown structure	None	No
✓ CBS URL 1	CBS URL 1	Cost breakdown structure	URL	No
CBS URL 2	CBS URL 2	Cost breakdown structure	URL	No
CBS URL 3	CBS URL 3	Cost breakdown structure	URL	No
CBS URL 4	CBS URL 4	Cost breakdown structure	URL	No
CBS URL 5	CBS URL 5	Cost breakdown structure	URL	No
Estimating resources ...	Estimating resources ...	Estimating resources	None	No

These quick links are accessible in the CBS and can contain detailed information pertaining to the cost item and project, which can also link to external reports.

In the CBS cost item details attributes slide-out panel, the URL is concatenated to include the attributes defined. A link is included on a cost item that opens a new tab.

1028
Miscellaneous Revenue Internal

Tasks

CBS position	Description
☐ 1	Financial Results ...
☒ 2	Miscellaneous Re...
☐ 2.1	Craft Cost
☐ 2.2	B/C To Parent 103...
☐ 2.3	Intercompany Aut...
☐ 3	Miscellaneous Re...
☐ 3.1	Miscellaneous Re...
☐ 4	Financial Result E...
☐ 4.1	Not in Use
☐ 4.2	Not in Use

DETAILS **ATTRIBUTES** **COST CATEGORIES** **RESOURCE**

CUD3 CUD4 CUD5

CUD6 CUD7 CUD8

CUD9 CUD10 CUD11

CUD12 CUD13 CUD14

CUD15 CBSURL1_EN CBSURL2_EN

CBSURL3_EN CBSURL4_EN CBSURL5_EN

[https://ineight.visualstudio.com/InterStellar/_workitems/edit/\[WBS phase code\]](https://ineight.visualstudio.com/InterStellar/_workitems/edit/[WBS phase code])

The links can also be accessed in the CBS register. Up to five CBS URL columns can be viewed in a data block in the CBS, per project.

Tasks	CBS URL 1	CBS URL 2	CBS URL 3	CBS URL 4	CBS URL 5	Forecast total cost
☐ 1 Job Overhead 1002						\$ 250,000.00
☒ 2 Earthwork 1069	https://ineight.visualstudio.com/InterStellar/_workitems/edit/[WBS phase code]					\$ 400,000.00
☐ 3 Concrete 1071						\$ 1,500,000.00
☐ 4 Structural Steel 1073						\$ 1,516,282.48
☐ 4.1 Erect Steel - Heavy 1074						\$ 25,666.00
☐ 4.2 Erect Steel - Light 1005						\$ 200,000.00
☐ 4.3 Bolted Connections 1006						\$ 49,955.00
☐ 5 Materials 1084						\$ 1,750,000.00
☐ 5.1 Earthwork - Mater... 1085						\$ 250,000.00
☐ 5.2 Concrete - Materi... 1086						\$ 1,000,000.00
☐ 5.3 Structure Steel - ... 1087						\$ 500,000.00
☐ 6 1088						\$ 0.00
Subtotals 12 (1 rows selected)						\$ 4,175,621.00

At the organization level, CBS URL columns 6, 7, and 8 have been added to the CBS register. When you define a CBS URL, it is then applied to each of the organization's projects.

>>

GLOBAL OPTIONS HOME PAGE FISCAL CALENDAR

	List name	Label name	Associated entity ↑	Field values	Inherited from parent org
	CBS tag 23	CBS tag 23	Cost breakdown structure	<u>CBS</u>	No
	CBS tag 24	CBS tag 24	Cost breakdown structure	None	No
	CBS tag 25	CBS tag 25	Cost breakdown structure	None	No
	CBS URL 1	CBS URL 1	Cost breakdown structure	<u>URL</u>	No
	CBS URL 2	CBS URL 2	Cost breakdown structure	<u>URL</u>	No
	CBS URL 3	CBS URL 3	Cost breakdown structure	<u>URL</u>	No
	CBS URL 4	CBS URL 4	Cost breakdown structure	<u>URL</u>	No
	CBS URL 5	CBS URL 5	Cost breakdown structure	<u>URL</u>	No
	☒ CBS URL 6	CBS URL 6	Cost breakdown structure	<u>URL</u>	Yes ↑
	☒ CBS URL 7	CBS URL 7	Cost breakdown structure	<u>URL</u>	Yes ↑
	☒ CBS URL 8	CBS URL 8	Cost breakdown structure	<u>URL</u>	Yes ↑

Creating organization-level CBS URL links lets you associate shared documentation, such as external standard reports that are used across the organization. Instead of setting up links for every project, you can create a CBS URL link in Settings > Custom Lists.

103961 | Ten Mile Slide - Phase 2 (Carrying) / Control / Workspaces

CBS ACS PAY ITEMS

Actions

Tasks

CBS position	Description	Actual vendor Mhrs (to date)	Actual Mhrs (to date)
1	Financial Results ...	0.000000000000	0.000000000000
2	Misc Rev Internal	0.000000000000	7,030.500000000000
2.1	Misc Rev Internal	0.000000000000	0.000000000000

Vendor

Actual vendor Mhrs (to date)	Actual Mhrs (to date)	CBS URL 6	CBS URL 7	CBS URL 8
0.000000000000	0.000000000000			
0.000000000000	7,030.500000000000			
0.000000000000	0.000000000000			

13.10 ATTRIBUTE DEFINITIONS

Attribute Definitions are used to define project attributes which can be of the types text/date/number or can have source values from Organization, Project, and Market master data. These definitions are inherited inas all projects in the organization.

	*Fuel type	*Cost per UoM	*Currency	*UoM	Account code	
+	Enter fuel type name		USD - US Dollar ▼	Select one ▼	Start typing account code	
	Gasoline	\$1.00000	USD - US Dollar	Gallon	71.06.32.016.02 - Turbine Enclosure - Install En...	✕

13.11 MENU OPTIONS

The below URL addresses specific to InEight products are updated when licenses are purchased or activated. The URLs are customer specific. The ability to maintain the URLs are intended for users with account admin only (root Org Setting) permissions. If no other products are purchased or activated, the URL opens an InEight related page to learn more about the products.

Menu links

Configure the URL addresses for your InEight Products

Product	* URL	* Target
Model	https://ineight.com/solutions/virtual-design-constr...	New tab
Document	https://ineight.com/solutions/collaborative-docum...	New tab
Basis	http://my.basisplanning.com	New tab

CHAPTER 14 – CONTROL SETTINGS

As an administrator, you can configure settings at the organization and project level in Control. The correct setting details must be added to manage projects successfully.

- **Organizational settings** — Settings configured at the organizational level are inherited when creating associated child organizations and new projects within the organization. You can configure organizational settings in Main menu > <organization> > Settings > **Control**.
- **Project settings** — At the project level, you can refine the default inherited organizational settings to customize how they are applied in each project. You can configure project settings in <project> > Settings > **Control**.

Organizational settings are applied as default settings for new projects. As an administrator, you can configure the default project settings to how they will apply to your individual project.

14.0.1 Considerations

You must have Level 3 – Account Admin permissions in InEight Platform, or an assignment to the root organization based on permission configuration.

14.1 PROJECT TRACKING

Project tracking settings configure how your project tracks progress and percent complete in Control. Organizational Project Tracking settings are configured in Main menu > organization > Settings > **Control**. For settings configured at the project level, go to project > Settings > **Control**.

These settings include the following options:

- Tasks
- Actuals
- Estimated actuals
- Time-phasing

14.2 TASKS

14.2.1 Organizational and project level

14.2.1.1 Generate WBS phase code automatically

In the Tasks section you can manage how WBS phase codes are generated. You can set the **Generate WBS phase code automatically** toggle to *Yes* or *No*.

When you set the toggle to *No*, phase codes for newly created cost items must be manually entered.

When you set the toggle to *Yes*, phase codes for newly created cost items are automatically generated and the **WBS Phase code generation method** list option activates. In the WBS Phase code generation method list, you can choose from the following:


- **Continue numbering from the last generated number**
- **Regenerates all values beginning from the specified start value** — This option activates the *WBS Phase code start value* field where you can enter a specified value. The value is the phase code for the first cost item created. When automatic phase code generation is activated, the proceeding new cost items is automatically created based on the phase code generation method selected.

14.2.1.2 Enable Manual Snapshots

You can create a manual snapshot of Control project data in the CBS and Pay Items registers. When the *Enable manual snapshots* toggle is enabled, and with the applicable permissions, you can capture a

snapshot at any point in time. When the setting is disabled, snapshots are captured only when *Push Live forecast* and *Push Forecast revenue syncs* are run or when the month-end plus days elapse.

Enabling the manual snapshots settings lets you select the **Take Live Snapshot** option from the Current Live Forecast drop-down menu in the CBS to capture current values in the Live Forecast, Current Budget and Current Estimate.

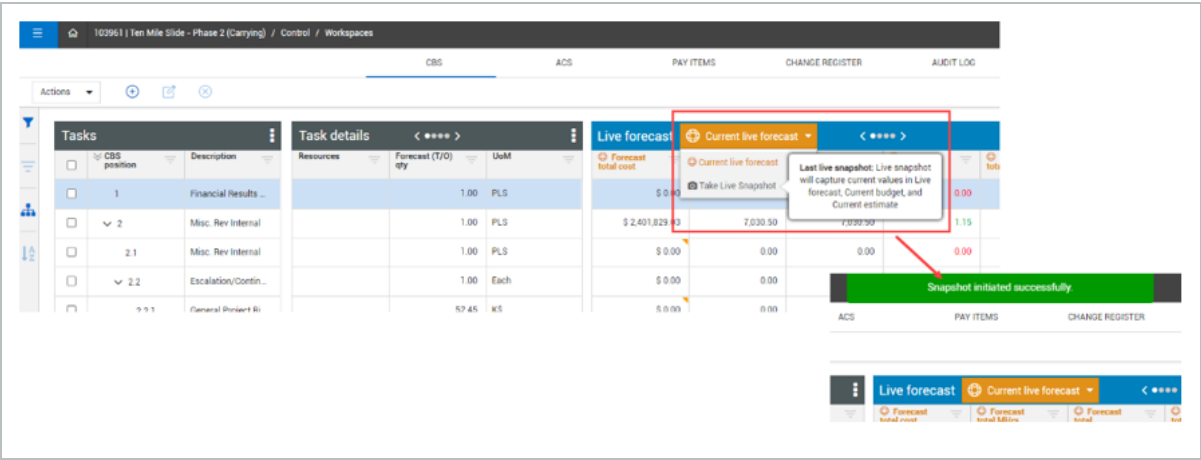

Snapshots can also be taken from the Actions menu.

Steel Structure Training Job 3 | 10... / Control / Workspaces

CBS ACS PAY ITEMS

Actions ▾ (+) (✎) (✕)

- Global forecast method..
- Set forecast method
- Time phased forecasting
- Update Forecast (T/O) qty with Plan compone...
- Claim multiple CBS quantities
- Budget move and contract adjustment ▶
- Lock/unlock budget ▶
- Sync ▶
- Take snapshots**

Snapshots will capture current values in Live forecast, Current budget, Current estimate, and Revenue

Task details < ● ● ● ● >		
Resources	Forecast (T/O) qty	UoM
	1.00	Lump Sum
5	10,000.00	CY
5	10,000.00	Each
	1.00	Each
5	1.00	Ton
5	1.00	Ton
4.3 Bolted connections	1.00	Each
4.4 Labor	10,000.00	Each

You can view the draft snapshot by selecting the **View draft snapshot** from the Current live forecast drop-down menu. This lets you know that the draft snapshot is not yet finalized for the current month.

Live forecast **Current live forecast**

Forecast total cost

\$ 4,599,637,039.68...

\$ 209,224.9771109...

\$ 234,421.2919300...

\$ 123,466.0000029...

Forecast unit

21,706,409.70

373,039.24

Forecast total productivity

0.002030

0.004223

Take Live Snapshot

View draft snapshot

June 2023

May 2023

April 2023

Last Live snapshot : 7/12/2023, 12:28:01 PM
The draft snapshot is not yet finalized for the current month.

When you select **View draft snapshot**, the snapshot values load into the CBS in a read-only status.

Live forec... View draft snapshot					
Forecast total cost	Forecast total MHrs	Forecast total MHrs/unit	Forecast total productivity	Forecast total unit cost	Forecast method
\$ 0.00	0.00	0.00	0.00	\$ 0.00	Current estimate
\$ 2,401,829.03	7,030.50	7,030.50	1.15	\$ 2,401,829.03	Rollup
\$ 0.00	0.00	0.00	0.00	\$ 0.00	Manual (EAC)
\$ 0.00	0.00	0.00	0.00	\$ 0.00	Rollup
\$ 0.00	0.00	0.00	0.00	\$ 0.00	Manual (EAC)
\$ 705,957.35	3,821.00	3,821.00	1.38	\$ 705,957.35	Rollup
\$ 203,410.93	3,067.00	3,067.00	1.37	\$ 203,410.93	Rollup
\$ 15,337.63	268.00	268.00	1.45	\$ 15,337.63	Rollup
\$ 2,478.22	46.00	0.02	1.30	\$ 0.99	Average performan...
\$ 2,946.01	49.00	4.45	3.18	\$ 267.82	Manual (EAC)

When you select the **Take Live Snapshot** option consecutively, a message lets you know that an existing snapshot already exists and a choice to override the previous snapshot.

Live forecast

Current live forecast

Forecast total cost

\$ 0.00

\$ 2,401,829.03

Current live forecast

Take Live Snapshot

View draft snapshot

Take Live Snapshot

An existing snapshot for 6/26/2023, 12:23:46 PM already exists. Do you want to override the previous snapshot?

Last Live snapshot taken: 6/26/2023, 12:23:46 PM by Paul (via Manual snapshot)

No Yes

The same snapshot functionality now exists in Pay Items, with the exact same option.

103961 | Ten Mile Slide - Phase 2 (Carrying)

QA-T01-23.8

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

Revenue snapshot: Current revenue forecast

Current revenue forecast

Take revenue snapshot.

Last revenue snapshot: Tue Jun 06 2023 9:47:00 PM.

Snapshot will capture current Revenue values.

UoM

Current billing method

Price lock status

Change order

Original price

Original unit price

May 2023

(T/O) qty

method

14.2.1.3 Default CE values to be updated from CB values

You can select for the Current estimate cost, man-hours, and quantity values to be updated by default from an approved change order that contains adjustments to the Current budget cost, man-hours, and quantity. To set CE values to be updated from CB values, enable the **Default CE values to be updated from CB values** toggle. The check boxes are automatically selected in the change orders.

Whether the **Default CE values to be updated from CB values** toggle is enabled or disabled, you have the option to manually select or deselect to update the values using the check box options under the Update CE total cost, Update CE total MHrs, and Update forecast (T/O) qty in the change order.

Change register		Contract adjustment		Net budget change	Net quantity change	Net man hour change	Markup	Fee	Net contract change	Approval probability
				\$ 0.00	No	0.00	\$ 0.00	\$ 0.00	\$ 0.00	

Assign cost to				Adjusted CB fees	Cost source	Update CE total cost	Update CE total MHrs	Update forecast (T/O) qty	CB allowance total cost	Adj allo
☐	CBS position	Description	WBS phase code			☒	☒	☒		
☒	Pay item 002 - Concrete - Labor & Material	Adjusted current price: \$ 0.00				☒	☒	☒		
☐	3	Concrete	1071		Plug	☒	☒	☒	\$ 0.00	
Subtotals 2					\$ 0.00				\$ 0.00	

14.2.2 Project level

At the project level, you can further define settings for maintaining the CBS structure at a specific level and allowing syncs to replace manual snapshots.

Steel Structure Training Job 3 | 105093 / Settings

PROJECT TRACKING FORECAST ESTIMATE RESOURCES SCHEDULE REVENUE SYNC INTEGRATIONS OTHERS

Cancel Save

Tasks

Maintain CBS Structure at a specific level? ☒ Yes ☐ No

Level to Maintain CBS Structure at

Generate WBS phase code automatically? ☒ Yes ☐ No

WBS Phase code generation method

WBS Phase codes start value

Enable manual snapshots ⓘ ☐

Default CE values to be updated from CB values ⓘ ☐

Allow syncs to replace manual snapshots ⓘ ☐

14.2.2.4 Maintain CBS Structure at a specific level

When set to *Yes*, the *Level to Maintain CBS structure at* field is enabled. You can enter at what level to maintain the CBS structure.

14.2.2.5 Allow syncs to replace manual snapshots

When set to *On*, the *Allow syncs to replace manual snapshots* toggle is enabled. When you enable the *Allow syncs to replace manual snapshots* toggle, the manual snapshot is replaced when the Push Live Forecast or Push Forecast revenue is synced. When the *Allow syncs to replace manual snapshots* setting is disabled, syncs are replaced with manual snapshots.

Tasks

WBS Phase code generation method
 Continue numbering from the last generated number

WBS Phase codes start value
 1000

Enable manual snapshots  

Allow syncs to replace manual snapshots  

If this setting is enabled, a manual snapshot will be replaced when Push Live forecast and/or Push Forecast revenue is synced. If this setting is disabled, syncs will not replace manual snapshots.

14.3 ACTUALS

In the Actuals section of the Project Tracking tab, you can configure actuals settings for your organization and projects. The image and table below give a brief explanation of Actuals settings.

Actuals

1 Calculate percent complete for individual cost items as a percentage of
 Forecast (T/O) qty

3 Calculate percent complete for roll-up items such as superior cost items and account code by:
 Cost

5 Calculate man hours earned at the parent level by 

☒ The summation of man hours earned from direct child items
☐ The total man hours multiplied by percent complete

6 Get actual cost from Contract 

9 Drive committed cost values from Contract 

2 Cap percent complete at 100%
 Yes ☐

4 Roll-up percent complete weighted by
 Current Budget

7 Update % complete from Contract 

8 Calculate percent complete for individual cost items as a percentage of

Current budget total cost

Current budget total cost

Committed total cost

Forecast total cost


Current estimate total cost

Title		Function	Level
1	Calculate percent complete for individual cost items as a percentage of	Calculate percent complete for individual cost items as a percentage of: • Forecast (T/O) Quantity • Current Budget Quantity	Organizational and project
2	Cap percent complete at 100%	Option to select to cap any cost item percent complete at 100%.	Organizational and project
3	Calculate percent complete for roll-up items such as superior cost items and account code by	Controls whether earned cost or hours are used when calculating percent complete for roll up items. The roll up result can differ depending on whether progress is measured by cost or by man hours. • Cost – Roll up percent complete is based on earned cost compared to total cost. • Man hours – Roll up percent complete is	Organizational and project

Title		Function	Level
		based on earned hours compared to total hours. This setting does not change the subordinate item percent complete. It only changes the basis used when rolling those subordinate values up to a superior item or account code. The calculation is: $\text{Roll up \% Complete} = \frac{\text{Earned cost or man hours from Current Budget or Current Estimate}}{\text{Total cost or man hours from Current Budget or Current Estimate}}$	
4	Roll-up percent complete weighted by	Controls whether Current Budget or Current Estimate is used as the weighting basis when combining subordinate items into a roll up percent complete. • Current	Organizational and project

Title		Function	Level
		Budget – Weights each subordinate based on its budgeted size. • Current Estimate – Weights each subordinate based on its estimated final size. Control applies a weighted average, so larger items have a greater influence on the superior result. The calculation is: Roll up % Complete = Earned cost or man hours from Current Budget or Current Estimate ÷ Total cost or man hours from Current Budget or Current Estimate	
5	Calculate man hours earned at the superior level by	Calculate man-hours earned for roll-up items by summing the man-hours earned of the contributing items	Organizational and project

Title		Function	Level
		(regardless of roll-up items percent complete) by: • The summation of man hours earned from direct subordinate items. • The total man hours multiplied by percent complete.	
6	Get actual cost from Contract	When switched to <i>On</i>, the subcontract actual cost is received from Contracts. Actual costs from Contract can consist of a goods receipt, an accrual, or an invoice receipt/payment form. If a goods receipt and an invoice receipt come in at the same time for a record, the higher cost is recognized and not duplicated.	Project level only
7	Update % complete from Contract	When switched to	Project level only

Title		Function	Level
8	Calculate percent complete for individual	On, quantities that are claimed in Contract for SOV items updates the percent complete in Control. You must enable this setting before the contract is created. Updating the percent complete provides you with another way to claim quantities against schedule of value items in Contract. When quantities are claimed against a schedule of values item in Contract and the Get quantities sync is executed in Control, the cost items actuals quantity completed gets updated with a percentage claimed toward the contract's schedule value total cost.	Project level
			

Title		Function	Level
cost items as a percentage of		percent complete for individual cost items as a percentage of: • Current estimate total cost • Committed total cost • Forecast total cost • Current estimate total cost	only
9	Drive committed cost values from Contract	When switched to <i>On</i> , the committed costs are driven from Contracts. When switched to <i>Off</i> , committed costs are derived from the ERP.	Organizational and project

14.4 ESTIMATED ACTUALS

In the Estimated actuals section of the Project Tracking tab, you can configure estimated actuals settings for your organization and projects. Organizational settings are inherited in new projects. You can further define these settings at the project level.

The Estimated actuals settings allows estimated actuals to be accrued to a cost item, then used to contribute to the forecast. This results in the forecast being more accurate. The estimated actuals are calculated based on the cost category values associated to the cost items.

When *Turn on estimate actuals* is switched to *On*, you can choose to turn estimated actuals to *On* or *Off* for Control and InEight Progress cost categories. The Estimated actual quantities from InEight Plan and InEight Progress are also enabled.

When any one of the cost categories are switched to *On*, the Actuals details Claim Actuals tab shows the option when claiming quantity to accrue estimated cost based on the amount claimed.

Estimated actuals

Turn on estimated actuals: ☒

Actual type	Enable estimated actuals for:	
	Control	Progress
Labor cost	☒	☒
Labor man hours	☒	☒
Construction Equipment cost	☒	☒
Construction equipment hours	☒	☒
FOM Rented Equipment cost	☒	
Supplies cost	☒	
Materials cost	☒	
Subcontract cost	☒	
Fees cost	☒	
Allowance cost	☒	
G & A cost	☒	
Undefined cost	☒	

On the CBS, you can access the Claim actuals tab by right clicking the cost item, and then selecting **Actuals details**. In the Actuals details slide-out panel you can select the estimated actuals option.

14.5 TIME-PHASING

Time phasing lets you take for example, your budget, and break it down into more consumable, estimate related time blocks or periods.

14.5.1 Budget

Time-phasing your budget lets you plan expenditures for your project within active fiscal periods, letting you break down budget planning into manageable short-term goals. Enabling time-phasing lets you plan your budget and spread it throughout the length of the project per cost item.

Time phasing

Enable time phasing for the following:

Budget 

 Edit past Time phased budget values 

You can enable time-phasing for budget at the organizational level to set the default for all the projects within that organization. By default, new projects will inherit the organization settings.

14.5.2 Enable time-phasing for budget

To enable time-phasing the budget for your project, you must have start and end dates assigned to cost items. When you switch the *Budget* toggle to *On*, and do not have start and end dates assigned to cost items, a *Cost items are missing start and end dates* dialog box shows.

Cost items are missing start and end dates.

How would you like to populate the missing cost item start and end dates?

☒ **Default all budget to current fiscal period**

☐ Default to project start and end dates

☐ Go back and populate the missing dates

Cancel

Confirm

You can select from the following options:

- **Default all budget to current fiscal period** — The first option you have is to default all of the budget to the current fiscal period. Then, all cost items that don't have defined start and finish dates have the current budget going to the current fiscal period.

For example, if you look at WBS phase code 1007, you would have \$100,000 put into December 2020.

Tasks				Time phased budget				
	CBS position	Description	WBS phase code	CB total cost	Start	Finish	Cost curve	Pending budget cost
☐	1	Electrical devices	1000	\$ 48,790.00	01/01/2020	03/31/2022	Linear	\$ 150.00
☐	1.1	Install conduit	1002	\$ 25,020.00	01/01/2020	07/30/2021	Back Loaded	(\$ 5,060.00)
☐	1.2	Fiber optic cable-1	1001.1	\$ 5,050.00	12/30/2020	12/31/2020	Front Loaded	\$ 4,640.00
☐	1.3	Pull cable	1003	\$ 5,120.00	01/01/2021	05/31/2021	Linear	\$ 540.00
☐	1.4	CCTV devices	1004	\$ 1,600.00	12/01/2020	03/31/2021	Custom curve 1	\$ 10.00
☐	1.5	Terminations	1005	\$ 1,000.00	12/01/2020	05/15/2021	Bell Shaped	\$ 10.00
☐	1.6	Light poles	1006	\$ 11,000.00	12/01/2020	03/31/2022	Custom curve 2	\$ 10.00
☐	2	Indirects	1008	\$ 305,000.00			Linear	\$ 0.00
☐	2.1	Staff	1010	\$ 305,000.00			Linear	\$ 0.00
☐	2.1.1	PM	1007	\$ 100,000.00			Linear	\$ 0.00
☐	2.1.2	PE	1009	\$ 85,000.00			Linear	\$ 0.00
☐	2.1.3	Super	1011	\$ 120,000.00			Linear	\$ 0.00
☐	3	Staff training	1012	\$ 5,500.00			Linear	\$ 0.00
☐	4	Craft training	1013	\$ 17,500.00			Linear	\$ 0.00
☐	5	ST&S	1014	\$ 45,000.00			Linear	\$ 0.00
Subtotals 64				\$ 431,790.00				\$ 150.00

- **Default to project start and end dates** — On the project details page you define all the project start and end dates. After those are defined, then we can default all those missing start and end dates to just the project start and end dates.
- **Go back and populate the missing dates** — You can also return to the Time phased budget step and manually populate the missing dates. If you choose this option, the budget setting turns off

again (if it wasn't already turned off and on again in previous sections). You then have to go into the CBS and manually enter all the start and finish dates. Then, you could turn the budget setting back on and it should distribute the budget.

Currently, time-phased budget data can only be seen in the CBS contract adjustment.

Click **Confirm** after selecting an option and then save your setting.

14.5.3 Edit previous time-phased budget values

You can enable the *Edit past Time phased budget values* toggle to edit past fiscal period time phased budget values.


When this setting is enabled and with the applicable permissions, you can edit your past time phased budget values via a budget move or a contract adjustment in the time phased budget step.

You can also select to edit time phased budget for closed periods. When you want to edit time phased budget for closed periods, enable the **Edit past Time phased budget values** toggle.

For more information, see [Time-phased budget](#).

14.5.4 Switching off time phasing budget

When the Time phasing budget is enabled, it means that there is time phasing budget data in the database. If you disable time-phasing for the budget at the project level, the following warning message shows:

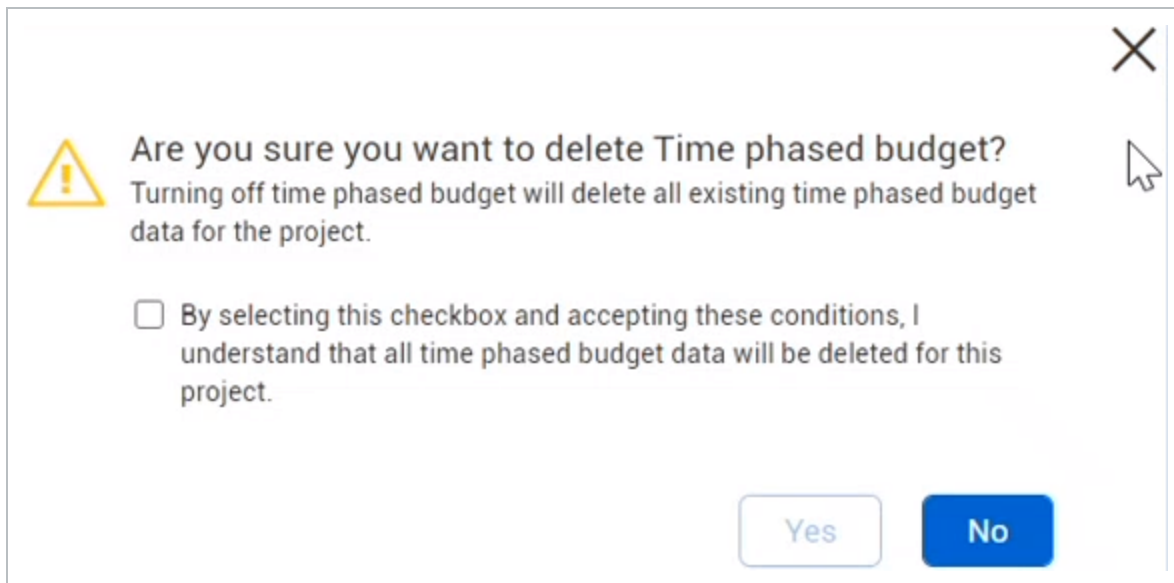

All of your time phased budget data is deleted when you switch time phased budget off. You must acknowledge that the data will be deleted by selecting the check box in the dialog box.

To disable time phasing budget, select **Yes**, and then click **Save**. This will delete the time phasing budget data from the database.


14.6 FORECAST

14.7 TIME-PHASING

Time phasing lets you take for example, forecasting, and break it down into more consumable, estimate related time blocks or periods.

14.7.1 Forecasting


Time-phasing your forecast gives you more visibility into what activities and costs are going to occur in smaller time periods.

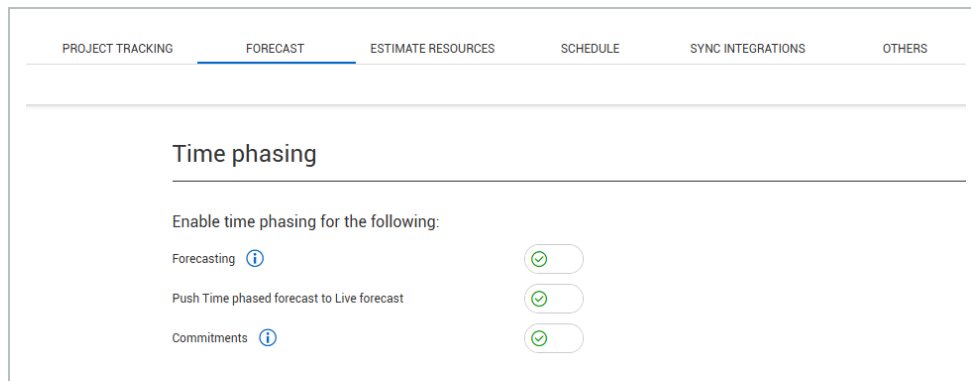

The screenshot shows a web interface with a top navigation bar containing the following tabs: PROJECT TRACKING, FORECAST (which is the active tab), ESTIMATE RESOURCES, SCHEDULE, SYNC INTEGRATIONS, and OTHERS. Below the navigation bar, the 'Time phasing' section is displayed. It includes the heading 'Time phasing' and a sub-heading 'Enable time phasing for the following:'. There are three settings listed, each with a toggle switch that is currently turned on (indicated by a green checkmark): 'Forecasting' (with an information icon), 'Push Time phased forecast to Live forecast', and 'Commitments' (with an information icon).

- **Forecasting** — Set the Forecasting toggle to *On* to enable time-phase forecasting to spread forecast remaining values into the project's fiscal periods.
- **Push Time phased forecast to Live forecast** — Set the Push Time phased forecast to Live forecast toggle to *On* to update the live forecast in the CBS with the modified values in time-phased forecasting.
- **Commitments** — Set the Commitments toggle to *On* to spread committed remaining cost and

uncommitted remaining cost values into the project's fiscal periods.

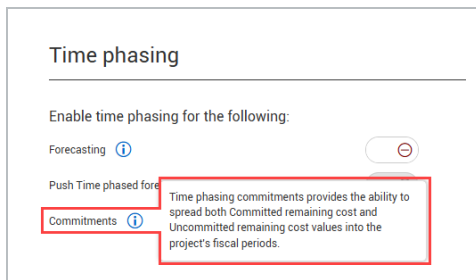

In Project details you can see the start and end dates which define the earliest and latest project periods.

When time-phased forecasting is enabled, the Time phase forecasting option shows in the CBS's Action drop-down list.

For more information, see [Time Phased Forecasting](#).

14.8 FORECAST

In the Forecast section of the Forecast setting, you can configure the percent complete threshold from a straight-line calculation and select to have mandatory notes when using a manual forecast.

14.8.1 Percent complete value at which delta from straight line calculation utilizes average performance

By configuring the value of the % complete value at which delta from straight line calculation utilizes average performance field, you can determine the equation used for the Delta from Straight-Line column depending on if those cost items have their % complete greater than or less than the value set in configurations.

Changing the threshold and impacting the formula is necessary because when a cost item has not been sufficiently completed, the actuals data is not yet reliable enough to predict the final anticipated cost (forecast cost) of that scope of work, so a different equation should be used until that cost item has been sufficiently completed.

For example, if the threshold is 3% complete, and a cost item is less than 3%, then delta from straight line = Forecast total cost - CB total cost. Once the cost item has reached 3% complete, then the calc switches to Forecast total cost - Average performance total cost.

14.8.2 Mandatory notes for manual forecasts

You can set manual forecast notes to be mandatory for Manual (EAC) and Manual (ETC) forecasts when switching to a manual forecast type. This feature helps to keep track of manually entered forecasts. You can use the notes to explain the forecast. For example, you can enter a rationale for why a manual forecast is being used.

Forecast

% complete value at which delta from straight line calculation utilizes average performance

Mandatory notes for Manual forecasts ⓘ

☐

To set notes to be mandatory set the **Mandatory notes for Manual forecasts** toggle to *On*. When manually forecasting, notes are required to be entered in the Forecast notes are required dialog box. Once confirmed, the notes are captured, and the forecast method automatically changes to *Manual*.

CBS
 ACS
 PAY ITEMS
 CHANGE REGISTER

Actions
 +
 ✎
 ✕

Tasks	Description	UoM
☒ 1	Financial Results ...	1.00 PLS
☐ 2	Misc. Rev Internal	1.00 PLS
☐ 2.1	Misc. Rev Internal	1.00 PLS
☐ 2.2	Escalation/Contin...	1.00 Each

Forecast	Created from Live fore...	Forecast total cost	Forecast notes	Latest forecast note	Forecast method
1		\$ 3,048.24	2	Changed forecast total cost to \$3,048.24	Manual (EAC)
		\$ 2,453,29.03			Rollup
		\$ 0.00			
		\$ 52,000.00			

Forecast notes are required
 Please enter a note to update your forecast.

*Notes 500
 Changed forecast total cost to \$3,048.24

Cancel OK

14.9 CUSTOM FORECAST METHOD CALCULATIONS

You can create custom forecast methods at both the organization and project levels. The forecast methods are customized by configuring your own calculations. Custom forecast methods created at the organization level are inherited in new projects and can only be managed at the organization level. Custom forecast methods created at the project level can only be viewed and managed at the project level.

The screenshot shows a web application interface for managing forecast methods. At the top, a dark header bar contains a home icon, the text 'Steel Structure Training Job 3 | 105093 / Settings', and several utility icons (help, notifications, user, share, and a grid). Below the header is a navigation bar with tabs: 'PROJECT TRACKING', 'FORECAST' (which is active and underlined), 'ESTIMATE RESOURCES', 'SCHEDULE', 'REVENUE', and 'SYNC INTEGRATIONS'. To the right of the tabs are 'Cancel' and 'Save' buttons. On the left side of the main content area is a vertical sidebar with a series of icons representing different project management functions. The main content area is titled 'Custom forecast method calculations' and contains the following elements: a blue '+ Add custom forecast method' button; a section titled 'Custom forecast methods' containing three expandable items: 'Northeast Forecast' (with an info icon), 'Canada West Region Forecast' (with an info icon), and 'West' (with edit and delete icons); and a section titled 'Enable Forecast methods based on Allow as-built selections' containing two dropdown menus: 'Non-terminal cost items' and 'Terminal cost items'.

To create a custom Forecast Method, click the **Add custom forecast method** button. Enter the Forecast method name, Forecast total cost and Forecast total Mhrs calculations manually or click the **Formula** icon to choose from the list. You can create a maximum of 10 custom organization and project level forecast methods each at one time.

+ Add custom forecast method

New custom forecast method

1 Define calculations

2 Enable for cost items

* Forecast method name

Midwest Forecast

* Forecast total cost ⓘ

1000-4000+6000+3000+10

* Forecast total MHrs ⓘ

[Actual eqp hrs (to date)]

Cancel

Next

Search...

% complete

Actual cost (to date)

Actual eqp hrs (to date)

Actual labor cost (to date)

Actual labor cost/MHr (to date)

Actual labor unit cost (to date)

Actual MHrs (to date)

Actual MHrs/unit (to date)

Custom forecast methods

Midwest Forecast	
------------------	--

In the CBS you can select your custom forecast method in the Forecast method column of the cost item, which updates the Forecast total cost and Forecast total MHrs based on the forecast method's custom calculations.

Steel Structure Training Job | 105091 / Control / Workspaces

CBSACSPAY ITEMS

Actions

Tasks

☐	CBS position	Description	WBS phase code
☐	1	Job Overhead	1002
☐	2	Earthwork	1069
☐	3	Concrete	1071
☐	4	Structural Steel	1073
☒	4.1	Erect Steel - Heavy	1074
☐	4.2	Erect Steel - Light	1005
☐	4.3	Bolted Connections	1006
☐	5	Materials	1084
☐	5.1	Earthwork - Mater...	1085
☐	5.2	Concrete - Materi...	1086
☐	5.3	Structure Steel - ...	1087
☐	6		1088

Forecast

InEight Control

CB forecast total MHR G/L	Delta from straight line	Forecast notes	Forecast method
0.00	250,000.00		Current estimate
-8,000.00	400,000.00		Current estimate
-30,000.00	1,500,000.00		Current estimate
-4,999.10	1,516,282.48		Rollup
0.00	1,266,327.48		Canada West Region
-4,000.00	200,000.00		
-999.10	49,955.00		
0.00	0.00		
0.00	0.00		
0.00	0.00		
0.00	0.00		
0.00	0.00		

14.9.1 Enable Forecast methods based on Allow as-built selections

You can select which forecast methods can be used based on the allow as- built settings, for both terminal and non-terminal cost items.

There are multiple forecasts that allow as-built options to choose from to help you configure your forecasted cost items, in addition to the existing available Control forecasting methods. When an option is disabled, that method is not available to select for cost items with the allow as-built selected.

Enable Forecast methods based on Allow as-built selections

Non-terminal cost items

When Allow as-built is set to *All or Cost*
Enable the following Forecast methods for non-terminal cost items when Allow as-built is set to *All or Cost*

Current estimate	☒	Manual (ETC)	☒
Current budget	☒	Manual (EAC)	☒
Average performance	☒	None	☒
Committed cost	☒	Contract	☒

Default Forecast method for non-terminal cost items when Allow as-built is set to *All or Cost*

Current estimate

Only enabled selections above are eligible. 'Manual (ETC)' and 'Manual (EAC)' cannot be default options.

When Allow as-built is set to *Quantity*
Enable the following Forecast methods for non-terminal cost items when Allow as-built is set to *Quantity*

Current estimate	☒	Manual (ETC)	☒
Current budget	☒	Manual (EAC)	☒
Average performance	☒	None	☒

Default Forecast method for non-terminal cost items when Allow as-built is set to *Quantity*

Current estimate

Only enabled selections above are eligible. 'Manual (ETC)' and 'Manual (EAC)' cannot be default options.

When Allow as-built is set to *None*
Enable the following Forecast methods for non-terminal cost items when Allow as-built is set to *None*

Rollup	☒	None	☒
Manual (ETC)	☒	Manual (EAC)	☒

Default Forecast method for non-terminal cost items when Allow as-built is set to *None*

Rollup

Only 'Rollup' may be the default option.

Terminal cost items

When Allow as-built is set to *All or Cost*
Enable the following Forecast methods for terminal cost items when Allow as-built is set to *All or Cost*

Current estimate	☒	Manual (ETC)	☒
Current budget	☒	Manual (EAC)	☒
Average performance	☒	None	☒
Committed cost	☒	Contract	☒
Detailed ETC	☒		☒

Default Forecast method for terminal cost items when Allow as-built is set to *All or Cost*

Current estimate

Only enabled selections above are eligible. 'Manual (ETC)' and 'Manual (EAC)' cannot be default options.

When Allow as-built is set to *Quantity*
Enable the following Forecast methods for terminal cost items when Allow as-built is set to *Quantity*

Current estimate	☒	Manual (ETC)	☒
Current budget	☒	Manual (EAC)	☒
Average performance	☒	None	☒

Default Forecast method for terminal cost items when Allow as-built is set to *Quantity*

Current estimate

Only enabled selections above are eligible. 'Manual (ETC)' and 'Manual (EAC)' cannot be default options.

When Allow as-built is set to *None*
Enable the following Forecast methods for terminal cost items when Allow as-built is set to *None*

None	☒		
------	-------------------------------------	--	--

Default Forecast method for terminal cost items when Allow as-built is set to *None*

None

14.10 ESTIMATE RESOURCES

14.11 ESTIMATE RESOURCES

In Estimate resources you can configure three scale percentages for wage rate composition.

14.11.1 Wage rate composition

The Wage rate composition section lets you determine what default percentage each labor hour will be calculated at the scale 1, scale 2, or scale 3 rate.

Wage rate composition

Scale 1

80

Scale 2

10

Scale 3

10

14.12 SCHEDULE

14.13 SCHEDULE

In the Schedule settings tab, you can configure the following schedule settings:

- Define project schedule
- Cost curves
- Plug Day Calculation

- Schedule ID

Steel Structure Training Job 3 | 105093 / Settings

PROJECT TRACKINGFORECASTESTIMATE RESOURCES**SCHEDULE**REVENUESYNC INTEGRATIONS

CancelSave

Define project schedule

Schedule data source:

Duplicate field values for Baseline and Current schedule columns:

- ☒ Schedule ID and Baseline schedule ID
- ☒ Scheduled and Baseline Scheduled
- ☐ Schedule WBS and Baseline schedule WBS
- ☐ Roll up schedule and Baseline roll up schedule

Cost curves

Customize cost curve tables

Description	Data points
☐ Back Loaded	2
☐ Linear	20
☐ Employed Cost Item	
☒ Front Loaded	2
☐ Bell Shaped	21
☐ Back Loaded	2
☐ Linear	20
☐ Employed Cost Item	
☐ Front Loaded	2
☐ Bell Shaped	21

Plug Day Calculation

Plug days default rollup calculation

Longest child

Schedule ID

Schedule ID settings will only affect newly created cost items

Schedule ID prefix

0

Example schedule ID: PS.00000001

Schedule ID start value

0

Example schedule ID: PS.00000001

Define the delineator


Example schedule ID: PS.00000001

14.14 DEFINE PROJECT SCHEDULE

You can define the project schedule by selecting the following options:


- Schedule data source (Project level only)** – You can select which data source to use for your schedule. Click the drop-down list to select to use Manual entry or an XER file type.
- Duplicate field values for Baseline and Current schedule columns** – Select from the list to duplicate values for schedule columns. Values selected at the organization level are inherited in

new projects and cannot be changed. At the project level, you can further refine your selections.

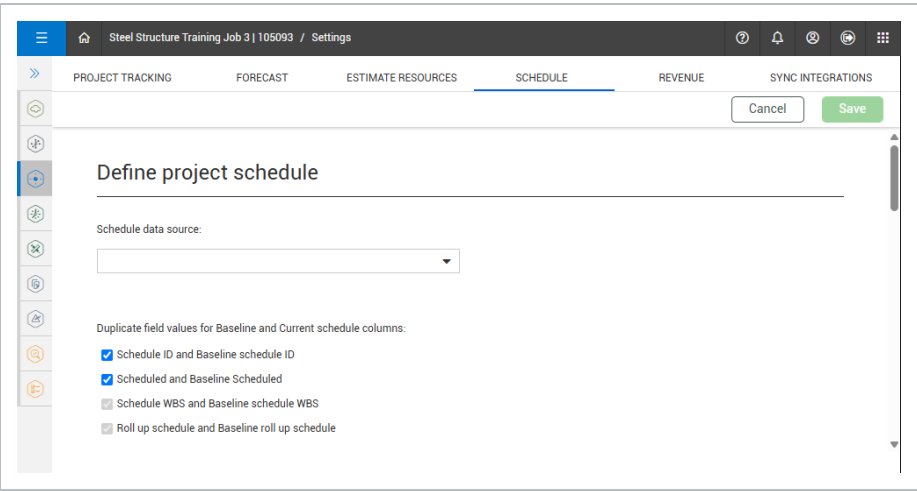

14.15 COST CURVES

Cost curves determine the proportion of money to be expended in a certain period. You can create custom cost curve tables to apply to your progressed work, based on actual costs and schedule. The default cost curve assigned to a cost item is *Linear*.

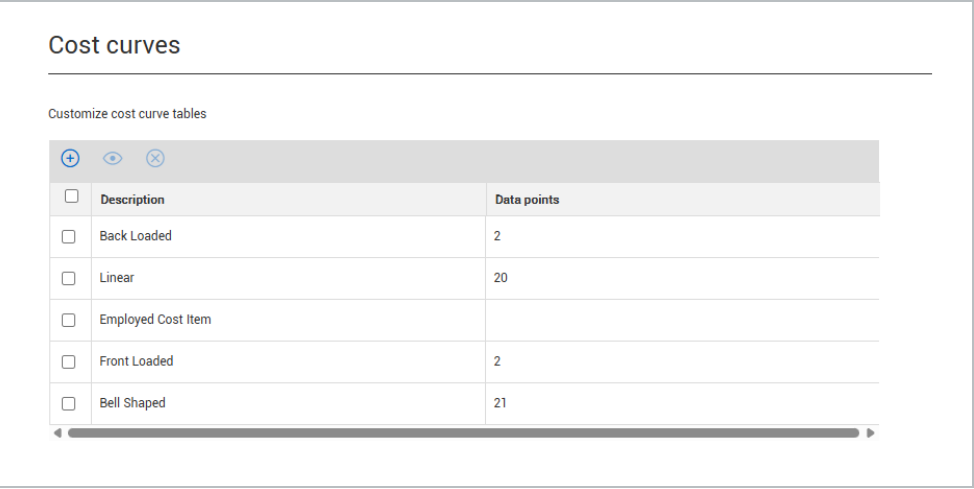

You can update the cost curve in the following ways:

- Cost curve column of the Schedule data block.
- When performing a contract adjustment. The budget time phasing option must be enabled in settings.

When the budget is locked, it sets the current budget and original budget equal to the current estimate. The cost curve can only be changed using a change order.

14.15.1 Manage cost curve tables

Add a custom cost curve table

- 1. Click the **Add** icon, and then enter the following:
 - Description of cost curve (required)
 - Number of data points (required)
 - Value percentages which must equal to 100%

Description

Linear - JS

Number of points

20

From duration %	To duration %	Value %
0.00%	5.00%	10.00%
5.00%	10.00%	20.00%
10.00%	15.00%	20.00%
15.00%	20.00%	5.00%
20.00%	25.00%	5.00%
Total		100.00%

Cancel

OK

- 2. Click **OK** to save.

View a cost curve table

Select a cost curve table, and then click the **View** icon. In view mode, you can only edit a cost curve table that is not yet assigned to any cost items.


Delete a cost curve table

To delete a cost curve table, select a cost curve table, and then click the **Delete** icon. You can only delete cost curve tables not yet assigned to cost items.

14.16 PLUG DAY CALCULATION

You can select from the following options to set as default for calculating plug days when rolling up cost items for scheduling purposes.

- Longest child
- Sum of all children

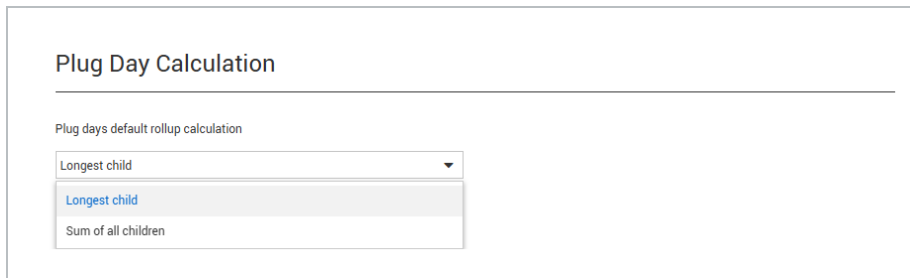

The screenshot shows a web interface titled "Plug Day Calculation". Below the title is a horizontal line. Underneath, the text "Plug days default rollup calculation" is followed by a dropdown menu. The dropdown menu is open, showing three options: "Longest child" (which is highlighted in blue), "Longest child" (in grey), and "Sum of all children" (in grey).

14.17 SCHEDULE ID

You can define new cost items schedule ID options. The settings you define determine your ID structure.

When integrating with InEight Schedule, Schedule IDs in Control must correspond to Activity IDs in InEight Schedule.

When integrating with Primavera, Schedule IDs in Control are used to map Primavera Activity IDs to import and export project information. The status of construction activities and progress are then integrated back into the InEight scheduling tools.

When using a XER type file to import a schedule, the *Schedule ID* in Control must match the *Activity ID* in the XER file.

Schedule ID

Schedule ID settings will only affect newly created cost items

Schedule ID prefix

0

Example schedule ID: PS.0000001

Schedule ID start value

0

Example schedule ID: PS.0000001

Define the delineator

Example schedule ID: PS.0000001

You can define the following:

- Schedule ID prefix
- Schedule ID start value
- Define the delineator

14.18 REVENUE

14.19 REVENUE

Revenue settings are available at the project level only. You can define and configure setting for the following:

- Revenue and Cost Timing
- Billing method default earnings rules
- Pay item to cost item forecast (T/O) quantity relationship
- Markup

14.20 REVENUE AND COST TIMING

In the Revenue and Cost Timing table, you can define a default retainage percentage and set the reoccurrence payment period at the cost category level for the following:

- Retention percentage
- Tax percentage
- Payment timing - The Payment timing provides the following options:
 - Same period
 - Next period
 - End of project
 - Set custom reoccurrence – When selected, the Next months column activates to set a customized reoccurrence.
 - Subcontract Retention released
 - Client Retention released

The default retainage percentage is held back from each bill on the pay items. Pay item retainage creates an incentive for contractors to complete contracted work on a project. Typically, contractors do not get paid the total amount of money until all work or a set milestone is completed. With pay item retention, an agreed upon retainage percentage is held back by the owner for each bill by the client until the owner agrees to release the retention.

You can set the average calendar days elapsed from the billing collection, in addition to setting the end of project date to any of the following options in the End of project date drop-down list.

- Project end date
- Forecast completion date
- Contract completion date
- Certificate of substantial completion (expected)
- Certificate of substantial completion (expected)

Revenue and Cost Timing

Category	Retention	Tax	Payment timing	Next __ months
Labor cost	0.00 %	0.00 %	Same period	
Construction Equipment cost	0.00 %	0.00 %	Same period	
FOM Rented Equipment cost	0.00 %	0.00 %	Same period	
Supplies cost	0.00 %	0.00 %	Same period	
Materials cost	0.00 %	0.00 %	Same period	
Subcontract cost	0.00 %	0.00 %	Same period	
Fees cost	0.00 %	0.00 %	Same period	
G & A cost	0.00 %	0.00 %	Same period	
Allowance cost	0.00 %	0.00 %	Same period	
Undefined cost	0.00 %	0.00 %	Same period	
Billing	0.00 %	0.00 %	Same period	


	Payment timing	Next __ months
Subcontract Retention released	Same period	
Client Retention released	Same period	

Average calendar days elapsed from billing to collection:

End of project date:

Enforce change order price values to match between Control and Change ☒

When changing the Default Billing retainage percent, a dialog box shows where you can choose to either update all existing items on a project, update matching existing pay items, or only apply to pay items created in the future.

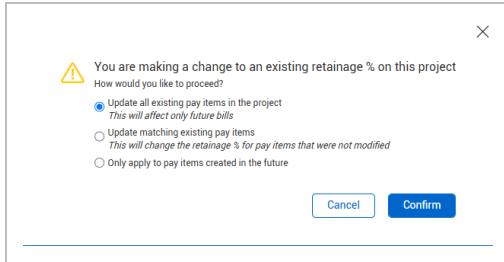

14.20.1 InEight Change integration

When integrated with Change and approving contract adjustments from Change to Control, you enable the *Enforce change order price values to match between Control and Change* toggle to allow change order pay item values to match or not match the amount received from Change. This is ideal when pay items are being used in a contract adjustment.

When the *Enforce change order price values to match between Control and Change* toggle is switched *OFF*, pay item amounts are not required to equal the amounts from Change to approve contract adjustments from Change.


When switched *ON*, Net contract changes for pay items must equal current price from the received change order.

14.21 BILLING METHOD DEFAULT EARNINGS RULES

You can manage the default cost item earnings amounts based on either Forecast (T/O) quantity or CE total cost for the following billing methods.

- Fixed final price
- Unit price

- Cost Plus

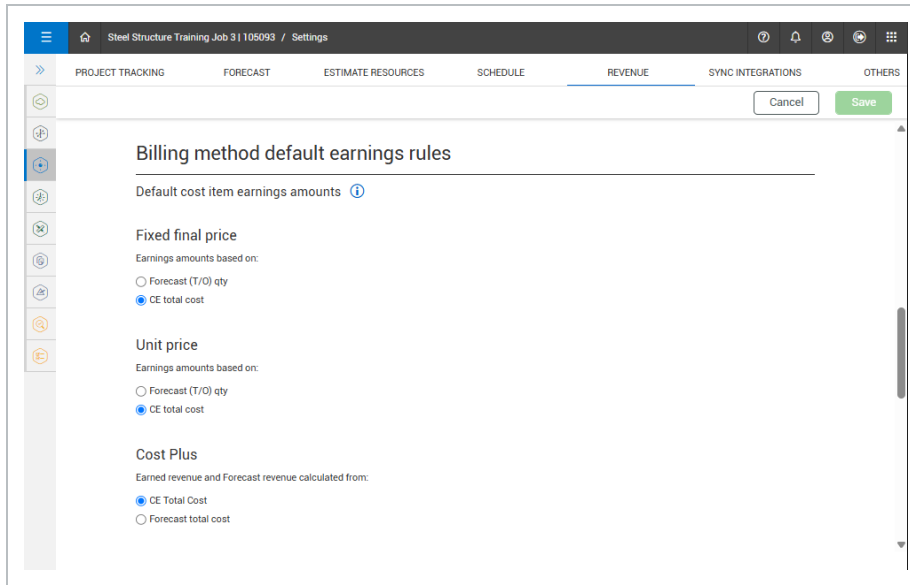

The default earnings are calculated using the forecast takeoff quantity of the cost item and comparing it to the total forecast takeoff quantities of all the cost items assigned to that pay item to generate the percentage.

14.21.1 Fixed final price and Unit price

Fixed final price and Unit price lets you select a default way to calculate those earnings amounts based on takeoff forecast quantity or CE final cost. After the settings are saved, all your fixed final price pay items that normally calculate based on CE final cost and unit price then calculate forecast takeoff quantity or any of the other options you select. You can still modify this selection at the pay item level.

14.21.2 Cost plus

Cost plus pay items can have revenue calculated based on the assigned cost items' CE total cost or Forecast total cost.

14.22 PAY ITEM TO COST ITEM FORECAST (T/O) QTY RELATIONSHIP

You can manage settings for pay the item to cost item forecast (T/O) quantity relationships using the Enable pay item Forecast (T/O) qty rollups and Enable pay item Forecast (T/O) qty roll down toggles.

14.22.1 Enable pay item Forecast (T/O) quantity rollups

The *Enable pay item Forecast (T/O) qty rollups* toggle is only applicable to unit price pay items. It lets you enable the pay item forecast take-off quantity to be calculated based on the sum of all the assigned cost items forecast takeoff quantities.

When the *Enable pay item Forecast (T/O) qty rollups* toggle is enabled, you can no longer edit your pay item forecast takeoff quantity in the Pay item register.

For example, you cannot add unlike units of measure. Only cost items that have the same unit of measure as the pay item can contribute to that pay item's forecast takeoff quantity.

In the following image, the two cost items have different units of measure.

Pay item number	Description	Total price	Unit price	Fore... T/O Qty	U...
☒ Pay item - de...	Demo	\$ 2,700.00	\$ 100.00	150.00	BOX
☐ Pay item - de...	Demo 2	\$ 5,000.00	\$ 5,000.00	0.00	PLS

CBS Position	Description	Forecast (T/O) qty	UoM	CE final cost
41	Cost item 1	150.00	BOX	\$1,500.00
42	Cost item 2	100.00	Bag	\$200.00
				\$ 1,700.00

Cost item 1 has a unit of measure of box, which also has the pay item contribute quantity box checked. Cost item 2 has a unit of measure of bag with the pay item contribute quantity box unchecked. When you go into the update earning rules editor, you cannot check the pay item contribute quantity box for cost item 2 because the unit of measure does not match with cost item 1.

Pay item ID

Pay item - demo

Description

Demo

Total Price

\$2,700.00

Calculate earning amounts by:

☒ Forecast (T/O) quantity

☐ CE final cost

CBS Position	Descript...	Pay item contrib... quantity	Earning %	Earning Amount (Forecast)	Earnings Timing	WBS Phas
41	Cost item 1	☒	100.00 %	\$ 15,000.00	Percent complete	1
42	Cost item 2	☐	0.00 %	\$ 0.00	Percent complete	2
			100.00 %	\$15,000.00		

☒ Default Earning Rules

Cancel

Save

If you deselect the pay item contribute quantity box for cost item 1, the cost item’s quantity does not contribute to the pay item’s quantity. Then, the pay item quantity is zero. If it is checked, cost item 1 with the unit of measure of box has a forecast takeoff quantity of 150. This means the pay item also has a forecast takeoff quantity of 150.

In the CBS, you can change the Unit of Measure from bag to box and then forecast take off quantity updates.

By default, they both now have the pay item contribute quantity checked and the pay item forecast take off quantity is the sum of any cost items that have pay item contribute quantity checked.

CBS

ACS

PAY ITEMS

CHANGE REG

Actions

+

Tasks

	CBS position	Description	WBS phase code
☐	41	Cost item 1	01
☒	42	Cost item 2	02
☐	43	Cost item 3	03
☐	44	Cost item 4	04


Task details

Resource	Forecast (T/O) quantity	UoM
	150.00	BOX
	100.00	Bag
	100.00	PLS
	1.00	PLS

For example, with cost item 2 updated, the forecast takeoff quantity from of 100 is added to the forecast takeoff quantity of cost item 1. The total forecast takeoff quantity is now 250. It includes both of them since they now both have a matching unit of measure.

Also, this affects your earnings percent as well if you have forecast takeoff quantity selected. The pay item contribute quantity for both cost items drives your earnings percent if the forecast takeoff quantity radio button is selected. It also decides which cost items are going to contribute to the pay item's forecast takeoff quantity.

When you turn to *ON* Enable pay item Forecast (T/O) qty rollups, the *Pay item contribute quantity* column does not show by default. To add it, go into the columns chooser, and then select that column. After it is added to your view, it remains there until you deselect it from the columns chooser.

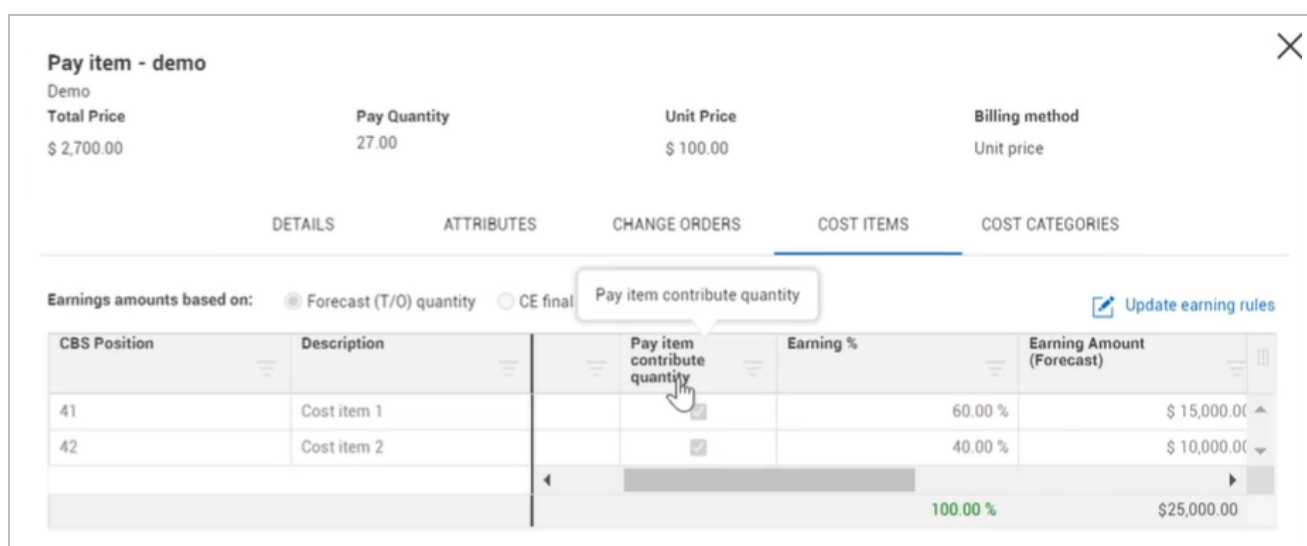

Pay item - demo

Demo

Total Price	Pay Quantity	Unit Price	Billing method
\$ 2,700.00	27.00	\$ 100.00	Unit price

DETAILS ATTRIBUTES CHANGE ORDERS **COST ITEMS** COST CATEGORIES

Earnings amounts based on: ☒ Forecast (T/O) quantity ☐ CE final Pay item contribute quantity [Update earning rules](#)

CBS Position	Description	Pay item contribute quantity	Earning %	Earning Amount (Forecast)
41	Cost item 1	☒	60.00 %	\$ 15,000.00
42	Cost item 2	☒	40.00 %	\$ 10,000.00
			100.00 %	\$25,000.00

In the *Update earnings rule* dialog box, the Pay item contribute quantity column is a default editable column in that view. The Pay item contribute quantity column is not editable in the main table. You can only select to add it to your main table view in the pay item slide-out panel for informational purposes.

The Pay item contribute quantity column is not available when the setting is turned to *OFF* or if you are not looking at a unit price pay item. If a user turns the setting to *ON* and added the column, and then decided to turn the setting to *OFF*, the columns no longer show.

14.22.2 Enable pay item Forecast (T/O) quantity roll down

When the amount of contract deliverables changes on unit price contracts, manually updating all the quantities for every associated cost item can be time consuming. Pay item forecast take off quantity allocations can be proportionally rolled down to the assigned cost items by setting the Enable pay item Forecast (T/O) qty roll down switch to On.

The unit price pay item Forecast (T/O) quantities proportionally rolls down to the contributing cost items' Forecast (T/O) quantities. Pay item to cost item roll down changes also show in the CBS Audit log.

CBS

ACS

PAY ITEMS

Actions

+ ×

Move to

Drag a column header and drop it here to group

	Pay item position	Pay item number	Description	Current unit price	Current pay qty	Current forecast (T/O) qty	UoM	Current billing method
☐	3	BP	Office	\$ 124,730.58	1.000	8.000	PLS	Cost plus

Carrying Job | ... / Control / Workspaces

CBS

Actions

+ ×

Tasks

	CBS position	Description
☐	2.1.1.1	Site ...
☐	2.1.1.1.1	Site ...
☐	2.1.1.1.2	Temp...

Task details

Resources	Forecast (T/O) qty
	1.000
6	75,181.000
9	8.000

The *Allow as-built* setting must be set to *All* or *Quantity* for the selected cost items.

14.23 MARKUP

On the Revenue tab, you can configure a default markup percentage that applies the markup to the entire project. The Markup percent table adds a markup per cost category and per resource type on all cost categories in resources in the project.

Markup

Default markup percent

14.00 %

Cost categories	Markup percent
Labor	14.00 %
Construction Equipment	14.00 %
FOM Rented Equipment	14.00 %
Supplies	14.00 %
Materials	14.00 %
Subcontract	14.00 %
Fees	14.00 %
Allowance	14.00 %
G & A	14.00 %
Undefined	14.00 %

Current estimate resources	Markup percent
Labor	14.00 %
Construction equipment	14.00 %
Rented construction equipment	14.00 %
Installed material	14.00 %
Installed equipment	14.00 %
Supplies	14.00 %

Unique resources will apply markup percent by cost category

For example, if you added 10% to Labor resources, then any labor resources automatically have a 10% markup added to it, and that affects the resources charge rate. Then that charge rate affects the amount of revenue that cost items can bill for and earn.

After you set labor at 10% and click **Save**, you can select from the following options to confirm your change:

Option	Description
Update all existing cost categories and resources in the project	This option adds 10% resource markup percent for all labor resources.
Update matching existing cost categories and resources	This option changes the current charge rates only for resources that were not manually modified. Anything that has not been modified such as a labor resource, this option overrides it with 10%.

Option	Description
Only apply to cost items and resources created in the future	This option makes no changes to existing resources. Any newly created resources, labor resources in this example, have a 10% markup added to them.maps

Cost categories are applicable in plug cost items that do not have resources or are not resource driven. The cost categories have only a blanket cost category markup that helps drive the total revenue amount on the cost item.

You can view this information from Markup columns such as Billing rate markup amount, CE billable amount, Markup amount, and CE revenue amount.

The screenshot shows the 'Cost categories' tab in the software. The table below represents the data visible in the 'Forecast remaining cost' and 'Billing rate markup amount' columns, which are highlighted in the red box in the image.

Cost category	Current budget	Actual cost (to date)	Current estimate	Forecast remaining cost	Billing rate markup amount
Total		\$ 0.00	\$ 250,000.00	\$ 250,000.00	
Labor		\$ 0.00	\$ 250,000.00	\$ 250,000.00	
Construction...		\$ 0.00	\$ 0.00		
FOM Rented ...		\$ 0.00	\$ 0.00		
Supplies		\$ 0.00	\$ 0.00		

The following table shows markup column information in the Cost categories tab of the Cost item details slide out.

Column	Formula
CE billable amount	Current estimate amount + your Billing rate markup amount = CE billable amount
Markup amount	Markup percent x your current estimate = markup amount - The Billing rate markup amount for plug cost items is always set to zero because you can only have a billing rate on resources. When this is a detailed cost item, this will shows your billing rate markup amount for all those resources.

Column	Formula
CE revenue amount	CE billable amount + your Markup amount = CE revenue amount - The CE revenue amount is how much revenue a cost item can have. This is only applicable for cost plus pay items. You can apply markups on cost items, and they do not affect the revenue on those cost items. The markups affect the revenue for cost plus pay items and any cost items that are assigned to cost plus pay items.

For more information, see [Markup percent](#).

14.24 SYNC INTEGRATIONS

14.25 SYNC INTEGRATIONS

You can configure sync integrations for actual cost and man-hour options at the organizational level, and manage sync schedules at the project level.

14.25.1 Organizational level

14.25.1.1 Actual cost and man-hour sync options

You have the option to choose to receive just one payload request instead of multiple ones for when the following occurs:

- If there are multiple fiscal periods since the last successful actual cost and man-hour sync.
- If the sync has never been ran and the project start date is longer than one fiscal month.


To opt to receive one request, set the **Send one request** toggle to *ON*.

The screenshot shows the 'Actual Cost and Mhr Sync Options' configuration page. At the top, there is a navigation bar with tabs: PROJECT TRACKING, FORECAST, ESTIMATE RESOURCES, SCHEDULE, SYNC INTEGRATIONS (selected), and OTHERS. Below the tabs, there are 'Cancel' and 'Save' buttons. The main section is titled 'Actual Cost and Mhr Sync Options'. It features a toggle switch labeled 'Send one request' with an information icon (i) to its right. A tooltip box is visible, stating: 'When the actuals cost and mhr sync has not been ran successfully for multiple fiscal periods send one request instead of multiple'. The toggle switch is currently in the 'OFF' position.

14.25.2 Project level

14.25.2.2 Sync integrations schedule

You can schedule sync integrations to run at specific times. Sync types include pushing the CBS structure, pay items, billed revenue, budget, live forecast, forecast revenue and getting quantities, actual cost, and man-hours. For more information about push and get actions, see [Push and Get actions](#) in InEight Control Interfaces.

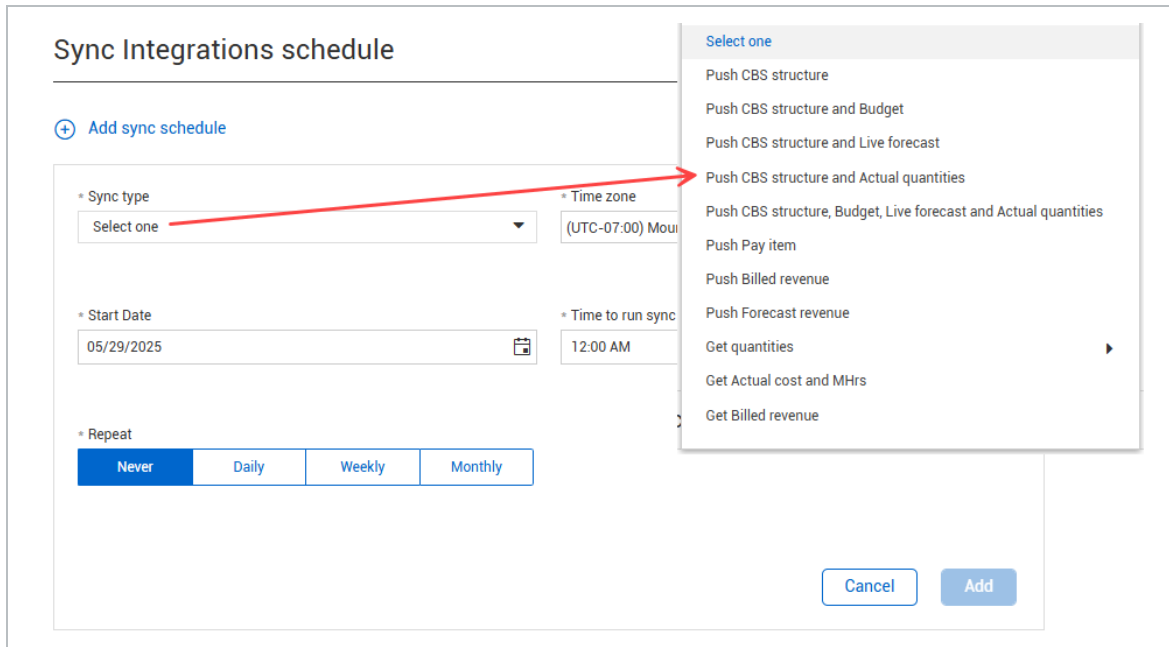


The screenshot shows the 'Sync Integrations schedule' form. It includes a '+ Add sync schedule' button, a 'Sync type' dropdown menu (currently showing 'Select one'), a 'Time zone' field (showing '(UTC-07:00) Mountain'), a 'Start Date' field (showing '05/29/2025'), a 'Time to run sync' field (showing '12:00 AM'), and a 'Repeat' section with buttons for 'Never', 'Daily', 'Weekly', and 'Monthly'. A red arrow points from the 'Sync type' dropdown to a list of options: 'Push CBS structure', 'Push CBS structure and Budget', 'Push CBS structure and Live forecast', 'Push CBS structure and Actual quantities', 'Push CBS structure, Budget, Live forecast and Actual quantities', 'Push Pay item', 'Push Billed revenue', 'Push Forecast revenue', 'Get quantities', 'Get Actual cost and MHRs', and 'Get Billed revenue'. The 'Add' button is highlighted in blue.

When adding a sync schedule, you can define the following:

- Sync type
- Time zone
- Start Date
- Time to run sync
- Repeat (Never/Daily/Weekly/Monthly)

The scheduled syncs show at the under the Scheduled syncs section. You can edit or delete scheduled syncs.

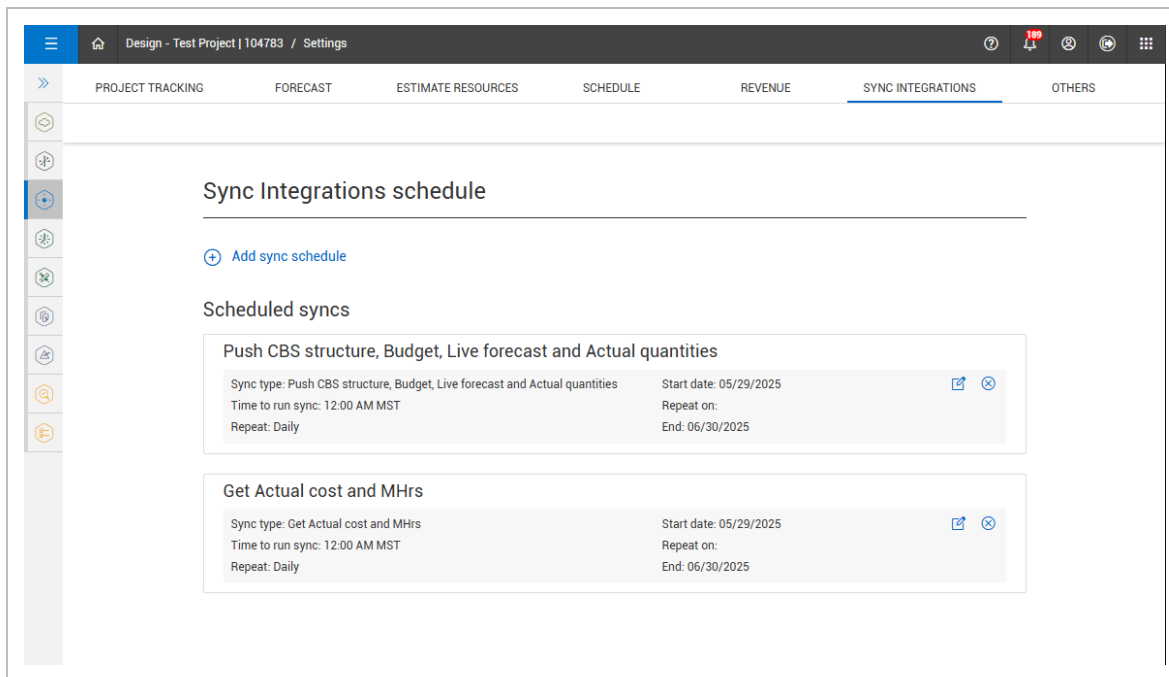

For more information about scheduled syncs , see [Scheduled syncs](#) in InEight Control Interfaces.

14.25.3 Considerations

- To use the sync features in Control, you must first select **Control with confirmation** in Global Options. For more information, see [Cost item integration behavior](#).
- To schedule syncs, you must first configure them for your organization in Application integrations. You can open Application integrations in Main menu > Suite administration > **Application integrations**.

14.26 OTHERS

14.27 OTHERS

The Others tab contains other Control related items you can define and configure at the organizational and project level.

14.27.1 Organizational level

The following items are Control related settings you can define and configure at the organizational level:

- Required cost items
- Change order details

14.27.1.1 Required cost items

The Required cost items feature lets you create standardized or most commonly used cost items at the organization level and then add them to the project structure in the CBS register.

Required cost items ?

Prevent project from syncing if required cost items are not added ⊖

⊕
✎
✕

☐	Description	WBS phase code	UoM	Account code	Allow as-built
☐	RC1	44446666	Acre	99.99	Quantities
☐	RC2	44445555	Cubic Meter		Quantities
☐	RC3	44447777	Barrel	00.03.01.010	Quantities

You can turn to *ON* the *Prevent project from syncing if required cost items are not added* toggle to prevent the project from syncing if required cost items are not added.

In the cost item grid, you can add, edit, and delete required cost items.

14.27.1.2 Change order details

Change Order fields can be configured as validated drop-down list fields at the organization level.

When you set the toggle to *ON*, the discipline list is populated from Master Data Libraries in InEight Platform, and the issue number and CCO fields are populated from inEight Change. When the toggle is set to *OFF*, these fields are free editable text fields with no validations.

In the example below, six validated issues have been selected to be associated with this change order after it is submitted.

The screenshot displays the 'OTHERS' tab in the InEight interface. The 'Required cost items' section shows a table with the following data:

Description	WBS phase code	UoM	Account code	Allow as-built
RCL1	888888	Bag		All
RCL2	88900	cm2		All
RequiredTest1233434	9834343	Acre	00.03.01.004.5thr...	None
ROCI_1	56789	Barrel		All
ROCI_12	7788990	Bag	00.03.01.004	None

Below the table, the 'Change order details' section features a toggle labeled 'Make fields validated dropdowns' which is currently turned ON. A red arrow points from this toggle to the 'Associated Issues' dialog box.

The 'Associated Issues' dialog box shows a list of issues with the following details:

Issue ID	Issue name
11	test issue
10	issue - demo
9	Asbestos removal
8	Extra camera request
7	Frayed cable
5	Schedule delay
4	Cracked concrete
3	Broken valve
2	Scope increase
1	Feed motor on drill malfunction, procure M...

At the bottom of the dialog, the 'Associated' tab is selected, showing a list of associated issues: 11 - test issue, 10 - issue - demo, 9 - Asbestos remo..., 8 - Extra camera re..., and 7 - Frayed cable. Below this, the 'Discipline' field is empty, and there are three 'Change management tag' and 'Change management user defined' fields.


14.27.2 Project level

The following items are Control related settings you can define and configure at the project level:

- Required cost items
- Decimal precision

14.27.2.3 Required cost items

You can prevent the project from syncing when required cost items are not included by setting the *Prevent project from syncing if required cost items are not added* toggle to *ON*.



Required cost items

Prevent project from syncing if required cost items are not added ☒

14.27.2.4 Decimal precision

The image and table below summarize the different decimal precision options:

Decimal precision

1

Currency - How many digits should be displayed after the decimal? (standard rounding applied)

4

2

Cost Summary - How many digits should be displayed after the decimal? (standard rounding applied)

4

3

Unit Cost - How many digits should be displayed after the decimal? (standard rounding applied)

2

4

Quantities - How many digits should be displayed after the decimal? (standard rounding applied)

2

5

Percentages - How many digits should be displayed after the decimal? (standard rounding applied)

4

CBS

ACS

PAY ITEMS

CHANGE REGISTER

AUDIT LOG

Tasks

CBS position

Description

WBS phase code

1

Job Overhead

1002

2

Earthwork

1069

3

Concrete

1071

4

Structural Steel

1073

4.1

Erect Steel - Heavy

1074

4.2

Erect Steel - Light

1005

4.3

Bolted Connections

1006

4.4

Labor

1088

4.5

Equipment

1089

4.6

3rd Party

1090

5

Materials

1084

5.1

Earthwork - Mater...

1085

5.2

Concrete - Mater...

1086

5.3

Structure Steel - ...

1087

Forecast

Created from Live fore...

Forecast total cost

Forecast total labor

Forecast total M/hr/unit

Forecast total productivity

Forecast total unit cost

Forecast remaining cost

\$ 250,000.0000

0.00

0.00

0.0000

\$ 250,000.00

\$ 250,000.0000

\$ 400,000.0000

8,000.00

0.80

1.0000

\$ 40.00

\$ 400,000.0000

\$ 0.0000

30,000.00

3.00

1.0000

\$ 0.00

\$ 0.0000

\$ 1,050,000.0000

21,000.00

21,000.00

1.9523

\$ 1,050,000.00

\$ 1,050,000.0000

\$ 800,000.0000

16,000.00

16,000.00

1.0000

\$ 800,000.00

\$ 800,000.0000

\$ 200,000.0000

4,000.00

4,000.00

1.0000

\$ 200,000.00

\$ 200,000.0000

\$ 50,000.0000

1,000.00

1,000.00

1.0000

\$ 50,000.00

\$ 50,000.0000

\$ 0.0000

0.00

0.00

0.0000

\$ 0.00

\$ 0.0000

\$ 0.0000

0.00

0.00

0.0000

\$ 0.00

\$ 0.0000

\$ 0.0000

0.00

0.00

0.0000

\$ 0.00

\$ 0.0000

\$ 1,750,000.0000

0.00

0.00

0.0000

\$ 1,750,000.00

\$ 1,750,000.0000

\$ 250,000.0000

0.00

0.00

0.0000

\$ 25.00

\$ 250,000.0000

\$ 1,000,000.0000

0.00

0.00

0.0000

\$ 100.00

\$ 1,000,000.0000

\$ 500,000.0000

0.00

0.00

0.0000

\$ 500.00

\$ 500,000.0000

Subtotals 14

\$ 3,450,000.0000

58,000.00

\$ 3,450,000.0000

	Name	Function
1	Currency	Number of decimal places for currencies. Any field that includes currency data will be affected by this setting.
2	Cost Summary	Number of decimal places for total cost information both at the terminal and non-terminal level.
3	Unit Cost	Number of decimal places for any unit cost displayed.
4	Quantities	Number of decimal places for any quantities displayed.
5	Percentages	Percent complete calculations at both the terminal and non-terminal level.

14.28 FREQUENTLY ASKED QUESTIONS

Why is the actual quantity not rolling up to the parent cost item?

Actual qty (to date) is calculated at the parent level rather than a roll up value of *Actual qty (to date)* on the children. There is a section in Control Project Settings > Project Tracking > **Actuals** which determines how this is calculated. These settings are *Calculate percent complete for roll-up*

InEight Inc. | Release 26.7

Page 627 of 639

items such as superior cost items and account code by: and Roll-up percent complete weighted by:.

For example, if the project has the following options in the Actuals settings:

- *Calculate percent complete for roll-up items such as superior cost items and account code by: **Cost***
- *Roll-up percent complete weighted by: **Current Budget***

Then, if *CB earned cost* is \$500 and *CB total cost* is \$1000, the parent cost item is calculated as $\$500/\$1000 = 50\%$ as the *% complete*. *Actual qty (to-date)* is then *% complete* multiplied by the *Forecast (T/O) qty* or *CB total qty* depending on what you have selected in settings against *Calculate percent complete for individual cost items as a percentage of*. If you had *Forecast (T/O) qty* as this setting and the *Forecast (T/O) qty* on the parent is 1.00, then the *Actual qty (to date)* would be $50\% \times 1.00 = 0.50$.

See Also:

[Project Settings](#)

[Progress Measurement Overview](#)

Related Videos:



[Video Link Title Here](#)

How do I get my Current Budget (CB) and Current Estimate (CE) values to be in sync?

Set the desired values in the CBS for CE total cost, CE total MHrs, and Forecast (T/O) qty. Within a Contract adjustment using the **Start with Cost items** option or a Non-associated budget move, click the **Calculate** icon to auto-populate the adjusted cost, man-hours, and/or quantities with values to match the current estimate. Within a Contract adjustment using the **Start with Pay items** option or an Associated budget move, click on the **Advanced options** button to do the same.

See Also:

[Associated Budget Move \(Net Zero Dollar Move\)](#)

[Non-Associated Budget Move](#)

[Contract Adjustment](#)

Related Videos:

[Video Link Title Here](#)

I can't edit resource values on a cost item - why?

The cost item's cost source must be set to Detail to edit the resource attributes and values on a cost item.

See Also:

[Cost Item Details](#)

[Estimate Resources](#)

Related Videos:

[Video Link Title Here](#)

I can't submit or approve a budget move - why?

Does the overall adjusted cost = 0? If not, you cannot submit. Do you have the permission to approve change orders? If not, someone else on your project with the **Approve change orders** permission will need to approve.

See Also:

*Title Link Here

Related Videos:

[Video Link Title Here](#)

I can't submit or approve a contract adjustment - why?

Was the contract adjustment initiated from Change? If so, the total adjusted price in the **Pay items** step must equal the executed price on the change order from Change.

See Also:

[Contract Adjustment](#)

Related Videos:

[Video Link Title Here](#)

My Forecast (T/O) qty changed without me directly changing it - why?

Check the Qty driver, is it set to Superior CI? And then did someone change the parent qty? This updates the children with a Qty driver of Superior CI.

See Also:

*Title Link Here

Related Videos:



[Video Link Title Here](#)

I can't change my Allow as-built option on my cost item - why?

Check the Qty driver, is it set to Superior CI? And then did someone change the parent qty? This updates the children with a Qty driver of Superior CI.

See Also:

[Progress Control Settings](#)

[Actuals by Sync](#)

[Actuals by Manual Entry](#)

Related Videos:



[Video Link Title Here](#)

I can't see the change to this field in the audit log - why?

Was it changed through Excel import? Excel import changes do not create an entry in the audit log.

See Also:

[Audit Log](#)

Related Videos:



[Video Link Title Here](#)

When I send a view to an organization, do people assigned to projects get the view or just people assigned to the org?

People assigned to either the organization or any project under that org will receive the view.

See Also:

*Title Link Here

Related Videos:

[Video Link Title Here](#)

My forecast calculations are wrong!

Check that your organization isn't within "plus days", and if it is, then make sure you are calculating excluding any actuals with a posting date after the month end date.

See Also:

*Title Link Here

Related Videos:

[Video Link Title Here](#)

14.29 FREQUENTLY ASKED QUESTIONS

Why is the actual quantity not rolling up to the parent cost item?

Actual qty (to date) is calculated at the parent level rather than a roll up value of *Actual qty (to date)* on the children. There is a section in Control Project Settings > Project Tracking > **Actuals** which determines how this is calculated. These settings are *Calculate percent complete for roll-up items such as superior cost items and account code by:* and *Roll-up percent complete weighted by:*.

For example, if the project has the following options in the Actuals settings:

- *Calculate percent complete for roll-up items such as superior cost items and account code by:* **Cost**
- *Roll-up percent complete weighted by:* **Current Budget**

Then, if *CB earned cost* is \$500 and *CB total cost* is \$1000, the parent cost item is calculated as $\$500/\$1000 = 50\%$ as the *% complete*. *Actual qty (to-date)* is then *% complete* multiplied by the *Forecast (T/O) qty* or *CB total qty* depending on what you have selected in settings against *Calculate percent complete for individual cost items as a percentage of*. If you had *Forecast (T/O) qty* as this setting and the *Forecast (T/O) qty* on the parent is 1.00, then the *Actual qty (to date)* would be $50\% \times 1.00 = 0.50$.

See Also:[Project Settings](#)[Progress Measurement Overview](#)**Related Videos:**[Video Link Title Here](#)

How do I get my Current Budget (CB) and Current Estimate (CE) values to be in sync?

Set the desired values in the CBS for CE total cost, CE total MHrs, and Forecast (T/O) qty. Within a Contract adjustment using the **Start with Cost items** option or a Non-associated budget move, click the **Calculate** icon to auto-populate the adjusted cost, man-hours, and/or quantities with values to match the current estimate. Within a Contract adjustment using the **Start with Pay items** option or an Associated budget move, click on the **Advanced options** button to do the same.

See Also:[Associated Budget Move \(Net Zero Dollar Move\)](#)[Non-Associated Budget Move](#)[Contract Adjustment](#)**Related Videos:**[Video Link Title Here](#)

I can't edit resource values on a cost item - why?

The cost item's cost source must be set to Detail to edit the resource attributes and values on a cost item.

See Also:[Cost Item Details](#)[Estimate Resources](#)**Related Videos:**[Video Link Title Here](#)

I can't submit or approve a budget move - why?

Does the overall adjusted cost = 0? If not, you cannot submit. Do you have the permission to approve change orders? If not, someone else on your project with the **Approve change orders** permission will need to approve.

See Also:

*Title Link Here

Related Videos:



[Video Link Title Here](#)

I can't submit or approve a contract adjustment - why?

Was the contract adjustment initiated from Change? If so, the total adjusted price in the **Pay items** step must equal the executed price on the change order from Change.

See Also:

[Contract Adjustment](#)

Related Videos:



[Video Link Title Here](#)

My Forecast (T/O) qty changed without me directly changing it - why?

Check the Qty driver, is it set to Superior CI? And then did someone change the parent qty? This updates the children with a Qty driver of Superior CI.

See Also:

*Title Link Here

Related Videos:



[Video Link Title Here](#)

I can't change my Allow as-built option on my cost item - why?

Check the Qty driver, is it set to Superior CI? And then did someone change the parent qty? This updates the children with a Qty driver of Superior CI.

See Also:

[Progress Control Settings](#)

[Actuals by Sync](#)

[Actuals by Manual Entry](#)

Related Videos:



[Video Link Title Here](#)

I can't see the change to this field in the audit log - why?

Was it changed through Excel import? Excel import changes do not create an entry in the audit log.

See Also:

[Audit Log](#)

Related Videos:



[Video Link Title Here](#)

When I send a view to an organization, do people assigned to projects get the view or just people assigned to the org?

People assigned to either the organization or any project under that org will receive the view.

See Also:

*Title Link Here

Related Videos:



[Video Link Title Here](#)

My forecast calculations are wrong!

Check that your organization isn't within "plus days", and if it is, then make sure you are calculating excluding any actuals with a posting date after the month end date.

See Also:

*Title Link Here

Related Videos:




Video Link Title Here

14.30 WORKFLOWS


14.30.1 Product Workflows

14.30.1.1 InEight Control General Workflow

This workflow illustrates the main features of InEight Control, including managing account codes, measuring progress, forecasting final man-hours and costs, managing revenue and managing budget and contract changes.

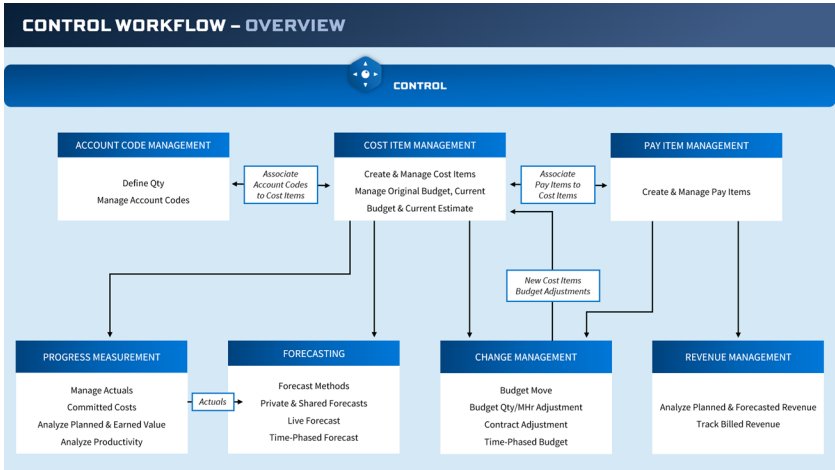


InEight Control General Workflow

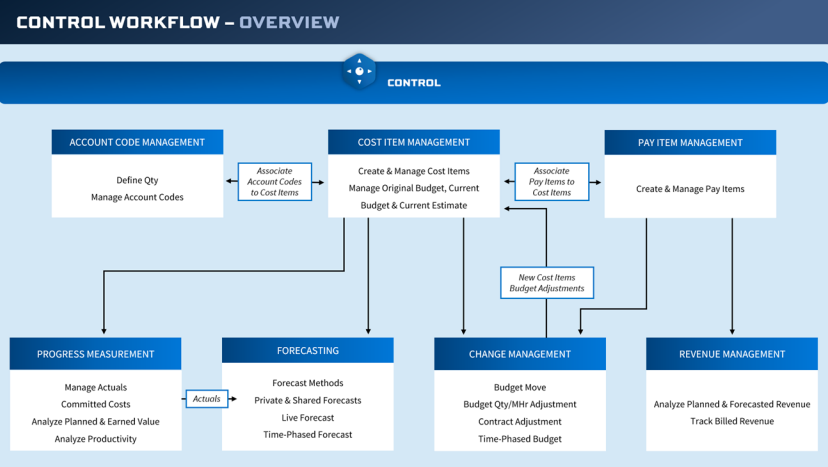

14.30.2 Business Process Workflows


14.30.2.2 Cost Budgeting and Forecasting: Budget Management

This workflow illustrates the main features of InEight Control, including managing account codes, measuring progress, forecasting final man-hours and costs, managing revenue and managing budget and contract changes.

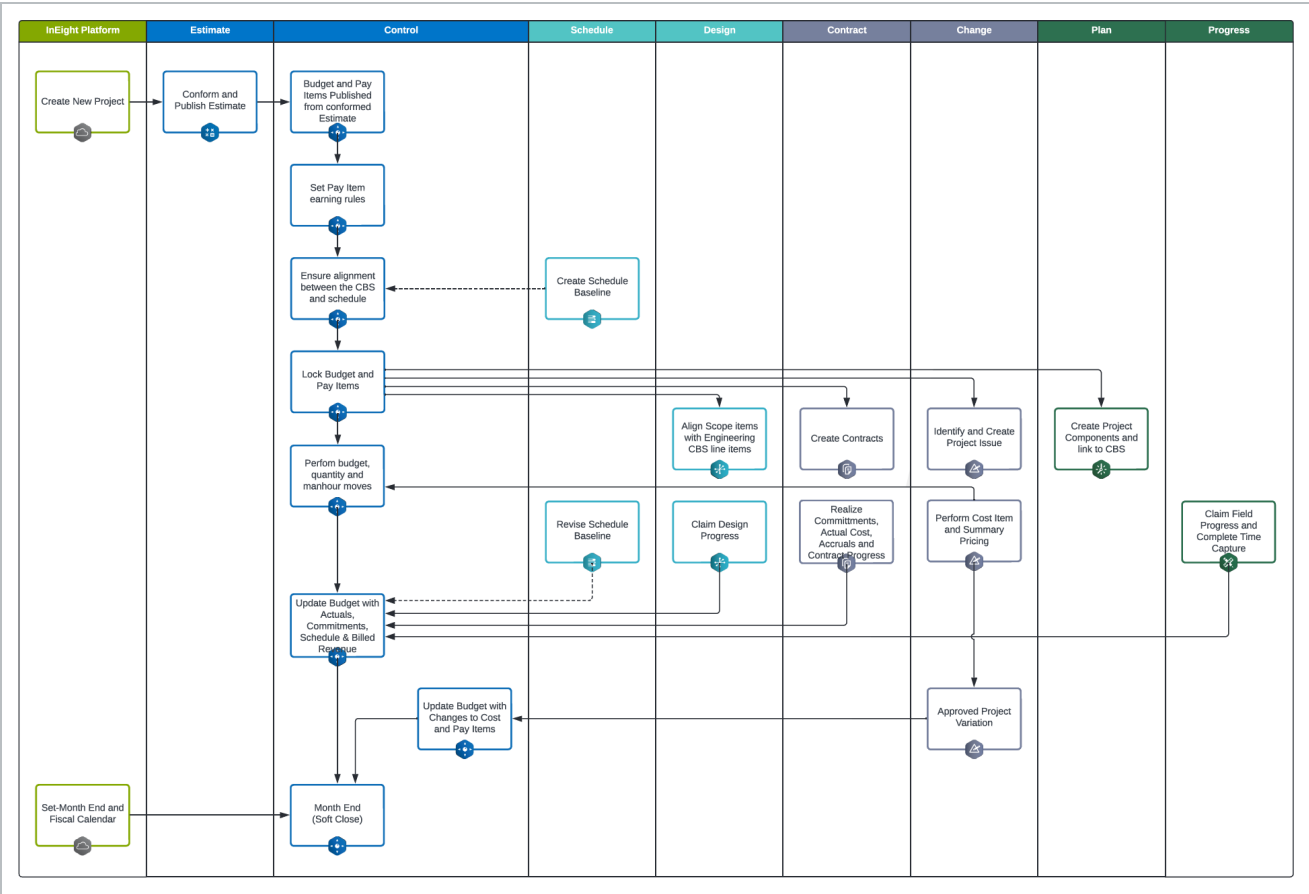


14.30.2.3 Cost Budgeting and Forecasting: Forecasting

This workflow shows how InEight Control can be used to create multiple shareable forecasts as needed, either through automatic calculation or manual entry.

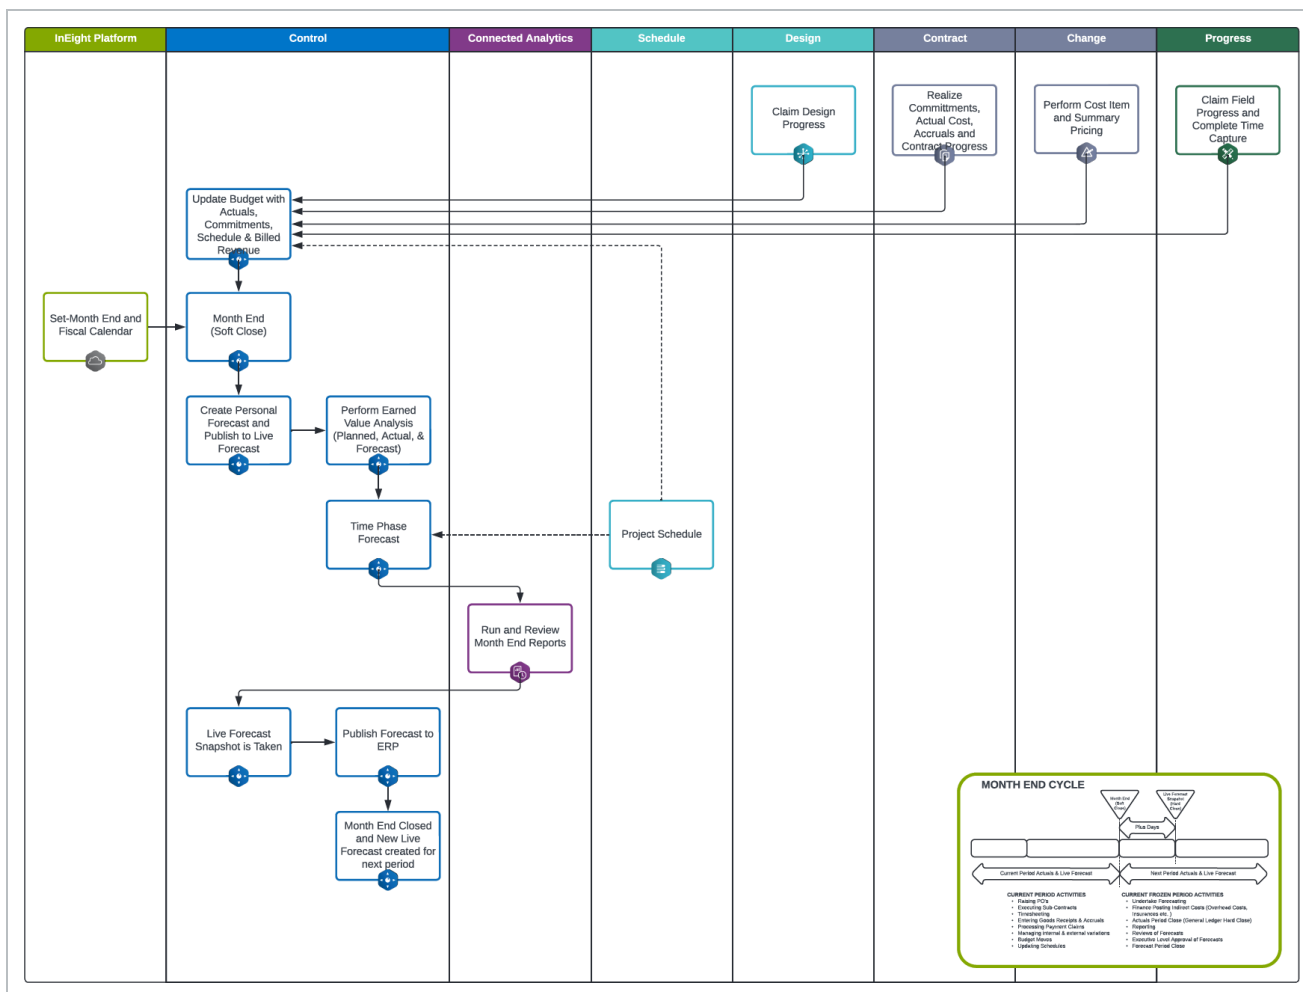

14.30.2.4 Billing Management

This workflow shows how InEight Control can be used to access current budget and pay item details and keep the budget up to date throughout the billing cycle.

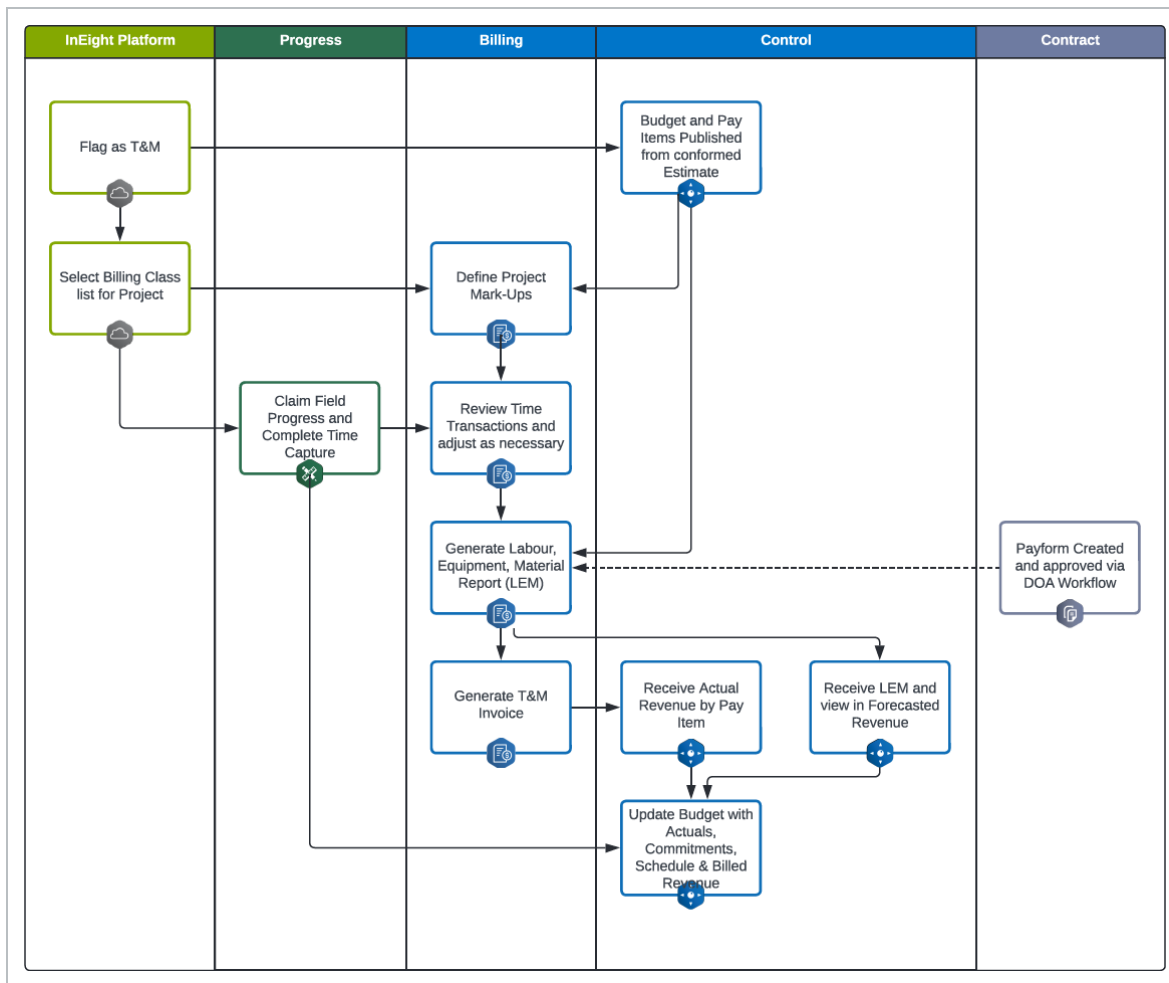

14.30.2.5 Earned Value Management

This workflow illustrates how InEight Control can be used to track earned value through a variety of performance indicators.

